

One Energy Place
Pensacola, Florida 32520

Tel 850.444.6111



September 6, 2002

Ms. Blanca S. Bayo, Director
Division of the Commission Clerk and Administrative Services
Florida Public Service Commission
2540 Shumard Oak Boulevard
Tallahassee FL 32399-0870

Dear Ms. Bayo:

RE: Docket No. 020943-EI

In order to file the FDEP/Gulf Power Company Agreement in a timely manner, Gulf relied on a faxed copy of Exhibit A. Enclosed is a color copy of Exhibit A that is legible.

Sincerely,

A handwritten signature in cursive script that reads "Susan D. Ritenour".

Susan D. Ritenour
Assistant Secretary and Assistant Treasurer


lw

cc: Beggs and Lane
Jeffrey A. Stone, Esquire
Parties of Record

DOCUMENT NUMBER - DATE
09472 SEP-98
FPSC-COMMISSION CLERK

Exhibit "A"

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish	Total Float	2002		2003		2004		2005			
						F	M	A	M	J	J	A	S	O	N
PRECIPITATOR															
TIE-IN OUTAGE															
CST186	Precipitator Tie-In	65	06MAR04	09MAY04	0										
ENGINEERING															
ENG001	Project Start	0	01APR02*		0										
ENG138	Preliminary Engineering	65	01APR02	28JUN02	8										
ENG105	Detail Engineering/Design and Support- Precip	204	01JUL02	03APR03	10										
ENG186	SCS Design Ductwork and Supports	100	20AUG02	04JAN03	78										
ENG116	Receive Foundation Info From Precip Vendor	0	02SEP02		0										
ENG176	SCS Design Pile and Foundations	40	02SEP02	25OCT02	0										
ENG186	SCS Prepare Pile Erection Spec	20	23SEP02	18OCT02	0										
ENG186	Award Pile Erection	0	06DEC02		0										
PROCUREMENT															
PRO160	Prep Spec for Precipitator Design and Supply	30	01APR02	10MAY02	0										
PRO190	Issue Precipitator Inquiry for Bids	0		13MAY02	0										
PRO200	Receive Precipitator Bids	0		24JUN02	0										
PRO210	Evaluate Precipitator Bids	20	25JUN02	22JUL02	0										
PRO170	Award Precipitator Design and Supply	0		22JUL02	0										
PRO115	Vendor Design Precipitator	130	23JUL02	17JAN03	0										
PRO155	Flow Modeling - Precipitator	60	20AUG02	11NOV02	10										
PRO180	Precipitator - Fabricate and Deliver	150	18JAN03	08AUG03	55										
CONSTRUCTION															
CST104	Relocations	66	28AUG02	25NOV02	8										
CST106	Install Piles	50	06DEC02	06FEB03	0										
CST128	Install Pile Caps	50	07FEB03	16APR03	0										
CST138	Erect Precip and Ductwork Supt Steel	80	17APR03	08AUG03	0										
CST146	Erect Ductwork	60	03JUL03	24SEP03	40										
CST166	Erect Precipitator Box	125	07AUG03	28JAN04	0										
CST176	Erect Precipitator Mechanical Equipment	105	02OCT03	17FEB04	17										
CST166	Erect Precipitator Electrical Equipment	105	27OCT03	05MAR04	0										
STARTUP															
SU196	Checkout and Start-up	40	31MAR04	09MAY04	0										
SELECTIVE CATALYTIC REDUCTION															
TIE-IN OUTAGE															
CST113	SCR Relocations Outage	35	08MAR03*	11APR03	0										
CST101	Building Relocation Outage	85	06MAR04	09MAY04	0										
CST103	SCR Tie-In Outage	70	03FEB05	13APR05	0										
ENGINEERING															
ENG000	Project Start	0	20MAY02*		0										
ENG137	Preliminary Engineering	60	20MAY02	09AUG02	0										
ENG100	Detail Engineering/Design	340	12AUG02	20NOV03	0										
ENG110	Construction Support	320	24SEP03	23NOV04	69										
ENG120	Startup Support	100	04JAN05	13APR05	48										
PROCUREMENT															
PRO140	Award Catalyst	0		08NOV02	13										
PRO150	Flow Modeling	85	11NOV02	28FEB03	228										
PRO130	Award ID Fans and Motors	0		28JAN03	44										
PRO100	Award Structural Steel	0		14FEB03	21										
PRO105	Fabricate and Deliver Structural Steel	140	17FEB03	28AUG03	21										
PRO145	Fabricate and Deliver Catalyst	270	28DEC03	16DEC04	13										
PRO135	Fabricate and Deliver ID Fans and Motors	250	09JAN04	02DEC04	44										
CONSTRUCTION															
CST100	Relocations	70	13JAN03	11APR03	0										
CST105	Install Piles	100	14APR03	28AUG03	0										
CST125	Install Pile Caps	80	09JUN03	26SEP03	0										
CST110	Award General Contractor	0		12SEP03	10										
CST115	Erect Structural Steel	125	28SEP03	05MAR04	0										
CST130	Structural Building Modifications	50	07MAR04	10MAY04	0										
CST135	Erect Steel to Reactor Level	40	11MAY04	05JUL04	0										
CST140	Erect Remaining Steel	164	11MAY04	24DEC04	7										
CST145	Erect Reactor Box	125	08JUN04	29NOV04	0										
CST150	Install Mechanical Systems	115	06JUL04	19DEC04	0										
CST155	Install Electrical Systems	115	26JUL04	04JAN05	0										
CST160	Load Catalyst	21	05JAN05	02FEB05	0										
STARTUP															
SU0165	Checkout and Start-Up	100	04JAN05	13APR05	0										

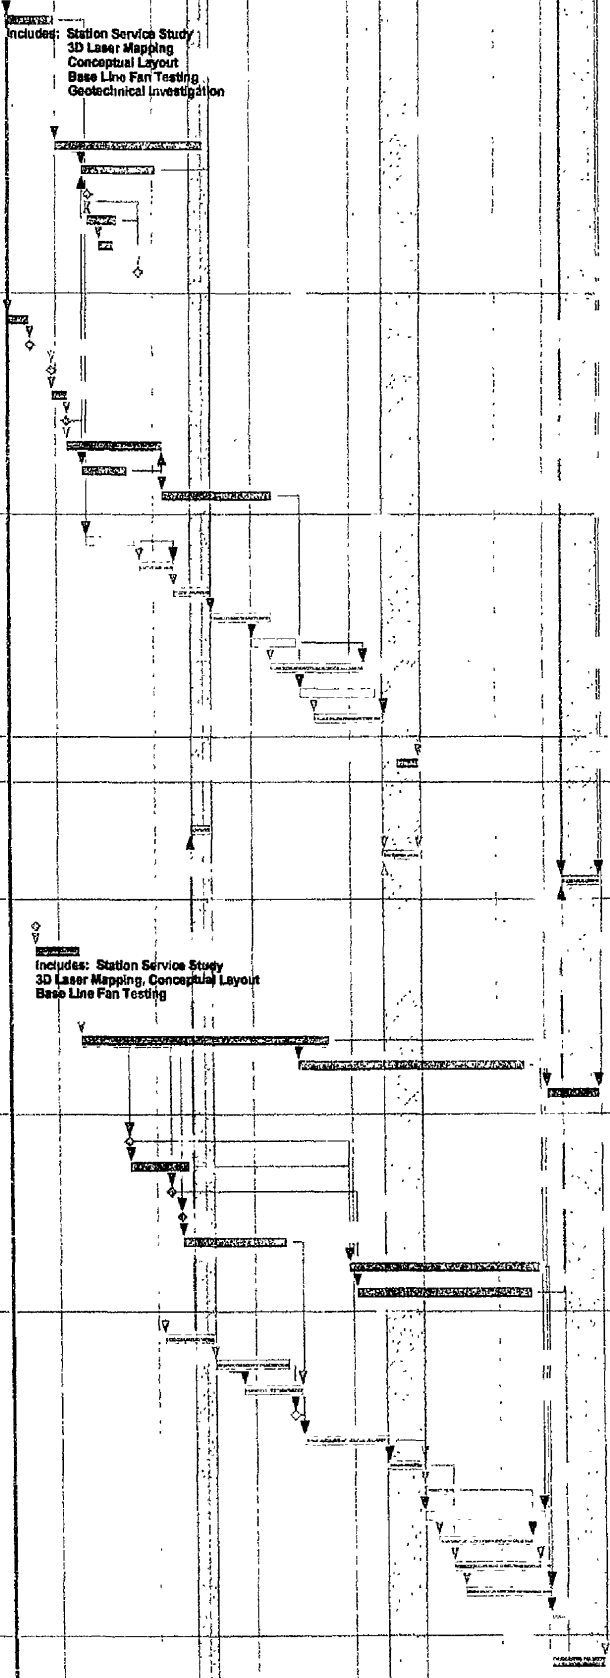

Start Date 01APR02 C7PS
 Finish Date 13APR05
 Data Date 01APR02
 Run Date 11APR02 07:31

SOUTHERN COMPANY GENERATION

CRIST UNIT 7 SCR / PRECIPITATOR

Sheet 1 of 1

Date	Revision	Checked/Approved
28MAR02	Review and Comment	
29MAR02	Include Total Project for Review	
