



Stephanie A. Cuello
SENIOR COUNSEL

July 31, 2024

VIA ELECTRONIC FILING

Adam J. Teitzman, Commission Clerk
Florida Public Service Commission
2540 Shumard Oak Boulevard
Tallahassee, Florida 32399-0850

Re: *Petition by Duke Energy Florida, LLC, to Approve Transaction with Accelerated Decommissioning Partners, LLC, for Accelerated Decommissioning Services at the CR3 Facility, etc.*
Docket No. 20190140-EI

Dear Mr. Teitzman:

Enclosed for filing on behalf of Duke Energy Florida, LLC (“DEF”), please find the Decommissioning Quarterly Report received from Accelerated Decommissioning Partners (ADP) on July 18, 2024 for the quarter ending June 2024. Order No. PSC-2020-0289-FOF-EI, dated August 27, 2020, issued in the above-referenced docket, provides that “2. The information responsive to items identified in the DSA [Decommission Services Agreement], Attachment 9, Section B through E should be provided to the Commission within two weeks of DEF’s receipt of this information from ADP.”

Thank you for your assistance in this matter and if you have any questions, please feel free to contact me at (850) 521-1425.

Sincerely,

/s/ Stephanie A. Cuello

Stephanie A. Cuello

SAC/clg
Enclosure

CERTIFICATE OF SERVICE

I HEREBY CERTIFY that a true and correct copy of the foregoing has been furnished via electronic mail to the following this 31st day of July, 2024.

/s/ Stephanie A. Cuello

Attorney

<p>Suzanne Brownless Florida Public Service Commission 2540 Shumard Oak Blvd. Tallahassee, FL 32399-0850 sbrownle@psc.state.fl.us</p> <p>Jon C. Moyle, Jr. / Karen A. Putnal Moyle Law Firm, P.A. 118 North Gadsden Street Tallahassee, FL 32301 jmoyle@moylelaw.com kputnal@moylelaw.com mqualls@moylelaw.com</p>	<p>Charles J. Rehwinkel Office of Public Counsel c/o The Florida Legislature 111 West Madison Street, Room 812 Tallahassee, FL 32399 rehwinkel.charles@leg.state.fl.us</p> <p>James W. Brew / Laura Wynn Baker Stone Mattheis Xenopoulos & Brew, PC 1025 Thomas Jefferson St., N.W. Suite 800 West Washington, DC 20007-5201 jbrew@smxblaw.com lwb@smxblaw.com</p>
---	---



Billy E. Reid, Decommissioning Program Manager

c.865.384.6789

BReid@NorthStar.com

ADP24-0011

July 18, 2024

Gene Flavors (via electronic mail)
DEF General Manager
Site Administration Building
Crystal River Energy Complex (CREC)

Subject: Materials for Quarterly Meeting

Dear Mr. Flavors,

In accordance with the Decommissioning Services Agreement (DSA) section 6.12.1 and Attachment 9, attached you will find the materials prepared by ADP CR3, LLC (ADP) for the upcoming quarterly meeting scheduled for July 25, 2023. Please note that the schedule included in the attached also satisfies the requirements for the quarterly schedule update stipulated at section 6.7 of the DSA.

Should you have any questions or comments, contact me at your convenience at either bereid@northstar.com or 865-384-6789.

Sincerely,

A handwritten signature in blue ink, appearing to read "Billy E. Reid".

Billy E. Reid
Decommissioning Program Manager

Cc: Luke Self (ADP / NS)
Nelson Langub (ADP / NS)
David Pearson (ADP / NS)
James Seals (ADP / Orano)



ADP CR3, LLC

Decommissioning Quarterly Report

for quarter ending

June 2024

Contents

1.0	EXECUTIVE SUMMARY	3
2.0	SUMMARY OF REGULATORY EVENTS AND REPORTS	3
3.0	PAY ITEM DISPUTE SUMMARY	4
4.0	ADP CR3 NON-COMPLIANCE ITEMS.....	4
5.0	CONCERNS NEEDING MANAGEMENT ATTENTION	4
6.0	SUBMITTED AND PENDING REGULATORY SUBMITTALS.....	5
7.0	COMPLETED AND NEAR-TERM SCHEDULE MILESTONES	7

1.0 EXECUTIVE SUMMARY

This is the ADP CR3 quarterly report on the decommissioning of the Crystal River Unit 3 nuclear plant in accordance with the requirements of the First Amendment to the Decommissioning Services Agreement (DSA), Attachment 9, *Reporting and Notification Requirements*, reflecting the quarter from April 1, through June 30, 2024.

Q2 Safety and Environmental Performance

Injury/Illness Summary	2nd Quarter 2024	YTD 2024	PTD 2024
Project Hours	71,190	150,747	1,253,169
First Aid Cases	0	1	17
Recordable Cases	0	0	1
Lost Workday Cases	0	0	0

- First Aid Case
 - None this Quarter
- ALARA Actual exposure YTD = 4430 mrem actual vs 6933 mrem budget
- Personnel Contamination = 2 Level 1 PCE
 - Metal sliver cut through rubber boot
 - PC doffing at contaminated area
- NRC RP Inspections identified no discrepancies.
- Heat Stress = 0

2.0 This quarter commenced with the shipping of the Reactor Vessel and Internal packages from Texas storage area to WCS site in Texas. Packages containing the components of the RPV were shipped from the port to WCS by heavy haul conveyance. The RPV head and Bottom pieces have made it to WCS and were disposed of in Q2 of 2024. The RPV middle package was received at WCS in the second quarter and the top package is still waiting transport from the port to WCS. Upon arrival to WCS, the RPV top and middle packages should be disposed of in Q3 of 2024. Continued progress on the building demolition with the Intermediate building structural demolition finishing in June. Interior demolition of the Auxiliary building progressed this quarter and is scheduled to complete August 2024. Reactor building systems removal to be completed in Q3 of 2024. Decon of the Reactor Building will continue through the third quarter. Mobilization of interior demolition crew completed in the second quarter and is scheduled to start in July. Other miscellaneous yard structures completed this quarter including Nuclear Admin Building. Planning and preparations for other sequences of work continued this quarter. No used nuclear fuel related violations, environmental non-compliance, or significant industrial safety events occurred or were reported.

3.0 SUMMARY OF REGULATORY EVENTS AND REPORTS

1. Reportable events to Governmental Authority (e.g., NRC, OSHA, FDEP, EPA):

NONE

2. Receipt of any correspondence from any Governmental Authority of violation or finding:

NONE

3. Any breach of debt covenants, default acceleration, insolvency, reorganization, bankruptcy or liquidation of NorthStar Group Services, Inc., and/or proposed organizational changes in equity ownership of NorthStar Group Holdings, LLC or ORANO SA:

NONE

4. Events that require Duke Energy Florida (DEF) to make a report to ANI:

NONE

5. Events that require Duke Energy Florida (DEF) to make a report to NEIL:

NONE

4.0 PAY ITEM DISPUTE SUMMARY

There are no pay items in dispute. DEF has communicated that the quality of the documentation of Pay Item completion has been very good, with progress of all Pay Item being validated.

5.0 ADP CR3 NON-COMPLIANCE ITEMS

There have been no non-compliance items this quarter.

6.0 CONCERNS NEEDING MANAGEMENT ATTENTION

No concerns needing management attention currently.

ADP CR3 Decommissioning Quarterly Report
2Q-2024

7.0 SUBMITTED AND PENDING REGULATORY SUBMITTALS

NRC Letter Log and Submittal Register

NUMBER	DATE	FROM ORG	FROM PERSON	SUBJECT	NRC ACCESSION #	Notes
3F0124-01	1/18/2024	CR3	Reid	Response to Environmental RAls	ML24018A151	3F and REG0016 submitted to records
3F0124-02	1/18/2024	CR3	Reid	Proof of Financial Protection	ML24018A213	3F submitted to records
3F0124-03	1/19/2024	CR3	Reid	Late Received Radiological Shipment	ML24021A001	3F and REG0016 submitted to records
3F0224-01	2/5/2024	CR3	Jernigan	Email Clarifications related to the NRC Staff's EA for Crystal River	ML24025A095	3F and REG0016 submitted to records
3F0224-02	2/6/2024	CR3	Reid	Crystal River 3 - Application to for Minor Revision to NPDES, FLOA00004	ML24039A099	3F and REG0016 submitted to records
3F0224-03	2/7/2024	CR3	Reid	Late Received Radiological Shipment	ML24039A108	3F and REG0016 submitted to records
3F0224-04	2/20/2024	CR3	Reid	CR3 ISFSI Security Plan, Security Training and Qualificiation Plan, and Safeguards Contingency Plan, Rev. 4		-Safeguards Information, hard copy mailed. -Submitted to records.
3F0224-05	2/24/2024	CR3	Reid	Late Received Radiological Shipment	ML24053A388	3F and REG0016 submitted to records
3F0324-01	3/27/2024	CR3	State	CR3 Annual Decommissioning and Irradiated Fuel Management Financial Status Report for 2023	ML24087A205	3F submitted to records.
3F0324-02	3/22/2024	CR3	Reid	Crystal River 3 – Onsite Property Insurance Coverage	ML24082A011	3F and REG0016 submitted to records
3F0324-03	3/29/2024	CR3	Reid	Response to RAls - LTP Submittal	ML24089A036 ML24090A004 ML24090A005 ML24090A006 ML24090A007	3F and REG0016 submitted to records
3F0324-04	3/27/2024	CR3	Van Sicklen	Crystal River 3 – 2022 Individual Monitoring NRC Form 5 Report	ML24087A186	3F submitted to records.
3F0424-01	4/12/2024	CR3	Reid	Late Received Radiological Shipment	ML24103A068	3F and REG0016 submitted to records
3F0424-02	4/29/2024	CR3	Reid	Crystal River 3 - 2023 Annual Radioactive Effluent Release Report (ARERR)	ML24120A336	3F and REG0016 submitted to records
3F0424-03	4/30/2024	CR3	Van Sicklen	Crystal River Unit 3 - 2023 Annual Radiological Environmental Operating Report (AREOR)	ML24121A121	3F Submitted to records
3F0524-01	5/10/2024	CR3	Reid	Response to Environmental RAls with Encl 5 withheld from public disclosure	ML24131A075 ML24131A076- (proprietary)	3F and REG0016 submitted to records
3F0524-02	5/29/2024	CR3	Reid	Biennial DSAR - QAPM - 50.59 - 72.48 Change Report	ML24150A264	3F Submitted to records
3F0524-03	5/30/2024	CR3	Adix	Annual Corporate Financial Report (Att1 and Att2/Confidential)	ML24155A153 ML24155A154- (Confidential)	3F Submitted to records
3F0624-01	6/6/2024	CR3	Reid	Response to NRC Environmental Assessment, Florida Fish and Wildlife, Questions	ML24166A079 ML24166A080- (proprietary)	3F Submitted to records
3F0624-02	6/14/2024	CR3	Reid	Late Received Radiological Shipment	ML24165A121	3F and REG0016 submitted to records

ADP CR3 Decommissioning Quarterly Report
2Q-2024


2024 Crystal River 3 – NRC Submittals		
Submittal	Submittal to be Signed	Comments
Proof of Financial Protection, Financial Liability Policy Renewal (ANI)	January 31, 2024	10 CFR 140.15, 140.11(a)(4) Exempted, 10 CFR 140.17(b)
Annual Decommissioning and Irradiated Fuel Management Financial Status Report	March 31, 2024	10 CFR 50.82(a)(8)(v), (vi) and (vii) and 10 CFR 50.75(f)(1) and (2)
Copy of Material Balance Report and Physical Inventory Listing Report (12 month frequency requirement from last submittal)	March 31, 2024	10 CFR 74.13(a) and 10 CFR 74.15, 10 CFR 70.55, 10 CFR 72.76, 10 CFR 72.78, (Within 60 days following the start of the annual physical inventory of special nuclear material and/or source material)
Onsite Property Insurance Coverage (NEIL)	April 1, 2024	10 CFR 50.54(w)(3)
Radiation Exposure Report To Employees (RPCM initiates)	April 30, 2024	10 CFR 19.13(b) and 10 CFR 20.2206
Annual Radioactive Effluent Release Report and a copy of the ODCM	May 1, 2024	Submit report per 10 CFR 50.36a(a)(2) and ODCM; CP-500
Annual Radioactive Radiological Environmental Operating Report	May 15, 2024	10 CFR 50 Appendix I; Submit report per ODCM; CP-500
Annual Copy of Corporate Financial Report See 10 CFR 140.15 (a)	Annually (within 30 days of issuance of annual report)	10 CFR 50.71(b) 10 CFR 72.80(b)
Biennial DSAR – QAPM - 50.59 - 72.48 - Change Report	May 31, 2024	Submit report per 10 CFR 50.71(e), 10 CFR 50.54(a)(3), 10 CFR 50.59(d)(2) and 10 CFR 72.48(d)(2)
Crystal River Unit 3 – Reporting Related to the National Pollutant Discharge Elimination System (NPDES) Permit ID# FL0A00004-001-IW1S	As needed	CP-500
Crystal River 3 – Report of Investigation Pursuant to 10 CFR 20, Appendix G.	As needed	10 CFR 20, Appendix G, as exempted

Submittals	NRC Accession/ TAC Number	NRC Approval Requested	Next Expected Action	Comments
Response to Environmental RAIs	ML24018A151 ML24131A075 ML24131A076 ML24166A079 ML24166A080			
Crystal River 3 – Report of Investigation Pursuant to 10 CFR 20, Appendix G	ML24021A001 ML24039A108 ML24053A388 ML24103A068 ML24165A121			
Physical Security Plan, Rev. 4	n/a			Received by NRC 2/22/24
NPDES Permit Revision	ML24039A099			

Submittals	NRC Accession/ TAC Number	NRC Approval Requested	Next Expected Action	Comments
Response to LTP RAIs	ML24089A036 ML24090A004 ML24090A005 ML24090A006 ML24090A007			

Environmental

AOC Status Table attached.

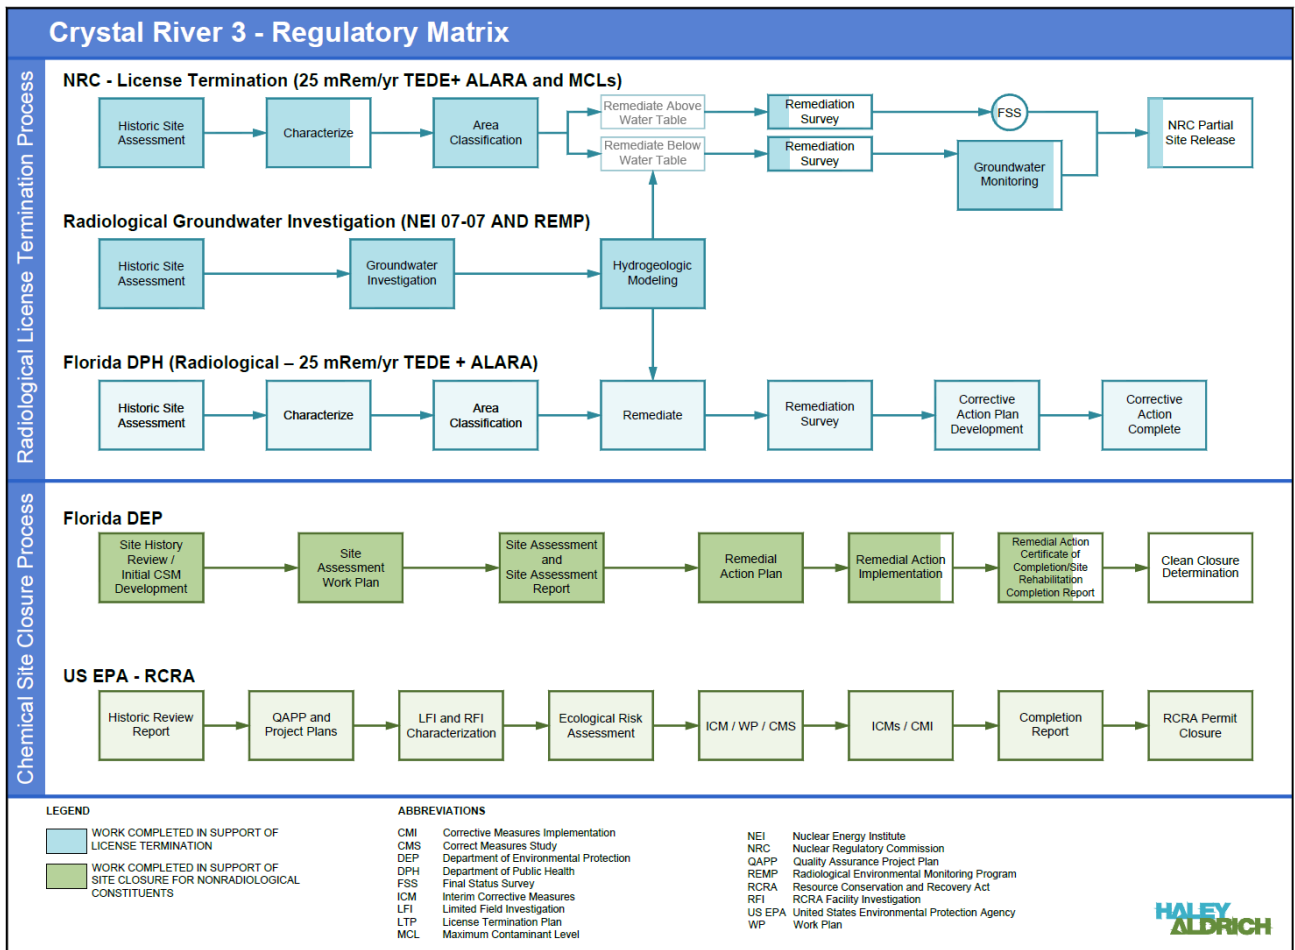

8.0 COMPLETED AND NEAR-TERM SCHEDULE MILESTONES

	PAY ITEM/MILESTONE	PLANNED COMPLETE	STATUS
3.1.1.1	Planning & Site Preparation Utilities Reactivation		100% Complete
3.1.1.2	Planning & Site Preparation Containment Access, Waste Handling Areas		100% Complete
3.1.2	Planning & Site Preparation Site Characterization		100% Complete
3.1.3.1	Planning & Site Preparation LCR and RV/RVI Planning and Engineering General transition Planning/Engineering		100% Complete

ADP CR3 Decommissioning Quarterly Report
2Q-2024

	PAY ITEM/MILESTONE	PLANNED COMPLETE	STATUS
3.1.3.2	Planning & Site Preparation LCR and RV/RVI Planning and Engineering Site/Plant infrastructure Planning and Engineering		100% Complete
3.1.3.3	Planning & Site Preparation LCR and RV/RVI Planning and Engineering RVI Planning and Engineering		100 % Complete
3.1.3.4	Planning & Site Preparation LCR and RV/RVI Planning and Engineering RV Planning and Engineering		77% Complete
3.1.3.5	Planning & Site Preparation LCR and RV/RVI Planning and Engineering LCR Planning and Engineering		100% Complete
3.1.4.1	Planning & Site Preparation Balance of Plant D&D Planning Temporary Utilities, Site Preparation Planning		100% Complete
3.1.4.2	Planning & Site Preparation Balance of Plant D&D Planning Turbine, Condenser, Steam Generator Removal Planning		100% Complete
3.1.4.3	Planning & Site Preparation Balance of Plant D&D Planning Systems Removal and Decon Work Planning		100% Complete
3.1.4.4	Planning & Site Preparation Balance of Plant D&D Planning Demolition Work Planning	5/31/2024	49% Complete
4.A.1.1	Large Component Removal Reactor Internals Segmentation Reactor Internals Mobilization, Setup & Commissioning		100% Complete
4.A.1.2	Large Component Removal Reactor Internals Segmentation Reactor Internals Segmentation (Plenum Assembly)		100% Complete
4.A.1.3	Large Component Removal Reactor Internals Segmentation Reactor Internals Segmentation (Core Support Assembly/Remaining)		100% Complete
4.A.1.4	Large Component Removal Reactor Internals Segmentation Reactor Internals Waste Packaging, Transportation and Disposal	5/31/2024	20% Complete
4.A.2.1	Large Component Removal Reactor Vessel Segmentation Reactor Vessel Mobilization		100% Complete
4.A.2.2	Large Component Removal Reactor Vessel Segmentation Reactor Vessel Segmentation		100% Complete

ADP CR3 Decommissioning Quarterly Report
2Q-2024

	PAY ITEM/MILESTONE	PLANNED COMPLETE	STATUS
4.A.3	Large Component Removal Reactor Vessel Segmentation Reactor CRDMs, ICIs, Services Structure		100% Complete
4.A.4.1	Large Component Removal Reactor Coolant System Reactor Coolant Piping		100% Complete
4.A.4.2	Large Component Removal Reactor Coolant System Reactor Coolant System Pumps and Motors		100% Complete
4.A.5	Large Component Removal Reactor Coolant System Pressurizer and Relief Tank		100% Complete
4.A.6.5	Large Component Removal Steam Generators Steam Generator Package, Transportation and Disposal		100% Complete
4.A.7.1	Large Component Removal Main Turbine/Generator/Condensers Turbine and Generator Removal		100% Complete
4.A.7.1	Large Component Removal Condenser Removal		100% Complete
4.B.1.1	Site Decontamination Remove Plant Systems Reactor Building	7/31/2024	85% Complete
4.B.1.2	Site Decontamination Remove Plant Systems Auxiliary Building elev 95'	7/31/2024	95% Complete
4.B.1.3	Site Decontamination Remove Plant Systems Auxiliary Building elev 119'	7/31/2024	95% Complete
4.B.1.4	Site Decontamination Remove Plant Systems Intermediate Building		100% Complete
4.B.1.5	Site Decontamination Remove Plant Systems Turbine Building		100% Complete
4.B.2.1-3	Decontaminate Reactor Building	3/31/2025	10% Complete
4.B.2.4	Decontaminate Auxiliary Building	8/30/2024	33% Complete
4.B.2.5	Decontaminate Intermediate Building		100% Complete
4.B.4	Site Decontamination Decontaminate Buildings License Termination Planning		100% Complete

ADP CR3 Decommissioning Quarterly Report
2Q-2024

	PAY ITEM/MILESTONE	PLANNED COMPLETE	STATUS
4.B.5.1	Site Decontamination Decontaminate Buildings West Settling Pond Remediation		100% Complete
4.B.5.3	Site Decontamination Decontaminate Buildings Transfer Canal Sand Removal		100% Complete
5.1.1	Site Restoration Demolish Turbine Building		100% Complete
5.1.2	Site Restoration Demolish Miscellaneous Site Structures Emergency Feed Water Building		100% Complete
5.1.2	Site Restoration Demolish Miscellaneous Site Structures Diesel Generator Building		100% Complete
5.1.2	Site Restoration Demolish Miscellaneous Site Structures Alternate AC Diesel Generator Bldg Demo		100% Complete
5.1.2	Site Restoration Demolish Miscellaneous Site Structures Fire Pump House Building		100% Complete
5.1.2	Site Restoration Demolish Miscellaneous Site Structures RB Maintenance Bldg Demo		100% Complete
5.1.2	Site Restoration Demolish Miscellaneous Site Structures RX Vessel Closure Head Storage Bldg Demo		100% Complete
5.1.2	Site Restoration Demolish Miscellaneous Site Structures Hot and Cold Shop Bldg Demo		100% Complete
5.1.2	Site Restoration Demolish Miscellaneous Site Structures PAB Building Demo		100% Complete
5.1.2	Site Restoration Demolish Miscellaneous Site Structures BWST Building Demo	12/30/2024	0% Complete
5.1.2	Site Restoration Demolish Miscellaneous Site Structures NAB Building Demo		100% Complete
5.1.3	Site Restoration Demolish Miscellaneous Site Structures Auxiliary Building Demo	12/30/2024	0% Complete
5.1.5	Site Restoration Demolish Miscellaneous Site Structures Intermediate Building Demo		100% Complete
5.2.1	Site Restoration Firing Range Closure		100% Complete

Notes:

Progress Photos

Large Component Removal Work

Reactor Vessel Transportation and Disposal



CR3 Middle Package



CR3 Middle Package




CR3 Middle Package



CR3 Middle Package


Reactor Building System Removal

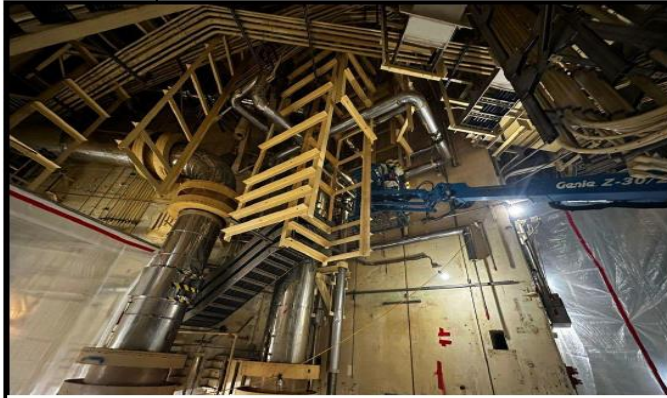

RB 119' Components Removal



RB 119' Wall Openings

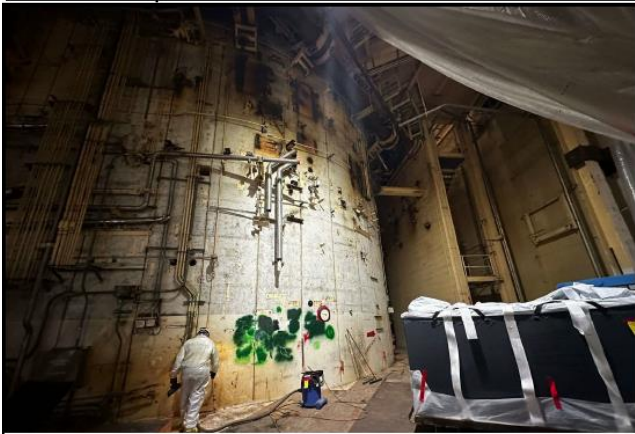

RB 119' Components Removal



RB 119' Components Removal



RB 119' Components Removal

Auxiliary Building Plant System Removal and Decon



AB 119' Phase 3 Demolition



AB 95' Phase 3 Demolition



AB 95 Decay Heat Scabbling



AB 119' Filling Drains with Concrete

Intermediate & Control Complex




IB 119 Drains Removal



IB 119 Decon Coating Removal



IB 119 Surveys

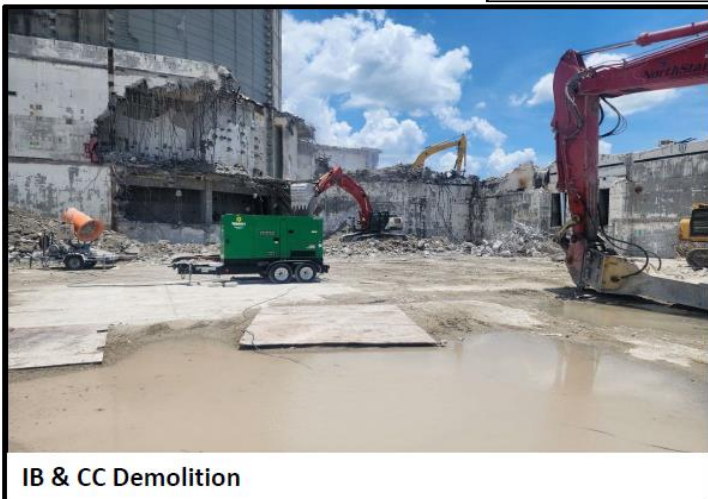

IB & CC Demolition

Nuclear Admin Building Demolition



NAB Demolition



NAB Demolition



NAB Demolition

Activity ID	Activity Name	Orig Dur	Rem Dur	% Comp	Start	Finish	2024			2025				2026						
							Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4			
Crystal River #3 Decommissioning BL March 31, 2024 Schedule Update							1400	718												
A2800	Complete Milestone #1 Partial License Termination	0	0	0%		31-Dec-26*														
3 - Planning / Site Preparation							118	118		01-Apr-24	11-Sep-24									
D&D Planning & Preparations							118	118		01-Apr-24	11-Sep-24									
LCR & RV/RVI Planning & Engineering							0	0		01-Apr-24	01-Apr-24									
RV Planning, Engineering, & Procurement							0	0		01-Apr-24	01-Apr-24									
Balance of Plant D&D Planning							118	118		01-Apr-24	11-Sep-24									
Demolition Planning							118	118		01-Apr-24	11-Sep-24									
4 - Decommissioning							1191	509		19-Aug-21 A	12-Mar-26									
4A - Large Component Removal							680	200		11-Oct-21 A	03-Jan-25									
Reactor Internals Segmentation							95	95		01-Apr-24	09-Aug-24									
Reactor Internals Waste Packaging, Transportation & Disposal							95	95		01-Apr-24	09-Aug-24									
Reactor Vessel Segmentation							95	95		01-Apr-24	09-Aug-24									
Reactor Vessel Waste Packaging, Transportation & Disposal							95	95		01-Apr-24	09-Aug-24									
Large Component Removal Additional Cost							680	200		11-Oct-21 A	03-Jan-25									
Asbestos Abatement							572	92		11-Oct-21 A	06-Aug-24									
Remove Contaminated Outdoor Piping							200	200		01-Apr-24	03-Jan-25									
4B - Site Decontamination							1042	360		19-Aug-21 A	15-Aug-25									
Remove Plant Systems							743	150		08-Sep-21 A	25-Oct-24									
Reactor Building							180	65		16-Jan-23 A	28-Jun-24									
Auxiliary Building (95' Elev.)							140	65		08-Sep-21 A	28-Jun-24									
Auxiliary Building (119' Elev. and Above)							80	65		11-Oct-21 A	28-Jun-24									
Remove Plant Systems Waste P,T,&D							400	150		03-Jan-22 A	25-Oct-24									
Decontaminate Buildings							426	249		03-Jul-23 A	13-Mar-25									
Reactor Building (95' Elev.)							120	120		30-Oct-23 A	13-Sep-24									
Reactor Building (119' Elev.)							120	120		16-Sep-24	28-Feb-25									
Reactor Building (160' Elev. and Above)							249	249		01-Apr-24	13-Mar-25									
Auxiliary Building							339	80		27-Jul-23 A	08-Oct-24									
Intermediate Building							120	22		03-Jul-23 A	30-Apr-24									
Miscellaneous Site Structures							100	100		24-May-24	10-Oct-24									
Decontaminate Buildings Waste P,T & D							685	360		02-Jan-23 A	15-Aug-25									
Reactor Building Waste P,T,&D							360	360		01-Apr-24	15-Aug-25									
Auxiliary, Intermediate, and Misc Building Waste P,T,&D							520	153		02-Jan-23 A	30-Oct-24									
License Termination Planning							5	5		01-Apr-24	05-Apr-24									
Decon Additional Costs							1002	320		19-Aug-21 A	20-Jun-25									
Underground Services Excavation							120	120		06-Jan-25	20-Jun-25									
Remedial Action Surveys							760	78		19-Aug-21 A	17-Jul-24									
Lead Abatement							80	80		01-Apr-24	19-Jul-24									
4F - License Termination							260	260		14-Mar-25	12-Mar-26									
License Termination Planning, Final Surveys, Reporting							260	260		14-Mar-25	12-Mar-26									
License Termination							140	140		14-Mar-25	25-Sep-25									
Confirmation & Verification Surveys							110	110		18-Jul-25	18-Dec-25									
Terminate License							60	60		19-Dec-25	12-Mar-26									
5 - Site Restoration							913	718		10-Aug-20 A	30-Dec-26									
Demolition, Backfill, Grading							913	718		10-Aug-20 A	30-Dec-26									
Turbine Building							130	10		03-Jul-23 A	12-Apr-24									
Miscellaneous Site Structures							250	135		10-Aug-20 A	17-Apr-25									
Auxiliary Building							80	53		23-Jan-23 A	20-Dec-24									
Reactor Building							524	469		21-Oct-24 A	30-Dec-26									
Intermediate Building							155	45		09-Jan-23 A	24-Jul-24									
Backfill and Grade							479	479		15-Apr-24	12-Feb-26									
Site Restoration Additional Costs							295	378		13-Nov-23 A	10-Sep-25									

█ Remaining Level of Effort
 █ Actual Work
 █ Critical Remaining Work
 Primary Baseline
 Remaining Work
◆ Milestone

Activity ID	Activity Name	Orig Dur	Rem Dur	% Comp	Start	Finish	2024			2025				2026										
							Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4							
Crystal River #3 Decommissioning BL March 31, 2024 Schedule Update							828	718																
A2800	Complete Milestone #1 Partial License Termination	0	0	0%		31-Dec-26*																		
3 - Planning / Site Preparation							0	0		01-Apr-24	01-Apr-24	01-Apr-24, 3 - Planning / Site Preparation												
D&D Planning & Preparations							0	0		01-Apr-24	01-Apr-24	01-Apr-24, D&D Planning & Preparations												
LCR & RV/RVI Planning & Engineering							0	0		01-Apr-24	01-Apr-24	01-Apr-24, LCR & RV/RVI Planning & Engineering												
RV Planning, Engineering, & Procurement							0	0		01-Apr-24	01-Apr-24	01-Apr-24, RV Planning, Engineering, & Procurement												
4 - Decommissioning							619	509		16-Jan-23 A	12-Mar-26	12-Mar-26, 4 - Decommissioning												
4B - Site Decontamination							359	249		16-Jan-23 A	13-Mar-25	13-Mar-25, 4B - Site Decontamination												
Remove Plant Systems							180	65		16-Jan-23 A	28-Jun-24	28-Jun-24, Remove Plant Systems												
Reactor Building							180	65		16-Jan-23 A	28-Jun-24	28-Jun-24, Reactor Building												
Decontaminate Buildings							359	249		30-Oct-23 A	13-Mar-25	13-Mar-25, Decontaminate Buildings												
Reactor Building (95' Elev.)							120	120		30-Oct-23 A	13-Sep-24	13-Sep-24, Reactor Building (95' Elev.)												
Reactor Building (119' Elev.)							120	120		16-Sep-24	28-Feb-25	28-Feb-25, Reactor Building (119' Elev.)												
Reactor Building (160' Elev. and Above)							129	129		16-Sep-24	13-Mar-25	13-Mar-25, Reactor Building (160' Elev. and Above)												
4F - License Termination							260	260		14-Mar-25	12-Mar-26	12-Mar-26, 4F - License Termination												
License Termination Planning, Final Surveys, Reporting							260	260		14-Mar-25	12-Mar-26	12-Mar-26, License Termination Planning, Final Surveys, Reporting												
License Termination							100	100		14-Mar-25	31-Jul-25	31-Jul-25, License Termination												
Confirmation & Verification Surveys							110	110		18-Jul-25	18-Dec-25	18-Dec-25, Confirmation & Verification Surveys												
Terminate License							60	60		19-Dec-25	12-Mar-26	12-Mar-26, Terminate License												
5 - Site Restoration							524	469		21-Oct-24 A	30-Dec-26	30-Dec-26, 5 - Site Restoration												
Demolition, Backfill, Grading							524	469		21-Oct-24 A	30-Dec-26	30-Dec-26, Demolition, Backfill, Grading												
Reactor Building							524	469		21-Oct-24 A	30-Dec-26	30-Dec-26, Reactor Building												

█ Remaining Level of Effort
 █ Actual Work
 █ Critical Remaining Work
 Primary Baseline
 Remaining Work
 ◆ Milestone
