

120009-EI

REDACTED


EXHIBIT B

COM	_____
APA	_____
ECR	_____
GCL	_____
RAD	_____
SRC	_____
ADM	_____
OPC	_____
CLK	_____

DOCUMENT NUMBER-DATE

01244 MAR-12

FPSC-COMMISSION CLERK

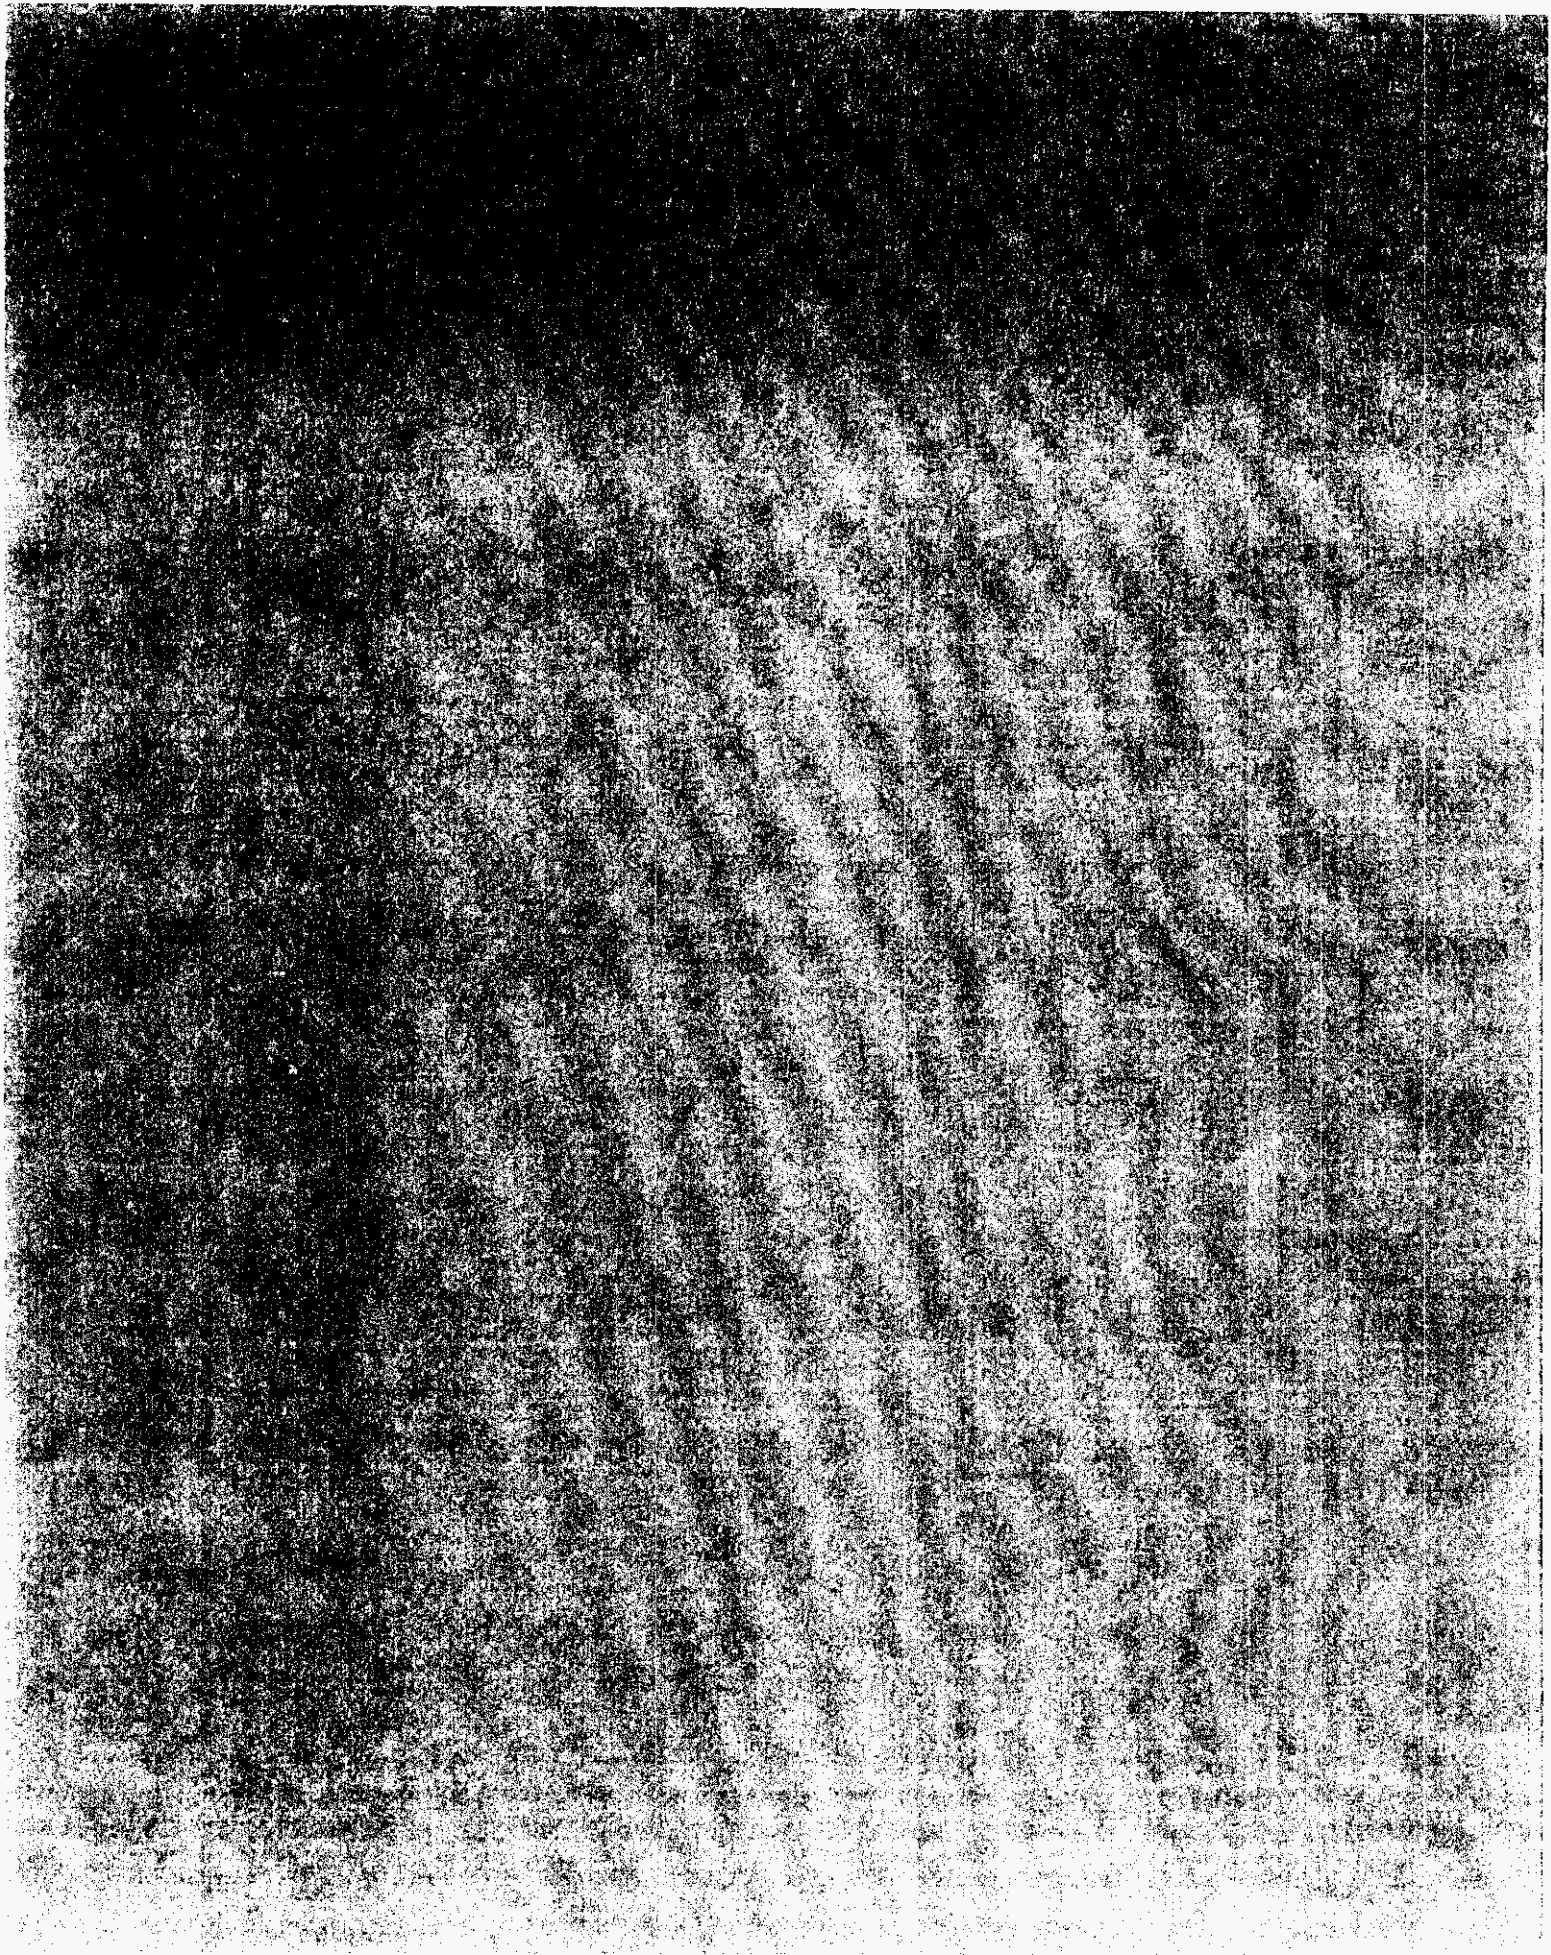

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO. 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
1	121869	Open	4/29/09 - open	4/29/09 - open					AAF MCQUAY	Competitive	Supply Normal Containment Coolers and Testing Services (PTN)
2	120766	Open	3/26/09 - open	3/26/09 - open					Calvert Company Inc	Competitive	Iso Phase Bus Duct Coolers and Testing Services (PSL)
3	124436	Open	7/17/09 - open	7/17/09 - open					Calvert Company Inc	Competitive	Iso Phase Bus Duct Coolers, Install, Demo & Testing Services (PTN)
4	121985	Open	4/24/09 - open	4/24/09 - open					Flowsolve Corp.	Competitive	Replacement Main Feedwater Pumps & Various Testing (PSL)
5	123137	Open	5/28/09 - open	5/28/09 - open					Flowsolve Corp.	Competitive	Main Feedwater Isolation Valves and Testing Services (PTN)
6	125454	Open	8/28/09 - open	8/28/09 - open					Flowsolve Corp.	Competitive	Replacement Heater Drain Pumps (PSL)
7	122154	Complete	4/27/09 - 6/15/11	4/27/09 - 6/15/11					Siemens Energy Inc.	Competitive	Step-Up Transformer (PTN)
8	119078	Open	12/9/08 - open	12/9/08 - open					Westinghouse	OEM	NSSS Engineering Analysis and LAR (PTN)
9	119653	Open	11/24/08 - open	11/24/08 - open					Westinghouse	OEM	NSSS Engineering Analysis and LAR (PSL)
10	121947	Open	4/24/09 - open	4/24/09 - open					Westinghouse	OEM	New & Spent Fuel Criticality and Thermal Hydraulic Analysis (PTN)
11	119670	Open	2/18/09 - open	2/18/09 - open					Proto-Power	Single Source	Project Engineering Support (PSL)
12	115297	Open	8/27/08 - open	8/27/08 - open					Areva	Single Source	RSG Design Review and LAR Work (PSL)
13	115338	Open	8/27/08 - open	8/27/08 - open					Areva	Single Source	RCS Design Review (PTN)
14	105353	Complete	10/02/07 - 12/01/11	10/02/07 - 12/01/11					Shaw - Stone & Webster	Sole Source	Engineering Support (PSL & PTN)
15	117809	Open	12/02/08 - open	12/02/08 - open					Bechtel	Competitive Bid	Engineering Procurement Construction (PTN)
16	116088	Open	09/29/08 - open	09/29/08 - open					Siemens	Single Source	Low Pressure Turbine, Exciter, Exciter Inst. (PSL)
17	117820	Open	12/02/08 - open	12/02/08 - open					Bechtel	Competitive Bid	Engineering Procurement Construction (PSL)
18	116090	Open	9/29/08 - open	9/29/08 - open					Siemens	Single Source	Turbine, Generator/Exciter Upgrades & Inst. (PTN)
19	118326	Open	12/19/08 - open	12/19/08 - open					TEI	Competitive Bid	Condenser Tubes (PTN)
20	118206	Open	12/17/08 - open	12/17/08 - open					TEI	Competitive Bid	Moisture Separator Reheaters (PTN)
21	118205	Open	12/17/08 - open	12/17/08 - open					TEI	Competitive Bid	Moisture Separator Reheaters (PSL)
22	118241	Open	12/19/08 - open	12/19/08 - open					TEI	Competitive Bid	Feed Water Heaters (PTN)
23	112221	Open	4/22/08 - open	4/22/08 - open					Shaw - Stone & Webster	Single Source	Licensing Engineering and BOP Spec Development (PSL)
24	112177	Open	4/22/08 - open	4/22/08 - open					Shaw - Stone & Webster	Single Source	Licensing Engineering and BOP Spec Development (PTN)

A B C D

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO. 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

	(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
25	117272	Open	11/13/08 - open	11/13/08 - open					American Crane	Single Source	Gantry Crane Upgrade (PSL)
26	118224	Open	12/17/08 - open	12/17/08 - open					TEI	Competitive Bid	Feed Water Heaters (PSL)
27	115465	Open	9/03/08 - open	9/03/08 - open					Proto-Power	Single Source	Engineering Services (PTN)
28	118278	Open	12/19/08 - open	12/19/08 - open					TEI	Competitive Bid	TCW Heat Exchangers (PSL)
29	105720	Open	9/12/07 - open	9/12/07 - open					AREVA	Single Source	Neutronics Analysis (PSL)
30	116798	Complete	10/29/08 - 12/22/11	10/29/08 - 12/22/11					Cameron	Single Source	Ultrasonic Flow Meter Measuring System (PTN)
31	116107	Open	9/29/08 - open	9/29/08 - open					Cameron	Single Source	Ultrasonic Flow Meter Measuring System (PSL)
32	114114	Open	7/03/08 - open	7/03/08 - open					Richard Sipos	Single Source	Staff Augmentation (PSL)
33	115035	Complete	8/14/08 - 1/06/11	8/14/08 - 01/06/11					Babcock & Wilcox	Single Source	Steam Generator Component Design Review (PSL)
34	112228	Complete	4/23/08 - 06/11/11	4/23/08 - 06/11/11					Westinghouse	Single Source	Steam Generator Services for Moisture Carryover (PTN)
35	113030	Open	5/20/08 - open	5/20/08 - open					FPL Seabrook	Single Source	FPLE personnel supporting FPL Upgrades (PSL & PTN)
36	115391	Open	8/29/08 - open	8/29/08 - open					NAI	Single Source	Radiological Consequence Analysis (PSL)
37	112987	Open	5/19/08 - open	5/19/08 - open					NAI	Single Source	Radiological Consequence Analysis (PTN)
38	4500521317	Open	9/08/09 - open	9/08/09 - open					Areva	Competitive	Inductors (PTN)
39	126248	Open	10/08/09 - open	10/08/09 - open					ABB	Competitive	Replacement Transformer Coolers (PSL)
40	126453	Open	11/05/09 - open	11/05/09 - open					Joseph Oat Corporation	Competitive	Cooling Water Heat Exchangers (PTN)
41	127777	Open	12/08/09 - open	12/08/09 - open					High Bridge	Single Source	Estimating Services (PTN)
42	127881	Open	12/22/09 - open	12/22/09 - open					Absolute Consulting	Single Source	Procedure Writers (PTN)
43	123762	Open	6/25/09 -open	6/25/09 -open					Key Controls of Tampa	OEM	Control System Tuning and Dynamic Analysis (PTN)
44	118998	Open	01/22/09 - open	01/22/09 - open					Holtec	Single Source	Fuel Storage Criticality and related analysis (PSL 2)
45	118563	Open	1/14/09 - open	1/14/09 - open					Holtec	Competitive	Fuel Storage Criticality and related analysis (PSL 1)
46	118627	Open	7/26/09 - open	7/26/09 - open					Western Services	Competitive	NSSS Simulator Reactor Core Model Upgrade (PSL)
47	118944	Open	01/15/09 - open	01/15/09 - open					Western Services	Competitive	NSSS Simulator Reactor Core Model Upgrade (PTN)
48	4500467077	Open	11/10/08 - open	11/10/08 - open					Siemens	Competitive	Generator Step -up Transformers (PSL)

A B C D

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO: 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

(A)		(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended In Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
49	130579	Open	5/01/10 - open	5/01/10 - open					Fisher Controls	Competitive	Modified Feedwater Regulating Valves/Actuators (PSL)
50	130160	Open	3/29/10 - open	3/29/10 - open					Flowserve Corp.	Competitive	Replacement Condensate Pumps (PSL)
51	130612	Open	4/22/10 - open	4/22/10 - open					Flowserve Corp.	Competitive	Condensate Pumps (PTN)
52	130649	Open	4/22/10 - open	4/22/10 - open					Flowserve Corp.	Competitive	Main Feedwater Pumps (PTN)
53	126227	Open	10/13/09 - open	10/13/09 - open					Invensys	OEM	Control System FWH, Moisture Separator (PTN)
54	129689	Open	3/17/10 - open	3/17/10 - open					Invensys	Competitive	Turbine Digital Upgrade (PTN)
55	130272	Open	4/08/10 - open	4/08/10 - open					Siemens Energy Inc.	Competitive	Electro-Hydraulic Fluid Systems (PTN)
56	131356	Open	5/21/10 - open	5/21/10 - open					Brand Energy Solutions	Competitive	Supply Scaffolding Material (PTN)
57	131391	Complete	5/25/10 - 4/19/11	5/25/10 - 4/19/11					BRV Construction	Competitive	Design/Construct fabrication area inside the CSF (PTN)
58	131599	Open	5/27/10 - open	5/27/10 - open					All Star Toilets	Competitive	Supply Cleaning Services (PTN)
59	4500586420	Open	6/16/10 - open	6/16/10 - open					Energy Erectors	Competitive	Electrical contract labor work @ 230 kV substation (PTN)
60	131828	Complete	6/14/10 - 02/28/11	6/14/10 - 02/28/11					Siemens Energy Inc.	Single Source	SL2-19 Pre-planning TG installation Work (PSL2)
61	131533	Open	6/10/10 - open	6/10/10 - open					Areva	OEM	Non-Fuels NSSS Interim LAR (PSL 1 & 2)
62	131907	Open	6/11/10 - open	6/11/10 - open					Areva	OEM	Fuels Related Interim LAR/MOD for EPU (PSL)
63	131585	Open	6/15/10 - open	6/15/10 - open					Shaw - Stone & Webster	PDS	Interim LAR/MOD Support for EPU (PSL)
64	131393	Open	6/10/10 - open	6/10/10 - open					Fisher Controls	Competitive	Heater Drain BOP Replacement Valves (PSL)
65	131742	Open	6/15/10 - open	6/16/10 - open					Westinghouse	PDS	LAR/RAI for Non-Fuels NSSS related scope (PSL)
66	132077	Open	6/17/10 - open	6/17/10 - open					Siemens Energy Inc.	Single Source	Siemens Dedicated Resident Site Manager (PTN)
67	132078	Open	6/17/10 - open	6/17/10 - open					Siemens Energy Inc.	Single Source	Siemens Dedicated Resident Site Manager (PSL)
68	132235	Open	6/24/10 - open	6/24/10 - open					Enercon	Single Source	NFPA 805/Appendix R Support for (PTN)
69	131987	Open	6/25/10 - open	6/25/10 - open					Sargent & Lundy Inc	Single Source	Engineering for Steam Bypass Control (PSL1)
70	131940	Open	6/30/10 - open	6/30/10 - open					Westinghouse	Competitive	Main Steam Turbine Control Replacement (PSL)
71	132283	Open	6/29/10 - open	6/28/10 - open					Shaw - Stone & Webster	PDS	EPU Feedwater Pump Nozzle Load Reduction (PSL)
72	2259675	Open	7/23/10 - open	7/23/10 - open					Joseph Oat Corporation	Competitive	Furnish New Spent Fuel Pool Heat Exchangers (PTN)

A B C D

Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO. 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

	(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended In Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
73	2259669	Open	8/02/10 - open	8/02/10 - open					TAW	Competitive	Rewind/Refurbish/Upgrade Condensate Pumps (PTN)
74	2259997	Open	8/4/10 - open	8/4/10 - open					SPX Corporation	Replaces 115351	Valve Rework (PTN)
75	2259768	Open	8/06/10 - open	8/06/10 - open					Westinghouse	OEM	Design basis support for Umbrella Mods (PTN)
76	2260155	Open	8/16/10 - open	8/16/10 - open					Siemens Energy Inc.	Single Source	PSL 1-24 Pre-planning TG Installation Work
77	2260113	Open	9/23/10 - open	9/23/10 - open					Westinghouse	OEM	Rod Control System Upgrades (PSL)
78	2261536	Open	9/16/10 - open	9/16/10 - open					Washington Group	Competitive	Feedwater Heater Ultrasonic Testing (PTN)
79	2261750	Open	9/21/10 - open	9/21/10 - open					Modular Space	Competitive	Lease of 15-Wide Trailers for EPU (PTN)
80	2261747	Open	9/23/10 - open	9/23/10 - open					Westinghouse	PDS	EPU NSSS Engineering and Modification Support (PTN)
81	2262094	Open	9/28/10 - open	9/28/10 - open					Structural Integrity	Competitive	Assessment of Min Wall Thickness Effects (PTN)
82	2262201	Open	9/30/10 - open	9/30/10 - open					Fisher Controls	Replaces 131393	Heater Drain BOP Replacement Valves (PSL)
83	2262367	Open	10/04/10 - open	10/04/10 - open					Techcom International	Competitive	Engineering Services for Various Distributing Mods (PTN)
84	2262515	Open	10/06/10 - open	10/06/10 - open					Fisher Controls	Replaces 130579	Modified Feedwater Regulating Valves/Actuators (PSL)
85	2263036	Open	10/19/10 - open	10/19/10 - open					Flowserve Corp.	Replaces 130160	Replacement Condensate Pumps (PSL)
86	2264196	Complete	11/16/10 - 4/20/11	11/16/10 - 4/20/11					Siemens Energy Inc.	OEM	Replacement Blade Rings (PSL)
87	2264240	Open	11/17/10 - open	11/17/10 - open					Siemens Energy Inc.	Single Source	T/G Installation SL2-19 Outage (PSL)
88	2263052	Open	11/11/10 - open	11/11/10 - open					Invensys	Single Source	Steam Bypass Control System (PSL)
89	2263549	Open	11/10/10 - open	11/10/10 - open					Areva NP Inc	Competitive	Services of a Project Manager (PTN)
90	2264548	Complete	11/19/10 - 03/28/11	11/19/10 - 03/28/11					Graybar Electric	Competitive	Wire Cable (PTN)
91	2263990	Open	11/11/10 - open	11/11/10 - open					Brand Energy Solutions	Replaces 131356	Supply Scaffolding Material (PTN)
92	2264842	Open	11/30/10 - open	11/30/10 - open					Ronnies Turbine Services Inc	Single Source	On Site SL2-19 Tech Support (PSL)
93	2264841	Open	11/30/10 - open	11/30/10 - open					Balsch Industries	Single Source	On Site SL2-19 Tech Support (PSL)
94	2264377	Open	11/30/10 - open	11/30/10 - open					Techcom International	Competitive	Turbine Digital Controls Verification and Validation (PTN)
95	2264914	Open	12/07/10 - open	12/07/10 - open					Westinghouse Electric	OEM	CEDMS Power Switch Refurbishment (PSL2)
96	2263851	Open	11/4/10 - open	11/4/10 - open					Graybar Electric	Competitive	Temporary Power Unit Substations for EPU (PTN)

A B C D

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO. 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
97	2285418	Open	12/16/10 - open	12/16/10 - open					Siemens Energy Inc.	OEM	Impl. Spares for EPU Turbine Gen. Work During SL2-19 (PSL)
98	4500589986	Open	7/6/10 - open	7/6/10 - open					Kennedy Construction	Competitive	Site preparation contract labor work @ 230 kV substation (PTN)
99	2285720	Open	01/14/11 - open	01/14/11 - open					Enercon Services	Competitive	Licensing/Design Basis/Program Modification (PTN)
100	2291203	Open	04/21/11 - open	04/21/11 - open					Enertech	Competitive	Main Steam Isolation Valve Replacement Actuator (PSL)
101	2287242	Open	01/27/11 - open	01/27/11 - open					Engineering Planning & Management	Competitive	Environmental Qualification Document (PTN)
102	2287468	Open	02/10/11 - open	02/10/11 - open					Feedforward Inc.	Competitive	DCS Mods (PSL)
103	2290208	Open	03/25/11 - open	03/25/11 - open					Feedforward Inc.	Competitive	Leading Edge Flow Meter Addition (PTN)
104	2287971	Open	02/15/11 - open	02/15/11 - open					Foster Wheeler North America	Competitive	SJAE Inter/After Condensers (PTN)
105	2290465	Open	03/31/11 - open	03/31/11 - open					Siemens	OEM	Design and Fabrication of Turbine Crossover piping (PTN)
106	2290463	Open	03/31/11 - open	03/31/11 - open					Siemens	OEM	Iron Bolts for Main Steam Generator Stator (PTN)
107	2290842	Open	04/08/11 - open	04/08/11 - open					Siemens	OEM	Blower Stationary Blade Rings (PSL)
108	2286521	Open	01/18/11 - open	01/18/11 - open					Stone & Webster	PDS	MSIV/MSCV Modification to Support EPU (PSL)
109	2284476	Open	05/11/11 - open	05/11/11 - open					Batsch Industries	Single Source	Turbine Generator Technical Support (PTN)
110	2291815	Open	04/28/11 - open	04/28/11 - open					BRV Construction	Competitive	Fossil Warehouse Demolition (PTN)
111	2290814	Open	05/02/11 - open	05/02/11 - open					Flowserve Corp.	Replaces 130649	Main Feedwater Pump Casing Modification (PTN)
112	2292773	Open	05/26/11 - open	05/26/11 - open					AAF MCQUAY	OEM	Design, Engineer, Fabricate and Deliver CRDM Coils (PTN)
113	2293950	Open	06/24/11 - 04/20/11	06/24/11 - 04/20/11					Siemens	Single Source	Turbine Generator Pre-outage planning activities (PTN)
114	2293853	Open	06/29/11 - open	06/29/11 - open					Thermal Engineering	Competitive	Design and Fabrication of Gland Steam Condensers (PTN)
115	2294247	Open	07/06/11 - open	07/06/11 - open					Ecological Associates	Competitive	Biological Plan of Study (PSL)
116	2294341	Open	07/11/11 - open	07/11/11 - open					Allon	Single Source	GL2008-01 Support (PSL)
117	2294494	Open	07/13/11 - open	07/13/11 - open					Enercon Services	Competitive	Emergency Containment Cooler Auto-start (PTN)
118	2294221	Open	07/11/11 - open	07/11/11 - open					Flowserve Corp.	Competitive	Main Steam Isolation Replacement Valves (PSL)
119	2294855	Open	07/21/11 - open	07/21/11 - open					Zachary Nuclear Engineering	Single Source	Project Engineering Support for EPU (PSL)
120	2295186	Open	08/02/11 - open	08/02/11 - open					Holtec International	Single Source	Metamix Chevrons for Spent Fuel Pool (PSL)

A B C D

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO. 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

	(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
121	2295422	Open	8/10/11 - open	8/10/11 - open					Siemens Energy Inc.	OEM	Support Material for the EPU Turb-Gen Uprate (PTN)
122	2295071	Open	08/01/11 - open	08/01/11 - open					Stone & Webster	Single Source	Unit 1 Vibration and Support Mods for FW & Condensate (PSL)
123	2296048	Open	08/25/11 - open	08/25/11 - open					Cameron Tech.	Replaces 116796	Ultrasonic Flow Meter Measuring System (PTN)
124	2294671	Open	08/19/11 - open	08/19/11 - open					NWT Corporation	Competitive	Moisture Carry Over Testing for EPU (PTN)
125	2296556	Open	09/02/11 -open	09/02/11 - open					Sulzer Pumps	OEM	Modify, overhaul and refurbishment of the B & C APW (PTN)
126	2296519	Open	09/06/11 - open	09/06/11 - open					Techcom International	Competitive	DCS Integration Plan for 3R26 and 4R27 (PTN)
127	2296623	Open	09/06/11 - open	09/06/11 - open					Tricen Technologies	Competitive	Unit 3 Condenser Tube Eddy Current Testing (PTN)
128	2296797	Open	09/09/11 - open	09/09/11 - open					Coastal Bus & Charter Lines (dba Need A Bus)	Competitive	Shuttle Bus Services for EPU (PSL)
129	2296330	Open	09/09/11 - open	09/09/11 - open					Flowserve Corp.	Competitive	Motor Operated Valves (PTN)
130	2298266	Open	10/12/11 - open	10/12/11 - open					Franmar Corporation	Competitive	Shuttle Bus Services for EPU (PTN)
131	2298406	Open	10/12/11 - open	10/12/11 - open					Master Lee Energy Services	Competitive	Fuel Movers for Metamic Inserts (PSL)
132	2296635	Open	10/14/11 - open	10/14/11 - open					Sargent & Lundy Inc.	Single Source	Engineering Service for the Charging System Modification (PSL 2)
133	2297556	Open	09/27/11 - open	09/27/11 - open					Siemens Energy Inc.	Single Source	Siemens installation of 2A Main Power Transformer (PSL)
134	2299101	Open	10/27/11 - open	10/27/11 - open					Berkei & Company	Single Source	Mico Pile Construction (PTN)
135	2298894	Open	10/24/11 - open	10/24/11 - open					Day & Zimmermann NPS Inc.	Competitive	Installation of Trailer Support Services (PTN)
136	2299350	Open	11/01/11 - open	11/01/11 - open					Enercon Services Inc.	Competitive	Eng. Evaluation for EPU Mid-Cycle contingency plan (PSL)
137	2299618	Open	11/04/11 - open	11/04/11 - open					Radiation Safety & Control	Competitive	Truck Monitoring/Waste Characterization for EPU (PTN)
138	2297624	Open	10/27/11 - open	10/27/11 - open					Siemens Energy Inc.	OEM	Turbine Valve Conversion to EH (PTN)
139	2299631	Open	11/8/11 - open	11/8/11 - open					Tri-Tool Inc.	Single Source	Unit 1 LP Turbine Extraction Line Services (PSL)
140	2295953	Open	08/24/11 - open	08/24/11 - open					Marron Wire & Cable	OEM	Misc Safety Related Wire and Cable, line items 1 - 23 (PTN)
141	2297055	Open	09/16/11 - open	09/16/11 - open					Thermal Engineering	Single Source	Replacement LP #4 Feedwater Heaters for EPU (PSL 2)
142	2300139	Open	11/21/11 - open	11/21/11 - open					Siemens Energy Inc.	Single Source	SL1-24 Turb-Gen. Installation (PSL 1)
143	2299624	Open	11/16/11 - open	11/16/11 - open					Ames Group LLC	Single Source	Upgrade Services for Feedwater Pumps (PSL)
144	2300487	Open	11/28/11 - open	11/28/11 - open					Weldtech Services	Single Source	SL1-24 Construction Management Oversight Services (PSL 1)

A B C D

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO. 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

	(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended In Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
145	2299618	Open	11/04/11 - open	11/04/11 - open					Radiation Safety & Control	Competitive	Truck Monitoring/Waste Characterization for EPU (PTN)
146	2299350	Open	11/01/11 - open	11/01/11 - open					Enercon Services	Competitive	Engineering evaluation for EPU mid-cycle contingency plan (PSL)
147	2299631	Open	11/08/11 - open	11/08/11 - open					Tri-Tool	Single Source	LP Turbine Extraction Line Services for EPU (PSL 1)
148	NF-10-358 NF-11-178	Open	11/2/10 - open	11/2/10 - open					Westinghouse Electric	OEM	Spent Fuel Pool Criticality Safety Analysis Support (PTN)
149	2301813	Open	12/28/11 - open	12/28/11 - open					Enercon Services Inc.	Competitive	Motor Operated Valve Transfer Switches for EPU (PSL)
150	2301857	Open	12/28/11 - open	12/28/11 - open					Enercon Services Inc.	Single Source	Develop Engineering Change Packages for EPU (PTN)
151	2301038	Open	12/14/11 - open	12/14/11 - open					Graftel Inc.	Competitive	Integrated Leak Rate Testing for EPU (PTN)
152	2261600	Open	09/28/10 - open	08/28/10 - open					3 Communications Maps Inc.	OEM	Supply of Simulator SCD Software Translator Upgrade (PTN)
153	130340	Open	04/02/10 - open	04/02/10 - open					MPR Associates	Competitive	Third Party Review of Siemens Turb-Gen. Analysis (PSL)
154	2301737	Open	12/21/11 - open	12/21/11 - open					PSI Energy Services	Single Source	Construction Management Oversight Services (PTN)
155	2301736	Open	12/21/11 - open	12/21/11 - open					Weidtech Services	Single Source	Construction Management Oversight Services (PTN)
156	2301871	Open	12/28/11 - open	12/28/11 - open					Zachry Nuclear Engineering	Single Source	Develop Engineering Change Packages for EPU (PTN)
157	2301858	Open	12/28/11 - open	12/28/11 - open					Sargent & Lundy Inc.	Single Source	Develop TPCW Engineering Change Packages for EPU (PTN)
158	2000053226	Open	11/21/11 - open	11/21/11 - open					Ric-Man Construction	Competitive	Road and parking contract labor work 230kV substation (PTN)

A B C D

Legend:

PDS = Predetermined Source


OEM = Original Equipment Manufacturer

PSL = St. Lucie

PTN = Turkey Point

Notes:

In November 2011, FPL issued a Letter of Agreement (LOA) to Siemens for the PTN 3-26 Turbine Generator installation scope; however, the contract was not issued in 2011.

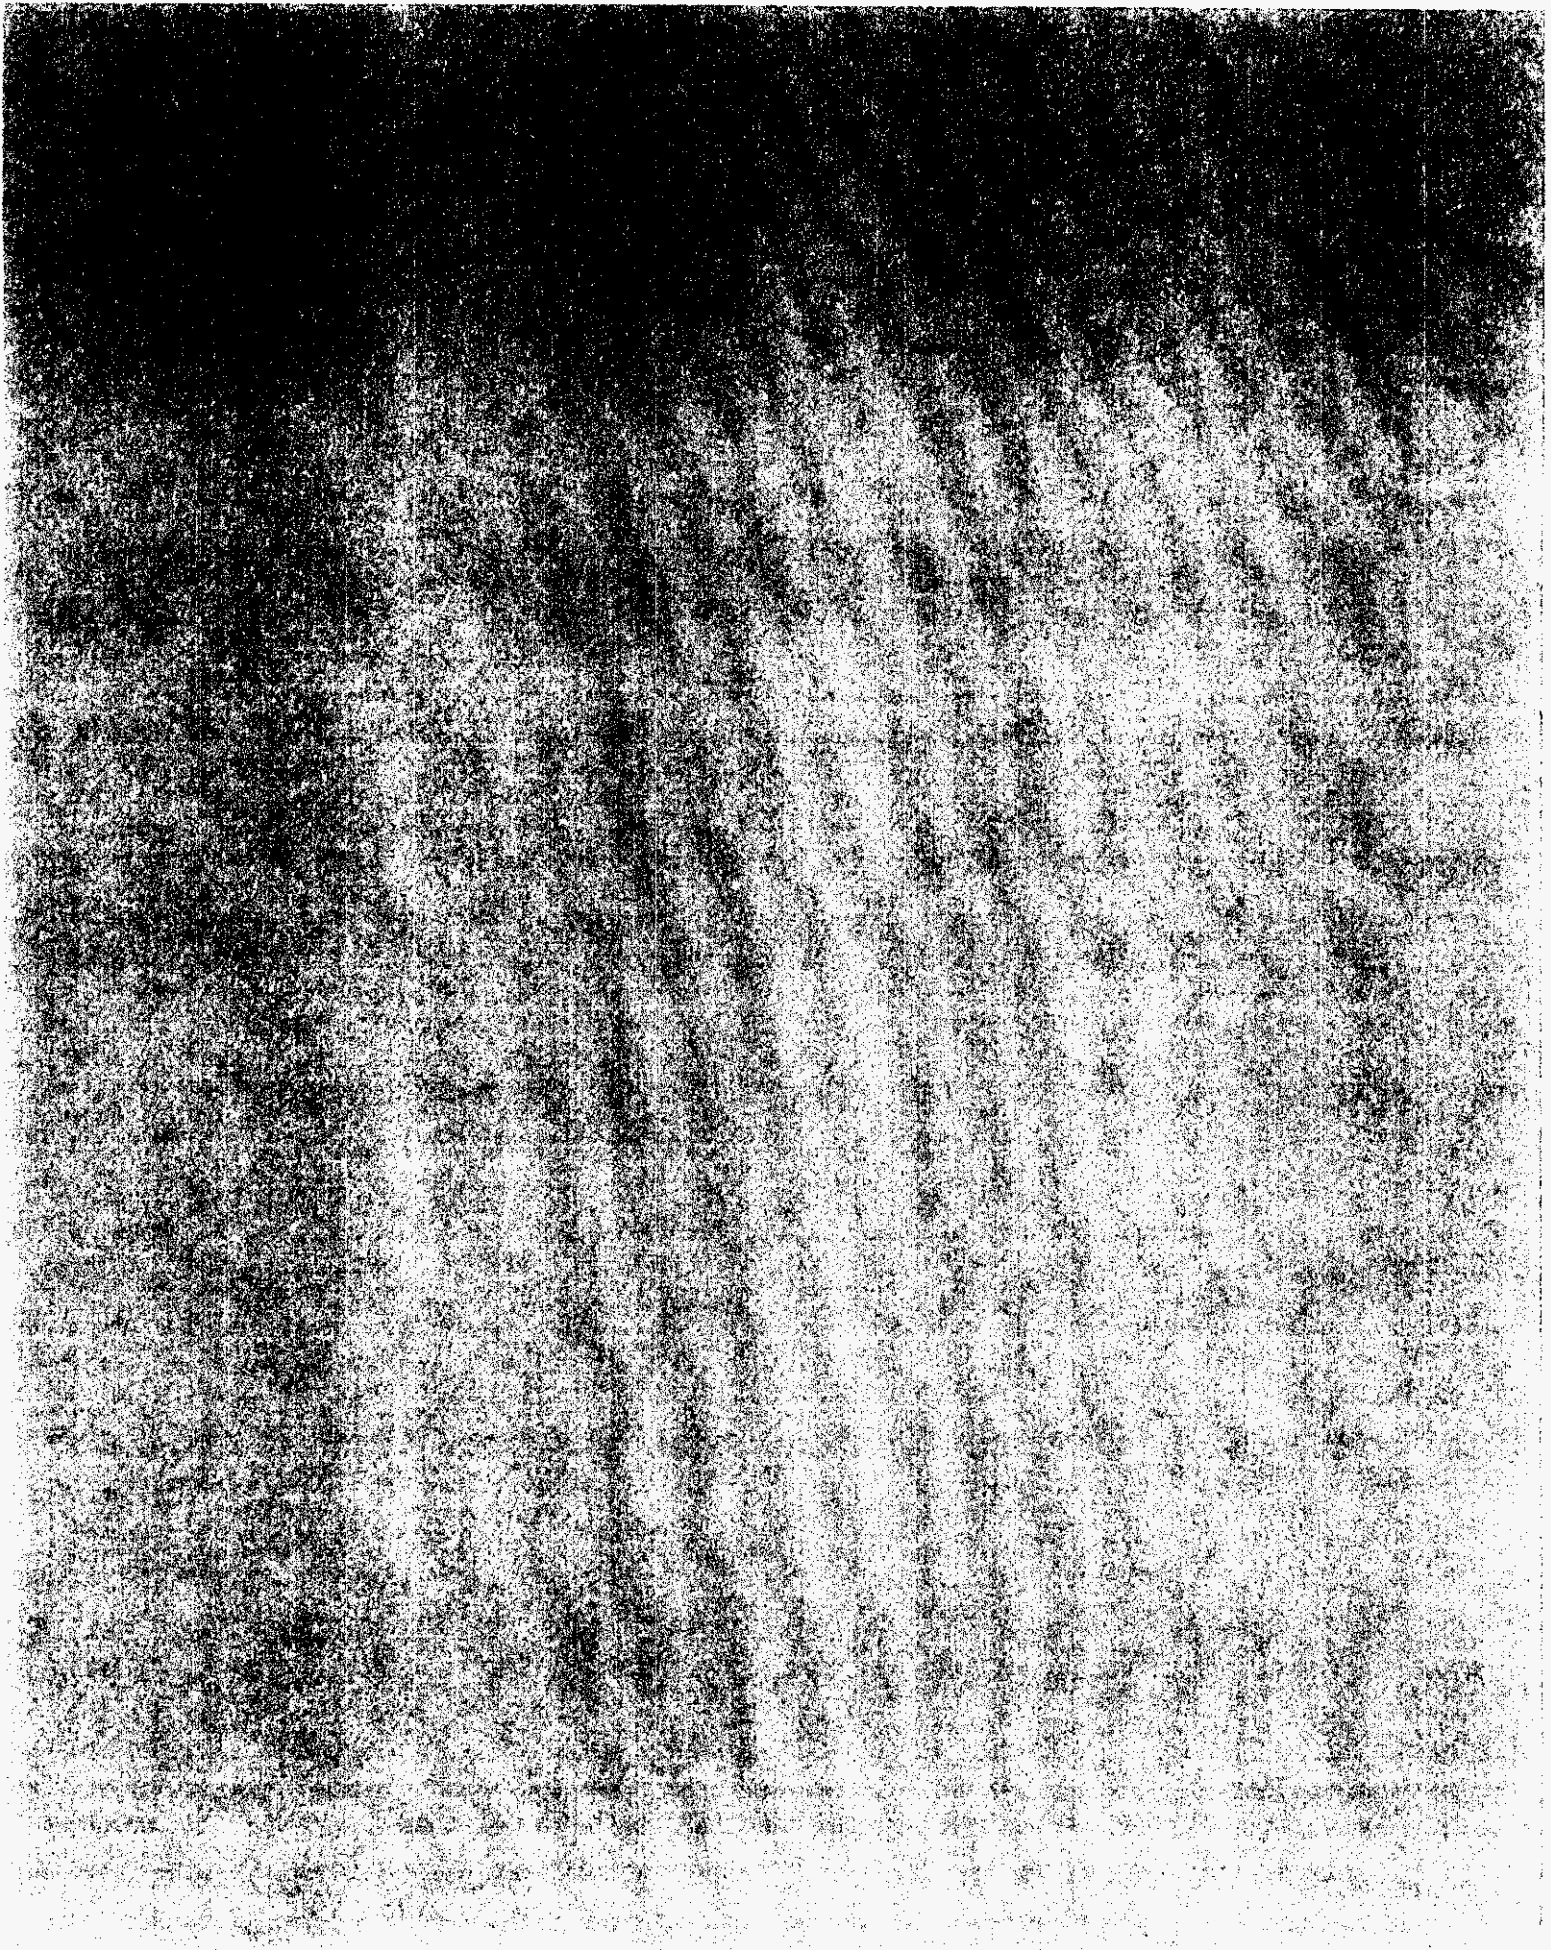

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO 121869

Major Task or Tasks Associated With:

Supply Eight (8) Normal Containment Coolers and provide Testing Services

Vendor Identity:

AAF MCQUAY

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to AAF McQuay.

Dollar Value:

Total Contract Value through Revision 3 is



Contract Status:

Active

Term Begin:

April 29, 2009

Term End:

March 2013

Nature and Scope of Work:

Supply Eight (8) Normal Containment Coolers and provide Testing Services

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO 120769

Major Task or Tasks Associated With:

Replacement IsoPhase Bus Duct Coolers

Vendor Identity:

Calvert Company Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

1

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Calvert Company Inc.

Dollar Value:

Total Dollar Value through Revision 2 is



Contract Status:

Active

Term Begin:

March 26, 2009

Term End:

June 2012

Nature and Scope of Work:

Replacement IsoPhase Bus Duct Coolers, Technical Installation Support and Field Testing.

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO 124436

Major Task or Tasks Associated With:

Replacement Isolated Phase BusDuct

Vendor Identity:

Calvert Company Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Calvert Company Inc.

Dollar Value:

Total Dollar Value through Revision 2 is

Contract Status:

Active

Term Begin:

July 17, 2009

Term End:

June 2012

Nature and Scope of Work:

Replacement Isolated Phase BusDuct, Demolition and Installation Services, Evaluation, Testing and Engineering

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.
For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO 121985

Major Task or Tasks Associated With:

Replacement Main Feedwater Pumps

Vendor Identity:

Flowserve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

5

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Flowserve Corp.

Dollar Value:

Total Dollar Value through Revision 3 is [REDACTED]

Contract Status:

Active

Term Begin:

April 24, 2009

Term End:

June 2012

Nature and Scope of Work:

Replacement Main Feedwater Pumps, spare parts and technical direction of installation.

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO 123137

Major Task or Tasks Associated With:

Main Feedwater Isolation Valves

Vendor Identity:

Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Flowsolve Corp.

Dollar Value:

Total Dollar Value through Revision 1 is



Contract Status:

Active

Term Begin:

May 28, 2009

Term End:

Open

Nature and Scope of Work:

Main Feedwater Isolation Valves, Technical Field Services, Testing, Engineering and Documentation

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO 125454

Major Task or Tasks Associated With:

Replacement Heater Drain Pumps

Vendor Identity:

Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Flowsolve Corp.

Dollar Value:

Total Dollar Value through Revision 1 is [REDACTED]

Contract Status:

Active

Term Begin:

August 28, 2009

Term End:

June 2012

Nature and Scope of Work:

Replacement Heater Drain Pumps, Spare Heater, Technical Direction

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO 122154

Major Task or Tasks Associated With:

Step-Up Transformers

Vendor Identity:

Siemens Energy Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

2

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Siemens Energy Inc.

Dollar Value:

[REDACTED]

Contract Status:

Complete

Term Begin:

April 27, 2009

Term End:

Complete

Nature and Scope of Work:

Uprate Step-Up Transformers from 850 MVA to 970 MVA

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO 119078

Major Task or Tasks Associated With:

NSSS Engineering Evaluation and LAR Analysis for PTN Units 3 & 4

Vendor Identity:

Westinghouse Electric Co.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Dollar Value through Revision 6 is [REDACTED]

Contract Status:

Active

Term Begin:

Letter of Authorization issued 12/9/09; PO issued 1/26/09

Term End:

Open

Nature and Scope of Work:

NSSS Engineering Evaluation and LAR Analysis for PTN Units 3 & 4

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO 119653

Major Task or Tasks Associated With:

NSSS Engineering Evaluation and LAR Analysis for PSL Units 1 & 2

Vendor Identity:

Westinghouse Electric Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Dollar Value through Revision 4 is [REDACTED]

Contract Status:

Active

Term Begin:

Letter of Authorization issued 11/24/08; PO issued 2/17/09

Term End:

open

Nature and Scope of Work:

NSSS Engineering Evaluation and LAR Analysis for PSL Units 1 & 2

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO 115297 (PSL)

Major Task or Tasks Associated With:

Design Review for LAR (Steam Generator and Reactor Head)

Vendor Identity:

AREVA

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Dollar Value through Revision 8 [REDACTED]

Contract Status:

Active

Term Begin:

August 27, 2008

Term End:

open

Nature and Scope of Work:

Design Review for LAR (Steam Generator and Reactor Head)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO 115338

Major Task or Tasks Associated With:

Engineering Analysis

Vendor Identity:

AREVA

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Dollar Value through Revision 10. [REDACTED]

Contract Status:

Active

Term Begin:

August 27, 2008

Term End:

Open

Nature and Scope of Work:

Design review for the Reactor Coolant system, Control Rod Mechanism, EMA, CFD and BMI

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY:

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 105353

Major Task or Tasks Associated With:

Initial BOP Scoping Support for EPU

Vendor Identity:

Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Sole Source

Dollar Value:

Total Dollar Value through Revision 5 is [REDACTED]

Contract Status:

Complete

Term Begin:

October 2, 2007

Term End:

December 1, 2011

Nature and Scope of Work:

BOP Scoping Support (engineering) for the EPU Project

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO 117809

Major Task or Tasks Associated With:

Provide Engineering, Procurement and Construction Services for PTN

Vendor Identity:

Bechtel

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

6

Number of Bids Received:

5

Brief Description of Selection Process:

Bidders were evaluated against predetermined technical and commercial criteria, awarding to the lowest evaluated bidder.

Dollar Value:

PO value through Rev 4/Rel D is [REDACTED]

Contract Status:

Active

Term Begin:

December 2, 2008

Term End:

April 2013

Nature and Scope of Work:

Bechtel's scope includes project management, design engineering, procurement and material handling services, work order planning, construction/implementation, project controls, quality assurance, quality control, radiation protection (alara), safety, security interface, and other services as designated in the Contract documents.

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 116088

Major Task or Tasks Associated With:

Turbine/Generator Uprate

Vendor Identity:

Siemens Power

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single source

Dollar Value:

Total Max Dollar Value through Revision 4/Release 0

Contract Status:

Active

Term Begin:

September 29, 2008

Term End:

March 2013

Nature and Scope of Work:

Engineering, Parts and Installation for PSL Turbine/Generator Uprate

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO 117820

Major Task or Tasks Associated With:

Provide Engineering, Procurement and Construction Services for PSL

Vendor Identity:

Bechtel

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

6

Number of Bids Received:

5

Brief Description of Selection Process:

Bidders were evaluated against predetermined technical and commercial criteria, awarding to the lowest evaluated bidder.

Dollar Value:

PO value through Rev 5/Rel 0 is [REDACTED]

Contract Status:

Active

Term Begin:

December 2, 2008

Term End:

December 2012

Nature and Scope of Work:

Bechtel's scope includes project management, design engineering, procurement and material handling services, work order planning, construction/implementation, project controls, quality assurance, quality control, radiation protection (alara), safety, security interface, and other services as designated in the Contract documents.

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 116090

Major Task or Tasks Associated With:

PTN Turbine Generator Uprate

Vendor Identity:

Siemens Power

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Max Contract Value through Rev. 3/Rel 0 is [REDACTED]

Contract Status:

Active

Term Begin:

September 29, 2008

Term End:

March 2013

Nature and Scope of Work:

PTN Engineering, Parts and Installation for Turbine/Generator Uprate

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 118328

Major Task or Tasks Associated With:

PTN Condenser Tube Bundles for Unit 3 & 4

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through Revision 5 is [REDACTED]

Contract Status:

Active

Term Begin:

December 19, 2008

Term End:

March 2013

Nature and Scope of Work:

Supply PTN Condenser Tube Bundles

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 118206

Major Task or Tasks Associated With:

PTN MSR's for Units 3 & 4

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

2

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through Revision 2 [REDACTED]

Contract Status:

Active

Term Begin:

December 17, 2008

Term End:

March 2013

Nature and Scope of Work:

Supply PTN Moisture Separator Reheaters

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 118205

Major Task or Tasks Associated With:

PSL MSR's for Units 1 & 2

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

2

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through Revision 5 is [REDACTED]

Contract Status:

Active

Term Begin:

December 17, 2008

Term End:

July 2012

Nature and Scope of Work:

Supply PSL Moisture Separator Reheaters

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 118241

Major Task or Tasks Associated With:

PTN Feedwater Heaters for Units 3 & 4

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

3

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Contract Value through Revision 2

Contract Status:

Active

Term Begin:

December 19, 2008

Term End:

March 2013

Nature and Scope of Work:

Supply PTN Feedwater Heaters

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 112221

Major Task or Tasks Associated With:

Engineering Services

Vendor Identity:

Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Blanket Purchase Order Max Value through Revision 17 to Release 0 is [REDACTED]

Contract Status:

Active

Term Begin:

April 22, 2008

Term End:

December 2012

Nature and Scope of Work:

PSL BOP Engineering

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 112177

Major Task or Tasks Associated With:

Engineering Services

Vendor Identity:

Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Blanket Purchase Order Max Value through Revision 8 to Release 0 is [REDACTED]

Contract Status:

Active

Term Begin:

April 22, 2008

Term End:

open

Nature and Scope of Work:

Engineering for the PSL Uprate Project

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO 117272

Major Task or Tasks Associated With:

Gantry crane repair/modification

Vendor Identity:

American Crane & Equip.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Sole Source/OEM

Dollar Value:

Total Dollar Value through Rev 6 is [REDACTED]

Contract Status:

Active

Term Begin:

November 13, 2008

Term End:

Open

Nature and Scope of Work:

Complete modification of Unit 1 crane and update of electrical components for Unit 2 crane

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 118224

Major Task or Tasks Associated With:

PSL Feedwater Heaters for Units 1 & 2

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Dollar Value thru Revision 6

Contract Status:

Active

Term Begin:

December 17, 2008

Term End:

open

Nature and Scope of Work:

Supply PSL Feedwater Heaters

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 115465

Major Task or Tasks Associated With:

Eng. Services for NSSS, BOP & Licensing Activities

Vendor Identity:

Proto-Power

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Dollar Value through revision 4 is [REDACTED]

Contract Status:

Active

Term Begin:

September 3, 2008

Term End:

Open

Nature and Scope of Work:

PTN Eng. Services for NSSS, BOP and Licensing Activities.

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 118278

Major Task or Tasks Associated With:

PSL Heat Exchangers for Units 1 & 2

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

3

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through revisions 4 is [REDACTED]

Contract Status:

Active

Term Begin:

December 19, 2008

Term End:

Open

Nature and Scope of Work:

Supply PSL Heat Exchangers

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY:

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 105720

Major Task or Tasks Associated With:

PSL Fuels Study

Vendor Identity:

Areva

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Order value through Revision 16 is [REDACTED]

Contract Status:

Active

Term Begin:

September 12, 2007

Term End:

open

Nature and Scope of Work:

Fuels Performance Study and Analysis

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 116796

Major Task or Tasks Associated With:

Ultrasonic Flow Measuring System

Vendor Identity:

Cameron Technologies

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Blanket Purchase Order Value through Revision 1 to Release 0
is [REDACTED]

Contract Status:

Complete

Term Begin:

October 29, 2008

Term End:

December 22, 2011

Nature and Scope of Work:

Ultrasonic Flow Measuring System for PTN

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO 116107

Major Task or Tasks Associated With:

Ultrasonic Flow Measuring System

Vendor Identity:

Cameron Technologies

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Purchase Order Value through Revision 1 is [REDACTED]

Contract Status:

Awarded

Term Begin:

September 29, 2008

Term End:

Open

Nature and Scope of Work:

Ultrasonic Flow Measuring System for PTN

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO 114114

Major Task or Tasks Associated With:

Staff Augmentation

Vendor Identity:

Richard Sipos

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source Justification

Dollar Value:

Total Blanket Purchase Order Value through Revision 6 is



Contract Status:

Active

Term Begin:

July 3, 2008

Term End:

open

Nature and Scope of Work:

Project Management Services

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 4500521317

Major Task or Tasks Associated With:

Inductors

Vendor Identity:

Areva

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive Selection

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

September 8, 2009

Term End:

Open

Nature and Scope of Work:

Supply of Inductors

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-BA

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 126248

Major Task or Tasks Associated With:

Replacement Transformer Coolers

Vendor Identity:

ABB

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

1

Brief Description of Selection Process:

Competitive Selection, Commercial and Technical Evaluation

Dollar Value:

Total Contract Value through Rev 2

Contract Status:

Active

Term Begin:

October 8, 2009

Term End:

Open

Nature and Scope of Work:

Replacement Transformer Coolers

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 126453

Major Task or Tasks Associated With:

Turbine Plant Cooling Water Heat Exchangers

Vendor Identity:

Joseph Oat Corporation

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive Selection, Commercial and Technical Evaluation

Dollar Value:

Total Contract Value through revision 1 is [REDACTED]

Contract Status:

Active

Term Begin:

November 5, 2009

Term End:

Open

Nature and Scope of Work:

Supply Turbine Plant Cooling Water Heat Exchangers

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO #127777

Major Task or Tasks Associated With:

Estimating Services

Vendor Identity:

High Bridge

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Contract Value through revision 2 is



Contract Status:

Active

Term Begin:

December 8, 2009

Term End:

Open

Nature and Scope of Work:

Estimating Services

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO # 127881

Major Task or Tasks Associated With:

Procedure Writers

Vendor Identity:

Absolute Consulting

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 22, 2009

Term End:

Open

Nature and Scope of Work:

Procedure Writers

Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO #118988

Major Task or Tasks Associated With:

Fuel Storage Criticality and Related Analysis (PSL 2)

Vendor Identity:

Holtec

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Purchase Order Value through Revision 4 is [REDACTED]

Contract Status:

Active

Term Begin:

January 22, 2009

Term End:

Open

Nature and Scope of Work:

Fuel Storage Criticality and Related Analysis (PSL 2)

Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.
For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO #118563

Major Task or Tasks Associated With:

Fuel Storage Criticality and Related Analysis (PSL 1)

Vendor Identity:

Holtec

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Purchase Order Value through Revision 5 is

Contract Status:

Active

Term Begin:

January 14, 2009

Term End:

Open

Nature and Scope of Work:

Fuel Storage Criticality and Related Analysis (PSL 1)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO # 4500467077

Major Task or Tasks Associated With:

PSL Generator Step-up Transformers

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

7

Number of Bids Received:

7

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

November 10, 2008

Term End:

Open

Nature and Scope of Work:

PSL Generator Step-up Transformers

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO # 130612

Major Task or Tasks Associated With:

Condensate Pumps

Vendor Identity:

Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Contract Value through Revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

April 22, 2010

Term End:

Open

Nature and Scope of Work:

Condensate Pumps

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO #130649

Major Task or Tasks Associated With:

Main Feedwater Pumps

Vendor Identity:

Flowsolve Corp

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

1

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

April 22, 2010

Term End:

Open

Nature and Scope of Work:

Main Feedwater Pumps

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO # 126227

Major Task or Tasks Associated With:

Control System FWH, Moisture Separator

Vendor Identity:

Invensys

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Dollar Value through revision 9

Contract Status:

Active

Term Begin:

October 13, 2009

Term End:

Open

Nature and Scope of Work:

Control System FWH, Moisture Separator

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO # 129689

Major Task or Tasks Associated With:

Turbine Digital Upgrade

Vendor Identity:

Invensys

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Dollar Value through Revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

March 17, 2010

Term End:

Open

Nature and Scope of Work:

Turbine Digital Upgrade

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 130272

Major Task or Tasks Associated With:

Electro-Hydraulic Fluid Systems

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Dollar Value through Rev 4 is [REDACTED]

Contract Status:

Active

Term Begin:

April 8, 2010

Term End:

Open

Nature and Scope of Work:

Electro-Hydraulic Fluid Systems

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO # 131928

Major Task or Tasks Associated With:

Pre-planning SL2-19

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Complete

Term Begin:

June 14, 2010

Term End:

February 28, 2011

Nature and Scope of Work:

SL2-19 Pre-planning work to support station milestones for the Turbine Generator Installation

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO # 131533

Major Task or Tasks Associated With:

Non-Fuels NSSS Interim LAR (PSL 1 & 2)

Vendor Identity:

Areva

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Predetermined Source

Dollar Value:

Total Contract Value through revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

June 10, 2010

Term End:

Open

Nature and Scope of Work:

Non-Fuels NSSS Interim LAR (PSL 1 & 2)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO # 131907

Major Task or Tasks Associated With:

Fuels Related Interim LAR/MOD for EPU at PSL

Vendor Identity:

Areva

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Predetermined Source

Dollar Value:

Total Contract Value through Revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

June 11, 2010

Term End:

Open

Nature and Scope of Work:

Fuels Related Interim LAR/MOD for EPU at PSL

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO # 131585

Major Task or Tasks Associated With:

Interim LAR/MOD for EPU at PSL

Vendor Identity:

Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Predetermined Source

Dollar Value:

Total Contract Value through Revision 4 is [REDACTED]

Contract Status:

Active

Term Begin:

June 15, 2010

Term End:

Open

Nature and Scope of Work:

Interim LAR/MOD for EPU at PSL

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO #131742

Major Task or Tasks Associated With:

LAR/Request for Additional Information

Vendor Identity:

Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Predetermined Source

Dollar Value:

Total Contract value through revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

June 16, 2010

Term End:

Open

Nature and Scope of Work:

LAR/Request for Additional Information for Non-Fuels related scope

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO #131940

Major Task or Tasks Associated With:

Main Steam Turbine Control Replacement

Vendor Identity:

Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

4

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Max Contract value through Rev 2 to Release 0

Contract Status:

Active

Term Begin:

June 30, 2010

Term End:

Open

Nature and Scope of Work:

Main Steam Turbine Control Replacement

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PQ #2259675

Major Task or Tasks Associated With:

Furnish New Spent Fuel Pool Heat Exchangers

Vendor Identity:

Joseph Oat Corporation

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

2

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

July 23, 2010

Term End:

Open

Nature and Scope of Work:

Furnish New Spent Fuel Pool Heat Exchangers

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 2259668

Major Task or Tasks Associated With:

Rewind/Refurbish Upgrade Condensate Pumps

Vendor Identity:

Tampa Armature Works

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

August 2, 2010

Term End:

Open

Nature and Scope of Work:

Rewind/Refurbish Upgrade Condensate Pumps

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO #2260113

Major Task or Tasks Associated With:

PSL Rod Control System Upgrades

Vendor Identity:

Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Contract Value through Amendment 3 [REDACTED]

Contract Status:

Active

Term Begin:

September 23, 2010

Term End:

Open

Nature and Scope of Work:

PSL Rod Control System Upgrades

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:
PTN PO #2261747

Major Task or Tasks Associated With:
EPU NSSS Engineering and Modification Support

Vendor Identity:
Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This Indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Predetermined Source

Dollar Value:
Total Contract Value through Amendment 2 [REDACTED]

Contract Status:
Active

Term Begin:
September 23, 2010

Term End:
Open

Nature and Scope of Work:
EPU NSSS Engineering and Modification Support

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO #2264240

Major Task or Tasks Associated With:

PSL 2-19 Turbine Generator Installation Contract

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

November 17, 2010

Term End:

Open

Nature and Scope of Work:

PSL 2-19 Turbine Generator Installation Contract

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.
For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO #2264841

Major Task or Tasks Associated With:

SL 2-19 Technical Support

Vendor Identity:

Batsch Industries

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Contract Value through Amendment 2 [REDACTED]

Contract Status:

Active

Term Begin:

November 30, 2010

Term End:

Open

Nature and Scope of Work:

SL 2-19 Technical Support

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

2264914

Major Task or Tasks Associated With:

CEDMS Power Switch Refurbishment (PSL 2)

Vendor Identity:

Westinhouse Electric

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 7, 2010

Term End:

Open

Nature and Scope of Work:

CEDMS Power Switch Refurbishment (PSL 2)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO #2285418

Major Task or Tasks Associated With:

Implementation Spares for Turbine Generator Work

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Contract Value through Amendment 2

Contract Status:

Active

Term Begin:

December 16, 2010

Term End:

Open

Nature and Scope of Work:

Implementation Spares for Turbine Generator Work

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO #2285720

Major Task or Tasks Associated With:

Licensing/Design Basis/Program Modification

Vendor Identity:

Enertcon

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

2

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

January 4, 2011

Term End:

Open

Nature and Scope of Work:

Licensing/Design Basis/Program Modification

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO# 2291203

Major Task or Tasks Associated With:

Main Steam Isolation Valve Replacement Actuator

Vendor Identity:

Enertech

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

2

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Contract Value through Amendment 3

Contract Status:

Active

Term Begin:

April 21, 2011

Term End:

Open

Nature and Scope of Work:

Main Steam Isolation Valve Replacement Actuator

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO# 2290465

Major Task or Tasks Associated With:

Design, Engineering and Fabrication of Turbine Crossover piping

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

March 31, 2011

Term End:

Open

Nature and Scope of Work:

Design, Engineering and Fabrication of Turbine Crossover piping

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO# 2290614

Major Task or Tasks Associated With:

Main Feedwater Pump Casing Modifications

Vendor Identity:

Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

N/A

Number of Bids Received:

N/A

Brief Description of Selection Process:

Replaces PO 130649

Dollar Value:

Total Contract Value through Amend 1

Contract Status:

Active

Term Begin:

May 2, 2011

Term End:

Open

Nature and Scope of Work:

Main Feedwater Pump Casing Modifications

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO# 2293950

Major Task or Tasks Associated With:

Turbine Generator Pre-Outage Planning PTN 3 & 4

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Contract value through Amendment 1 [REDACTED]

Contract Status:

Active

Term Begin:

June 24, 2011

Term End:

Open

Nature and Scope of Work:

Turbine Generator Pre-Outage Planning PTN 3 & 4
(Turbine Generator Installation)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO# 2295186

Major Task or Tasks Associated With:

Metamic Chevrons for Spent Fuel Pool

Vendor Identity:

Holtec

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

August 2, 2011

Term End:

Open

Nature and Scope of Work:

Metamic Chevrons for Spent Fuel Pool

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:
PTN PO# 2296556

Major Task or Tasks Associated With:
Modification, overhaul and refurbishment of the B and C AFW

Vendor Identity:
Sulzer Pumps

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
OEM

Dollar Value:
[REDACTED]

Contract Status:
Active

Term Begin:
September 2, 2011

Term End:
Open

Nature and Scope of Work:
Modification, overhaul and refurbishment of the B and C AFW

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO# 2298408

Major Task or Tasks Associated With:

Fuel Movers for Metamic Inserts

Vendor Identity:

Master Lee Energy Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

1

Brief Description of Selection Process:

Competitive

Dollar Value:

1

Contract Status:

Active

Term Begin:

October 12, 2011

Term End:

Open

Nature and Scope of Work:

Fuel Movers for Metamic Inserts

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:
PSL PO# 2297556

Major Task or Tasks Associated With:
Siemens Installation of 2A Main Power Transformer

Vendor Identity:
Siemens Energy Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
[REDACTED]

Contract Status:
Active

Term Begin:
September 27, 2011

Term End:
Open

Nature and Scope of Work:
Siemens Installation of 2A Main Power Transformer

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO# 2295953

Major Task or Tasks Associated With:

Misc Safety Related Wire and Cable

Vendor Identity:

Marmion Wire & Cable

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Contract Value through revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

August 24, 2011

Term End:

Open

Nature and Scope of Work:

Misc Safety Related Wire and Cable

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO# 2297055

Major Task or Tasks Associated With:

Replacement Unit 2 LP #4 Feedwater Heaters for EPU

Vendor Identity:

Thermal Engineering

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

September 16, 2011

Term End:

Open

Nature and Scope of Work:

Replacement Unit 2 LP #4 Feedwater Heaters for EPU

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO# 2300139

Major Task or Tasks Associated With:

SL 1-24 Turbine Generator Installation

Vendor Identity:

Siemens Energy Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

September 16, 2011

Term End:

Open

Nature and Scope of Work:

SL 1-24 Turbine Generator Installation

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO# 2290624

Major Task or Tasks Associated With:

Upgrade Services for Feedwater Pumps

Vendor Identity:

Ames Group LLC

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Contract Value through revision 1 [REDACTED]

Contract Status:

Active

Term Begin:

November 16, 2011

Term End:

Open

Nature and Scope of Work:

Upgrade Services for Feedwater Pumps

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO# 2300487

Major Task or Tasks Associated With:

Construction Management Oversight Services for SL1-24

Vendor Identity:

Weldtech Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Contract Status:

Active

Term Begin:

November 28, 2011

Term End:

Open

Nature and Scope of Work:

Construction Management Oversight Services for SL1-24

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

NF-10-358 and NF-11-178

Major Task or Tasks Associated With:

Spent Fuel Criticality Safety Analysis Support (PTN)

Vendor identity:

Westinhouse Electric

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

November 2, 2010

Term End:

Open

Nature and Scope of Work:

Spent Fuel Criticality Safety Analysis Support (PTN)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO # 2301867

Major Task or Tasks Associated With:

Develop Engineering Change Packages for EPU at PTN

Vendor Identity:

Enercon Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 28, 2011

Term End:

Open

Nature and Scope of Work:

Develop Engineering Change Packages for EPU at PTN

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO # 2261800

Major Task or Tasks Associated With:

Supply of Simulator SCD Software Translator Upgrade

Vendor Identity:

L 3 Communications Mapps inc

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Contract Value through Amendment 2 [REDACTED]

Contract Status:

Active

Term Begin:

September 28, 2010

Term End:

Open

Nature and Scope of Work:

Supply of Simulator SCD Software Translator Upgrade

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 2301737

Major Task or Tasks Associated With:

Construction Management Oversight Services for PTN

Vendor Identity:

PSI Energy Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 21, 2011

Term End:

Open

Nature and Scope of Work:

Construction Management Oversight Services for PTN

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.
For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 2301736

Major Task or Tasks Associated With:

Construction Management Oversight Services

Vendor Identity:

Weidtech Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 21, 2011

Term End:

Open

Nature and Scope of Work:

Construction Management Oversight Services

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO #2301871

Major Task or Tasks Associated With:

Develop Engineering Changes Packages for EPU at PTN

Vendor Identity:

Zachry Nuclear Engineering

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 28, 2011

Term End:

Open

Nature and Scope of Work:

Develop Engineering Changes Packages for EPU at PTN

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO #2301858

Major Task or Tasks Associated With:

Develop TPCW Changes Packages for EPU at PTN

Vendor Identity:

Sargent & Lundy

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:


December 28, 2011

Term End:

Open

Nature and Scope of Work:

Develop TPCW Changes Packages for EPU at PTN

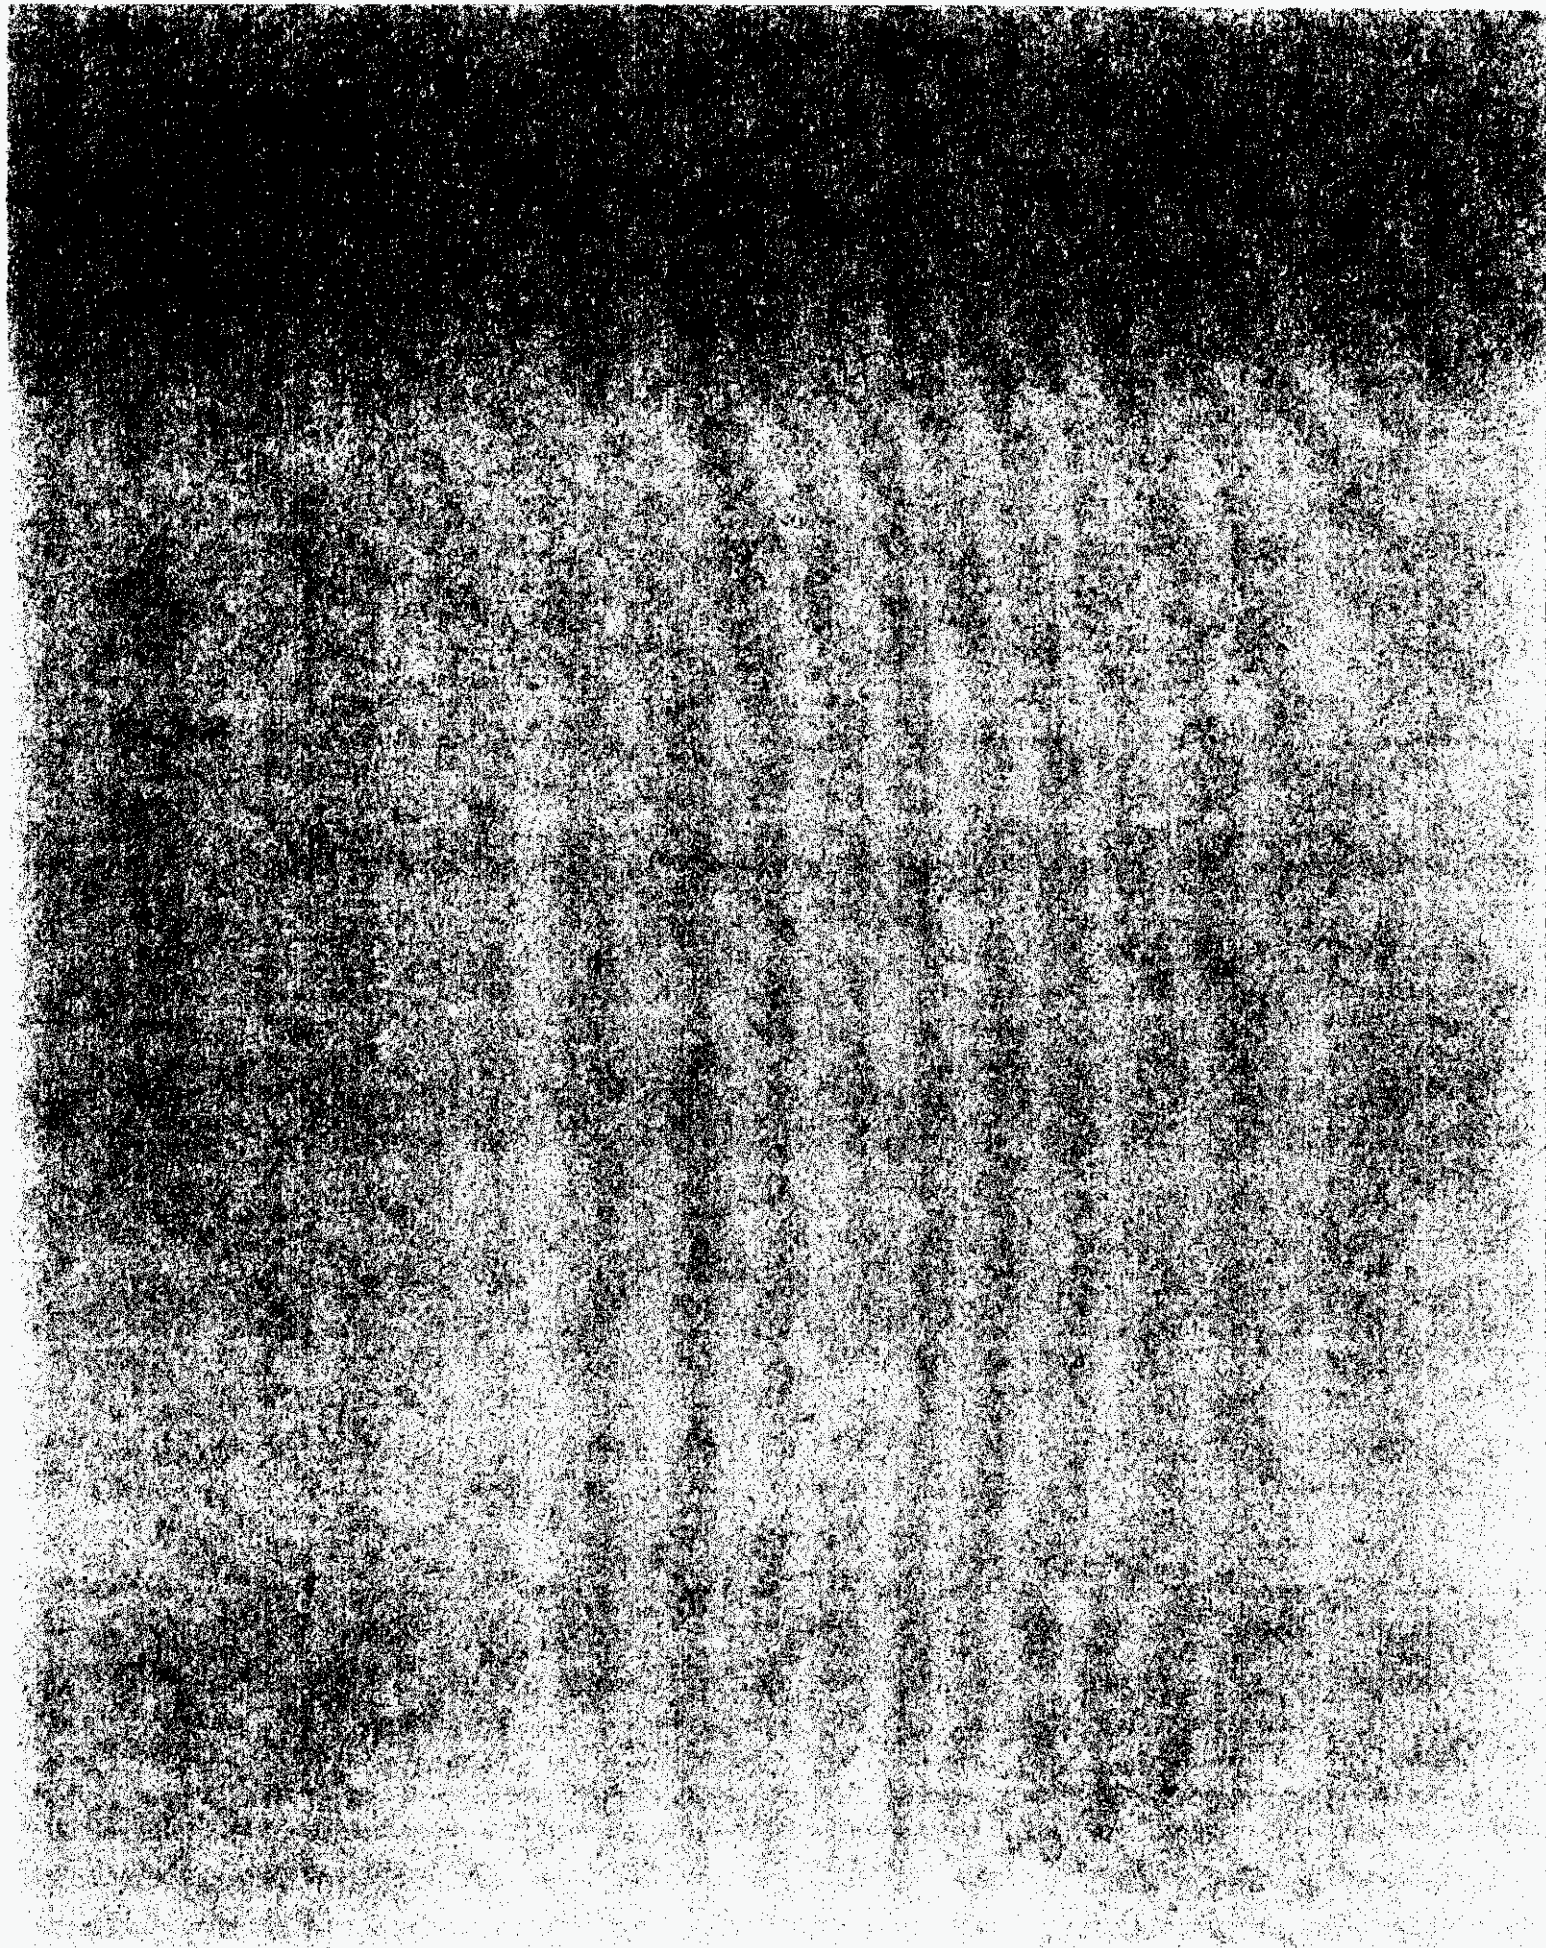

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed

Schedule T-7A

[Section 5(x)]

FLORIDA PUBLIC SERVICE COMMISSION

EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and description of work.

COMPANY: Florida Power & Light Company


For the Year Ended: 12/31/2011
Witness: Steven D. Scroggs

DOCKET NO.: 120009-EI

CONFIDENTIAL CONFIDENTIAL CONFIDENTIAL CONFIDENTIAL

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Actual amount expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
1	4500395492	Open- CO#38	11/5/2007- open	10/11/2011- open					Bechtel Power Corp	Comp Bid/ Single Source/ Predetermined Source	Engineering Services to Support Preparation of COLA and SCA and Response to post-submittal RAI's.
2	4500404639	Open- CO#6	1/31/2008- open	4/21/2011- open					Westinghouse Electric Co	Sole Source/ Predetermined Source	Engineering Services to Support Preparation of COLA and Response to post-submittal RAI's.
3	4500425707	Open-CO#5	5/23/2008- open	1/3/2011- open					HDR Engineering, Inc.	Comp Bid/ Single Source	Conceptual Engineering of Cooling Water Supply and Discharge
4	4500430034	Open- CO#1	6/16/2008- open	1/28/2011- open					Electric Power Research Institute	Single Source	Advanced Nuclear Technology; Near term deployment of Advanced Light Water Reactors
5	4500443122	Open-CO#3	8/6/2008- open	11/29/2011- open					Eco Metrics, Inc.	Single Source	Environmental Consulting Services
6	4500517152	Open-CO#3	7/10/2009- open	12/17/2010- open					McNabb Hydrogeologic Consulting Inc	Single Source	Turkey Point 6&7 Post SCA Submittal and UIC Licensing Support
7	4500518160	Open-CO#5	7/23/2009- open	5/24/2011- open					Golder Associates Inc	Single Source	Turkey Point 6&7 Post SCA Submittal Support
8	4500518167	Open- CO#6	7/23/2009- open	9/14/2011- open					Environmental Consulting and Technology Inc	Single Source/ Predetermined Source	Turkey Point 6&7 SCA Support
9	4500536449	Open-CO#2	10/12/2009- open	11/29/2011- open					McNabb Hydrogeologic Consulting Inc	Comp Bid/ Single Source	Turkey Point 6&7 UIC Subject Matter Expert Support
10	4500492222	Open-CO#2	3/17/2009- open	12/22/2011- open					Experis US LLC(F/K/A, Jefferson Wells International)	Comp Bid/ Single Source	New Nuclear Audit
11	4500587305	Open-CO#1	5/29/2010- open	9/1/2010- open					Dickerson Florida Inc	Comp Bid	Turkey Point 6&7 Exploratory/UIC Well Site Development
12	4500652043	Open-CO#1	3/3/2011- open	12/29/2011- open					Layne Christensen Company	Comp Bid	Turkey Point 6&7 Exploratory/UIC Well and Dual Zone Monitor Well Installation

A B C D

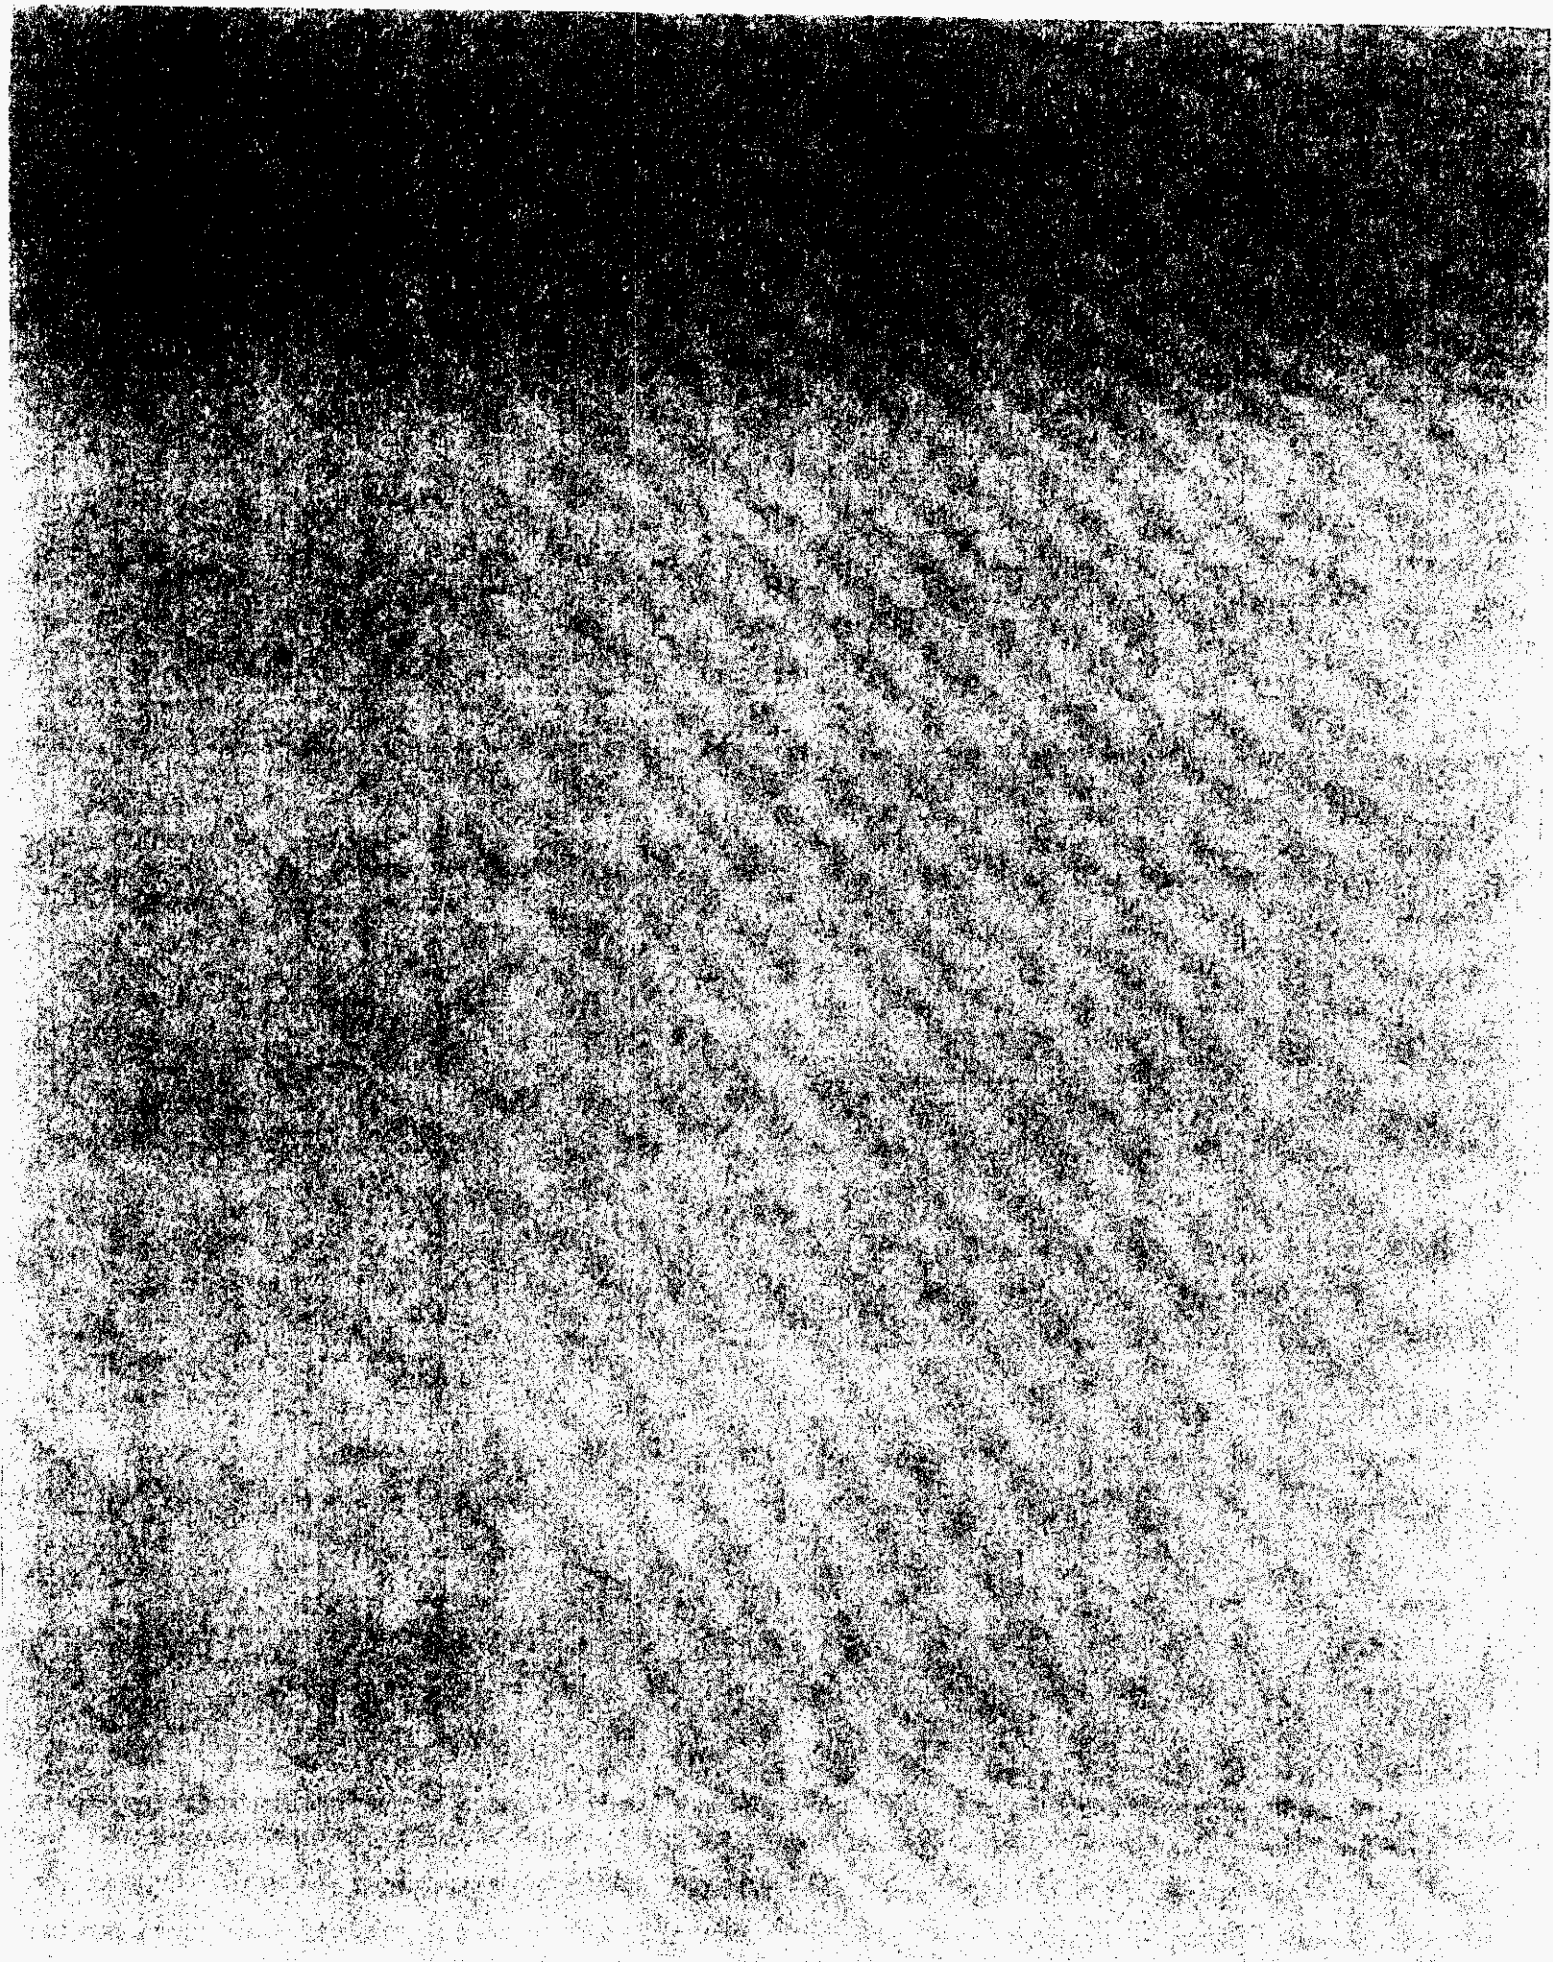

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (b)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: Florida Power & Light Company
DOCKET NO.: 120008-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:
4500395492

Major Task or Tasks Associated With:
COLA and SCA preparation and support

Vendor Identity:
Bechtel Power Corporation

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
Two

Number of Bids Received:
Two

Brief Description of Selection Process:
Initial contract competitively bid; change orders #01-#11
issued single source; all subsequent change orders
issued Predetermined Source

Dollar Value:

1

Contract Status:
Active- CO#38

Term Begin:
11/8/2007

Term End:
2/27/2018

Nature and Scope of Work:
Engineering Services to Support Preparation of COLA
and SCA, including post-submittal support for RAI
responses.

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (B)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:

4500404639

Major Task or Tasks Associated With:

COLA support

Vendor Identity:

Westinghouse Electric Company

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct

Number of Vendors Solicited:

One

Number of Bids Received:

One

Brief Description of Selection Process:

Sole source justification; designated as Predetermined
Source March 2009

Dollar Value:

1

Contract Status:

Active- CO#6

Term Begin:

1/31/2008

Term End:

6/28/2014

Nature and Scope of Work:

Engineering Services to Support Preparation of COLA,
including post-submittal support for RAI responses.

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO.: 120009-El

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:

4500430034

Major Task or Tasks Associated With:

COLA and SCA preparation and support

Vendor Identity:

Electric Power Research Institute

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct

Number of Vendors Solicited:

Two

Number of Bids Received:

Two

Brief Description of Selection Process:

Single

Dollar Value:

1

Contract Status:

Active- CO#1

Term Begin:

6/16/2008

Term End:

6/29/2014

Nature and Scope of Work:

Engineering Services to Support Preparation of COLA and SCA, including post-submittal support for RAI responses.

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

COMPANY: Florida Power & Light Company

DOCKET NO.: 120009-EI

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:

4500518160

Major Task or Tasks Associated With:

Post SCA Submittal support

Vendor Identity:

Golder Associates, Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct or Indirect relationship with the vendor

Number of Vendors Solicited:

One

Number of Bids Received:

One

Brief Description of Selection Process:

Single source; Designated as Predetermined Source February 2010

Dollar Value:

1

Contract Status:

Active- CO#5

Term Begin:

7/23/2009

Term End:

6/28/2012

Nature and Scope of Work:

Post SCA Submittal support

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: Florida Power & Light Company
DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:
4500518167

Major Task or Tasks Associated With:
SCA Support

Vendor Identity:
Environmental Consulting and Technology, Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
One

Number of Bids Received:
One

Brief Description of Selection Process:
Single source; Designated as Predetermined Source December 2009

Dollar Value:

1

Contract Status:
Active- CO#6

Term Begin:
7/23/2009

Term End:
6/28/2012

Nature and Scope of Work:
SCA Support

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

COMPANY: Florida Power & Light Company

DOCKET NO.: 120009-EI

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:

4500536449

Major Task or Tasks Associated With:

Turkey Point 6&7 UIC Subject Matter Expert Support

Vendor Identity:

McNabb Hydrogeologic Consulting

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct

Number of Vendors Solicited:

One

Number of Bids Received:

One

Brief Description of Selection Process:

Competitive Bid for Initial Order, Single Source justification for Change Orders

Dollar Value:

1 [REDACTED]

Contract Status:

Active- CO#2

Term Begin:

10/12/2009

Term End:

6/29/2013

Nature and Scope of Work:

Turkey Point 6&7 UIC Subject Matter Expert Support

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: Florida Power & Light Company
DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:
4500587305

Major Task or Tasks Associated With:
Turkey Point Units 6&7 Exploratory/UIC Well Site Development

Vendor Identity:
Dickerson Florida, Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
Eight

Number of Bids Received:
Five

Brief Description of Selection Process:
Competitive Bid

Dollar Value:

1

Contract Status:
Active- CO#1

Term Begin:
6/29/2010

Term End:
6/30/2011

Nature and Scope of Work:
Turkey Point Units 6&7 Exploratory/UIC Well Site Development

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

COMPANY: Florida Power & Light Company

DOCKET NO.: 120009-EI

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:

4500652043

Major Task or Tasks Associated With:

Turkey Point 6&7 Exploratory/UIC Well and Dual Zone Monitor Well Installation

Vendor Identity:

Layne Christensen Company

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct

Number of Vendors Solicited:

Three

Number of Bids Received:

Three

Brief Description of Selection Process:

Competitive Bid

Dollar Value:

1

Contract Status:

Active- CO#1

Term Begin:

3/3/2011


Term End:

9/27/2012

Nature and Scope of Work:

Turkey Point 6&7 Exploratory/UIC Well and Dual Zone Monitor Well Installation

EXHIBIT B

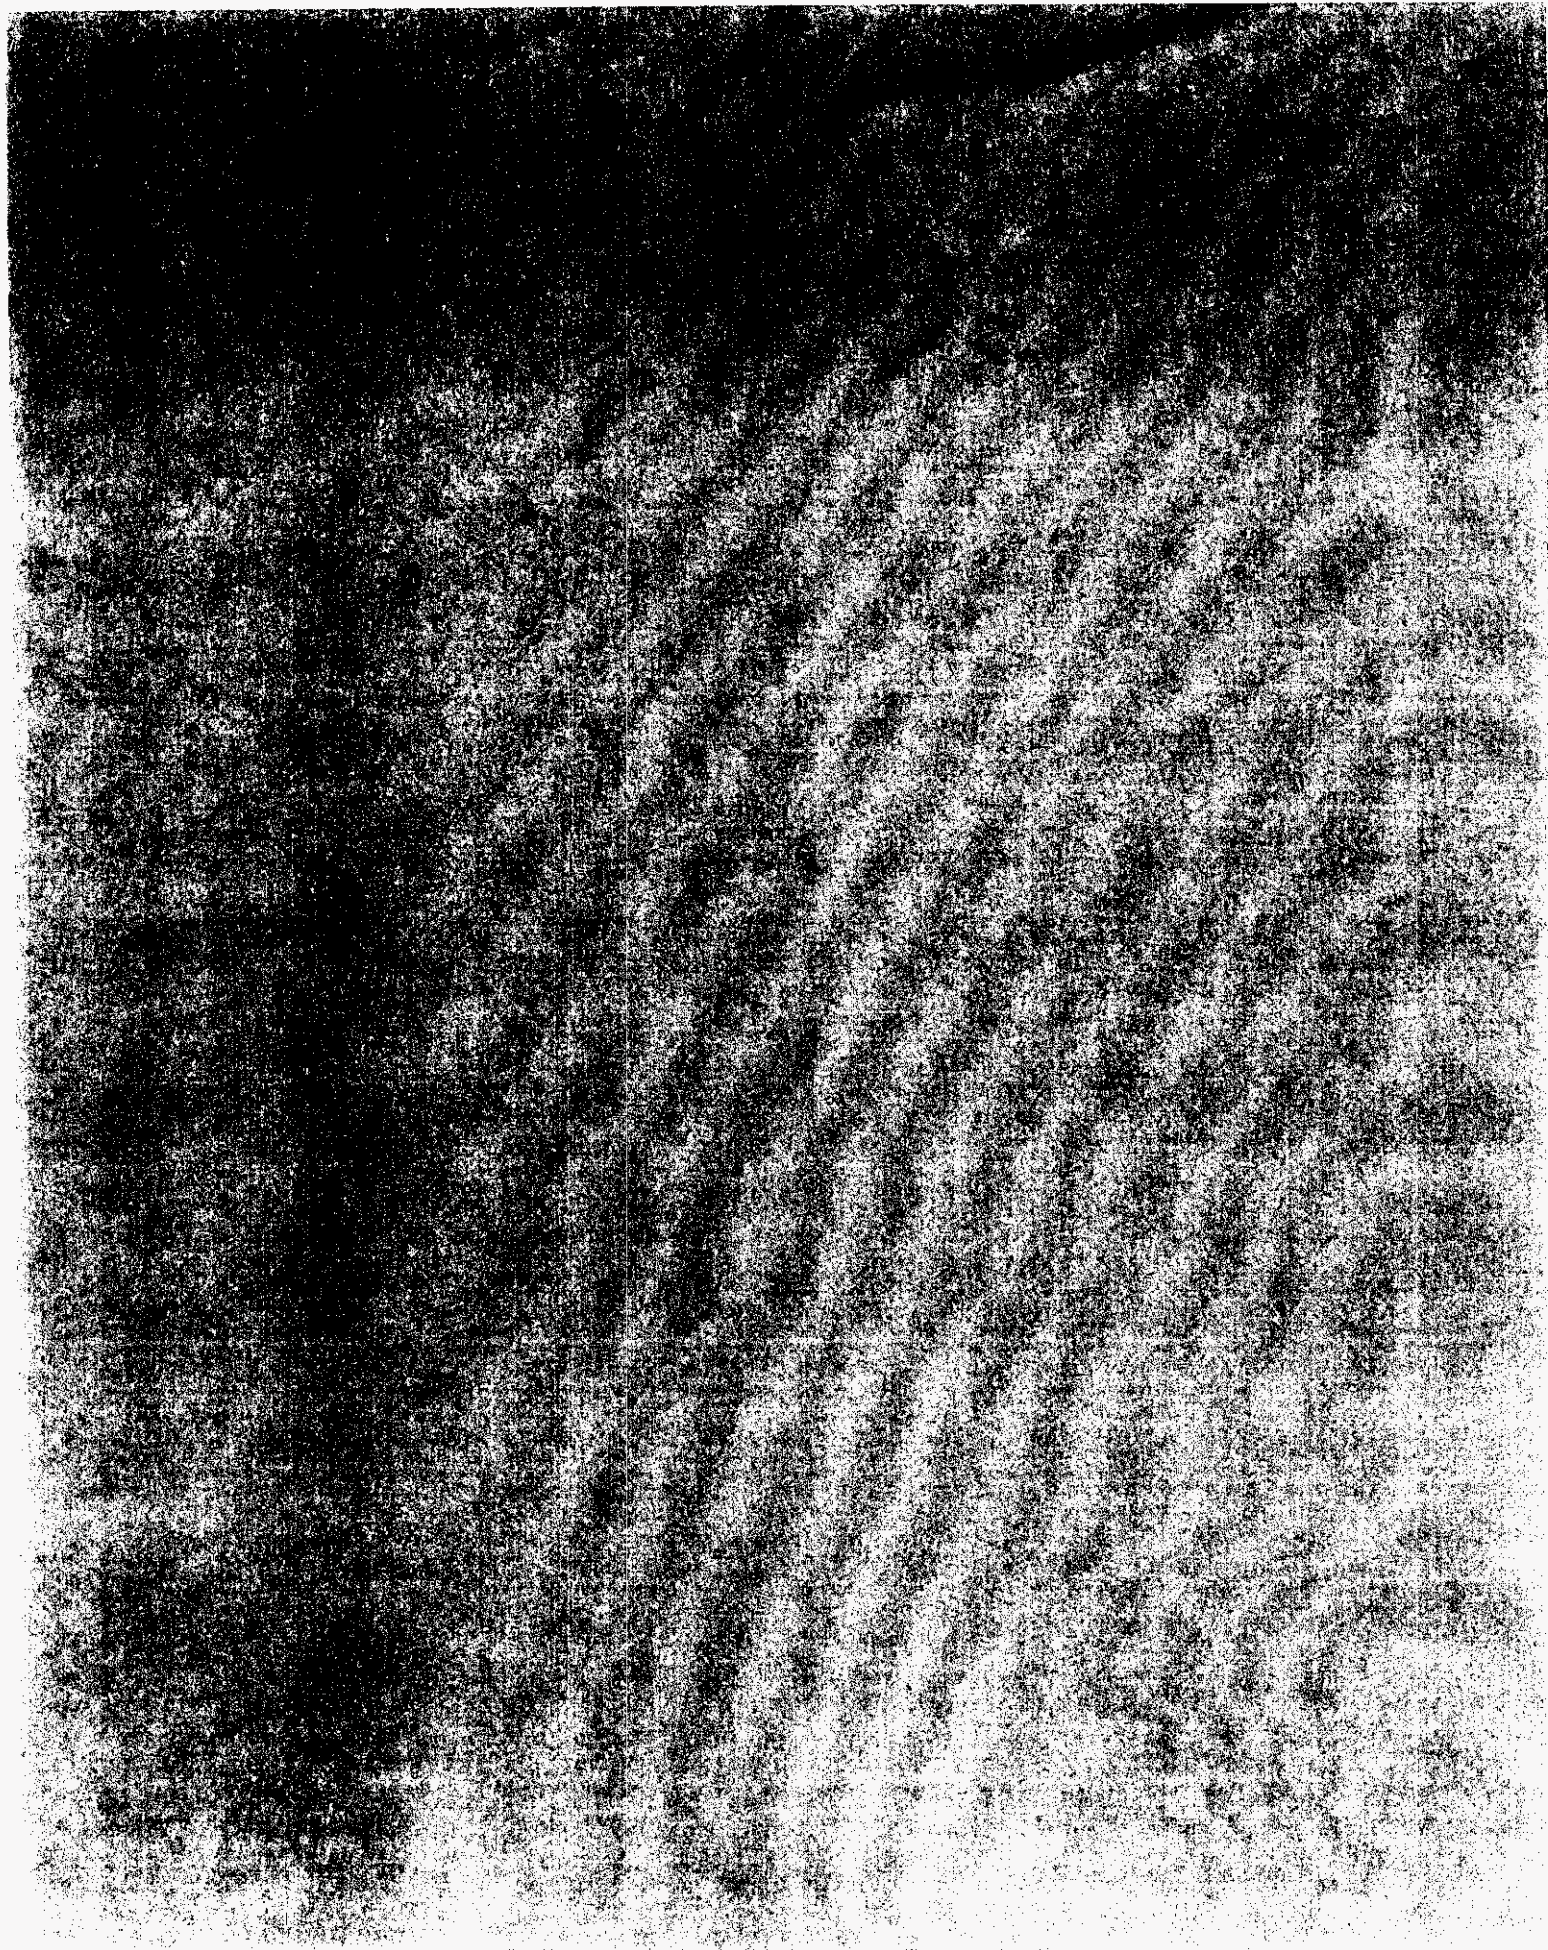

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO. 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

	(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
1	121869	Open	4/29/09 - open	4/29/09 - open					AAF MCQUAY	Competitive	Supply Normal Containment Coolers and Testing Services (PTN)
2	120769	Open	3/26/09 - open	3/26/09 - open					Calvert Company Inc	Competitive	Iso Phase Bus Duct Coolers and Testing Services (PSL)
3	124436	Open	7/17/09 - open	7/17/09 - open					Calvert Company Inc	Competitive	Iso Phase Bus Duct Coolers, Install, Demo & Testing Services (PTN)
4	121985	Open	4/24/09 - open	4/24/09 - open					Flowserve Corp.	Competitive	Replacement Main Feedwater Pumps & Various Testing (PSL)
5	123137	Open	5/28/09 - open	5/28/09 - open					Flowserve Corp.	Competitive	Main Feedwater Isolation Valves and Testing Services (PTN)
6	125454	Open	8/28/09 - open	8/28/09 - open					Flowserve Corp.	Competitive	Replacement Heater Drain Pumps (PSL)
7	122154	Complete	4/27/09 - 6/15/11	4/27/09 - 6/15/11					Siemens Energy Inc.	Competitive	Step-Up Transformer (PTN)
8	119078	Open	12/9/08 - open	12/9/08 - open					Westinghouse	OEM	NSSS Engineering Analysis and LAR (PTN)
9	119653	Open	11/24/08 - open	11/24/08 - open					Westinghouse	OEM	NSSS Engineering Analysis and LAR (PSL)
10	121947	Open	4/24/09 - open	4/24/09 - open					Westinghouse	OEM	New & Spent Fuel Criticality and Thermal Hydraulic Analysis (PTN)
11	119670	Open	2/18/09 - open	2/18/09 - open					Proto-Power	Single Source	Project Engineering Support (PSL)
12	116297	Open	8/27/08 - open	8/27/08 - open					Areva	Single Source	RSG Design Review and LAR Work (PSL)
13	115338	Open	8/27/08 - open	8/27/08 - open					Areva	Single Source	RCS Design Review (PTN)
14	105353	Complete	10/02/07 - 12/01/11	10/02/07 - 12/01/11					Shaw - Stone & Webster	Sole Source	Engineering Support (PSL & PTN)
15	117809	Open	12/02/08 - open	12/02/08 - open					Bechtel	Competitive Bid	Engineering Procurement Construction (PTN)
16	116088	Open	09/29/08 - open	09/29/08 - open					Siemens	Single Source	Low Pressure Turbine, Exciter, Exciter Inst. (PSL)
17	117620	Open	12/02/08 - open	12/02/08 - open					Bechtel	Competitive Bid	Engineering Procurement Construction (PSL)
18	116090	Open	9/29/08 - open	9/29/08 - open					Siemens	Single Source	Turbine, Generator/Exciter Upgrades & Inst. (PTN)
19	116326	Open	12/19/08 - open	12/19/08 - open					TEI	Competitive Bid	Condenser Tubes (PTN)
20	118206	Open	12/17/08 - open	12/17/08 - open					TEI	Competitive Bid	Moisture Separator Reheaters (PTN)
21	118205	Open	12/17/08 - open	12/17/08 - open					TEI	Competitive Bid	Moisture Separator Reheaters (PSL)
22	118241	Open	12/19/08 - open	12/19/08 - open					TEI	Competitive Bid	Feed Water Heaters (PTN)
23	112221	Open	4/22/08 - open	4/22/08 - open					Shaw - Stone & Webster	Single Source	Licensing Engineering and BOP Spec Development (PSL)
24	112177	Open	4/22/08 - open	4/22/08 - open					Shaw - Stone & Webster	Single Source	Licensing Engineering and BOP Spec Development (PTN)

A B C D

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO. 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

(A)		(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
25	117272	Open	11/13/08 - open	11/13/08 - open					American Crane	Single Source	Gantry Crane Upgrade (PSL)
26	118224	Open	12/17/08 - open	12/17/08 - open					TEI	Competitive Bid	Feed Water Heaters (PSL)
27	115465	Open	9/03/08 - open	9/03/08 - open					Proto-Power	Single Source	Engineering Services (PTN)
28	118278	Open	12/19/08 - open	12/19/08 - open					TEI	Competitive Bid	TCW Heat Exchangers (PSL)
29	105720	Open	9/12/07 - open	9/12/07 - open					AREVA	Single Source	Neutronics Analysis (PSL)
30	116796	Complete	10/29/08 - 12/22/11	10/29/08 - 12/22/11					Cameron	Single Source	Ultrasonic Flow Meter Measuring System (PTN)
31	116107	Open	9/29/08 - open	9/29/08 - open					Cameron	Single Source	Ultrasonic Flow Meter Measuring System (PSL)
32	114114	Open	7/03/08 - open	7/03/08 - open					Richard Sipos	Single Source	Staff Augmentation (PSL)
33	115036	Complete	8/14/08 - 1/06/11	8/14/08 - 01/06/11					Babcock & Wilcox	Single Source	Steam Generator Component Design Review (PSL)
34	112228	Complete	4/23/08 - 03/11/11	4/23/08 - 03/11/11					Westinghouse	Single Source	Steam Generator Services for Moisture Carryover (PTN)
35	113030	Open	5/20/08 - open	5/20/08 - open					FPL Seabrook	Single Source	FPLE personnel supporting FPL Upgrades (PSL & PTN)
36	116391	Open	8/29/08 - open	8/29/08 - open					NAI	Single Source	Radiological Consequence Analysis (PSL)
37	112987	Open	5/19/08 - open	5/19/08 - open					NAI	Single Source	Radiological Consequence Analysis (PTN)
38	4500521317	Open	9/08/09 - open	9/08/09 - open					Areva	Competitive	Inductors (PTN)
39	126248	Open	10/08/09 - open	10/08/09 - open					ABB	Competitive	Replacement Transformer Coolers (PSL)
40	126453	Open	11/05/09 - open	11/05/09 - open					Joseph Oat Corporation	Competitive	Cooling Water Heat Exchangers (PTN)
41	127777	Open	12/08/09 - open	12/08/09 - open					High Bridge	Single Source	Estimating Services (PTN)
42	127681	Open	12/22/09 - open	12/22/09 - open					Absolute Consulting	Single Source	Procedure Writers (PTN)
43	123762	Open	6/25/09 - open	6/25/09 - open					Key Controls of Tampa	OEM	Control System Tuning and Dynamic Analysis (PTN)
44	118986	Open	01/22/09 - open	01/22/09 - open					Holtec	Single Source	Fuel Storage Criticality and related analysis (PSL 2)
45	118563	Open	1/14/09 - open	1/14/09 - open					Holtec	Competitive	Fuel Storage Criticality and related analysis (PSL 1)
46	118827	Open	7/28/09 - open	7/28/09 - open					Western Services	Competitive	NSSS Simulator Reactor Core Model Upgrade (PSL)
47	118844	Open	01/15/09 - open	01/15/09 - open					Western Services	Competitive	NSSS Simulator Reactor Core Model Upgrade (PTN)
48	4500467077	Open	11/10/08 - open	11/10/08 - open					Siemens	Competitive	Generator Step-up Transformers (PSL)

A B C D

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO: 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

DOCKET NO. 120009-E1

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended In Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
49	130579	Open	5/01/10 - open	5/01/10 - open					Fisher Controls	Competitive	Modified Feedwater Regulating Valves/Actuators (PSL)
50	130160	Open	3/29/10 - open	3/29/10 - open					Flowserve Corp.	Competitive	Replacement Condensate Pumps (PSL)
51	130612	Open	4/22/10 - open	4/22/10 - open					Flowserve Corp.	Competitive	Condensate Pumps (PTN)
52	130649	Open	4/22/10 - open	4/22/10 - open					Flowserve Corp.	Competitive	Main Feedwater Pumps (PTN)
53	125227	Open	10/13/09 - open	10/13/09 - open					Invensys	OEM	Control System FWH, Moisture Separator (PTN)
54	129589	Open	3/17/10 - open	3/17/10 - open					Invensys	Competitive	Turbine Digital Upgrade (PTN)
55	130272	Open	4/08/10 - open	4/08/10 - open					Siemens Energy Inc.	Competitive	Electro-Hydraulic Fluid Systems (PTN)
56	131356	Open	5/21/10 - open	5/21/10 - open					Brand Energy Solutions	Competitive	Supply Scaffolding Material (PTN)
57	131391	Complete	5/25/10 - 4/19/11	5/25/10 - 4/19/11					BRV Construction	Competitive	Design/Construct fabrication area inside the CSF (PTN)
58	131599	Open	5/27/10 - open	5/27/10 - open					All Star Toilets	Competitive	Supply Cleaning Services (PTN)
59	4500586420	Open	6/16/10 - open	6/16/10 - open					Energy Erectors	Competitive	Electrical contract labor work @ 230 kV substation (PTN)
60	131928	Complete	6/14/10 - 02/28/11	6/14/10 - 02/28/11					Siemens Energy Inc.	Single Source	SL2-19 Pre-planning TG Installation Work (PSL2)
61	131533	Open	6/10/10 - open	6/10/10 - open					Areva	OEM	Non-Fuels NSSS Interim LAR (PSL 1 & 2)
62	131907	Open	6/11/10 - open	6/11/10 - open					Areva	OEM	Fuels Related Interim LAR/MOD for EPU (PSL)
63	131585	Open	6/15/10 - open	6/15/10 - open					Shaw - Stone & Webster	PDS	Interim LAR/MOD Support for EPU (PSL)
64	131393	Open	6/10/10 - open	6/10/10 - open					Fisher Controls	Competitive	Heater Drain BOP Replacement Valves (PSL)
65	131742	Open	6/16/10 - open	6/16/10 - open					Westinghouse	PDS	LAR/RAI for Non-Fuels NSSS related scope (PSL)
66	132077	Open	6/17/10 - open	6/17/10 - open					Siemens Energy Inc.	Single Source	Siemens Dedicated Resident Site Manager (PTN)
67	132078	Open	6/17/10 - open	6/17/10 - open					Siemens Energy Inc.	Single Source	Siemens Dedicated Resident Site Manager (PSL)
68	132235	Open	6/24/10 - open	6/24/10 - open					Enercon	Single Source	NFPA 805/Appendix R Support for (PTN)
69	131987	Open	6/25/10 - open	6/25/10 - open					Sargent & Lundy Inc.	Single Source	Engineering for Steam Bypass Control (PSL1)
70	131940	Open	6/30/10 - open	6/30/10 - open					Westinghouse	Competitive	Main Steam Turbine Control Replacement (PSL)
71	132283	Open	6/28/10 - open	6/28/10 - open					Shaw - Stone & Webster	PDS	EPU Feedwater Pump Nozzle Load Reduction (PSL)
72	2259675	Open	7/23/10 - open	7/23/10 - open					Joseph Oat Corporation	Competitive	Furnish New Spent Fuel Pool Heat Exchangers (PTN)

A B C D

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO: 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
73	2259689	Open	8/02/10 - open	8/02/10 - open					TAW	Competitive	Rewind/Refurbish/Upgrade Condensate Pumps (PTN)
74	2259997	Open	8/4/10 - open	8/4/10 - open					SPX Corporation	Replaces 115351	Valve Rework (PTN)
75	2259768	Open	8/06/10 - open	8/06/10 - open					Westinghouse	OEM	Design basis support for Umbrella Mods (PTN)
76	2260155	Open	8/19/10 - open	8/19/10 - open					Siemens Energy Inc.	Single Source	PSL 1-24 Pre-planning TG Installation Work
77	2260113	Open	9/23/10 - open	9/23/10 - open					Westinghouse	OEM	Rod Control System Upgrades (PSL)
78	2261536	Open	9/18/10 - open	9/18/10 - open					Washington Group	Competitive	Feedwater Heater Ultrasonic Testing (PTN)
79	2261750	Open	9/21/10 - open	9/21/10 - open					Modular Space	Competitive	Lease of 15-Wide Trailers for EPU (PTN)
80	2261747	Open	9/23/10 - open	9/23/10 - open					Westinghouse	PDS	EPU NSSS Engineering and Modification Support (PTN)
81	2262094	Open	9/28/10 - open	9/28/10 - open					Structural Integrity	Competitive	Assessment of Min Wall Thickness Effects (PTN)
82	2262201	Open	9/30/10 - open	9/30/10 - open					Fisher Controls	Replaces 131393	Heater Drain BOP Replacement Valves (PSL)
83	2262367	Open	10/04/10 - open	10/04/10 - open					Techcom International	Competitive	Engineering Services for Various Distributing Mods (PTN)
84	2262515	Open	10/06/10 - open	10/06/10 - open					Fisher Controls	Replaces 130575	Modified Feedwater Regulating Valves/Actuators (PSL)
85	2263036	Open	10/19/10 - open	10/19/10 - open					Flowsolve Corp.	Replaces 130160	Replacement Condensate Pumps (PSL)
86	2264196	Complete	11/16/10 - 4/20/11	11/16/10 - 4/20/11					Siemens Energy Inc.	OEM	Replacement Blade Rings (PSL)
87	2264240	Open	11/17/10 - open	11/17/10 - open					Siemens Energy Inc.	Single Source	T/G Installation SL2-19 Outage (PSL)
88	2263052	Open	11/11/10 - open	11/11/10 - open					Invensys	Single Source	Steam Bypass Control System (PSL)
89	2263549	Open	11/10/10 - open	11/10/10 - open					Areva NP Inc	Competitive	Services of a Project Manager (PTN)
90	2264548	Complete	11/19/10 - 03/28/11	11/19/10 - 03/28/11					Graybar Electric	Competitive	Wire Cable (PTN)
91	2263930	Open	11/11/10 - open	11/11/10 - open					Brand Energy Solutions	Replaces 131356	Supply Scaffolding Material (PTN)
92	2264842	Open	11/30/10 - open	11/30/10 - open					Ronnies Turbine Services Inc	Single Source	On Site SL2-19 Tech Support (PSL)
93	2264841	Open	11/30/10 - open	11/30/10 - open					Batsch Industries	Single Source	On Site SL2-19 Tech Support (PSL)
94	2264377	Open	11/30/10 - open	11/30/10 - open					Techcom International	Competitive	Turbine Digital Controls Verification and Validation (PTN)
95	2264914	Open	12/07/10 - open	12/07/10 - open					Westinghouse Electric	OEM	CEDMS Power Switch Refurbishment (PSL2)
96	2263861	Open	11/4/10 - open	11/4/10 - open					Graybar Electric	Competitive	Temporary Power Unit Substations for EPU (PTN)

A B C D

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO. 120009-El

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in this year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended In Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
97	2285418	Open	12/16/10 - open	12/16/10 - open					Siemens Energy Inc.	OEM	Impl. Spares for EPU Turbine Gen. Work During SL2-19 (PSL)
98	4500589986	Open	7/6/10 - open	7/6/10 - open					Kennedy Construction	Competitive	Site preparation contract labor work @ 230 kV substation (PTN)
99	2285720	Open	01/4/11 - open	01/4/11 - open					Enercon Services	Competitive	Licensing/Design Basis/Program Modification (PTN)
100	2291203	Open	04/21/11 - open	04/21/11 - open					Enertech	Competitive	Main Steam Isolation Valve Replacement Actuator (PSL)
101	2287242	Open	01/27/11 - open	01/27/11 - open					Engineering Planning & Management	Competitive	Environmental Qualification Document (PTN)
102	2287468	Open	02/10/11 - open	02/10/11 - open					Feedforward Inc.	Competitive	DCS Mods (PSL)
103	2290208	Open	03/25/11 - open	03/25/11 - open					Feedforward Inc.	Competitive	Leading Edge Flow Meter Addition (PTN)
104	2287971	Open	02/15/11 - open	02/15/11 - open					Foster Wheeler North America	Competitive	SJAE Inter/After Condensers (PTN)
105	2290485	Open	03/31/11 - open	03/31/11 - open					Siemens	OEM	Design and Fabrication of Turbine Crossover piping (PTN)
106	2290463	Open	03/31/11 - open	03/31/11 - open					Siemens	OEM	Iron Bolts for Main Steam Generator Stator (PTN)
107	2290842	Open	04/08/11 - open	04/08/11 - open					Siemens	OEM	Blower Stationary Blade Rings (PSL)
108	2286521	Open	01/18/11 - open	01/18/11 - open					Stone & Webster	PDS	MSIV/MSCV Modification to Support EPU (PSL)
109	2264476	Open	05/11/11 - open	05/11/11 - open					Batsch Industries	Single Source	Turbine Generator Technical Support (PTN)
110	2291815	Open	04/28/11 - open	04/28/11 - open					BRV Construction	Competitive	Fossil Warehouse Demolition (PTN)
111	2290614	Open	05/02/11 - open	05/02/11 - open					Flowserve Corp.	Replaces 130649	Main Feedwater Pump Casing Modification (PTN)
112	2292773	Open	05/26/11 - open	05/26/11 - open					AAF MCQUAY	OEM	Design, Engineer, Fabricate and Deliver CRDM Coils (PTN)
113	2293950	Open	06/24/11 - 04/20/11	06/24/11 - 04/20/11					Siemens	Single Source	Turbine Generator Pre-outage planning activities (PTN)
114	2293653	Open	06/29/11 - open	06/29/11 - open					Thermal Engineering	Competitive	Design and Fabrication of Gland Steam Condensers (PTN)
115	2294247	Open	07/06/11 - open	07/06/11 - open					Ecological Associates	Competitive	Biological Plan of Study (PSL)
116	2294341	Open	07/11/11 - open	07/11/11 - open					Allion	Single Source	GL2008-01 Support (PSL)
117	2294494	Open	07/13/11 - open	07/13/11 - open					Enercon Services	Competitive	Emergency Containment Cooler Auto-start (PTN)
118	2294221	Open	07/11/11 - open	07/11/11 - open					Flowserve Corp.	Competitive	Main Steam Isolation Replacement Valves (PSL)
119	2294855	Open	07/21/11 - open	07/21/11 - open					Zachary Nuclear Engineering	Single Source	Project Engineering Support for EPU (PSL)
120	2295186	Open	08/02/11 - open	08/02/11 - open					Holtec International	Single Source	Metamic Chevrons for Spent Fuel Pool (PSL)

A B C D

Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO: 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

	(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
121	2295422	Open	8/10/11 - open	8/10/11 - open					Siemens Energy Inc.	OEM	Support Material for the EPU Turb-Gen Upgate (PTN)
122	2295071	Open	08/01/11 - open	08/01/11 - open					Stone & Webster	Single Source	Unit 1 Vibration and Support Mods for FW & Condensate (PSL)
123	2296049	Open	08/25/11 - open	08/25/11 - open					Cameron Tech.	Replaces 116796	Ultrasonic Flow Meter Measuring System (PTN)
124	2294671	Open	08/19/11 - open	08/19/11 - open					NWT Corporation	Competitive	Moisture Carry Over Testing for EPU (PTN)
125	2296556	Open	09/02/11 - open	09/02/11 - open					Sulzer Pumps	OEM	Modify, overhaul and refurbishment of the B & C AFW (PTN)
126	2296519	Open	09/05/11 - open	09/05/11 - open					Techcom International	Competitive	DCS Integration Plan for 3R26 and 4R27 (PTN)
127	2296623	Open	09/06/11 - open	09/06/11 - open					Tricen Technologies	Competitive	Unit 3 Condenser Tube Eddy Current Testing (PTN)
128	2296797	Open	09/09/11 - open	09/09/11 - open					Coastal Bus & Charter Lines (dba Need A Bus)	Competitive	Shuttle Bus Services for EPU (PSL)
129	2296330	Open	09/09/11 - open	09/09/11 - open					Flowserve Corp.	Competitive	Motor Operated Valves (PTN)
130	2298266	Open	10/12/11 - open	10/12/11 - open					Franmar Corporation	Competitive	Shuttle Bus Services for EPU (PTN)
131	2298406	Open	10/12/11 - open	10/12/11 - open					Master Lee Energy Services	Competitive	Fuel Movers for Melanic Inserts (PSL)
132	2298635	Open	10/14/11 - open	10/14/11 - open					Sargent & Lundy Inc.	Single Source	Engineering Service for the Charging System Modification (PSL 2)
133	2297556	Open	09/27/11 - open	09/27/11 - open					Siemens Energy Inc.	Single Source	Siemens Installation of 2A Main Power Transformer (PSL)
134	2299101	Open	10/27/11 - open	10/27/11 - open					Berkel & Company	Single Source	Mico Pile Construction (PTN)
135	2298894	Open	10/24/11 - open	10/24/11 - open					Day & Zimmermann NPS Inc.	Competitive	Installation of Trailer Support Services (PTN)
136	2299350	Open	11/01/11 - open	11/01/11 - open					Enercon Services Inc.	Competitive	Eng. Evaluation for EPU Mid-Cycle contingency plan (PSL)
137	2299618	Open	11/04/11 - open	11/04/11 - open					Radiation Safety & Control	Competitive	Truck Monitoring/Waste Characterization for EPU (PTN)
138	2297624	Open	10/27/11 - open	10/27/11 - open					Siemens Energy Inc.	OEM	Turbine Valve Conversion to EH (PTN)
139	2299631	Open	11/8/11 - open	11/8/11 - open					Tri-Tool Inc.	Single Source	Unit 1 LP Turbine Extraction Line Services (PSL)
140	2295953	Open	08/24/11 - open	08/24/11 - open					Mammon Wire & Cable	OEM	Misc Safety Related Wire and Cable, line items 1 - 23 (PTN)
141	2297055	Open	09/16/11 - open	09/16/11 - open					Thermal Engineering	Single Source	Replacement LP #4 Feedwater Heaters for EPU (PSL 2)
142	2300139	Open	11/21/11 - open	11/21/11 - open					Siemens Energy Inc.	Single Source	SL1-24 Turb-Gen. Installation (PSL 1)
143	2299624	Open	11/16/11 - open	11/16/11 - open					Ames Group LLC	Single Source	Upgrade Services for Feedwater Pumps (PSL)
144	2300487	Open	11/28/11 - open	11/28/11 - open					Weldtech Services	Single Source	SL1-24 Construction Management Oversight Services (PSL 1)

A B C D

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO. 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
145	2299618	Open	11/04/11 - open	11/04/11 - open					Radiation Safety & Control	Competitive	Truck Monitoring/Waste Characterization for EPU (PTN)
146	2299350	Open	11/01/11 - open	11/01/11 - open					Enercon Services	Competitive	Engineering evaluation for EPU mid-cycle contingency plan (PSL)
147	2299631	Open	11/08/11 - open	11/08/11 - open					Tri-Tool	Single Source	LP Turbine Extraction Line Services for EPU (PSL 1)
148	NF-10-358 NF-11-178	Open	11/2/10 - open	11/2/10 - open					Westinghouse Electric	OEM	Spent Fuel Pool Criticality Safety Analysis Support (PTN)
149	2301813	Open	12/28/11 - open	12/28/11 - open					Enercon Services Inc	Competitive	Motor Operated Valve Transfer Switches for EPU (PSL)
150	2301867	Open	12/28/11 - open	12/28/11 - open					Enercon Services Inc	Single Source	Develop Engineering Change Packages for EPU (PTN)
151	2301038	Open	12/14/11 - open	12/14/11 - open					Graftel Inc.	Competitive	Integrated Leak Rate Testing for EPU (PTN)
152	2261800	Open	09/28/10 - open	09/28/10 - open					3 Communications Mapps Inc	OEM	Supply of Simulator SCD Software Translator Upgrade (PTN)
153	130340	Open	04/02/10 - open	04/02/10 - open					MPR Associates	Competitive	Third Party Review of Siemens Turb-Gen. Analysis (PSL)
154	2301737	Open	12/21/11 - open	12/21/11 - open					PSI Energy Services	Single Source	Construction Management Oversight Services (PTN)
155	2301736	Open	12/21/11 - open	12/21/11 - open					Weldtech Services	Single Source	Construction Management Oversight Services (PTN)
156	2301871	Open	12/28/11 - open	12/28/11 - open					Zachry Nuclear Engineering	Single Source	Develop Engineering Change Packages for EPU (PTN)
157	2301858	Open	12/28/11 - open	12/28/11 - open					Sargent & Lundy Inc	Single Source	Develop TPCW Engineering Change Packages for EPU (PTN)
158	2000053226	Open	11/21/11 - open	11/21/11 - open					Ric-Man Construction	Competitive	Road and parking contract labor work 230KV substation (PTN)

A B C D

Legend:

PDS = Predetermined Source

OEM = Original Equipment Manufacturer

PSL = St. Lucie

PTN = Turkey Point

Notes:

In November 2011, FPL issued a Letter of Agreement (LOA) to Siemens for the PTN 3-26 Turbine Generator installation scope; however, the contract was not issued in 2011.



**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO 121869

Major Task or Tasks Associated With:

Supply Eight (8) Normal Containment Coolers and provide Testing Services

Vendor Identity:

AAF MCQUAY

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to AAF McQuay.

Dollar Value:

Total Contract Value through Revision 3 is



Contract Status:

Active

Term Begin:

April 29, 2009

Term End:

March 2013

Nature and Scope of Work:

Supply Eight (8) Normal Containment Coolers and provide Testing Services

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO 120769

Major Task or Tasks Associated With:

Replacement IsoPhase Bus Duct Coolers

Vendor identity:

Calvert Company Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

1

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Calvert Company Inc.

Dollar Value:

Total Dollar Value through Revision 2 is



Contract Status:

Active

Term Begin:

March 26, 2009

Term End:

June 2012

Nature and Scope of Work:

Replacement IsoPhase Bus Duct Coolers, Technical Installation Support and Field Testing.

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO 124436

Major Task or Tasks Associated With:

Replacement Isolated Phase BusDuct

Vendor Identity:

Calvert Company Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Calvert Company Inc.

Dollar Value:

Total Dollar Value through Revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

July 17, 2009

Term End:

June 2012

Nature and Scope of Work:

Replacement Isolated Phase BusDuct, Demolition and Installation Services, Evaluation, Testing and Engineering

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO 121985

Major Task or Tasks Associated With:

Replacement Main Feedwater Pumps

Vendor Identity:

Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

5

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Flowsolve Corp.

Dollar Value:

Total Dollar Value through Revision 3 is [REDACTED]

Contract Status:

Active

Term Begin:

April 24, 2009

Term End:

June 2012

Nature and Scope of Work:

Replacement Main Feedwater Pumps, spare parts and technical direction of installation.

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO 123137

Major Task or Tasks Associated With:

Main Feedwater Isolation Valves

Vendor Identity:

Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Flowsolve Corp.

Dollar Value:

Total Dollar Value through Revision 1 is [REDACTED]

Contract Status:

Active

Term Begin:

May 28, 2009

Term End:

Open

Nature and Scope of Work:

Main Feedwater Isolation Valves, Technical Field Services, Testing, Engineering and Documentation

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO 125454

Major Task or Tasks Associated With:

Replacement Heater Drain Pumps

Vendor Identity:

Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Flowsolve Corp.

Dollar Value:

Total Dollar Value through Revision 1 is



Contract Status:

Active

Term Begin:

August 28, 2009

Term End:

June 2012

Nature and Scope of Work:

Replacement Heater Drain Pumps, Spare Heater, Technical Direction

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO 122154

Major Task or Tasks Associated With:

Step-Up Transformers

Vendor Identity:

Siemens Energy Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

2

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Siemens Energy Inc.

Dollar Value:

[REDACTED]

Contract Status:

Complete

Term Begin:

April 27, 2009

Term End:

Complete

Nature and Scope of Work:

Uprate Step-Up Transformers from 850 MVA to 970 MVA

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO 119078

Major Task or Tasks Associated With:

NSSS Engineering Evaluation and LAR Analysis for PTN Units 3 & 4

Vendor Identity:

Westinghouse Electric Co.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Dollar Value through Revision 6 is [REDACTED]

Contract Status:

Active

Term Begin:

Letter of Authorization issued 12/9/08; PO issued 1/26/09

Term End:

Open

Nature and Scope of Work:

NSSS Engineering Evaluation and LAR Analysis for PTN Units 3 & 4

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.
For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO 119653

Major Task or Tasks Associated With:

NSSS Engineering Evaluation and LAR Analysis for PSL Units 1 & 2

Vendor Identity:

Westinghouse Electric Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Dollar Value through Revision 4 is [REDACTED]

Contract Status:

Active

Term Begin:

Letter of Authorization issued 11/24/08; PO issued 2/17/09

Term End:

open

Nature and Scope of Work:

NSSS Engineering Evaluation and LAR Analysis for PSL Units 1 & 2

Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO 115297 (PSL)

Major Task or Tasks Associated With:

Design Review for LAR (Steam Generator and Reactor Head)

Vendor Identity:

AREVA

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Dollar Value through Revision 8

Contract Status:

Active

Term Begin:

August 27, 2008

Term End:

open

Nature and Scope of Work:

Design Review for LAR (Steam Generator and Reactor Head)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.
For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:
PTN PO 115338

Major Task or Tasks Associated With:
Engineering Analysis

Vendor Identity:
AREVA

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Dollar Value through Revision 10. [REDACTED]

Contract Status:
Active

Term Begin:
August 27, 2008

Term End:
Open

Nature and Scope of Work:
Design review for the Reactor Coolant system, Control Rod Mechanism, EMA, CFD and BMI

Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY:

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 105353

Major Task or Tasks Associated With:

Initial BOP Scoping Support for EPU

Vendor Identity:

Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Sole Source

Dollar Value:

Total Dollar Value through Revision 5 is

Contract Status:

Complete

Term Begin:

October 2, 2007

Term End:

December 1, 2011

Nature and Scope of Work:

BOP Scoping Support (engineering) for the EPU Project

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO 117809

Major Task or Tasks Associated With:

Provide Engineering, Procurement and Construction Services for
PTN

Vendor Identity:

Bechtel

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

6

Number of Bids Received:

5

Brief Description of Selection Process:

Bidders were evaluated against predetermined technical and commercial criteria, awarding to the lowest evaluated bidder.

Dollar Value:

PO value through Rev 4/Rel 0 is [REDACTED]

Contract Status:

Active

Term Begin:

December 2, 2008

Term End:

April 2013

Nature and Scope of Work:

Bechtel's scope includes project management, design engineering, procurement and material handling services, work order planning, construction/implementation, project controls, quality assurance, quality control, radiation protection (alara), safety, security interface, and other services as designated in the Contract documents.

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 116088

Major Task or Tasks Associated With:

Turbine/Generator Uprate

Vendor Identity:

Siemens Power

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single source

Dollar Value:

Total Max Dollar Value through Revision 4/Release 0

Contract Status:

Active

Term Begin:

September 29, 2008

Term End:

March 2013

Nature and Scope of Work:

Engineering, Parts and Installation for PSL Turbine/Generator Uprate

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO 117820

Major Task or Tasks Associated With:

Provide Engineering, Procurement and Construction Services for PSL

Vendor Identity:

Bechtel

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

6

Number of Bids Received:

5

Brief Description of Selection Process:

Bidders were evaluated against predetermined technical and commercial criteria, awarding to the lowest evaluated bidder.

Dollar Value:

PO value through Rev 5/Rel 0 is [REDACTED]

Contract Status:

Active

Term Begin:

December 2, 2008

Term End:

December 2012

Nature and Scope of Work:

Bechtel's scope includes project management, design engineering, procurement and material handling services, work order planning, construction/implementation, project controls, quality assurance, quality control, radiation protection (alara), safety, security interface, and other services as designated in the Contract documents.

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 116090

Major Task or Tasks Associated With:

PTN Turbine Generator Uprate

Vendor Identity:

Siemens Power

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Max Contract Value through Rev. 3/Rel 0 is [REDACTED]

Contract Status:

Active

Term Begin:

September 29, 2008

Term End:

March 2013

Nature and Scope of Work:

PTN Engineering, Parts and Installation for Turbine/Generator Uprate

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 118328

Major Task or Tasks Associated With:

PTN Condenser Tube Bundles for Unit 3 & 4

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through Revision 5 is [REDACTED]

Contract Status:

Active

Term Begin:

December 19, 2008

Term End:

March 2013

Nature and Scope of Work:

Supply PTN Condenser Tube Bundles

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 118206

Major Task or Tasks Associated With:

PTN MSR's for Units 3 & 4

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

2

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through Revision 2 [REDACTED]

Contract Status:

Active

Term Begin:

December 17, 2008

Term End:

March 2013

Nature and Scope of Work:

Supply PTN Moisture Separator Reheaters

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 118205

Major Task or Tasks Associated With:

PSL MSR's for Units 1 & 2

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

2

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through Revision 5 is [REDACTED]

Contract Status:

Active

Term Begin:

December 17, 2008

Term End:

July 2012

Nature and Scope of Work:

Supply PSL Moisture Separator Reheaters

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 118241

Major Task or Tasks Associated With:

PTN Feedwater Heaters for Units 3 & 4

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

3

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Contract Value through Revision 2

Contract Status:

Active

Term Begin:

December 19, 2008

Term End:

March 2013

Nature and Scope of Work:

Supply PTN Feedwater Heaters

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 112221

Major Task or Tasks Associated With:

Engineering Services

Vendor Identity:

Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Blanket Purchase Order Max Value through Revision 17 to
Release 0 is [REDACTED]

Contract Status:

Active

Term Begin:

April 22, 2008

Term End:

December 2012

Nature and Scope of Work:

PSL BOP Engineering

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.
For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 112177

Major Task or Tasks Associated With:

Engineering Services

Vendor Identity:

Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Blanket Purchase Order Max Value through Revision 8 to Release 0 is [REDACTED]

Contract Status:

Active

Term Begin:

April 22, 2008

Term End:

open

Nature and Scope of Work:

Engineering for the PSL Uprate Project

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO 117272

Major Task or Tasks Associated With:

Gantry crane repair/modification

Vendor Identity:

American Crane & Equip.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Sole Source/OEM

Dollar Value:

Total Dollar Value through Rev 6 is [REDACTED]

Contract Status:

Active

Term Begin:

November 13, 2008

Term End:

Open

Nature and Scope of Work:

Complete modification of Unit 1 crane and update of electrical components for Unit 2 crane

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 118224

Major Task or Tasks Associated With:

PSL Feedwater Heaters for Units 1 & 2

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Dollar Value thru Revision 6

Contract Status:

Active

Term Begin:

December 17, 2008

Term End:

open

Nature and Scope of Work:

Supply PSL Feedwater Heaters

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 115485

Major Task or Tasks Associated With:

Eng. Services for NSSS, BOP & Licensing Activities

Vendor Identity:

Proto-Power

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Dollar Value through revision 4 is



Contract Status:

Active

Term Begin:

September 3, 2008

Term End:

Open

Nature and Scope of Work:

PTN Eng. Services for NSSS, BOP and Licensing Activities.

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.
For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 118278

Major Task or Tasks Associated With:

PSL Heat Exchangers for Units 1 & 2

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

3

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through revisions 4 is [REDACTED]

Contract Status:

Active

Term Begin:

December 19, 2008

Term End:

Open

Nature and Scope of Work:

Supply PSL Heat Exchangers

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY:

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 105720

Major Task or Tasks Associated With:

PSL Fuels Study

Vendor Identity:

Areva

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Order value through Revision 16 is [REDACTED]

Contract Status:

Active

Term Begin:

September 12, 2007

Term End:

open

Nature and Scope of Work:

Fuels Performance Study and Analysis

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 116786

Major Task or Tasks Associated With:

Ultrasonic Flow Measuring System

Vendor Identity:

Cameron Technologies

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Blanket Purchase Order Value through Revision 1 to Release 0
is [REDACTED]

Contract Status:

Complete

Term Begin:

October 29, 2008

Term End:

December 22, 2011

Nature and Scope of Work:

Ultrasonic Flow Measuring System for PTN

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO 116107

Major Task or Tasks Associated With:

Ultrasonic Flow Measuring System

Vendor Identity:

Cameron Technologies

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Purchase Order Value through Revision 1 is [REDACTED]

Contract Status:

Awarded

Term Begin:

September 29, 2008

Term End:

Open

Nature and Scope of Work:

Ultrasonic Flow Measuring System for PTN

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO 114114

Major Task or Tasks Associated With:

Staff Augmentation

Vendor Identity:

Richard Sipos

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source Justification

Dollar Value:

Total Blanket Purchase Order Value through Revision 6 is



Contract Status:

Active

Term Begin:

July 3, 2008

Term End:

open

Nature and Scope of Work:

Project Management Services

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 4500521317

Major Task or Tasks Associated With:

Inductors

Vendor Identity:

Areva

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive Selection

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

September 8, 2009

Term End:

Open

Nature and Scope of Work:

Supply of Inductors

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-BA

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 126248

Major Task or Tasks Associated With:

Replacement Transformer Coolers

Vendor Identity:

ABB

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

1

Brief Description of Selection Process:

Competitive Selection, Commercial and Technical Evaluation

Dollar Value:

Total Contract Value through Rev 2

Contract Status:

Active

Term Begin:

October 8, 2009

Term End:

Open

Nature and Scope of Work:

Replacement Transformer Coolers

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 126453

Major Task or Tasks Associated With:

Turbine Plant Cooling Water Heat Exchangers

Vendor Identity:

Joseph Oat Corporation

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive Selection, Commercial and Technical Evaluation

Dollar Value:

Total Contract Value through revision 1 is [REDACTED]

Contract Status:

Active

Term Begin:

November 5, 2009

Term End:

Open

Nature and Scope of Work:

Supply Turbine Plant Cooling Water Heat Exchangers

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO #127777

Major Task or Tasks Associated With:

Estimating Services

Vendor Identity:

High Bridge

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Contract Value through revision 2 is



Contract Status:

Active

Term Begin:

December 8, 2009

Term End:

Open

Nature and Scope of Work:

Estimating Services

Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:
PTN PO # 127881

Major Task or Tasks Associated With:
Procedure Writers

Vendor Identity:
Absolute Consulting

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
[REDACTED]

Contract Status:
Active

Term Begin:
December 22, 2009

Term End:
Open

Nature and Scope of Work:
Procedure Writers

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO #118988

Major Task or Tasks Associated With:

Fuel Storage Criticality and Related Analysis (PSL 2)

Vendor Identity:

Holtec

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Purchase Order Value through Revision 4 is [REDACTED]

Contract Status:

Active

Term Begin:

January 22, 2009

Term End:

Open

Nature and Scope of Work:

Fuel Storage Criticality and Related Analysis (PSL 2)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO #118563

Major Task or Tasks Associated With:

Fuel Storage Criticality and Related Analysis (PSL 1)

Vendor Identity:

Holtec

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Purchase Order Value through Revision 5 is

Contract Status:

Active

Term Begin:

January 14, 2009

Term End:

Open

Nature and Scope of Work:

Fuel Storage Criticality and Related Analysis (PSL 1)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO # 4500467077

Major Task or Tasks Associated With:

PSL Generator Step-up Transformers

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

7

Number of Bids Received:

7

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

November 10, 2008

Term End:

Open

Nature and Scope of Work:

PSL Generator Step-up Transformers

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 130612

Major Task or Tasks Associated With:

Condensate Pumps

Vendor Identity:

Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Contract Value through Revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

April 22, 2010

Term End:

Open

Nature and Scope of Work:

Condensate Pumps

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO #130649

Major Task or Tasks Associated With:

Main Feedwater Pumps

Vendor Identity:

Flowsolve Corp

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

1

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

April 22, 2010

Term End:

Open

Nature and Scope of Work:

Main Feedwater Pumps

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 126227

Major Task or Tasks Associated With:

Control System FWH, Moisture Separator

Vendor Identity:

Invensys

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Dollar Value through revision 9

Contract Status:

Active

Term Begin:

October 13, 2009

Term End:

Open

Nature and Scope of Work:

Control System FWH, Moisture Separator

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.
For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 129689

Major Task or Tasks Associated With:

Turbine Digital Upgrade

Vendor Identity:

Invensys

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Dollar Value through Revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

March 17, 2010

Term End:

Open

Nature and Scope of Work:

Turbine Digital Upgrade

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 130272

Major Task or Tasks Associated With:

Electro-Hydraulic Fluid Systems

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Dollar Value through Rev 4 is [REDACTED]

Contract Status:

Active

Term Begin:

April 8, 2010

Term End:

Open

Nature and Scope of Work:

Electro-Hydraulic Fluid Systems

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO # 131928

Major Task or Tasks Associated With:

Pre-planning SL2-19

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Complete

Term Begin:

June 14, 2010

Term End:

February 28, 2011

Nature and Scope of Work:

SL2-19 Pre-planning work to support station milestones for the Turbine Generator Installation

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO # 131533

Major Task or Tasks Associated With:

Non-Fuels NSSS Interim LAR (PSL 1 & 2)

Vendor Identity:

Areva

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Predetermined Source

Dollar Value:

Total Contract Value through revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

June 10, 2010

Term End:

Open

Nature and Scope of Work:

Non-Fuels NSSS Interim LAR (PSL 1 & 2)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO # 131907

Major Task or Tasks Associated With:

Fuels Related Interim LAR/MOD for EPU at PSL

Vendor Identity:

Areva

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Predetermined Source

Dollar Value:

Total Contract Value through Revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

June 11, 2010

Term End:

Open

Nature and Scope of Work:

Fuels Related Interim LAR/MOD for EPU at PSL

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-El

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:
PSL PO # 131585

Major Task or Tasks Associated With:
Interim LAR/MOD for EPU at PSL

Vendor Identity:
Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Predetermined Source

Dollar Value:
Total Contract Value through Revision 4 is [REDACTED]

Contract Status:
Active

Term Begin:
June 15, 2010

Term End:
Open

Nature and Scope of Work:
Interim LAR/MOD for EPU at PSL

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO #131940

Major Task or Tasks Associated With:

Main Steam Turbine Control Replacement

Vendor Identity:

Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

4

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Max Contract value through Rev 2 to Release 0

Contract Status:

Active

Term Begin:

June 30, 2010

Term End:

Open

Nature and Scope of Work:

Main Steam Turbine Control Replacement

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO #2258675

Major Task or Tasks Associated With:

Furnish New Spent Fuel Pool Heat Exchangers

Vendor Identity:

Joseph Oat Corporation

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

2

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

Contract Status:

Active

Term Begin:

July 23, 2010

Term End:

Open

Nature and Scope of Work:

Furnish New Spent Fuel Pool Heat Exchangers

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO # 2259669

Major Task or Tasks Associated With:

Rewind/Refurbish Upgrade Condensate Pumps

Vendor Identity:

Tampa Armature Works

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

August 2, 2010

Term End:

Open

Nature and Scope of Work:

Rewind/Refurbish Upgrade Condensate Pumps

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO #2260113

Major Task or Tasks Associated With:

PSL Rod Control System Upgrades

Vendor Identity:

Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Contract Value through Amendment 3 [REDACTED]

Contract Status:

Active

Term Begin:

September 23, 2010

Term End:

Open

Nature and Scope of Work:

PSL Rod Control System Upgrades

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO #2261747

Major Task or Tasks Associated With:

EPU NSSS Engineering and Modification Support

Vendor Identity:

Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Predetermined Source

Dollar Value:

Total Contract Value through Amendment 2 [REDACTED]

Contract Status:

Active

Term Begin:

September 23, 2010

Term End:

Open

Nature and Scope of Work:

EPU NSSS Engineering and Modification Support

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:
PSL PO #2264240

Major Task or Tasks Associated With:
PSL 2-19 Turbine Generator Installation Contract

Vendor Identity:
Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
[REDACTED]

Contract Status:
Active

Term Begin:
November 17, 2010

Term End:
Open

Nature and Scope of Work:
PSL 2-19 Turbine Generator Installation Contract

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO #2264841

Major Task or Tasks Associated With:

SL 2-19 Technical Support

Vendor Identity:

Batsch Industries

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This Indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Contract Value through Amendment 2 [REDACTED]

Contract Status:

Active

Term Begin:

November 30, 2010

Term End:

Open

Nature and Scope of Work:

SL 2-19 Technical Support

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

2264914

Major Task or Tasks Associated With:

CEDMS Power Switch Refurbishment (PSL 2)

Vendor Identity:

Westinhouse Electric

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 7, 2010

Term End:

Open

Nature and Scope of Work:

CEDMS Power Switch Refurbishment (PSL 2)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO #2285418

Major Task or Tasks Associated With:

Implementation Spares for Turbine Generator Work

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Contract Value through Amendment 2

Contract Status:

Active

Term Begin:

December 16, 2010

Term End:

Open

Nature and Scope of Work:

Implementation Spares for Turbine Generator Work

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO #2285720

Major Task or Tasks Associated With:

Licensing/Design Basis/Program Modification

Vendor Identity:

Enercon

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

2

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

January 4, 2011

Term End:

Open

Nature and Scope of Work:

Licensing/Design Basis/Program Modification

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO# 2291203

Major Task or Tasks Associated With:

Main Steam Isolation Valve Replacement Actuator

Vendor Identity:

Enertech

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

2

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Contract Value through Amendment 3 [REDACTED]

Contract Status:

Active

Term Begin:

April 21, 2011

Term End:

Open

Nature and Scope of Work:

Main Steam Isolation Valve Replacement Actuator

Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, *current contract status, the current term of the contract,* and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO# 2290465

Major Task or Tasks Associated With:

Design, Engineering and Fabrication of Turbine Crossover piping

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

([REDACTED])

Contract Status:

Active

Term Begin:

March 31, 2011

Term End:

Open

Nature and Scope of Work:

Design, Engineering and Fabrication of Turbine Crossover piping

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO# 2290614

Major Task or Tasks Associated With:

Main Feedwater Pump Casing Modifications

Vendor Identity:

Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

N/A

Number of Bids Received:

N/A

Brief Description of Selection Process:

Replaces PO 130649

Dollar Value:

Total Contract Value through Amend 1

Contract Status:

Active

Term Begin:

May 2, 2011

Term End:

Open

Nature and Scope of Work:

Main Feedwater Pump Casing Modifications

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO# 2293950

Major Task or Tasks Associated With:

Turbine Generator Pre-Outage Planning PTN 3 & 4

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Contract value through Amendment 1 [REDACTED]

Contract Status:

Active

Term Begin:

June 24, 2011

Term End:

Open

Nature and Scope of Work:

Turbine Generator Pre-Outage Planning PTN 3 & 4
(Turbine Generator Installation)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO# 2295186

Major Task or Tasks Associated With:

Metamic Chevrons for Spent Fuel Pool

Vendor Identity:

Holtec

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

August 2, 2011

Term End:

Open

Nature and Scope of Work:

Metamic Chevrons for Spent Fuel Pool

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PQ# 2296556

Major Task or Tasks Associated With:

Modification, overhaul and refurbishment of the B and C AFW

Vendor Identity:

Sulzer Pumps

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

September 2, 2011

Term End:

Open

Nature and Scope of Work:

Modification, overhaul and refurbishment of the B and C AFW

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO# 2298406

Major Task or Tasks Associated With:

Fuel Movers for Melamic Inserts

Vendor Identity:

Master Lee Energy Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

1

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

October 12, 2011

Term End:

Open

Nature and Scope of Work:

Fuel Movers for Melamic Inserts

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO# 2297556

Major Task or Tasks Associated With:

Siemens Installation of 2A Main Power Transformer

Vendor Identity:

Siemens Energy Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

September 27, 2011

Term End:

Open

Nature and Scope of Work:

Siemens Installation of 2A Main Power Transformer

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO# 2295953

Major Task or Tasks Associated With:

Misc Safety Related Wire and Cable

Vendor Identity:

Marrion Wire & Cable

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Contract Value through revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

August 24, 2011

Term End:

Open

Nature and Scope of Work:

Misc Safety Related Wire and Cable

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO# 2297055

Major Task or Tasks Associated With:

Replacement Unit 2 LP #4 Feedwater Heaters for EPU

Vendor Identity:

Thermal Engineering

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

September 16, 2011

Term End:

Open

Nature and Scope of Work:

Replacement Unit 2 LP #4 Feedwater Heaters for EPU

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO# 2300139

Major Task or Tasks Associated With:

SL 1-24 Turbine Generator Installation

Vendor Identity:

Siemens Energy Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

September 16, 2011

Term End:

Open

Nature and Scope of Work:

SL 1-24 Turbine Generator Installation

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO# 2299624

Major Task or Tasks Associated With:

Upgrade Services for Feedwater Pumps

Vendor Identity:

Ames Group LLC

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Contract Value through revision 1 [REDACTED]

Contract Status:

Active

Term Begin:

November 16, 2011

Term End:

Open

Nature and Scope of Work:

Upgrade Services for Feedwater Pumps

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO #131742

Major Task or Tasks Associated With:

LAR/Request for Additional Information

Vendor Identity:

Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Predetermined Source

Dollar Value:

Total Contract value through revision 2 is: [REDACTED]

Contract Status:

Active

Term Begin:

June 15, 2010

Term End:

Open

Nature and Scope of Work:

LAR/Request for Additional Information for Non-Fuels related scope

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

NF-10-358 and NF-11-178

Major Task or Tasks Associated With:

Spent Fuel Criticality Safety Analysis Support (PTN)

Vendor Identity:

Westinhouse Electric

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This Indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

November 2, 2010

Term End:

Open

Nature and Scope of Work:

Spent Fuel Criticality Safety Analysis Support (PTN)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO # 2301867

Major Task or Tasks Associated With:

Develop Engineering Change Packages for EPU at PTN

Vendor Identity:

Enercon Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 28, 2011

Term End:

Open

Nature and Scope of Work:

Develop Engineering Change Packages for EPU at PTN

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO # 2261800

Major Task or Tasks Associated With:

Supply of Simulator SCD Software Translator Upgrade

Vendor Identity:

L 3 Communications Mapps Inc

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Contract Value through Amendment 2 [REDACTED]

Contract Status:

Active

Term Begin:

September 28, 2010

Term End:

Open

Nature and Scope of Work:

Supply of Simulator SCD Software Translator Upgrade

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 2301737

Major Task or Tasks Associated With:

Construction Management Oversight Services for PTN

Vendor Identity:

PSI Energy Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 21, 2011

Term End:

Open

Nature and Scope of Work:

Construction Management Oversight Services for PTN

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO # 2301736

Major Task or Tasks Associated With:

Construction Management Oversight Services

Vendor Identity:

Weldtech Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 21, 2011

Term End:

Open

Nature and Scope of Work:

Construction Management Oversight Services

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.
For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO #2301871

Major Task or Tasks Associated With:

Develop Engineering Changes Packages for EPU at PTN

Vendor Identity:

Zachry Nuclear Engineering

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 28, 2011

Term End:

Open

Nature and Scope of Work:

Develop Engineering Changes Packages for EPU at PTN

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO #2301858

Major Task or Tasks Associated With:

Develop TPCW Changes Packages for EPU at PTN

Vendor Identity:

Sargent & Lundy

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 28, 2011

Term End:

Open

Nature and Scope of Work:

Develop TPCW Changes Packages for EPU at PTN



Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed

Schedule T-7A

[Section (B)(c)]

FLORIDA PUBLIC SERVICE COMMISSION

EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and description of work.

COMPANY: Florida Power & Light Company


For the Year Ended: 12/31/2011
Witness: Steven D. Scroggs

DOCKET NO.: 120009-EI

CONFIDENTIAL CONFIDENTIAL CONFIDENTIAL CONFIDENTIAL

	(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Actual amount expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
1	4500395492	Open-CO#38	11/6/2007- open	10/11/2011- open					Bechtel Power Corp	Comp Bid/ Single Source/ Predetermined Source	Engineering Services to Support Preparation of COLA and SCA and Response to post-submittal RAI's.
2	4500404639	Open-CO#5	1/31/2008- open	4/21/2011- open					Westinghouse Electric Co	Sole Source/ Predetermined Source	Engineering Services to Support Preparation of COLA and Response to post-submittal RAI's.
3	4500425707	Open-CO#5	5/23/2008- open	1/3/2011- open					HDR Engineering, Inc.	Comp Bid/ Single Source	Conceptual Engineering of Cooling Water Supply and Discharge
4	4500430034	Open-CO#1	6/18/2008- open	1/28/2011- open					Electric Power Research Institute	Single Source	Advanced Nuclear Technology; Near term deployment of Advanced Light Water Reactors
5	4500443122	Open-CO#3	8/6/2008- open	11/29/2011- open					Eco Metrics, Inc.	Single Source	Environmental Consulting Services
6	4500517152	Open-CO#3	7/10/2009- open	12/17/2010- open					McNabb Hydrogeologic Consulting Inc	Single Source	Turkey Point 6&7 Post SCA Submittal and UIC Licensing Support
7	4500518160	Open-CO#5	7/23/2009- open	6/24/2011- open					Golder Associates Inc	Single Source	Turkey Point 6&7 Post SCA Submittal Support
8	4500518167	Open-CO#6	7/23/2009- open	9/14/2011- open					Environmental Consulting and Technology Inc	Single Source/ Predetermined Source	Turkey Point 6&7 SCA Support
9	4500538449	Open-CO#2	10/12/2009- open	11/29/2011- open					McNabb Hydrogeologic Consulting Inc	Comp Bid/ Single Source	Turkey Point 6&7 UIC Subject Matter Expert Support
10	4500492222	Open-CO#2	3/17/2009- open	12/22/2011- open					Expertis US LLC (FKA, Jefferson Wells International)	Comp Bid/ Single Source	New Nuclear Audit
11	4500587305	Open-CO#1	6/29/2010- open	9/1/2010- open					Dickerson Florida Inc	Comp Bid	Turkey Point 6&7 Exploratory/UIC Well Site Development
12	4500552043	Open-CO#1	3/3/2011- open	12/29/2011- open					Layne Christensen Company	Comp Bid	Turkey Point 6&7 Exploratory/UIC Well and Dual Zone Monitor Well Installation

A B C D

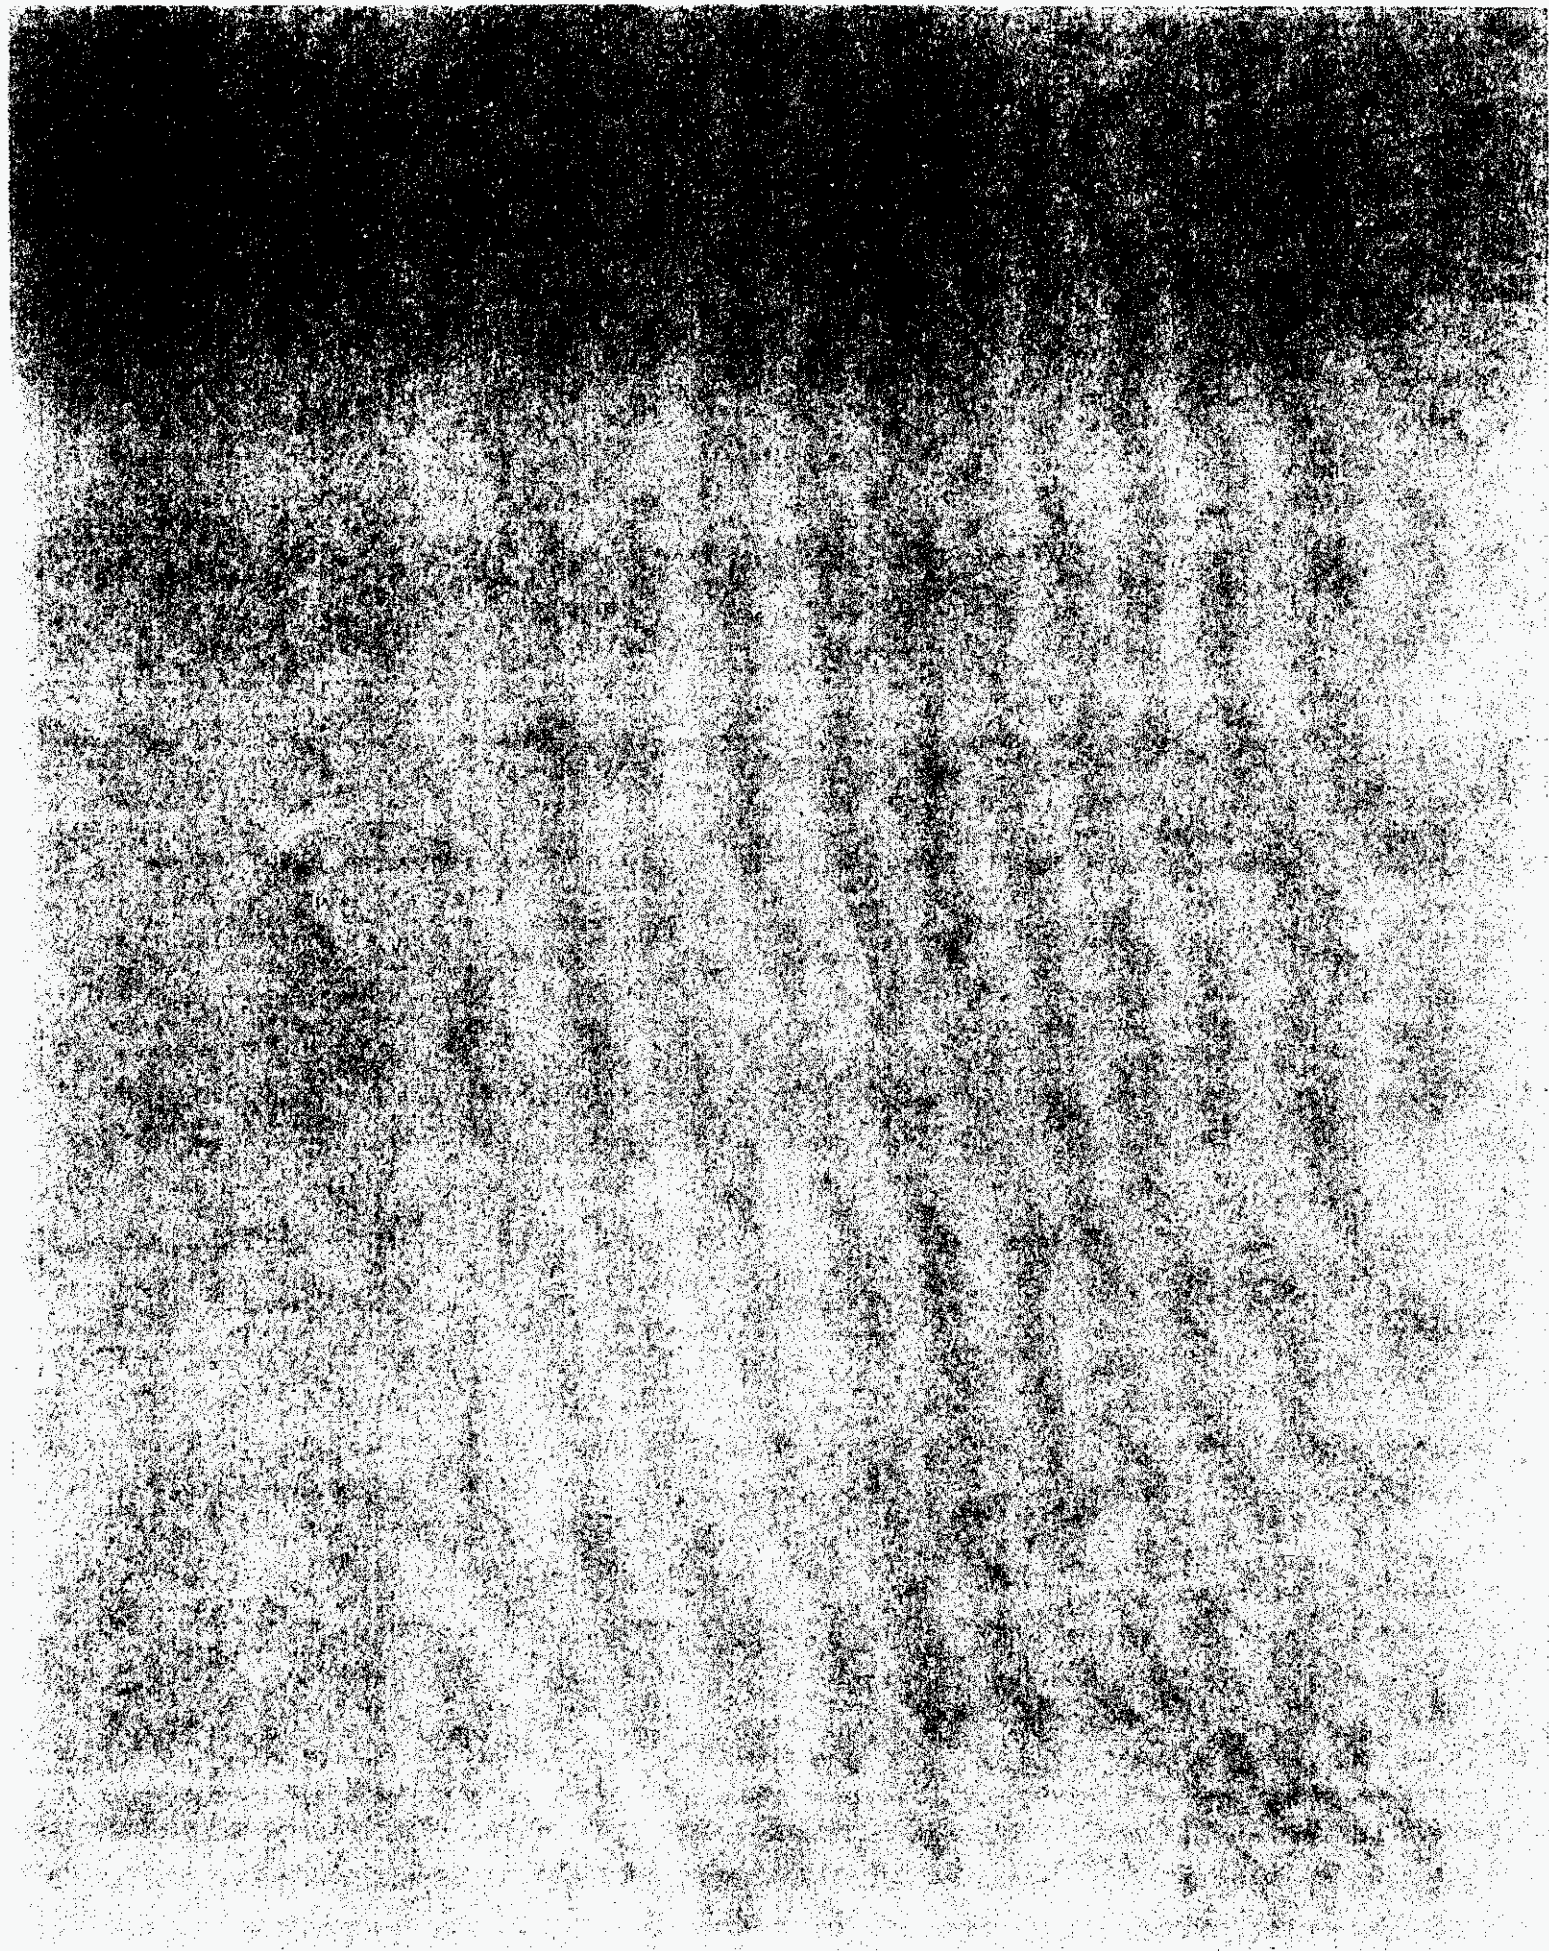

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: Florida Power & Light Company
DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:
4500395492

Major Task or Tasks Associated With:
COLA and SCA preparation and support

Vendor Identity:
Bechtel Power Corporation

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
Two

Number of Bids Received:
Two

Brief Description of Selection Process:
Initial contract competitively bid; change orders #01-#11
issued single source; all subsequent change orders
issued Predetermined Source

Dollar Value:

1

Contract Status:
Active- CO#38

Term Begin:
11/6/2007

Term End:
2/27/2016

Nature and Scope of Work:
Engineering Services to Support Preparation of COLA
and SCA, including post-submittal support for RAI
responses.

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (B)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: Florida Power & Light Company
DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:
4500404639

Major Task or Tasks Associated With:
COLA support

Vendor Identity:
Westinghouse Electric Company

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
One

Number of Bids Received:
One

Brief Description of Selection Process:
Sole source justification; designated as Predetermined
Source March 2009

Dollar Value:

1

Contract Status:
Active- CO#6

Term Begin:
1/31/2008

Term End:
6/29/2014

Nature and Scope of Work:
Engineering Services to Support Preparation of COLA,
including post-submittal support for RAI responses.

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: Florida Power & Light Company
DOCKET NO.: 120009-El

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:
4500430034

Major Task or Tasks Associated With:
COLA and SCA preparation and support

Vendor Identity:
Electric Power Research Institute

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
Two

Number of Bids Received:
Two

Brief Description of Selection Process:
Single

Dollar Value:

1

Contract Status:
Active- CO#1

Term Begin:
6/16/2008

Term End:
6/29/2014

Nature and Scope of Work:
Engineering Services to Support Preparation of COLA and SCA, including post-submittal support for RAI responses.

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:
4500518160

Major Task or Tasks Associated With:
Post SCA Submittal support

Vendor Identity:
Golder Associates, Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct or Indirect relationship with the vendor

Number of Vendors Solicited:
One

Number of Bids Received:
One

Brief Description of Selection Process:
Single source; Designated as Predetermined Source February 2010

Dollar Value:

1

Contract Status:
Active- CO#5

Term Begin:
7/23/2009

Term End:
6/28/2012

Nature and Scope of Work:
Post SCA Submittal support

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: Florida Power & Light Company
DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:
4500518167

Major Task or Tasks Associated With:
SCA Support

Vendor Identity:
Environmental Consulting and Technology, Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
One

Number of Bids Received:
One

Brief Description of Selection Process:
Single source; Designated as Predetermined Source December 2009

Dollar Value:
1 [REDACTED]

Contract Status:
Active- CO#6

Term Begin:
7/23/2009

Term End:
6/28/2012

Nature and Scope of Work:
SCA Support

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: Florida Power & Light Company
DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:
4500536449

Major Task or Tasks Associated With:
Turkey Point 6&7 UIC Subject Matter Expert Support

Vendor Identity:
McNabb Hydrogeologic Consulting

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
One

Number of Bids Received:
One

Brief Description of Selection Process:
Competitive Bid for Initial Order, Single Source justification for Change Orders

Dollar Value:
1 [REDACTED]

Contract Status:
Active- CO#2

Term Begin:
10/12/2009

Term End:
6/29/2013

Nature and Scope of Work:
Turkey Point 6&7 UIC Subject Matter Expert Support

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: Florida Power & Light Company
DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:
4500587305

Major Task or Tasks Associated With:
Turkey Point Units 6&7 Exploratory/UIC Well Site Development

Vendor Identity:
Dickerson Florida, Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
Eight

Number of Bids Received:
Five

Brief Description of Selection Process:
Competitive Bid

Dollar Value:

1

Contract Status:
Active- CO#1

Term Begin:
6/29/2010

Term End:
6/30/2011

Nature and Scope of Work:
Turkey Point Units 6&7 Exploratory/UIC Well Site Development

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: Florida Power & Light Company
DOCKET NO.: 120009-E1

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:
4500652043

Major Task or Tasks Associated With:
Turkey Point 6&7 Exploratory/UIC Well and Dual Zone Monitor Well Installation

Vendor Identity:
Layne Christensen Company

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
Three

Number of Bids Received:
Three

Brief Description of Selection Process:
Competitive Bid

Dollar Value:

1


Contract Status:
Active- CO#1

Term Begin:
3/3/2011

Term End:
9/27/2012

Nature and Scope of Work:
Turkey Point 6&7 Exploratory/UIC Well and Dual Zone Monitor Well Installation

EXHIBIT B

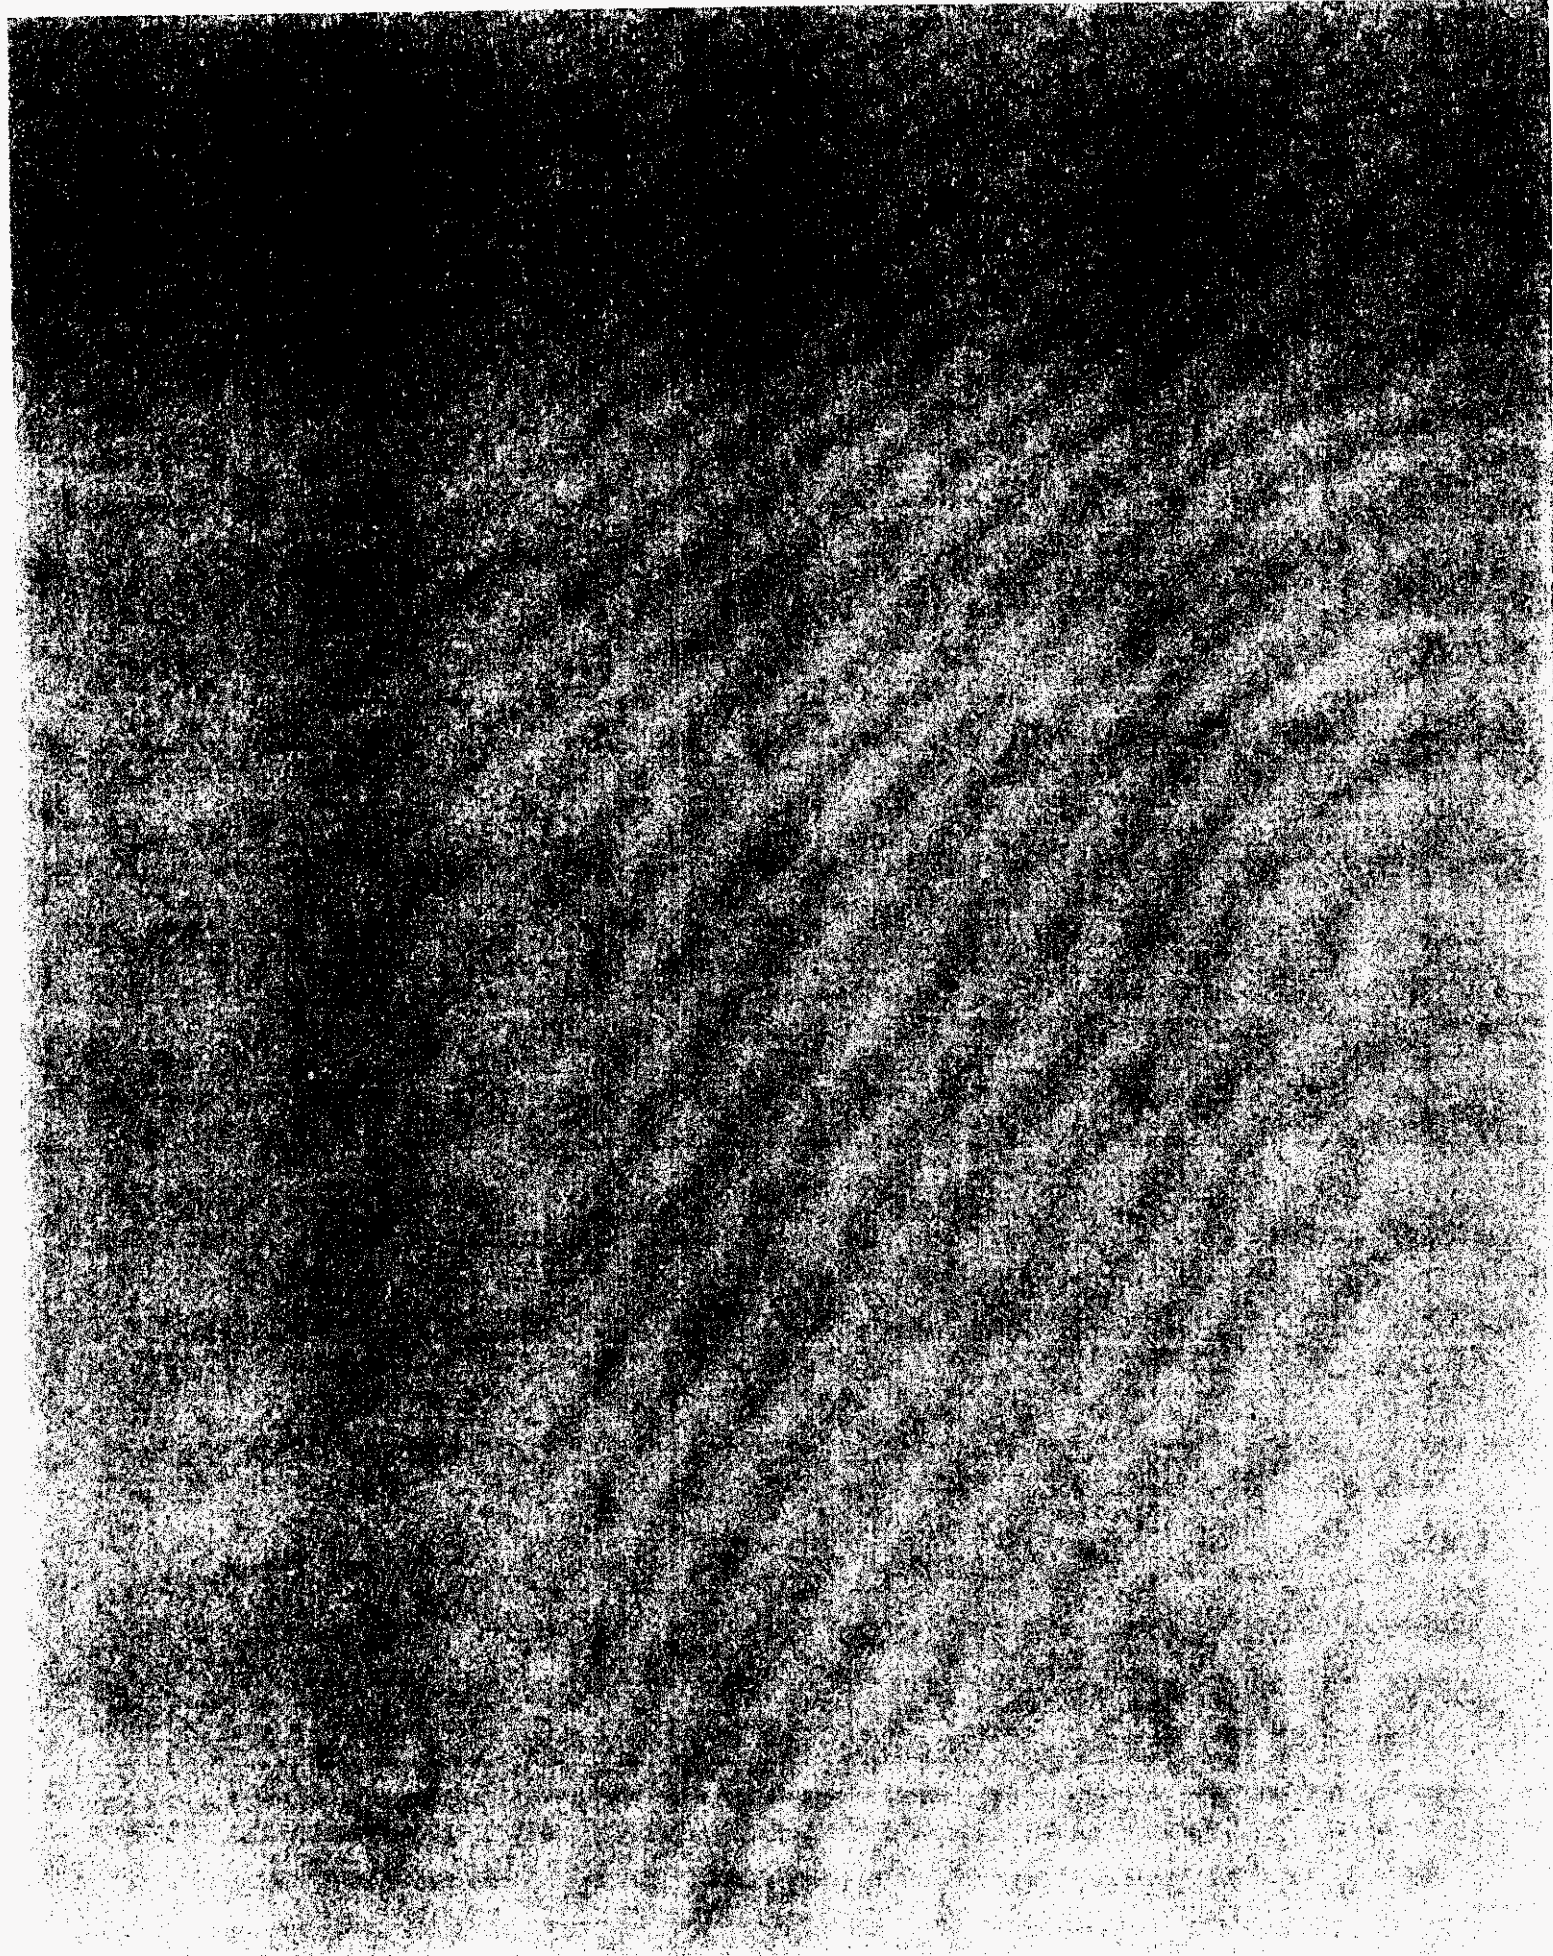

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET N° 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

	(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended In Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
1	121869	Open	4/29/09 - open	4/29/09 - open					AAF MCQUAY	Competitive	Supply Normal Containment Coolers and Testing Services (PTN)
2	120769	Open	3/26/09 - open	3/26/09 - open					Calvert Company Inc	Competitive	Iso Phase Bus Duct Coolers and Testing Services (PSL)
3	124436	Open	7/17/09 - open	7/17/09 - open					Calvert Company Inc	Competitive	Iso Phase Bus Duct Coolers, Install, Demo & Testing Services (PTN)
4	121985	Open	4/24/09 - open	4/24/09 - open					Flowsolve Corp.	Competitive	Replacement Main Feedwater Pumps & Various Testing (PSL)
5	123137	Open	5/28/09 - open	5/28/09 - open					Flowsolve Corp.	Competitive	Main Feedwater Isolation Valves and Testing Services (PTN)
6	125454	Open	8/28/09 - open	8/28/09 - open					Flowsolve Corp.	Competitive	Replacement Heater Drain Pumps (PSL)
7	122154	Complete	4/27/09 - 6/15/11	4/27/09 - 6/15/11					Siemens Energy Inc.	Competitive	Step-Up Transformer (PTN)
8	119078	Open	12/9/08 - open	12/9/08 - open					Westinghouse	OEM	NSSS Engineering Analysis and LAR (PTN)
9	119653	Open	11/24/08 - open	11/24/08 - open					Westinghouse	OEM	NSSS Engineering Analysis and LAR (PSL)
10	121847	Open	4/24/09 - open	4/24/09 - open					Westinghouse	OEM	New & Spent Fuel Criticality and Thermal Hydraulic Analysis (PTN)
11	119670	Open	2/18/09 - open	2/18/09 - open					Proto-Power	Single Source	Project Engineering Support (PSL)
12	115297	Open	8/27/08 - open	8/27/08 - open					Areva	Single Source	RSG Design Review and LAR Work (PSL)
13	115336	Open	8/27/08 - open	8/27/08 - open					Areva	Single Source	RCS Design Review (PTN)
14	105353	Complete	10/02/07 - 12/01/11	10/02/07 - 12/01/11					Shaw - Stone & Webster	Sole Source	Engineering Support (PSL & PTN)
15	117809	Open	12/02/08 - open	12/02/08 - open					Bechtel	Competitive Bid	Engineering Procurement Construction (PTN)
16	116068	Open	09/29/08 - open	09/29/08 - open					Siemens	Single Source	Low Pressure Turbine, Exciter, Exciter Inst. (PSL)
17	117820	Open	12/02/08 - open	12/02/08 - open					Bechtel	Competitive Bid	Engineering Procurement Construction (PSL)
18	116080	Open	9/29/08 - open	9/29/08 - open					Siemens	Single Source	Turbine, Generator/Exciter Upgrades & Inst. (PTN)
19	118328	Open	12/19/08 - open	12/19/08 - open					TEI	Competitive Bid	Condenser Tubes (PTN)
20	118206	Open	12/17/08 - open	12/17/08 - open					TEI	Competitive Bid	Moisture Separator Reheaters (PTN)
21	118205	Open	12/17/08 - open	12/17/08 - open					TEI	Competitive Bid	Moisture Separator Reheaters (PSL)
22	118241	Open	12/19/08 - open	12/19/08 - open					TEI	Competitive Bid	Feed Water Heaters (PTN)
23	112221	Open	4/22/08 - open	4/22/08 - open					Shaw - Stone & Webster	Single Source	Licensing Engineering and BOP Spec Development (PSL)
24	112177	Open	4/22/08 - open	4/22/08 - open					Shaw - Stone & Webster	Single Source	Licensing Engineering and BOP Spec Development (PTN)

A B C D

Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO. 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
 Witness: T. O. Jones

	(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended In Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
25	117272	Open	11/13/08 - open	11/13/08 - open					American Crane	Single Source	Gantry Crane Upgrade (PSL)
26	118224	Open	12/17/08 - open	12/17/08 - open					TEI	Competitive Bid	Feed Water Heaters (PSL)
27	115465	Open	9/03/08 - open	9/03/08 - open					Proto-Power	Single Source	Engineering Services (PTN)
28	118278	Open	12/19/08 - open	12/19/08 - open					TEI	Competitive Bid	TCW Heat Exchangers (PSL)
29	105720	Open	9/12/07 - open	9/12/07 - open					AREVA	Single Source	Neutronics Analysis (PSL)
30	116798	Complete	10/29/08 - 12/22/11	10/29/08 - 12/22/11					Cameron	Single Source	Ultrasonic Flow Meter Measuring System (PTN)
31	116107	Open	9/29/08 - open	9/29/08 - open					Cameron	Single Source	Ultrasonic Flow Meter Measuring System (PSL)
32	114114	Open	7/03/08 - open	7/03/08 - open					Richard Sipos	Single Source	Staff Augmentation (PSL)
33	115036	Complete	8/14/08 - 1/08/11	8/14/08 - 01/08/11					Babcock & Wilcox	Single Source	Steam Generator Component Design Review (PSL)
34	112228	Complete	4/23/08 - 06/11/11	4/23/08 - 08/11/11					Westinghouse	Single Source	Steam Generator Services for Moisture Carryover (PTN)
35	113030	Open	5/20/08 - open	5/20/08 - open					FPL Seabrook	Single Source	FPLE personnel supporting FPL Upates (PSL & PTN)
36	115391	Open	8/29/08 - open	8/29/08 - open					NAI	Single Source	Radiological Consequence Analysis (PSL)
37	112987	Open	5/19/08 - open	5/19/08 - open					NAI	Single Source	Radiological Consequence Analysis (PTN)
38	4500521317	Open	9/08/09 - open	9/08/09 - open					Areva	Competitive	Inductors (PTN)
39	126246	Open	10/08/09 - open	10/08/09 - open					ABB	Competitive	Replacement Transformer Coolers (PSL)
40	126453	Open	11/05/09 - open	11/05/09 - open					Joseph Ost Corporation	Competitive	Cooling Water Heat Exchangers (PTN)
41	127777	Open	12/08/09 - open	12/08/09 - open					High Bridge	Single Source	Estimating Services (PTN)
42	127881	Open	12/22/09 - open	12/22/09 - open					Absolute Consulting	Single Source	Procedure Writers (PTN)
43	123762	Open	6/25/09 - open	6/25/09 - open					Key Controls of Tampa	OEM	Control System Tuning and Dynamic Analysis (PTN)
44	118988	Open	01/22/09 - open	01/22/09 - open					Holtec	Single Source	Fuel Storage Criticality and related analysis (PSL 2)
45	118563	Open	1/14/09 - open	1/14/09 - open					Holtec	Competitive	Fuel Storage Criticality and related analysis (PSL 1)
46	118627	Open	7/28/09 - open	7/28/09 - open					Western Services	Competitive	NSSS Simulator Reactor Core Model Upgrade (PSL)
47	118844	Open	01/15/09 - open	01/15/09 - open					Western Services	Competitive	NSSS Simulator Reactor Core Model Upgrade (PTN)
48	4500487077	Open	11/10/08 - open	11/10/08 - open					Siemens	Competitive	Generator Step -up Transformers (PSL)

A B C D

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO: 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

	(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
49	130579	Open	5/01/10 - open	5/01/10 - open					Fisher Controls	Competitive	Modified Feedwater Regulating Valves/Actuators (PSL)
50	130160	Open	3/29/10 - open	3/29/10 - open					Flowserve Corp.	Competitive	Replacement Condensate Pumps (PSL)
51	130612	Open	4/22/10 - open	4/22/10 - open					Flowserve Corp.	Competitive	Condensate Pumps (PTN)
52	130649	Open	4/22/10 - open	4/22/10 - open					Flowserve Corp.	Competitive	Main Feedwater Pumps (PTN)
53	126227	Open	10/13/09 - open	10/13/09 - open					Invensys	OEM	Control System FWH, Moisture Separator (PTN)
54	129689	Open	3/17/10 - open	3/17/10 - open					Invensys	Competitive	Turbine Digital Upgrade (PTN)
55	130272	Open	4/08/10 - open	4/08/10 - open					Siemens Energy Inc.	Competitive	Electro-Hydraulic Fluid Systems (PTN)
56	131356	Open	5/21/10 - open	5/21/10 - open					Brand Energy Solutions	Competitive	Supply Scaffolding Material (PTN)
57	131391	Complete	5/25/10 - 4/19/11	5/25/10 - 4/19/11					BRV Construction	Competitive	Design/Construct fabrication area inside the CSF (PTN)
58	131599	Open	5/27/10 - open	5/27/10 - open					All Star Telfords	Competitive	Supply Cleaning Services (PTN)
59	4500586420	Open	6/16/10 - open	6/16/10 - open					Energy Erectors	Competitive	Electrical contract labor work @ 230 kV substation (PTN)
60	131926	Complete	6/14/10 - 02/28/11	6/14/10 - 02/28/11					Siemens Energy Inc.	Single Source	SL2-19 Pre-planning TG Installation Work (PSL2)
61	131533	Open	6/10/10 - open	6/10/10 - open					Areva	OEM	Non-Fuels NSSS Interim LAR (PSL 1 & 2)
62	131907	Open	6/11/10 - open	6/11/10 - open					Areva	OEM	Fuels Related Interim LAR/MOD for EPU (PSL)
63	131585	Open	6/15/10 - open	6/15/10 - open					Shaw - Stone & Webster	PDS	Interim LAR/MOD Support for EPU (PSL)
64	131393	Open	6/10/10 - open	6/10/10 - open					Fisher Controls	Competitive	Heater Drain BOP Replacement Valves (PSL)
65	131742	Open	6/16/10 - open	6/16/10 - open					Westinghouse	PDS	LAR/RAI for Non-Fuels NSSS related scope (PSL)
66	132077	Open	6/17/10 - open	6/17/10 - open					Siemens Energy Inc.	Single Source	Siemens Dedicated Resident Site Manager (PTN)
67	132078	Open	6/17/10 - open	6/17/10 - open					Siemens Energy Inc.	Single Source	Siemens Dedicated Resident Site Manager (PSL)
68	132235	Open	6/24/10 - open	6/24/10 - open					Enercon	Single Source	NFPA 805/Appendix R Support for (PTN)
69	131987	Open	6/25/10 - open	6/25/10 - open					Sargent & Lundy Inc	Single Source	Engineering for Steam Bypass Control (PSL1)
70	131940	Open	6/30/10 - open	6/30/10 - open					Westinghouse	Competitive	Main Steam Turbine Control Replacement (PSL)
71	132283	Open	6/28/10 - open	6/28/10 - open					Shaw - Stone & Webster	PDS	EPU Feedwater Pump Nozzle Load Reduction (PSL)
72	2259675	Open	7/23/10 - open	7/23/10 - open					Joseph Oat Corporation	Competitive	Furnish New Spent Fuel Pool Heat Exchangers (PTN)

A B C D

Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO. 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
 Witness: T. O. Jones

	(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended In Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
73	2259669	Open	8/02/10 - open	8/02/10 - open					TAW	Competitive	Rewind/Refurbish/Upgrade Condensate Pumps (PTN)
74	2259997	Open	8/4/10 - open	8/4/10 - open					SPX Corporation	Replaces 115351	Valve Rework (PTN)
75	2259768	Open	8/06/10 - open	8/06/10 - open					Westinghouse	OEM	Design basis support for Umbrella Mods (PTN)
76	2260155	Open	8/16/10 - open	8/16/10 - open					Siemens Energy Inc.	Single Source	PSL 1-24 Pre-planning TG Installation Work
77	2260113	Open	9/23/10 - open	9/23/10 - open					Westinghouse	OEM	Rod Control System Upgrades (PSL)
78	2261536	Open	9/16/10 - open	9/16/10 - open					Washington Group	Competitive	Feedwater Heater Ultrasonic Testing (PTN)
79	2261750	Open	9/21/10 - open	9/21/10 - open					Modular Space	Competitive	Lease of 15-Wide Trailers for EPU (PTN)
80	2261747	Open	9/23/10 - open	9/23/10 - open					Westinghouse	PDS	EPU NSSS Engineering and Modification Support (PTN)
81	2262084	Open	9/28/10 - open	9/28/10 - open					Structural Integrity	Competitive	Assessment of Min Wall Thickness Effects (PTN)
82	2262201	Open	9/30/10 - open	9/30/10 - open					Fisher Controls	Replaces 131395	Heater Drain BOP Replacement Valves (PSL)
83	2262367	Open	10/04/10 - open	10/04/10 - open					Techcom International	Competitive	Engineering Services for Various Distributing Mods (PTN)
84	2262515	Open	10/06/10 - open	10/06/10 - open					Fisher Controls	Replaces 130578	Modified Feedwater Regulating Valves/Actuators (PSL)
85	2263036	Open	10/19/10 - open	10/19/10 - open					Flowserve Corp.	Replaces 130160	Replacement Condensate Pumps (PSL)
86	2264196	Complete	11/16/10 - 4/20/11	11/16/10 - 4/20/11					Siemens Energy Inc.	OEM	Replacement Blade Rings (PSL)
87	2264240	Open	11/17/10 - open	11/17/10 - open					Siemens Energy Inc.	Single Source	T/G Installation SL2-19 Outage (PSL)
88	2263052	Open	11/11/10 - open	11/11/10 - open					Invensys	Single Source	Steam Bypass Control System (PSL)
89	2263549	Open	11/10/10 - open	11/10/10 - open					Areva NP Inc	Competitive	Services of a Project Manager (PTN)
90	2264548	Complete	11/19/10 - 03/28/11	11/19/10 - 03/28/11					Graybar Electric	Competitive	Wire Cable (PTN)
91	2263930	Open	11/11/10 - open	11/11/10 - open					Brand Energy Solutions	Replaces 131356	Supply Scaffolding Material (PTN)
92	2264842	Open	11/30/10 - open	11/30/10 - open					Ronnies Turbine Services Inc	Single Source	On Site SL2-19 Tech Support (PSL)
93	2264841	Open	11/30/10 - open	11/30/10 - open					Batsch Industries	Single Source	On Site SL2-19 Tech Support (PSL)
94	2264377	Open	11/30/10 - open	11/30/10 - open					Techcom International	Competitive	Turbine Digital Controls Verification and Validation (PTN)
95	2264914	Open	12/07/10 - open	12/07/10 - open					Westinghouse Electric	OEM	CEDMS Power Switch Refurbishment (PSL2)
96	2263851	Open	11/4/10 - open	11/4/10 - open					Graybar Electric	Competitive	Temporary Power Unit Substations for EPU (PTN)

A B C D

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO: 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

	(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
97	2285418	Open	12/16/10 - open	12/16/10 - open					Siemens Energy Inc.	OEM	Impl. Spares for EPU Turbine Gen. Work During SL2-19 (PSL)
98	4500589986	Open	7/6/10 - open	7/6/10 - open					Kennedy Construction	Competitive	Site preparation contract laborwork @ 230 kV substation (PTN)
99	2285720	Open	01/4/11 - open	01/4/11 - open					Enercon Services	Competitive	Licensing/Design Basis/Program Modification (PTN)
100	2291203	Open	04/21/11 - open	04/21/11 - open					Enertech	Competitive	Main Steam Isolation Valve Replacement Actuator (PSL)
101	2287242	Open	01/27/11 - open	01/27/11 - open					Engineering Planning & Management	Competitive	Environmental Qualification Document (PTN)
102	2287468	Open	02/10/11 - open	02/10/11 - open					Feedforward Inc.	Competitive	DCS Mods (PSL)
103	2290208	Open	03/25/11 - open	03/25/11 - open					Feedforward Inc.	Competitive	Leading Edge Flow Meter Addition (PTN)
104	2287971	Open	02/15/11 - open	02/15/11 - open					Foster Wheeler North America	Competitive	SJAE Inter/After Condensers (PTN)
105	2290465	Open	03/31/11 - open	03/31/11 - open					Siemens	OEM	Design and Fabrication of Turbine Crossover piping (PTN)
106	2290483	Open	03/31/11 - open	03/31/11 - open					Siemens	OEM	Iron Bolts for Main Steam Generator Stator (PTN)
107	2290842	Open	04/08/11 - open	04/08/11 - open					Siemens	OEM	Blower Stationary Blade Rings (PSL)
108	2286521	Open	01/18/11 - open	01/18/11 - open					Stone & Webster	PDS	MSIV/MSCV Modification to Support EPU (PSL)
109	2284476	Open	05/11/11 - open	05/11/11 - open					Batsch Industries	Single Source	Turbine Generator Technical Support (PTN)
110	2291815	Open	04/28/11 - open	04/28/11 - open					BRV Construction	Competitive	Fossil Warehouse Demolition (PTN)
111	2290814	Open	05/02/11 - open	05/02/11 - open					Flowsolve Corp.	Replaces 130649	Main Feedwater Pump Casing Modification (PTN)
112	2292773	Open	05/26/11 - open	05/26/11 - open					AAF MCQUAY	OEM	Design, Engineer, Fabricate and Deliver CRDM Coils (PTN)
113	2293950	Open	06/24/11 - 04/20/11	06/24/11 - 04/20/11					Siemens	Single Source	Turbine Generator Pre-outage planning activities (PTN)
114	2293653	Open	06/29/11 - open	06/29/11 - open					Thermal Engineering	Competitive	Design and Fabrication of Gland Steam Condensers (PTN)
115	2294247	Open	07/06/11 - open	07/06/11 - open					Ecological Associates	Competitive	Biological Plan of Study (PSL)
116	2294341	Open	07/11/11 - open	07/11/11 - open					Allon	Single Source	GL2008-01 Support (PSL)
117	2294494	Open	07/13/11 - open	07/13/11 - open					Enercon Services	Competitive	Emergency Containment Cooler Auto-start (PTN)
118	2294221	Open	07/11/11 - open	07/11/11 - open					Flowsolve Corp.	Competitive	Main Steam Isolation Replacement Valves (PSL)
119	2294855	Open	07/21/11 - open	07/21/11 - open					Zachary Nuclear Engineering	Single Source	Project Engineering Support for EPU (PSL)
120	2295186	Open	08/02/11 - open	08/02/11 - open					Hotec International	Single Source	Metamic Chevrons for Spent Fuel Pool (PSL)

A B C D

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO: 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation If any)	Method of Selection and Document ID	Work Description
121	2295422	Open	8/10/11 - open	8/10/11 - open					Siemens Energy Inc.	OEM	Support Material for the EPU Turb-Gen Upate (PTN)
122	2295071	Open	08/01/11 - open	08/01/11 - open					Stone & Webster	Single Source	Unit 1 Vibration and Support Mods for FW & Condensate (PSL)
123	2296049	Open	08/25/11 - open	08/25/11 - open					Cameron Tech.	Replaces 115796	Ultrasonic Flow Meter Measuring System (PTN)
124	2294671	Open	08/19/11 - open	08/19/11 - open					NWT Corporation	Competitive	Moisture Carry Over Testing for EPU (PTN)
125	2296556	Open	09/02/11 - open	09/02/11 - open					Sulzer Pumps	OEM	Modify, overhaul and refurbishment of the B & C AFW (PTN)
126	2296519	Open	09/06/11 - open	09/06/11 - open					Techcom International	Competitive	DCS Integration Plan for 3R26 and 4R27 (PTN)
127	2296623	Open	09/06/11 - open	09/06/11 - open					Tricen Technologies	Competitive	Unit 3 Condenser Tube Eddy Current Testing (PTN)
128	2296797	Open	09/09/11 - open	09/09/11 - open					Coastal Bus & Charter Lines (dba Need A Bus)	Competitive	Shuttle Bus Services for EPU (PSL)
129	2296330	Open	09/09/11 - open	09/09/11 - open					Flowserve Corp.	Competitive	Motor Operated Valves (PTN)
130	2296266	Open	10/12/11 - open	10/12/11 - open					Franmar Corporation	Competitive	Shuttle Bus Services for EPU (PTN)
131	2298406	Open	10/12/11 - open	10/12/11 - open					Master Lee Energy Services	Competitive	Fuel Movers for Melanic Inserts (PSL)
132	2298635	Open	10/14/11 - open	10/14/11 - open					Sargent & Lundy Inc.	Single Source	Engineering Service for the Charging System Modification (PSL 2)
133	2297556	Open	09/27/11 - open	09/27/11 - open					Siemens Energy Inc.	Single Source	Siemens Installation of 2A Main Power Transformer (PSL)
134	2299101	Open	10/27/11 - open	10/27/11 - open					Berkel & Company	Single Source	Mico Pile Construction (PTN)
135	2298894	Open	10/24/11 - open	10/24/11 - open					Day & Zimmermann NPS Inc	Competitive	Installation of Trailer Support Services (PTN)
136	2299350	Open	11/01/11 - open	11/01/11 - open					Enercon Services Inc	Competitive	Eng. Evaluation for EPU Mid-Cycle contingency plan (PSL)
137	2299618	Open	11/04/11 - open	11/04/11 - open					Radiation Safety & Control	Competitive	Truck Monitoring/Waste Characterization for EPU (PTN)
138	2297624	Open	10/27/11 - open	10/27/11 - open					Siemens Energy Inc.	OEM	Turbine Valve Conversion to EH (PTN)
139	2299631	Open	11/8/11 - open	11/8/11 - open					Tri-Tool Inc	Single Source	Unit 1 LP Turbine Extraction Line Services (PSL)
140	2295953	Open	08/24/11 - open	08/24/11 - open					Marmon Wire & Cable	OEM	Misc Safety Related Wire and Cable, line items 1 - 23 (PTN)
141	2297055	Open	09/16/11 - open	09/16/11 - open					Thermal Engineering	Single Source	Replacement LP #4 Feedwater Heaters for EPU (PSL 2)
142	2300139	Open	11/21/11 - open	11/21/11 - open					Siemens Energy Inc.	Single Source	SL1-24 Turb-Gen. Installation (PSL 1)
143	2296624	Open	11/16/11 - open	11/16/11 - open					Ames Group LLC	Single Source	Upgrade Services for Feedwater Pumps (PSL)
144	2300487	Open	11/28/11 - open	11/28/11 - open					Weldtech Services	Single Source	SL1-24 Construction Management Oversight Services (PSL 1)

A B C D

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET # 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
145	2299618	Open	11/04/11 - open	11/04/11 - open				Radiation Safety & Control	Competitive	Truck Monitoring/Waste Characterization for EPU (PTN)	
146	2299350	Open	11/01/11 - open	11/01/11 - open				Enercon Services	Competitive	Engineering evaluation for EPU mid-cycle contingency plan (PSL)	
147	2299631	Open	11/08/11 - open	11/08/11 - open				Tri-Tool	Single Source	LP Turbine Extraction Line Services for EPU (PSL 1)	
148	NF-10-358 NF-11-178	Open	11/2/10 - open	11/2/10 - open				Westinghouse Electric	OEM	Spent Fuel Pool Criticality Safety Analysis Support (PTN)	
149	2301813	Open	12/28/11 - open	12/28/11 - open				Enercon Services Inc	Competitive	Motor Operated Valve Transfer Switches for EPU (PSL)	
150	2301867	Open	12/28/11 - open	12/28/11 - open				Enercon Services Inc	Single Source	Develop Engineering Change Packages for EPU (PTN)	
151	2301038	Open	12/14/11 - open	12/14/11 - open				Graftel Inc.	Competitive	Integrated Leak Rate Testing for EPU (PTN)	
152	2261800	Open	09/28/10 - open	09/28/10 - open				3 Communications Mepps Inc	OEM	Supply of Simulator SCD Software Translator Upgrade (PTN)	
153	130340	Open	04/02/10 - open	04/02/10 - open				MPR Associates	Competitive	Third Party Review of Siemens Turb-Gen. Analysis (PSL)	
154	2301737	Open	12/21/11 - open	12/21/11 - open				PSI Energy Services	Single Source	Construction Management Oversight Services (PTN)	
155	2301736	Open	12/21/11 - open	12/21/11 - open				Weidtech Services	Single Source	Construction Management Oversight Services (PTN)	
156	2301871	Open	12/28/11 - open	12/28/11 - open				Zachry Nuclear Engineering	Single Source	Develop Engineering Change Packages for EPU (PTN)	
157	2301858	Open	12/28/11 - open	12/28/11 - open				Sargent & Lundy Inc	Single Source	Develop TPCW Engineering Change Packages for EPU (PTN)	
158	2000053226	Open	11/21/11 - open	11/21/11 - open				Ric-Man Construction	Competitive	Road and parking contract labor work 230kV substation (PTN)	

A B C D

Legend:
PDS = Predetermined Source
OEM = Original Equipment Manufacturer
PSL = St. Lucie
PTN = Turkey Point

Notes:
In November 2011, FPL issued a Letter of Agreement (LOA) to Siemens for the PTN 3-26 Turbine Generator installation scope; however, the contract was not issued in 2011.



**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO 121869

Major Task or Tasks Associated With:

Supply Eight (8) Normal Containment Coolers and provide Testing Services

Vendor Identity:

AAF MCQUAY

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4


Number of Bids Received:

2

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to AAF McQuay.

Dollar Value:

Total Contract Value through Revision 3 is 

Contract Status:

Active

Term Begin:

April 29, 2009

Term End:

March 2013

Nature and Scope of Work:

Supply Eight (8) Normal Containment Coolers and provide Testing Services

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO 120769

Major Task or Tasks Associated With:

Replacement IsoPhase Bus Duct Coolers

Vendor Identity:

Calvert Company Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

1

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Calvert Company Inc.

Dollar Value:

Total Dollar Value through Revision 2 is



Contract Status:

Active

Term Begin:

March 26, 2009

Term End:

June 2012

Nature and Scope of Work:

Replacement IsoPhase Bus Duct Coolers, Technical Installation Support and Field Testing.

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO 124436

Major Task or Tasks Associated With:

Replacement Isolated Phase BusDuct

Vendor Identity:

Calvert Company Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Calvert Company Inc.

Dollar Value:

Total Dollar Value through Revision 2 is



Contract Status:

Active

Term Begin:

July 17, 2009

Term End:

June 2012

Nature and Scope of Work:

Replacement Isolated Phase BusDuct, Demolition and Installation Services, Evaluation, Testing and Engineering

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO 121985

Major Task or Tasks Associated With:

Replacement Main Feedwater Pumps

Vendor Identity:

Flowserve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

5

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Flowserve Corp.

Dollar Value:

Total Dollar Value through Revision 3 is



Contract Status:

Active

Term Begin:

April 24, 2009

Term End:

June 2012

Nature and Scope of Work:

Replacement Main Feedwater Pumps, spare parts and technical direction of installation.

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO 123137

Major Task or Tasks Associated With:

Main Feedwater Isolation Valves

Vendor Identity:

Flowserve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Flowserve Corp.

Dollar Value:

Total Dollar Value through Revision 1 is



Contract Status:

Active

Term Begin:

May 28, 2009

Term End:

Open

Nature and Scope of Work:

Main Feedwater Isolation Valves, Technical Field Services, Testing, Engineering and Documentation

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO 125454

Major Task or Tasks Associated With:

Replacement Heater Drain Pumps

Vendor Identity:

Flowserve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Flowserve Corp.

Dollar Value:

Total Dollar Value through Revision 1 is

Contract Status:

Active

Term Begin:

August 28, 2009

Term End:

June 2012

Nature and Scope of Work:

Replacement Heater Drain Pumps, Spare Heater, Technical Direction

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO 122154

Major Task or Tasks Associated With:

Step-Up Transformers

Vendor Identity:

Siemens Energy Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

2

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Siemens Energy Inc.

Dollar Value:

[REDACTED]

Contract Status:

Complete

Term Begin:

April 27, 2009

Term End:

Complete

Nature and Scope of Work:

Uprate Step-Up Transformers from 850 MVA to 970 MVA

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO 119078

Major Task or Tasks Associated With:

NSSS Engineering Evaluation and LAR Analysis for PTN Units 3 & 4

Vendor Identity:

Westinghouse Electric Co.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Dollar Value through Revision 6 is [REDACTED]

Contract Status:

Active

Term Begin:

Letter of Authorization issued 12/9/08; PO issued 1/26/09

Term End:

Open

Nature and Scope of Work:

NSSS Engineering Evaluation and LAR Analysis for PTN Units 3 & 4

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO 119653

Major Task or Tasks Associated With:

NSSS Engineering Evaluation and LAR Analysis for PSL Units 1 & 2

Vendor Identity:

Westinghouse Electric Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Dollar Value through Revision 4 is [REDACTED]

Contract Status:

Active

Term Begin:

Letter of Authorization issued 11/24/08; PO issued 2/17/09

Term End:

open

Nature and Scope of Work:

NSSS Engineering Evaluation and LAR Analysis for PSL Units 1 & 2

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO 115297 (PSL)

Major Task or Tasks Associated With:

Design Review for LAR (Steam Generator and Reactor Head)

Vendor Identity:

AREVA

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Dollar Value through Revision 8

Contract Status:

Active

Term Begin:

August 27, 2008

Term End:

open

Nature and Scope of Work:

Design Review for LAR (Steam Generator and Reactor Head)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO 115338

Major Task or Tasks Associated With:

Engineering Analysis

Vendor Identity:

AREVA

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Dollar Value through Revision 10. [REDACTED]

Contract Status:

Active

Term Begin:

August 27, 2008

Term End:

Open

Nature and Scope of Work:

Design review for the Reactor Coolant system, Control Rod Mechanism, EMA, CFD and BMI

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY:

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 105353

Major Task or Tasks Associated With:

Initial BOP Scoping Support for EPU

Vendor Identity:

Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Sole Source

Dollar Value:

Total Dollar Value through Revision 5 is 

Contract Status:

Complete

Term Begin:

October 2, 2007

Term End:

December 1, 2011

Nature and Scope of Work:

BOP Scoping Support (engineering) for the EPU Project

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO 117809

Major Task or Tasks Associated With:

Provide Engineering, Procurement and Construction Services for
PTN

Vendor Identity:

Bechtel

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

6

Number of Bids Received:

5

Brief Description of Selection Process:

Bidders were evaluated against predetermined technical and commercial criteria, awarding to the lowest evaluated bidder.

Dollar Value:

PO value through Rev 4/Rel 0 is [REDACTED]

Contract Status:

Active

Term Begin:

December 2, 2008

Term End:

April 2013

Nature and Scope of Work:

Bechtel's scope includes project management, design engineering, procurement and material handling services, work order planning, construction/implementation, project controls, quality assurance, quality control, radiation protection (aiara), safety, security interface, and other services as designated in the Contract documents.

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 116088

Major Task or Tasks Associated With:

Turbine/Generator Uprate

Vendor Identity:

Siemens Power

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single source

Dollar Value:

Total Max Dollar Value through Revision 4/Release 0

Contract Status:

Active

Term Begin:

September 29, 2008

Term End:

March 2013

Nature and Scope of Work:

Engineering, Parts and Installation for PSL Turbine/Generator Uprate

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO 117820

Major Task or Tasks Associated With:

Provide Engineering, Procurement and Construction Services for PSL

Vendor Identity:

Bechtel

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

6

Number of Bids Received:

5

Brief Description of Selection Process:

Bidders were evaluated against predetermined technical and commercial criteria, awarding to the lowest evaluated bidder.

Dollar Value:

PO value through Rev 5/Rel 0 is [REDACTED]

Contract Status:

Active

Term Begin:

December 2, 2008

Term End:

December 2012

Nature and Scope of Work:

Bechtel's scope includes project management, design engineering, procurement and material handling services, work order planning, construction/implementation, project controls, quality assurance, quality control, radiation protection (alara), safety, security interface, and other services as designated in the Contract documents.

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 116090

Major Task or Tasks Associated With:

PTN Turbine Generator Uprate

Vendor Identity:

Siemens Power

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Max Contract Value through Rev. 3/Rel 0 is [REDACTED]

Contract Status:

Active

Term Begin:

September 29, 2008

Term End:

March 2013

Nature and Scope of Work:

PTN Engineering, Parts and Installation for Turbine/Generator Uprate

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 118328

Major Task or Tasks Associated With:

PTN Condenser Tube Bundles for Unit 3 & 4

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through Revision 5 is [REDACTED]

Contract Status:

Active

Term Begin:

December 19, 2008

Term End:

March 2013

Nature and Scope of Work:

Supply PTN Condenser Tube Bundles

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.
For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 118208

Major Task or Tasks Associated With:

PTN MSR's for Units 3 & 4

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

2

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through Revision 2 [REDACTED]

Contract Status:

Active

Term Begin:

December 17, 2008

Term End:

March 2013

Nature and Scope of Work:

Supply PTN Moisture Separator Reheaters

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 118205

Major Task or Tasks Associated With:

PSL MSR's for Units 1 & 2

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

2

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through Revision 5 is



Contract Status:

Active

Term Begin:

December 17, 2008

Term End:

July 2012

Nature and Scope of Work:

Supply PSL Moisture Separator Reheaters

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 118241

Major Task or Tasks Associated With:

PTN Feedwater Heaters for Units 3 & 4

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

3

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Contract Value through Revision 2

Contract Status:

Active

Term Begin:

December 19, 2008

Term End:

March 2013

Nature and Scope of Work:

Supply PTN Feedwater Heaters

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 112221

Major Task or Tasks Associated With:

Engineering Services

Vendor Identity:

Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Blanket Purchase Order Max Value through Revision 17 to
Release 0 is [REDACTED]

Contract Status:

Active

Term Begin:

April 22, 2008

Term End:

December 2012

Nature and Scope of Work:

PSL BOP Engineering

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:
PO # 112177

Major Task or Tasks Associated With:
Engineering Services

Vendor Identity:
Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Blanket Purchase Order Max Value through Revision 8 to Release 0 is [REDACTED]

Contract Status:
Active

Term Begin:
April 22, 2008

Term End:
open

Nature and Scope of Work:
Engineering for the PSL Uprate Project

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO 117272

Major Task or Tasks Associated With:

Gantry crane repair/modification

Vendor Identity:

American Crane & Equip.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Sole Source/OEM

Dollar Value:

Total Dollar Value through Rev 6 is [REDACTED]

Contract Status:

Active

Term Begin:

November 13, 2008

Term End:

Open

Nature and Scope of Work:

Complete modification of Unit 1 crane and update of electrical components for Unit 2 crane

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 118224

Major Task or Tasks Associated With:

PSL Feedwater Heaters for Units 1 & 2

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Dollar Value thru Revision 6

Contract Status:

Active

Term Begin:

December 17, 2008

Term End:

open

Nature and Scope of Work:

Supply PSL Feedwater Heaters

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 115465

Major Task or Tasks Associated With:

Eng. Services for NSSS, BOP & Licensing Activities

Vendor Identity:

Proto-Power

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Dollar Value through revision 4 is [REDACTED]

Contract Status:

Active

Term Begin:

September 3, 2008

Term End:

Open

Nature and Scope of Work:

PTN Eng. Services for NSSS, BOP and Licensing Activities.

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 118278

Major Task or Tasks Associated With:

PSL Heat Exchangers for Units 1 & 2

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

3

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through revisions 4 is [REDACTED]

Contract Status:

Active

Term Begin:

December 19, 2008

Term End:

Open

Nature and Scope of Work:

Supply PSL Heat Exchangers

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY:

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 105720

Major Task or Tasks Associated With:

PSL Fuels Study

Vendor Identity:

Areva

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Order value through Revision 16 is [REDACTED]

Contract Status:

Active

Term Begin:

September 12, 2007

Term End:

open

Nature and Scope of Work:

Fuels Performance Study and Analysis

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 116796

Major Task or Tasks Associated With:

Ultrasonic Flow Measuring System

Vendor Identity:

Cameron Technologies

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Blanket Purchase Order Value through Revision 1 to Release 0 is [REDACTED]

Contract Status:

Complete

Term Begin:

October 29, 2008

Term End:

December 22, 2011

Nature and Scope of Work:

Ultrasonic Flow Measuring System for PTN

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO 116107

Major Task or Tasks Associated With:

Ultrasonic Flow Measuring System

Vendor Identity:

Cameron Technologies

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Purchase Order Value through Revision 1 is [REDACTED]

Contract Status:

Awarded

Term Begin:

September 29, 2008

Term End:

Open

Nature and Scope of Work:

Ultrasonic Flow Measuring System for PTN

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO 114114

Major Task or Tasks Associated With:

Staff Augmentation

Vendor Identity:

Richard Sipos

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source Justification

Dollar Value:

Total Blanket Purchase Order Value through Revision 6 is



Contract Status:

Active

Term Begin:

July 3, 2008

Term End:

open

Nature and Scope of Work:

Project Management Services

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 4500521317

Major Task or Tasks Associated With:

Inductors

Vendor Identity:

Areva

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive Selection

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

September 8, 2009

Term End:

Open

Nature and Scope of Work:

Supply of Inductors

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-BA

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 126248

Major Task or Tasks Associated With:

Replacement Transformer Coolers

Vendor Identity:

ABB

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

1

Brief Description of Selection Process:

Competitive Selection, Commercial and Technical Evaluation

Dollar Value:

Total Contract Value through Rev 2 [REDACTED]

Contract Status:

Active

Term Begin:

October 8, 2009

Term End:

Open

Nature and Scope of Work:

Replacement Transformer Coolers

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 126453

Major Task or Tasks Associated With:

Turbine Plant Cooling Water Heat Exchangers

Vendor Identity:

Joseph Oat Corporation

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive Selection, Commercial and Technical Evaluation

Dollar Value:

Total Contract Value through revision 1 is [REDACTED]

Contract Status:

Active

Term Begin:

November 5, 2009

Term End:

Open

Nature and Scope of Work:

Supply Turbine Plant Cooling Water Heat Exchangers

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.
For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO #127777

Major Task or Tasks Associated With:

Estimating Services

Vendor Identity:

High Bridge

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Contract Value through revision 2 is



Contract Status:

Active

Term Begin:

December 8, 2009

Term End:

Open

Nature and Scope of Work:

Estimating Services

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 127881

Major Task or Tasks Associated With:

Procedure Writers

Vendor Identity:

Absolute Consulting

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 22, 2009

Term End:

Open

Nature and Scope of Work:

Procedure Writers

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:
PSL PO #118988

Major Task or Tasks Associated With:
Fuel Storage Criticality and Related Analysis (PSL 2)

Vendor Identity:
Holtec

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Purchase Order Value through Revision 4 is [REDACTED]

Contract Status:
Active

Term Begin:
January 22, 2009

Term End:
Open

Nature and Scope of Work:
Fuel Storage Criticality and Related Analysis (PSL 2)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO #118563

Major Task or Tasks Associated With:

Fuel Storage Criticality and Related Analysis (PSL 1)

Vendor Identity:

Holtec

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Purchase Order Value through Revision 5 is

Contract Status:

Active

Term Begin:

January 14, 2009

Term End:

Open

Nature and Scope of Work:

Fuel Storage Criticality and Related Analysis (PSL 1)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.
For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO # 4500467077

Major Task or Tasks Associated With:

PSL Generator Step-up Transformers

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

7

Number of Bids Received:

7

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

November 10, 2008

Term End:

Open

Nature and Scope of Work:

PSL Generator Step-up Transformers

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 130612

Major Task or Tasks Associated With:

Condensate Pumps

Vendor Identity:

Flowserve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Contract Value through Revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

April 22, 2010

Term End:

Open

Nature and Scope of Work:

Condensate Pumps

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO #130649

Major Task or Tasks Associated With:

Main Feedwater Pumps

Vendor Identity:

Flowsolve Corp

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

1

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

April 22, 2010

Term End:

Open

Nature and Scope of Work:

Main Feedwater Pumps

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.
For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 126227

Major Task or Tasks Associated With:

Control System FWH, Moisture Separator

Vendor Identity:

Invensys

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Dollar Value through revision 9 [REDACTED]

Contract Status:

Active

Term Begin:

October 13, 2009

Term End:

Open

Nature and Scope of Work:

Control System FWH, Moisture Separator

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 129688

Major Task or Tasks Associated With:

Turbine Digital Upgrade

Vendor Identity:

Invensys

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Dollar Value through Revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

March 17, 2010

Term End:

Open

Nature and Scope of Work:

Turbine Digital Upgrade

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PQ # 130272

Major Task or Tasks Associated With:

Electro-Hydraulic Fluid Systems

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Dollar Value through Rev 4 is: [REDACTED]

Contract Status:

Active

Term Begin:

April 8, 2010

Term End:

Open

Nature and Scope of Work:

Electro-Hydraulic Fluid Systems

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO # 131928

Major Task or Tasks Associated With:

Pre-planning SL2-19

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Complete

Term Begin:

June 14, 2010

Term End:

February 28, 2011

Nature and Scope of Work:

SL2-19 Pre-planning work to support station milestones for the Turbine Generator Installation

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO # 131533

Major Task or Tasks Associated With:

Non-Fuels NSSS Interim LAR (PSL 1 & 2)

Vendor Identity:

Areva

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Predetermined Source

Dollar Value:

Total Contract Value through revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

June 10, 2010

Term End:

Open

Nature and Scope of Work:

Non-Fuels NSSS Interim LAR (PSL 1 & 2)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO # 131907

Major Task or Tasks Associated With:

Fuels Related Interim LAR/MOD for EPU at PSL

Vendor Identity:

Areva

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Predetermined Source

Dollar Value:

Total Contract Value through Revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

June 11, 2010

Term End:

Open

Nature and Scope of Work:

Fuels Related Interim LAR/MOD for EPU at PSL

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO # 131585

Major Task or Tasks Associated With:

Interim LAR/MOD for EPU at PSL

Vendor Identity:

Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Predetermined Source

Dollar Value:

Total Contract Value through Revision 4 is [REDACTED]

Contract Status:

Active

Term Begin:

June 15, 2010

Term End:

Open

Nature and Scope of Work:

Interim LAR/MOD for EPU at PSL

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO #131742

Major Task or Tasks Associated With:

LAR/Request for Additional Information

Vendor Identity:

Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Predetermined Source

Dollar Value:

Total Contract value through revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

June 16, 2010

Term End:

Open

Nature and Scope of Work:

LAR/Request for Additional Information for Non-Fuels related scope

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO #131940

Major Task or Tasks Associated With:

Main Steam Turbine Control Replacement

Vendor Identity:

Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

4

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Max Contract value through Rev 2 to Release 0

Contract Status:

Active

Term Begin:

June 30, 2010

Term End:

Open

Nature and Scope of Work:

Main Steam Turbine Control Replacement

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:
PTN PO #2259675

Major Task or Tasks Associated With:
Furnish New Spent Fuel Pool Heat Exchangers

Vendor Identity:
Joseph Oat Corporation

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
2

Number of Bids Received:
2

Brief Description of Selection Process:
Competitive

Dollar Value:
[REDACTED]

Contract Status:
Active

Term Begin:
July 23, 2010

Term End:
Open

Nature and Scope of Work:
Furnish New Spent Fuel Pool Heat Exchangers

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 2259669

Major Task or Tasks Associated With:

Rewind/Refurbish Upgrade Condensate Pumps

Vendor Identity:

Tampa Armature Works

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

August 2, 2010

Term End:

Open

Nature and Scope of Work:

Rewind/Refurbish Upgrade Condensate Pumps

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO #2260113

Major Task or Tasks Associated With:

PSL Rod Control System Upgrades

Vendor Identity:

Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Contract Value through Amendment 3 [REDACTED]

Contract Status:

Active

Term Begin:

September 23, 2010

Term End:

Open

Nature and Scope of Work:

PSL Rod Control System Upgrades

Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO #2261747

Major Task or Tasks Associated With:

EPU NSSS Engineering and Modification Support

Vendor Identity:

Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Predetermined Source

Dollar Value:

Total Contract Value through Amendment 2

Contract Status:

Active

Term Begin:

September 23, 2010

Term End:

Open

Nature and Scope of Work:

EPU NSSS Engineering and Modification Support

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO #2264240

Major Task or Tasks Associated With:

PSL 2-19 Turbine Generator Installation Contract

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

November 17, 2010

Term End:

Open

Nature and Scope of Work:

PSL 2-19 Turbine Generator Installation Contract

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO #2264841

Major Task or Tasks Associated With:

SL 2-19 Technical Support

Vendor Identity:

Batsch Industries

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Contract Value through Amendment 2 [REDACTED]

Contract Status:

Active

Term Begin:

November 30, 2010

Term End:

Open

Nature and Scope of Work:

SL 2-19 Technical Support

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

2264914

Major Task or Tasks Associated With:

CEDMS Power Switch Refurbishment (PSL 2)

Vendor Identity:

Westinhouse Electric

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 7, 2010

Term End:

Open

Nature and Scope of Work:

CEDMS Power Switch Refurbishment (PSL 2)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO #2285418

Major Task or Tasks Associated With:

Implementation Spares for Turbine Generator Work

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1


Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Contract Value through Amendment 2 

Contract Status:

Active

Term Begin:

December 16, 2010

Term End:

Open

Nature and Scope of Work:

Implementation Spares for Turbine Generator Work

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO #2285720

Major Task or Tasks Associated With:

Licensing/Design Basis/Program Modification

Vendor Identity:

Enercon

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

2

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

January 4, 2011

Term End:

Open

Nature and Scope of Work:

Licensing/Design Basis/Program Modification

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO# 2291203

Major Task or Tasks Associated With:

Main Steam Isolation Valve Replacement Actuator

Vendor Identity:

Enertech

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

2

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Contract Value through Amendment 3 [REDACTED]

Contract Status:

Active

Term Begin:

April 21, 2011

Term End:

Open

Nature and Scope of Work:

Main Steam Isolation Valve Replacement Actuator

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO# 2290465

Major Task or Tasks Associated With:

Design, Engineering and Fabrication of Turbine Crossover piping

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

March 31, 2011

Term End:

Open

Nature and Scope of Work:

Design, Engineering and Fabrication of Turbine Crossover piping

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO# 2290614

Major Task or Tasks Associated With:

Main Feedwater Pump Casing Modifications

Vendor Identity:

Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

N/A

Number of Bids Received:

N/A

Brief Description of Selection Process:

Replaces PO 130649

Dollar Value:

Total Contract Value through Amend 1 [REDACTED]

Contract Status:

Active

Term Begin:

May 2, 2011

Term End:

Open

Nature and Scope of Work:

Main Feedwater Pump Casing Modifications

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO# 2293850

Major Task or Tasks Associated With:

Turbine Generator Pre-Outage Planning PTN 3 & 4

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Contract value through Amendment \$ [REDACTED]

Contract Status:

Active

Term Begin:

June 24, 2011

Term End:

Open

Nature and Scope of Work:

Turbine Generator Pre-Outage Planning PTN 3 & 4

(Turbine Generator Installation)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO# 2295186

Major Task or Tasks Associated With:

Metamix Chevrans for Spent Fuel Pool

Vendor Identity:

Holtec

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

August 2, 2011

Term End:

Open

Nature and Scope of Work:

Metamix Chevrans for Spent Fuel Pool

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO# 2296556

Major Task or Tasks Associated With:

Modification, overhaul and refurbishment of the B and C AFW

Vendor Identity:

Sulzer Pumps

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

September 2, 2011

Term End:

Open

Nature and Scope of Work:

Modification, overhaul and refurbishment of the B and C AFW

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO# 2298406

Major Task or Tasks Associated With:

Fuel Movers for Metamic Inserts

Vendor Identity:

Master Lee Energy Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

1

Brief Description of Selection Process:

Competitive

Dollar Value:

1 [REDACTED]

Contract Status:

Active

Term Begin:

October 12, 2011

Term End:

Open

Nature and Scope of Work:

Fuel Movers for Metamic Inserts

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO# 2297556

Major Task or Tasks Associated With:

Siemens Installation of 2A Main Power Transformer

Vendor Identity:

Siemens Energy Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

September 27, 2011

Term End:

Open

Nature and Scope of Work:

Siemens Installation of 2A Main Power Transformer

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO# 2295953

Major Task or Tasks Associated With:

Misc Safety Related Wire and Cable

Vendor Identity:

Marron Wire & Cable

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Contract Value through revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

August 24, 2011

Term End:

Open

Nature and Scope of Work:

Misc Safety Related Wire and Cable

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:
PSL PO# 2297055

Major Task or Tasks Associated With:
Replacement Unit 2 LP #4 Feedwater Heaters for EPU

Vendor Identity:
Thermal Engineering

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:
Single Source

Dollar Value:

Contract Status:
Active

Term Begin:
September 16, 2011

Term End:
Open

Nature and Scope of Work:
Replacement Unit 2 LP #4 Feedwater Heaters for EPU

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO# 2300139

Major Task or Tasks Associated With:

SL 1-24 Turbine Generator Installation

Vendor Identity:

Siemens Energy Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

September 16, 2011

Term End:

Open

Nature and Scope of Work:

SL 1-24 Turbine Generator Installation

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO# 2299624

Major Task or Tasks Associated With:

Upgrade Services for Feedwater Pumps

Vendor Identity:

Ames Group LLC

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Contract Value through revision 1 [REDACTED]

Contract Status:

Active

Term Begin:

November 16, 2011

Term End:

Open

Nature and Scope of Work:

Upgrade Services for Feedwater Pumps

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO# 2300487

Major Task or Tasks Associated With:

Construction Management Oversight Services for SL1-24

Vendor Identity:

Weldtech Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

November 28, 2011

Term End:

Open

Nature and Scope of Work:

Construction Management Oversight Services for SL1-24

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

NF-10-358 and NF-11-178

Major Task or Tasks Associated With:

Spent Fuel Criticality Safety Analysis Support (PTN)

Vendor Identity:

Westinhouse Electric

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

1 [REDACTED]

Contract Status:

Active

Term Begin:

November 2, 2010

Term End:

Open

Nature and Scope of Work:

Spent Fuel Criticality Safety Analysis Support (PTN)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO # 2301867

Major Task or Tasks Associated With:

Develop Engineering Change Packages for EPU at PTN

Vendor Identity:

Ensercon Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 28, 2011

Term End:

Open

Nature and Scope of Work:

Develop Engineering Change Packages for EPU at PTN

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PQ # 2261800

Major Task or Tasks Associated With:

Supply of Simulator SCD Software Translator Upgrade

Vendor Identity:

L 3 Communications Mapps Inc

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Contract Value through Amendment 2 [REDACTED]

Contract Status:

Active

Term Begin:

September 28, 2010

Term End:

Open

Nature and Scope of Work:

Supply of Simulator SCD Software Translator Upgrade

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 2301737

Major Task or Tasks Associated With:

Construction Management Oversight Services for PTN

Vendor Identity:

PSI Energy Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 21, 2011

Term End:

Open

Nature and Scope of Work:

Construction Management Oversight Services for PTN

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO # 2301736

Major Task or Tasks Associated With:

Construction Management Oversight Services

Vendor Identity:

Weldtech Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 21, 2011

Term End:

Open

Nature and Scope of Work:

Construction Management Oversight Services

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO #2301871

Major Task or Tasks Associated With:

Develop Engineering Changes Packages for EPU at PTN

Vendor Identity:

Zachry Nuclear Engineering

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 28, 2011

Term End:

Open

Nature and Scope of Work:

Develop Engineering Changes Packages for EPU at PTN

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO #2301858

Major Task or Tasks Associated With:

Develop TPCW Changes Packages for EPU at PTN

Vendor Identity:

Sargent & Lundy

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 28, 2011

Term End:

Open

Nature and Scope of Work:

Develop TPCW Changes Packages for EPU at PTN



Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed

Schedule T-7A

[Section (8)(c)]

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company


DOCKET NO.: 120009-EI

EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and description of work.

For the Year Ended: 12/31/2011
Witness: Steven D. Scroggs

CONFIDENTIAL CONFIDENTIAL CONFIDENTIAL CONFIDENTIAL											
(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Actual amount expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
1	4500395492	Open- CO#38	11/6/2007- open	10/11/2011- open					Bechtel Power Corp	Comp Bid/ Single Source/ Predetermined Source	Engineering Services to Support Preparation of COLA and SCA and Response to post-submittal RA's.
2	4500404639	Open- CO#5	1/31/2008- open	4/21/2011- open					Westinghouse Electric Co	Sole Source/ Predetermined Source	Engineering Services to Support Preparation of COLA and Response to post-submittal RA's.
3	4500425707	Open-CO#5	5/23/2008- open	1/3/2011- open					HDR Engineering, Inc.	Comp Bid/ Single Source	Conceptual Engineering of Cooling Water Supply and Discharge
4	4500430034	Open- CO#1	6/16/2006- open	1/28/2011- open					Electric Power Research Institute	Single Source	Advanced Nuclear Technology; Near term deployment of Advanced Light Water Reactors
5	4500443122	Open-CO#3	8/6/2008- open	11/29/2011- open					Eco Metrics, Inc.	Single Source	Environmental Consulting Services
6	4500517152	Open-CO#3	7/10/2009- open	12/17/2010- open					McNabb Hydrogeologic Consulting Inc	Single Source	Turkey Point 6&7 Post SCA Submittal and UIC Licensing Support
7	4500518160	Open-CO#5	7/23/2009- open	6/24/2011- open					Golder Associates Inc	Single Source	Turkey Point 6&7 Post SCA Submittal Support
8	4500518167	Open- CO#6	7/23/2009- open	9/14/2011- open					Environmental Consulting and Technology Inc	Single Source/ Predetermined Source	Turkey Point 6&7 SCA Support
9	4500536449	Open-CO#2	10/12/2009- open	11/29/2011- open					McNabb Hydrogeologic Consulting Inc	Comp Bid/ Single Source	Turkey Point 6&7 UIC Subject Matter Expert Support
10	4500492222	Open-CO#2	3/17/2009- open	12/22/2011- open					Experts US LLC (F&KA, Jefferson Wells International)	Comp Bid/ Single Source	New Nuclear Audit
11	4500587305	Open-CO#1	5/29/2010- open	9/1/2010- open					Dickerson Florida Inc	Comp Bid	Turkey Point 6&7 Exploratory/UIC Well Site Development
12	4500652043	Open-CO#1	3/3/2011- open	12/29/2011- open					Layne Christensen Company	Comp Bid	Turkey Point 6&7 Exploratory/UIC Well and Dual Zone Monitor Well Installation

A B C D

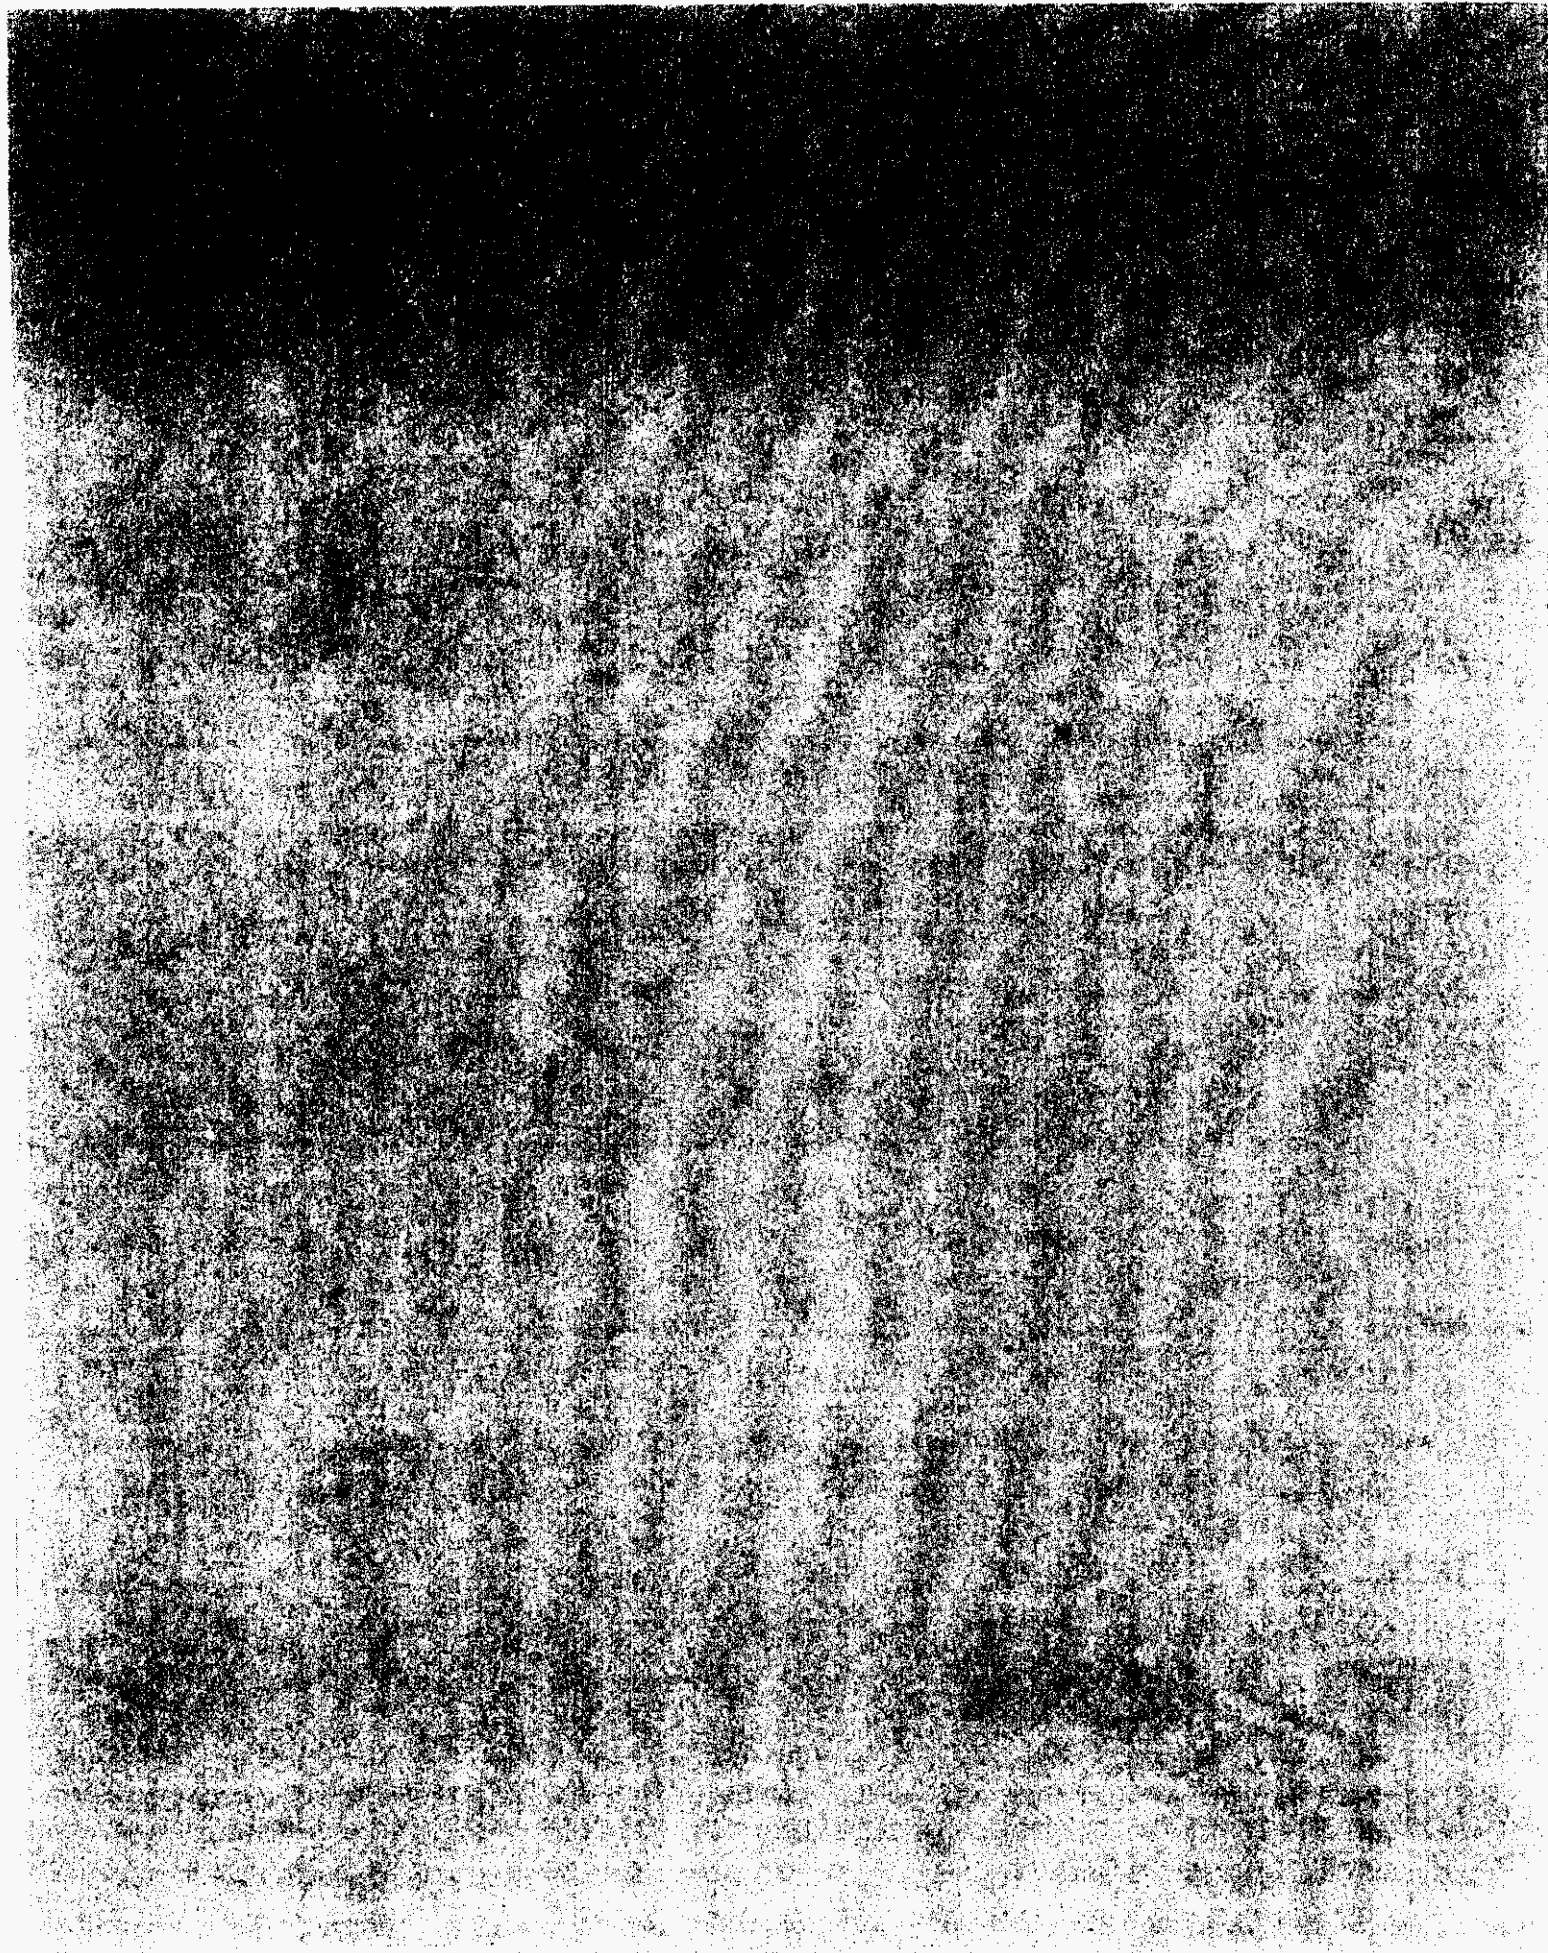

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:
4500395492

Major Task or Tasks Associated With:
COLA and SCA preparation and support

Vendor Identity:
Bechtel Power Corporation

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
Two

Number of Bids Received:
Two

Brief Description of Selection Process:
Initial contract competitively bid; change orders #01-#11
issued single source; all subsequent change orders
issued Predetermined Source

Dollar Value:

1

Contract Status:
Active- CO#38

Term Begin:
11/6/2007

Term End:
2/27/2016

Nature and Scope of Work:
Engineering Services to Support Preparation of COLA
and SCA, including post-submittal support for RAI
responses.

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: Florida Power & Light Company
DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:
4500404639

Major Task or Tasks Associated With:
COLA support

Vendor Identity:
Westinghouse Electric Company

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
One

Number of Bids Received:
One

Brief Description of Selection Process:
Sole source justification; designated as Predetermined
Source March 2009

Dollar Value:
1 [REDACTED]

Contract Status:
Active- CO#6

Term Begin:
1/31/2008

Term End:
6/29/2014

Nature and Scope of Work:
Engineering Services to Support Preparation of COLA,
including post-submittal support for RAI responses.

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: Florida Power & Light Company
DOCKET NO.: 120009-El

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:
4500430034

Major Task or Tasks Associated With:
COLA and SCA preparation and support

Vendor Identity:
Electric Power Research Institute

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
Two

Number of Bids Received:
Two

Brief Description of Selection Process:
Single

Dollar Value:

1

Contract Status:
Active- CO#1

Term Begin:
6/16/2008

Term End:
6/29/2014

Nature and Scope of Work:
Engineering Services to Support Preparation of COLA and SCA, including post-submittal support for RAI responses.

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:

4500518160

Major Task or Tasks Associated With:

Post SCA Submittal support

Vendor Identity:

Golder Associates, Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct or indirect relationship with the vendor

Number of Vendors Solicited:

One

Number of Bids Received:

One

Brief Description of Selection Process:

Single source; Designated as Predetermined Source February 2010

Dollar Value:

1

Contract Status:

Active- CO#5

Term Begin:

7/23/2009

Term End:

6/28/2012

Nature and Scope of Work:

Post SCA Submittal support

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: Florida Power & Light Company
DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:
4500518167

Major Task or Tasks Associated With:
SCA Support

Vendor Identity:
Environmental Consulting and Technology, Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
One

Number of Bids Received:
One

Brief Description of Selection Process:
Single source; Designated as Predetermined Source December 2009

Dollar Value:
1 [REDACTED]

Contract Status:
Active- CO#6

Term Begin:
7/23/2009

Term End:
6/28/2012

Nature and Scope of Work:
SCA Support

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (B)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: Florida Power & Light Company
DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:
4500536449

Major Task or Tasks Associated With:
Turkey Point 6&7 UIC Subject Matter Expert Support

Vendor Identity:
McNabb Hydrogeologic Consulting

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
One

Number of Bids Received:
One

Brief Description of Selection Process:
Competitive Bid for initial Order, Single Source justification for Change Orders

Dollar Value:

1

Contract Status:
Active- CO#2

Term Begin:
10/12/2009

Term End:
6/29/2013

Nature and Scope of Work:
Turkey Point 6&7 UIC Subject Matter Expert Support

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: Florida Power & Light Company
DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:
4500587305

Major Task or Tasks Associated With:
Turkey Point Units 6&7 Exploratory/UIC Well Site Development

Vendor Identity:
Dickerson Florida, Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
Eight

Number of Bids Received:
Five

Brief Description of Selection Process:
Competitive Bid

Dollar Value:

1

Contract Status:
Active- CO#1

Term Begin:
6/29/2010

Term End:
6/30/2011

Nature and Scope of Work:
Turkey Point Units 6&7 Exploratory/UIC Well Site Development

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: Florida Power & Light Company
DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:
4500652043

Major Task or Tasks Associated With:
Turkey Point 6&7 Exploratory/UIC Well and Dual Zone Monitor Well Installation

Vendor Identity:
Layne Christensen Company

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
Three

Number of Bids Received:
Three

Brief Description of Selection Process:
Competitive Bid

Dollar Value:

1


Contract Status:
Active- CO#1

Term Begin:
3/3/2011

Term End:
9/27/2012

Nature and Scope of Work:
Turkey Point 6&7 Exploratory/UIC Well and Dual Zone Monitor Well Installation

EXHIBIT B

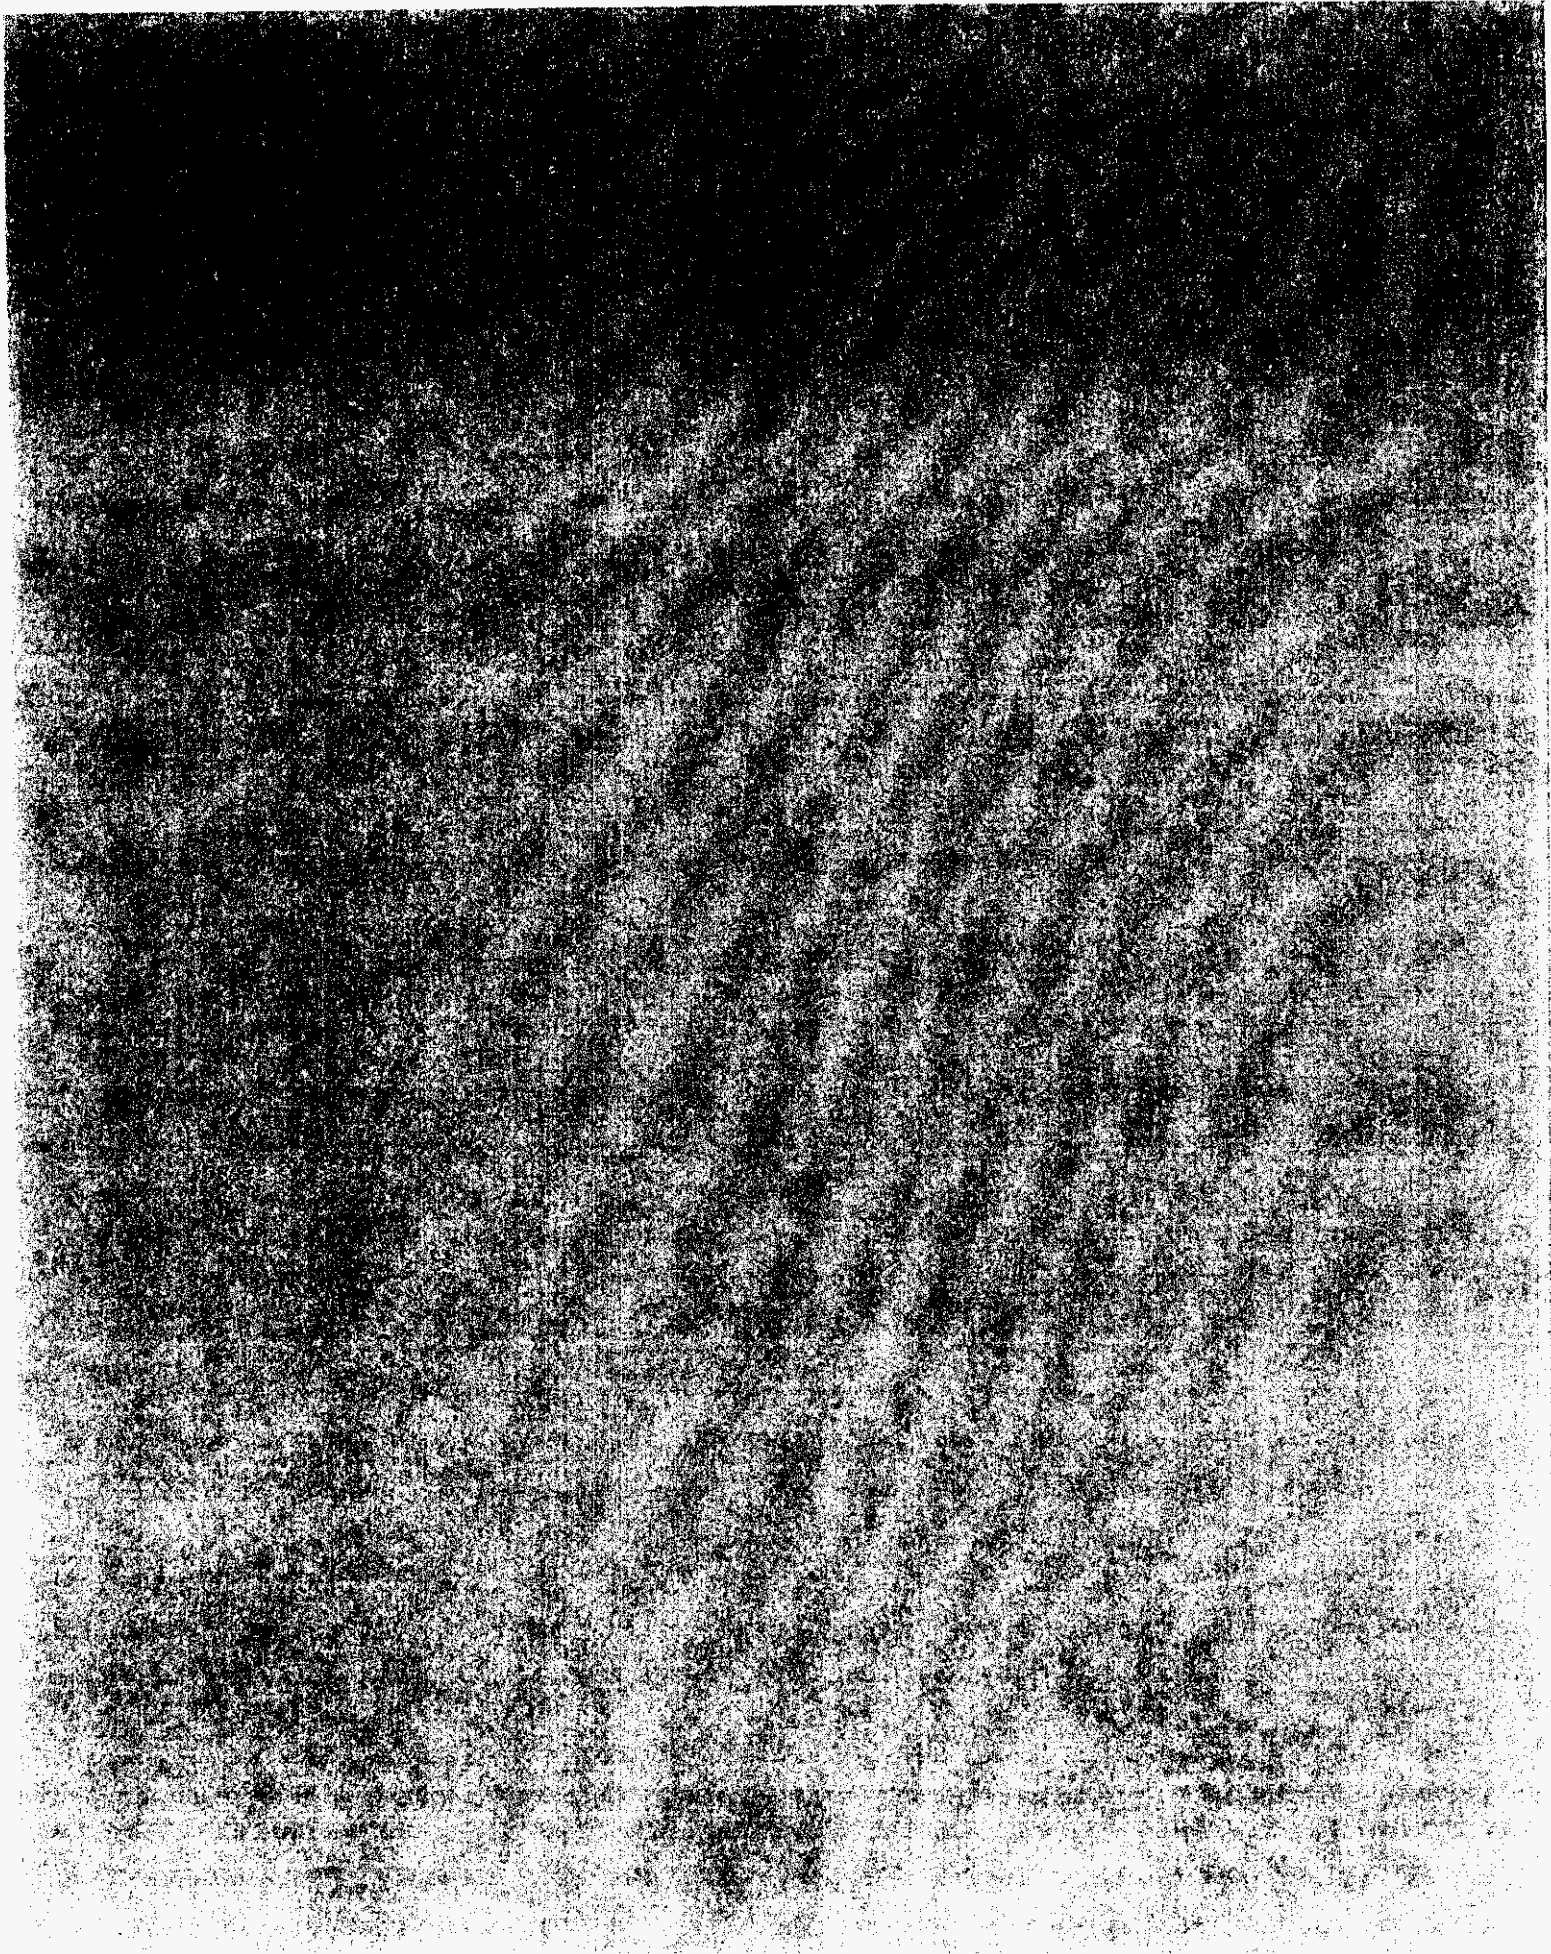

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO. 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

(A)		(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
1	121869	Open	4/29/09 - open	4/29/09 - open					AAF MCQUAY	Competitive	Supply Normal Containment Coolers and Testing Services (PTN)
2	120769	Open	3/26/09 - open	3/26/09 - open					Calvert Company Inc	Competitive	Iso Phase Bus Duct Coolers and Testing Services (PSL)
3	124438	Open	7/17/09 - open	7/17/09 - open					Calvert Company Inc	Competitive	Iso Phase Bus Duct Coolers, Install, Demo & Testing Services (PTN)
4	121985	Open	4/24/09 - open	4/24/09 - open					Flowserve Corp.	Competitive	Replacement Main Feedwater Pumps & Various Testing (PSL)
5	123137	Open	5/28/09 - open	5/28/09 - open					Flowserve Corp.	Competitive	Main Feedwater Isolation Valves and Testing Services (PTN)
6	125454	Open	8/28/09 - open	8/28/09 - open					Flowserve Corp.	Competitive	Replacement Heater Drain Pumps (PSL)
7	122154	Complete	4/27/09 - 6/15/11	4/27/09 - 6/15/11					Siemens Energy Inc.	Competitive	Step-Up Transformer (PTN)
8	119078	Open	12/9/08 - open	12/9/08 - open					Westinghouse	OEM	NSSS Engineering Analysis and LAR (PTN)
9	119653	Open	11/24/08 - open	11/24/08 - open					Westinghouse	OEM	NSSS Engineering Analysis and LAR (PSL)
10	121947	Open	4/24/09 - open	4/24/09 - open					Westinghouse	OEM	New & Spent Fuel Critically and Thermal Hydraulic Analysis (PTN)
11	119670	Open	2/18/09 - open	2/18/09 - open					Proto-Power	Single Source	Project Engineering Support (PSL)
12	115297	Open	8/27/08 - open	8/27/08 - open					Areva	Single Source	RSG Design Review and LAR Work (PSL)
13	115338	Open	8/27/08 - open	8/27/08 - open					Areva	Single Source	RCS Design Review (PTN)
14	105353	Complete	10/02/07 - 12/01/11	10/02/07 - 12/01/11					Shaw - Stone & Webster	Sole Source	Engineering Support (PSL & PTN)
15	117808	Open	12/02/08 - open	12/02/08 - open					Bechtel	Competitive Bid	Engineering Procurement Construction (PTN)
16	116088	Open	09/29/08 - open	09/29/08 - open					Siemens	Single Source	Low Pressure Turbine, Exciter, Exciter Inst. (PSL)
17	117820	Open	12/02/08 - open	12/02/08 - open					Bechtel	Competitive Bid	Engineering Procurement Construction (PSL)
18	116090	Open	9/29/08 - open	9/29/08 - open					Siemens	Single Source	Turbine, Generator/Exciter Upgrades & Inst. (PTN)
19	118328	Open	12/19/08 - open	12/19/08 - open					TEI	Competitive Bid	Condenser Tubes (PTN)
20	118205	Open	12/17/08 - open	12/17/08 - open					TEI	Competitive Bid	Moisture Separator Reheaters (PTN)
21	118205	Open	12/17/08 - open	12/17/08 - open					TEI	Competitive Bid	Moisture Separator Reheaters (PSL)
22	118241	Open	12/19/08 - open	12/19/08 - open					TEI	Competitive Bid	Feed Water Heaters (PTN)
23	112221	Open	4/22/08 - open	4/22/08 - open					Shaw - Stone & Webster	Single Source	Licensing Engineering and BOP Spec Development (PSL)
24	112177	Open	4/22/08 - open	4/22/08 - open					Shaw - Stone & Webster	Single Source	Licensing Engineering and BOP Spec Development (PTN)

A B C D

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET # 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

	(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
25	117272	Open	11/13/08 - open	11/13/08 - open					American Crane	Single Source	Gantry Crane Upgrade (PSL)
26	118224	Open	12/17/08 - open	12/17/08 - open					TEi	Competitive Bid	Feed Water Heaters (PSL)
27	115455	Open	9/03/08 - open	9/03/08 - open					Proto-Power	Single Source	Engineering Services (PTN)
28	118278	Open	12/19/08 - open	12/19/08 - open					TEi	Competitive Bid	TCW Heat Exchangers (PSL)
29	105720	Open	9/12/07 - open	9/12/07 - open					AREVA	Single Source	Neutronics Analysis (PSL)
30	116796	Complete	10/29/08 - 12/22/11	10/29/08 - 12/22/11					Cameron	Single Source	Ultrasonic Flow Meter Measuring System (PTN)
31	116107	Open	9/29/08 - open	9/29/08 - open					Cameron	Single Source	Ultrasonic Flow Meter Measuring System (PSL)
32	114114	Open	7/03/08 - open	7/03/08 - open					Richard Sipos	Single Source	Staff Augmentation (PSL)
33	115036	Complete	8/14/08 - 1/06/11	8/14/08 - 01/06/11					Babcock & Wilcox	Single Source	Steam Generator Component Design Review (PSL)
34	112228	Complete	4/23/08 - 05/11/11	4/23/08 - 05/11/11					Westinghouse	Single Source	Steam Generator Services for Moisture Carryover (PTN)
35	113030	Open	5/20/08 - open	5/20/08 - open					FPL Seabrook	Single Source	FPLE personnel supporting FPL Upgrades (PSL & PTN)
36	115391	Open	8/29/08 - open	8/29/08 - open					NAI	Single Source	Radiological Consequence Analysis (PSL)
37	112987	Open	5/19/08 - open	5/19/08 - open					NAI	Single Source	Radiological Consequence Analysis (PTN)
38	4600521317	Open	9/08/09 - open	9/08/09 - open					Areva	Competitive	Inductors (PTN)
39	126248	Open	10/08/09 - open	10/08/09 - open					ABB	Competitive	Replacement Transformer Coolers (PSL)
40	126453	Open	11/05/09 - open	11/05/09 - open					Joseph Oat Corporation	Competitive	Cooling Water Heat Exchangers (PTN)
41	127777	Open	12/08/09 - open	12/08/09 - open					High Bridge	Single Source	Estimating Services (PTN)
42	127881	Open	12/22/09 - open	12/22/09 - open					Absolute Consulting	Single Source	Procedure Writers (PTN)
43	123762	Open	6/25/09 -open	6/25/09 -open					Key Controls of Tampa	OEM	Control System Tuning and Dynamic Analysis (PTN)
44	118988	Open	01/22/09 - open	01/22/09 - open					Holtec	Single Source	Fuel Storage Criticality and related analysis (PSL 2)
45	118563	Open	1/14/09 - open	1/14/09 - open					Holtec	Competitive	Fuel Storage Criticality and related analysis (PSL 1)
46	116627	Open	7/28/09 - open	7/28/09 - open					Western Services	Competitive	NSSS Simulator Reactor Core Model Upgrade (PSL)
47	118844	Open	01/15/09 - open	01/15/09 - open					Western Services	Competitive	NSSS Simulator Reactor Core Model Upgrade (PTN)
48	4500467077	Open	11/10/08 - open	11/10/08 - open					Siemens	Competitive	Generator Step-up Transformers (PSL)

A B C D

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO. 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

Line No.	(A) Contract No.	(B) Status of Contract	(C) Original Term of Contract	(D) Current Term of Contract	(E) Original Amount	(F) Actual Expended as of Prior Year End (2010)	(G) Amount Expended in Current Year (2011)	(H) Estimate of Final Contract Amount	(I) Name of Contractor (and Affiliation if any)	(J) Method of Selection and Document ID	(K) Work Description
49	130579	Open	5/01/10 - open	5/01/10 - open					Fisher Controls	Competitive	Modified Feedwater Regulating Valves/Actuators (PSL)
50	130160	Open	3/29/10 - open	3/29/10 - open					Flowserve Corp.	Competitive	Replacement Condensate Pumps (PSL)
51	130612	Open	4/22/10 - open	4/22/10 - open					Flowserve Corp.	Competitive	Condensate Pumps (PTN)
52	130649	Open	4/22/10 - open	4/22/10 - open					Flowserve Corp.	Competitive	Main Feedwater Pumps (PTN)
53	128227	Open	10/13/09 - open	10/13/09 - open					Invensys	OEM	Control System FWH, Moisture Separator (PTN)
54	129689	Open	3/17/10 - open	3/17/10 - open					Invensys	Competitive	Turbine Digital Upgrade (PTN)
55	130272	Open	4/08/10 - open	4/08/10 - open					Siemens Energy Inc.	Competitive	Electro-Hydraulic Fluid Systems (PTN)
56	131356	Open	5/21/10 - open	5/21/10 - open					Brand Energy Solutions	Competitive	Supply Scaffolding Material (PTN)
57	131391	Complete	5/25/10 - 4/19/11	5/25/10 - 4/19/11					BRV Construction	Competitive	Design/Construct fabrication area inside the CSF (PTN)
58	131599	Open	5/27/10 - open	5/27/10 - open					All Star Toleits	Competitive	Supply Cleaning Services (PTN)
59	4500586420	Open	6/16/10 - open	6/16/10 - open					Energy Erectors	Competitive	Electrical contract labor work @ 230 KV substation (PTN)
60	131928	Complete	6/14/10 - 02/28/11	6/14/10 - 02/28/11					Siemens Energy Inc.	Single Source	SL2-19 Pre-planning TG Installation Work (PSL2)
61	131533	Open	6/10/10 - open	6/10/10 - open					Areva	OEM	Non-Fuels NSSS Interim LAR (PSL 1 & 2)
62	131807	Open	6/11/10 - open	6/11/10 - open					Areva	OEM	Fuels Related Interim LAR/MOD for EPU (PSL)
63	131595	Open	6/15/10 - open	6/15/10 - open					Shaw - Stone & Webster	PDS	Interim LAR/MOD Support for EPU (PSL)
64	131393	Open	6/10/10 - open	6/10/10 - open					Fisher Controls	Competitive	Heater Drain BOP Replacement Valves (PSL)
65	131742	Open	6/16/10 - open	6/16/10 - open					Westinghouse	PDS	LAR/RAI for Non-Fuels NSSS related scope (PSL)
66	132077	Open	6/17/10 - open	6/17/10 - open					Siemens Energy Inc.	Single Source	Siemens Dedicated Resident Site Manager (PTN)
67	132078	Open	6/17/10 - open	6/17/10 - open					Siemens Energy Inc.	Single Source	Siemens Dedicated Resident Site Manager (PSL)
68	132235	Open	6/24/10 - open	6/24/10 - open					Enercon	Single Source	NFPA 805/Appendix R Support for (PTN)
69	131987	Open	6/25/10 - open	6/25/10 - open					Sargent & Lundy Inc	Single Source	Engineering for Steam Bypass Control (PSL1)
70	131940	Open	6/30/10 - open	6/30/10 - open					Westinghouse	Competitive	Main Steam Turbine Control Replacement (PSL)
71	132283	Open	6/28/10 - open	6/28/10 - open					Shaw - Stone & Webster	PDS	EPU Feedwater Pump Nozzle Load Reduction (PSL)
72	2259675	Open	7/23/10 - open	7/23/10 - open					Joseph Oat Corporation	Competitive	Furnish New Spent Fuel Pool Heat Exchangers (PTN)

A B C D

Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO: 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
 Witness: T. O. Jones

	(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
73	2259669	Open	8/02/10 - open	8/02/10 - open					TAW	Competitive	Rewind/Refurbish/Upgrade Condensate Pumps (PTN)
74	2259997	Open	8/4/10 - open	8/4/10 - open					SPX Corporation	Replaces 115351	Valve Rework (PTN)
75	2259768	Open	8/06/10 - open	8/06/10 - open					Westinghouse	OEM	Design basis support for Umbrella Mods (PTN)
76	2260155	Open	8/16/10 - open	8/16/10 - open					Siemens Energy Inc.	Single Source	PSL 1-24 Pre-planning TG Installation Work
77	2260113	Open	9/23/10 - open	9/23/10 - open					Westinghouse	OEM	Rod Control System Upgrades (PSL)
78	2261536	Open	9/16/10 - open	9/16/10 - open					Washington Group	Competitive	Feedwater Heater Ultrasonic Testing (PTN)
79	2261750	Open	9/21/10 - open	9/21/10 - open					Modular Space	Competitive	Lease of 15-Wide Trailers for EPU (PTN)
80	2261747	Open	9/23/10 - open	9/23/10 - open					Westinghouse	POS	EPU NSSS Engineering and Modification Support (PTN)
81	2262094	Open	9/26/10 - open	9/26/10 - open					Structural Integrity	Competitive	Assessment of Min Wall Thickness Effects (PTN)
82	2262201	Open	9/30/10 - open	9/30/10 - open					Fisher Controls	Replaces 131395	Heater Drain BOP Replacement Valves (PSL)
83	2262367	Open	10/04/10 - open	10/04/10 - open					Techcom International	Competitive	Engineering Services for Various Distributing Mods (PTN)
84	2262515	Open	10/06/10 - open	10/06/10 - open					Fisher Controls	Replaces 130579	Modified Feedwater Regulating Valves/Actuators (PSL)
85	2263036	Open	10/19/10 - open	10/19/10 - open					Flowsolve Corp.	Replaces 130160	Replacement Condensate Pumps (PSL)
86	2264196	Complete	11/16/10 - 4/20/11	11/16/10 - 4/20/11					Siemens Energy Inc.	OEM	Replacement Blade Rings (PSL)
87	2264240	Open	11/17/10 - open	11/17/10 - open					Siemens Energy Inc.	Single Source	T/G Installation SL2-19 Outage (PSL)
88	2263052	Open	11/11/10 - open	11/11/10 - open					Invensys	Single Source	Steam Bypass Control System (PSL)
89	2263549	Open	11/10/10 - open	11/10/10 - open					Areva NP Inc	Competitive	Services of a Project Manager (PTN)
90	2264548	Complete	11/19/10 - 03/28/11	11/19/10 - 03/28/11					Graybar Electric	Competitive	Wire Cable (PTN)
91	2263930	Open	11/11/10 - open	11/11/10 - open					Brand Energy Solutions	Replaces 131356	Supply Scaffolding Material (PTN)
92	2264842	Open	11/30/10 - open	11/30/10 - open					Ronnies Turbine Services Inc	Single Source	On Site SL2-19 Tech Support (PSL)
93	2264841	Open	11/30/10 - open	11/30/10 - open					Batsch Industries	Single Source	On Site SL2-19 Tech Support (PSL)
94	2264377	Open	11/30/10 - open	11/30/10 - open					Techcom International	Competitive	Turbine Digital Controls Verification and Validation (PTN)
95	2264914	Open	12/07/10 - open	12/07/10 - open					Westinghouse Electric	OEM	CEDMS Power Switch Refurbishment (PSL2)
96	2263861	Open	11/4/10 - open	11/4/10 - open					Graybar Electric	Competitive	Temporary Power Unit Substations for EPU (PTN)

A B C D

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO: 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
97	2285418	Open	12/16/10 - open	12/16/10 - open					Siemens Energy Inc.	OEM	Impl. Spares for EPU Turbine Gen. Work During SL2-19 (PSL)
98	4500589966	Open	7/6/10 - open	7/6/10 - open					Kennedy Construction	Competitive	Site preparation contract labor work @ 230 kV substation (PTN)
99	2285720	Open	01/4/11 - open	01/4/11 - open					Enercon Services	Competitive	Licensing/Design Basis/Program Modification (PTN)
100	2291203	Open	04/21/11 - open	04/21/11 - open					Enertech	Competitive	Main Steam Isolation Valve Replacement Actuator (PSL)
101	2287242	Open	01/27/11 - open	01/27/11 - open					Engineering Planning & Management	Competitive	Environmental Qualification Document (PTN)
102	2287468	Open	02/10/11 - open	02/10/11 - open					Feedforward Inc.	Competitive	DCS Mods (PSL)
103	2290206	Open	03/25/11 - open	03/25/11 - open					Feedforward Inc.	Competitive	Leading Edge Flow Meter Addition (PTN)
104	2287971	Open	02/15/11 - open	02/15/11 - open					Foster Wheeler North America	Competitive	SJAE Inter/After Condensers (PTN)
105	2290465	Open	03/31/11 - open	03/31/11 - open					Siemens	OEM	Design and Fabrication of Turbine Crossover piping (PTN)
106	2290463	Open	03/31/11 - open	03/31/11 - open					Siemens	OEM	Iron Bolts for Main Steam Generator Stator (PTN)
107	2290842	Open	04/08/11 - open	04/08/11 - open					Siemens	OEM	Blower Stationary Blade Rings (PSL)
108	2286521	Open	01/18/11 - open	01/18/11 - open					Stone & Webster	PDS	MSIV/MSCV Modification to Support EPU (PSL)
109	2264476	Open	05/11/11 - open	05/11/11 - open					Batsch Industries	Single Source	Turbine Generator Technical Support (PTN)
110	2291815	Open	04/28/11 - open	04/28/11 - open					BRV Construction	Competitive	Fossil Warehouse Demolition (PTN)
111	2290614	Open	05/02/11 - open	05/02/11 - open					Flowserve Corp.	Replaces 130649	Main Feedwater Pump Casing Modification (PTN)
112	2292773	Open	05/26/11 - open	05/26/11 - open					AAF MCQUAY	OEM	Design, Engineer, Fabricate and Deliver CRDM Coils (PTN)
113	2293950	Open	06/24/11 - 04/20/11	06/24/11 - 04/20/11					Siemens	Single Source	Turbine Generator Pre-outage planning activities (PTN)
114	2293663	Open	06/29/11 - open	06/29/11 - open					Thermal Engineering	Competitive	Design and Fabrication of Gland Steam Condensers (PTN)
115	2294247	Open	07/06/11 - open	07/06/11 - open					Ecological Associates	Competitive	Biological Plan of Study (PSL)
116	2294341	Open	07/11/11 - open	07/11/11 - open					Ailon	Single Source	GL2006-01 Support (PSL)
117	2294494	Open	07/13/11 - open	07/13/11 - open					Enercon Services	Competitive	Emergency Containment Cooler Auto-start (PTN)
118	2294221	Open	07/11/11 - open	07/11/11 - open					Flowserve Corp.	Competitive	Main Steam Isolation Replacement Valves (PSL)
119	2294855	Open	07/21/11 - open	07/21/11 - open					Zachary Nuclear Engineering	Single Source	Project Engineering Support for EPU (PSL)
120	2295186	Open	08/02/11 - open	08/02/11 - open					Holtec International	Single Source	Metamix Chevrans for Spent Fuel Pool (PSL)

A B C D

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO. 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended In Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
121	2295422	Open	8/10/11 - open	8/10/11 - open					Siemens Energy Inc.	OEM	Support Material for the EPU Turb-Gen Uprate (PTN)
122	2295071	Open	08/01/11 - open	08/01/11 - open					Stone & Webster	Single Source	Unit 1 Vibration and Support Mods for FW & Condensate (PSL)
123	2296049	Open	08/25/11 - open	08/25/11 - open					Cameron Tech.	Replaces 116796	Ultrasonic Flow Meter Measuring System (PTN)
124	2294671	Open	08/19/11 - open	08/19/11 - open					NWT Corporation	Competitive	Moisture Carry Over Testing for EPU (PTN)
125	2296556	Open	09/02/11 - open	09/02/11 - open					Sulzer Pumps	OEM	Modify, overhaul and refurbishment of the B & C AFW (PTN)
126	2296519	Open	09/06/11 - open	09/06/11 - open					Techcom International	Competitive	DCS Integration Plan for 3R26 and 4R27 (PTN)
127	2296623	Open	09/06/11 - open	09/06/11 - open					Tricon Technologies	Competitive	Unit 3 Condenser Tube Eddy Current Testing (PTN)
128	2296797	Open	09/09/11 - open	09/09/11 - open					Coastal Bus & Charter Lines (dba Need A Bus)	Competitive	Shuttle Bus Services for EPU (PSL)
129	2296330	Open	09/09/11 - open	09/09/11 - open					Flowserve Corp.	Competitive	Motor Operated Valves (PTN)
130	2298266	Open	10/12/11 - open	10/12/11 - open					Franmar Corporation	Competitive	Shuttle Bus Services for EPU (PTN)
131	2298406	Open	10/12/11 - open	10/12/11 - open					Master Lee Energy Services	Competitive	Fuel Movers for Metamix Inserts (PSL)
132	2296635	Open	10/14/11 - open	10/14/11 - open					Sargent & Lundy Inc.	Single Source	Engineering Service for the Charging System Modification (PSL 2)
133	2297556	Open	09/27/11 - open	09/27/11 - open					Siemens Energy Inc.	Single Source	Siemens Installation of 2A Main Power Transformer (PSL)
134	2299101	Open	10/27/11 - open	10/27/11 - open					Berkel & Company	Single Source	Mico Pile Construction (PTN)
135	2298894	Open	10/24/11 - open	10/24/11 - open					Day & Zimmermann NPS Inc	Competitive	Installation of Trailer Support Services (PTN)
136	2299350	Open	11/01/11 - open	11/01/11 - open					Enercon Services Inc	Competitive	Eng. Evaluation for EPU Mid-Cycle contingency plan (PSL)
137	2299618	Open	11/04/11 - open	11/04/11 - open					Radiation Safety & Control	Competitive	Truck Monitoring/Waste Characterization for EPU (PTN)
138	2297624	Open	10/27/11 - open	10/27/11 - open					Siemens Energy Inc.	OEM	Turbine Valve Conversion to EH (PTN)
139	2299631	Open	11/8/11 - open	11/8/11 - open					Tri-Tool Inc	Single Source	Unit 1 LP Turbine Extraction Line Services (PSL)
140	2295953	Open	08/24/11 - open	08/24/11 - open					Marron Wire & Cable	OEM	Misc Safety Related Wire and Cable, line items 1 - 23 (PTN)
141	2297055	Open	09/16/11 - open	09/16/11 - open					Thermal Engineering	Single Source	Replacement LP #4 Feedwater Heaters for EPU (PSL 2)
142	2300139	Open	11/21/11 - open	11/21/11 - open					Siemens Energy Inc	Single Source	SL1-24 Turb-Gen. Installation (PSL 1)
143	2298624	Open	11/16/11 - open	11/16/11 - open					Ames Group LLC	Single Source	Upgrade Services for Feedwater Pumps (PSL)
144	2300487	Open	11/28/11 - open	11/28/11 - open					Weldtech Services	Single Source	SL1-24 Construction Management Oversight Services (PSL 1)

A B C D

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO. 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

	(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended In Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation If any)	Method of Selection and Document ID	Work Description
145	2299618	Open	11/04/11 - open	11/04/11 - open					Radiation Safety & Control	Competitive	Truck Monitoring/Waste Characterization for EPU (PTN)
146	2299350	Open	11/01/11 - open	11/01/11 - open					Enercon Services	Competitive	Engineering evaluation for EPU mid-cycle contingency plan (PSL)
147	2299631	Open	11/08/11 - open	11/08/11 - open					Tri-Tool	Single Source	LP Turbine Extraction Line Services for EPU (PSL 1)
148	NF-10-358 NF-11-178	Open	11/2/10 - open	11/2/10 - open					Westinghouse Electric	OEM	Spent Fuel Pool Criticality Safety Analysis Support (PTN)
149	2301813	Open	12/28/11 - open	12/28/11 - open					Enercon Services Inc	Competitive	Motor Operated Valve Transfer Switches for EPU (PSL)
150	2301867	Open	12/28/11 - open	12/28/11 - open					Enercon Services Inc	Single Source	Develop Engineering Change Packages for EPU (PTN)
151	2301038	Open	12/14/11 - open	12/14/11 - open					Graftel Inc.	Competitive	Integrated Leak Rate Testing for EPU (PTN)
152	2261800	Open	09/28/10 - open	09/28/10 - open					3 Communications Mapps Inc	OEM	Supply of Simulator SCD Software Translator Upgrade (PTN)
153	130340	Open	04/02/10 - open	04/02/10 - open					MPR Associates	Competitive	Third Party Review of Siemens Turb-Gen. Analysis (PSL)
154	2301737	Open	12/21/11 - open	12/21/11 - open					PSI Energy Services	Single Source	Construction Management Oversight Services (PTN)
155	2301736	Open	12/21/11 - open	12/21/11 - open					Weidtech Services	Single Source	Construction Management Oversight Services (PTN)
156	2301871	Open	12/28/11 - open	12/28/11 - open					Zachry Nuclear Engineering	Single Source	Develop Engineering Change Packages for EPU (PTN)
157	2301858	Open	12/28/11 - open	12/28/11 - open					Sargent & Lundy Inc	Single Source	Develop TPCW Engineering Change Packages for EPU (PTN)
158	2000053226	Open	11/21/11 - open	11/21/11 - open					Ric-Man Construction	Competitive	Road and parking contract labor work 230kV substation (PTN)

A B C D

Legend:

PDS = Predetermined Source


OEM = Original Equipment Manufacturer

PSL = St. Lucie

PTN = Turkey Point

Notes:

In November 2011, FPL issued a Letter of Agreement (LOA) to Siemens for the PTN 3-26 Turbine Generator installation scope; however, the contract was not issued in 2011.

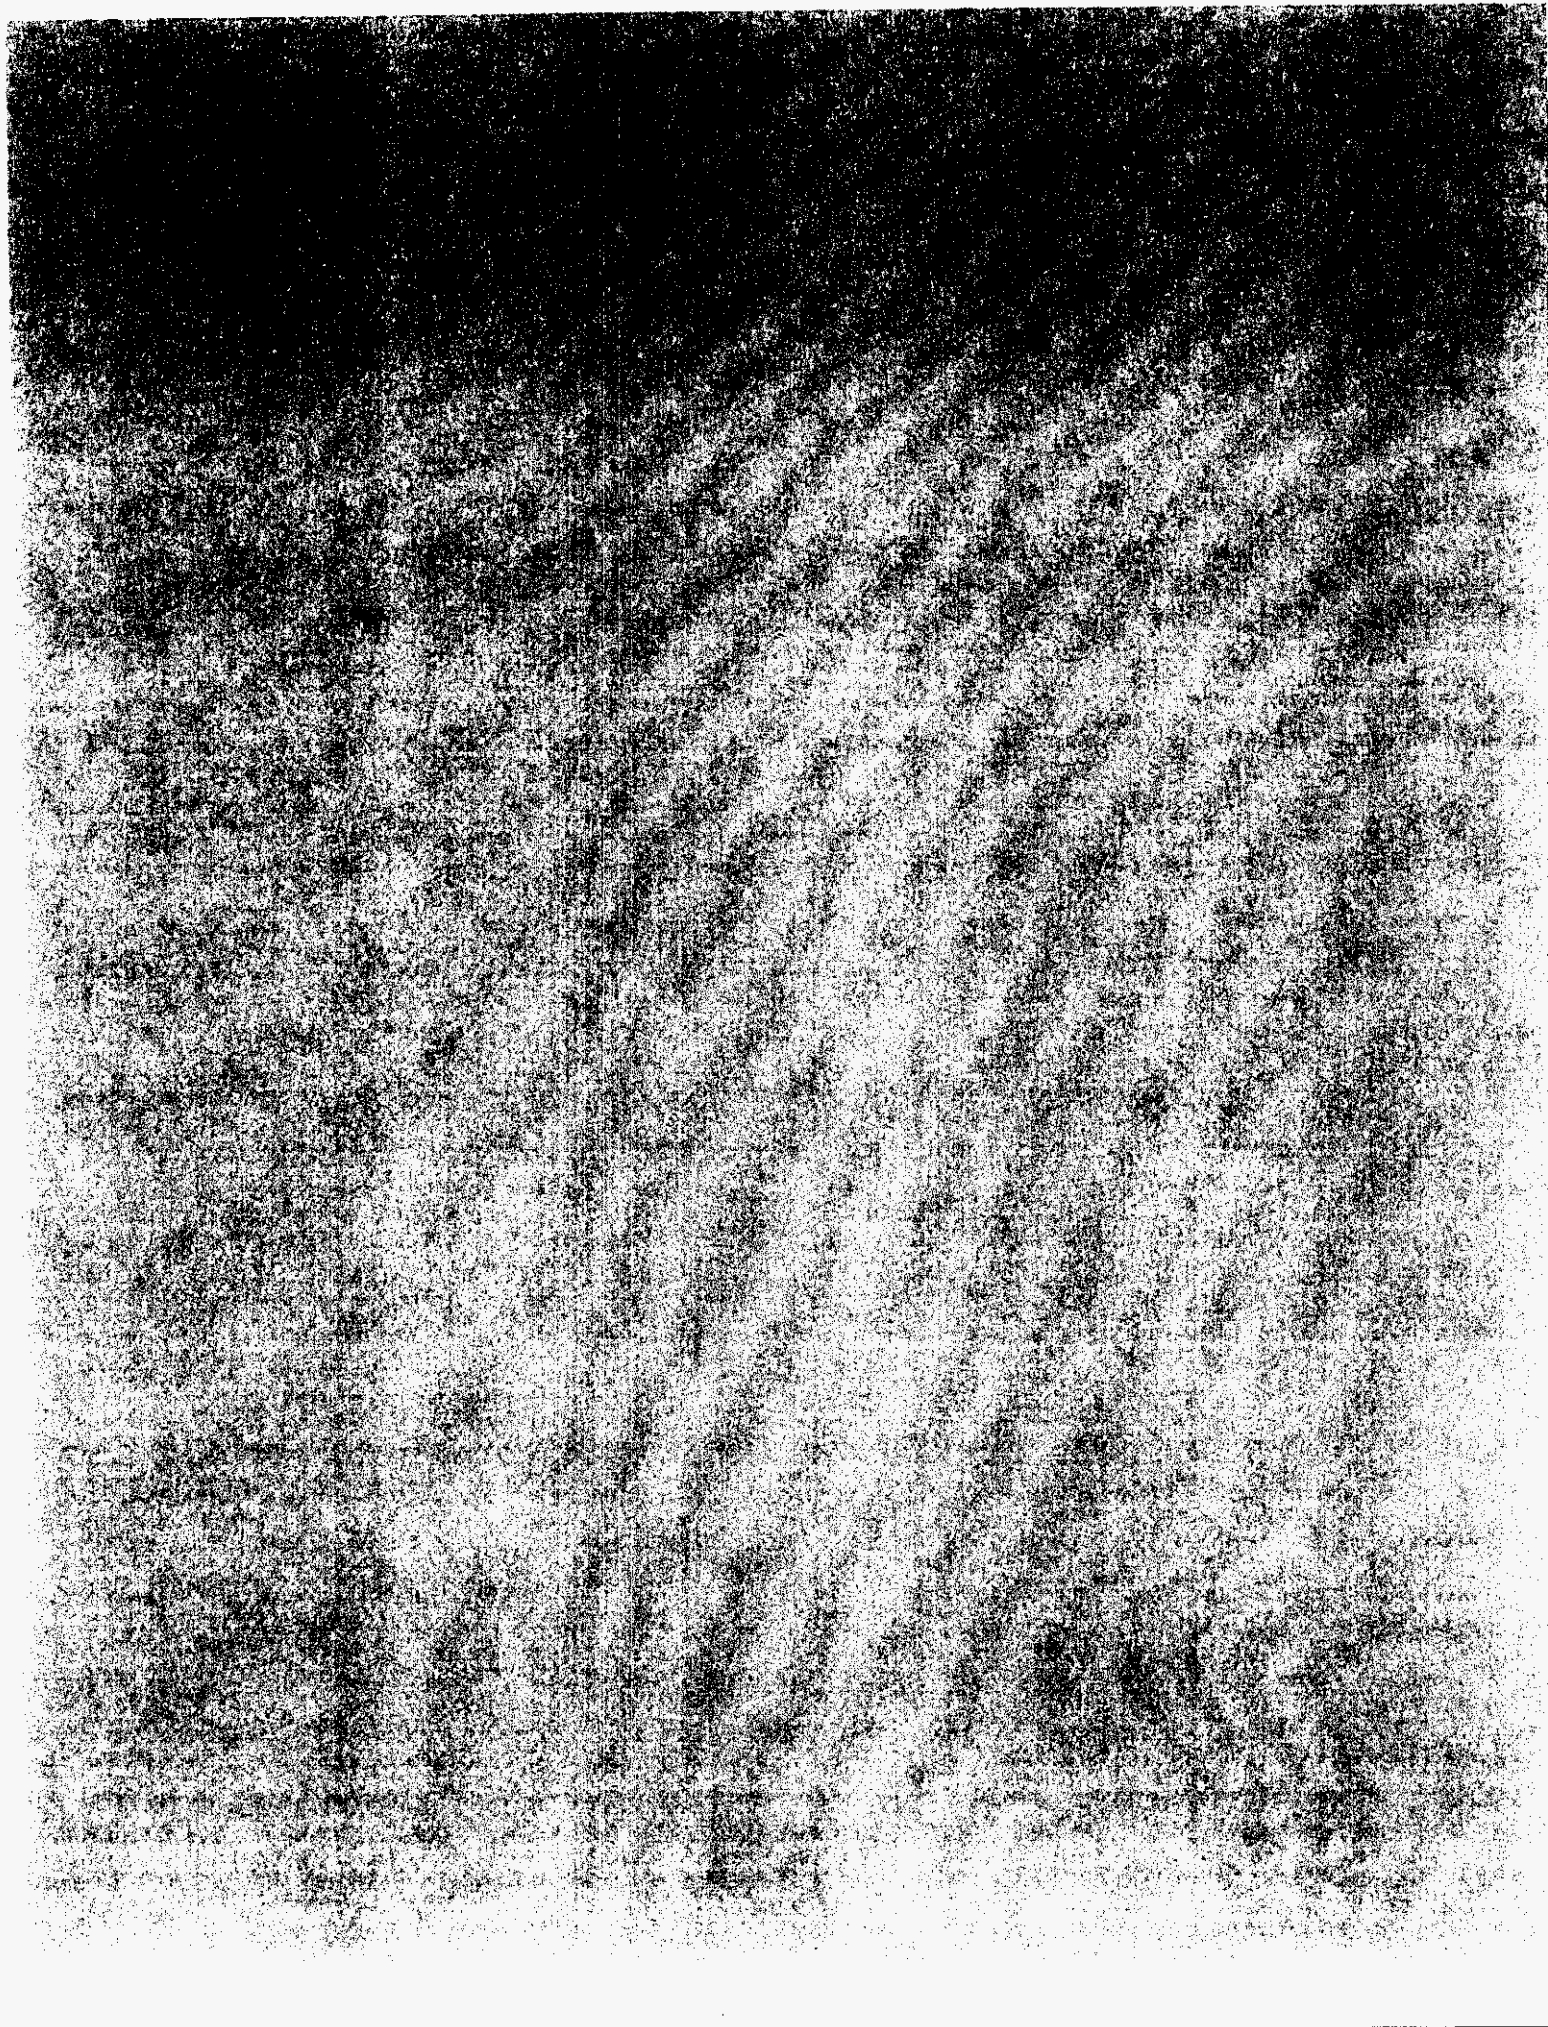

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO 121869

Major Task or Tasks Associated With:

Supply Eight (8) Normal Containment Coolers and provide Testing Services

Vendor Identity:

AAF MCQUAY

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to AAF McQuay.

Dollar Value:

Total Contract Value through Revision 3 is



Contract Status:

Active

Term Begin:

April 29, 2009

Term End:

March 2013

Nature and Scope of Work:

Supply Eight (8) Normal Containment Coolers and provide Testing Services

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO 120769

Major Task or Tasks Associated With:

Replacement IsoPhase Bus Duct Coolers

Vendor Identity:

Calvert Company Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

1

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Calvert Company Inc.

Dollar Value:

Total Dollar Value through Revision 2 is



Contract Status:

Active

Term Begin:

March 26, 2009

Term End:

June 2012

Nature and Scope of Work:

Replacement IsoPhase Bus Duct Coolers, Technical Installation Support and Field Testing.

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO 124436

Major Task or Tasks Associated With:

Replacement Isolated Phase BusDuct

Vendor Identity:

Calvert Company Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Calvert Company Inc.

Dollar Value:

Total Dollar Value through Revision 2 is



Contract Status:

Active

Term Begin:

July 17, 2009

Term End:

June 2012

Nature and Scope of Work:

Replacement Isolated Phase BusDuct, Demolition and Installation Services, Evaluation, Testing and Engineering

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO 121985

Major Task or Tasks Associated With:

Replacement Main Feedwater Pumps

Vendor Identity:

Flowserve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

5

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Flowserve Corp.

Dollar Value:

Total Dollar Value through Revision 3 is [REDACTED]

Contract Status:

Active

Term Begin:

April 24, 2009

Term End:

June 2012

Nature and Scope of Work:

Replacement Main Feedwater Pumps, spare parts and technical direction of installation.

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO 123137

Major Task or Tasks Associated With:

Main Feedwater Isolation Valves

Vendor Identity:

Flowserve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Flowserve Corp.

Dollar Value:

Total Dollar Value through Revision 1 is [REDACTED]

Contract Status:

Active

Term Begin:

May 28, 2009

Term End:

Open

Nature and Scope of Work:

Main Feedwater Isolation Valves, Technical Field Services, Testing, Engineering and Documentation

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO 125454

Major Task or Tasks Associated With:

Replacement Heater Drain Pumps

Vendor Identity:

Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Flowsolve Corp.

Dollar Value:

Total Dollar Value through Revision 1 is



Contract Status:

Active

Term Begin:

August 28, 2009

Term End:

June 2012

Nature and Scope of Work:

Replacement Heater Drain Pumps, Spare Heater, Technical Direction

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO 122154

Major Task or Tasks Associated With:

Step-Up Transformers

Vendor Identity:

Siemens Energy Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

2

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Siemens Energy Inc.

Dollar Value:

[REDACTED]

Contract Status:

Complete

Term Begin:

April 27, 2009

Term End:

Complete

Nature and Scope of Work:

Uprate Step-Up Transformers from 850 MVA to 970 MVA

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO 119078

Major Task or Tasks Associated With:

NSSS Engineering Evaluation and LAR Analysis for PTN Units 3 & 4

Vendor Identity:

Westinghouse Electric Co.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Dollar Value through Revision 6 is [REDACTED]

Contract Status:

Active

Term Begin:

Letter of Authorization issued 12/9/08; PO issued 1/26/09

Term End:

Open

Nature and Scope of Work:

NSSS Engineering Evaluation and LAR Analysis for PTN Units 3 & 4

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO 119653

Major Task or Tasks Associated With:

NSSS Engineering Evaluation and LAR Analysis for PSL Units 1 & 2

Vendor Identity:

Westinghouse Electric Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Dollar Value through Revision 4 is [REDACTED]

Contract Status:

Active

Term Begin:

Letter of Authorization issued 11/24/08; PO issued 2/17/09

Term End:

open

Nature and Scope of Work:

NSSS Engineering Evaluation and LAR Analysis for PSL Units 1 & 2

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO 115297 (PSL)

Major Task or Tasks Associated With:

Design Review for LAR (Steam Generator and Reactor Head)

Vendor Identity:

AREVA

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Dollar Value through Revision 8

Contract Status:

Active

Term Begin:

August 27, 2008

Term End:

open

Nature and Scope of Work:

Design Review for LAR (Steam Generator and Reactor Head)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:
PTN PO 115338

Major Task or Tasks Associated With:
Engineering Analysis

Vendor Identity:
AREVA

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Dollar Value through Revision 10, [REDACTED]

Contract Status:
Active

Term Begin:
August 27, 2008

Term End:
Open

Nature and Scope of Work:
Design review for the Reactor Coolant system, Control Rod Mechanism, EMA, CFD and BMI

Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY:

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 105353

Major Task or Tasks Associated With:

Initial BOP Scoping Support for EPU

Vendor Identity:

Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Sole Source

Dollar Value:

Total Dollar Value through Revision 5 is [REDACTED]

Contract Status:

Complete

Term Begin:

October 2, 2007

Term End:

December 1, 2011

Nature and Scope of Work:

BOP Scoping Support (engineering) for the EPU Project

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO 117809

Major Task or Tasks Associated With:

Provide Engineering, Procurement and Construction Services for
PTN

Vendor Identity:

Bechtel

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

6

Number of Bids Received:

5

Brief Description of Selection Process:

Bidders were evaluated against predetermined technical and commercial criteria, awarding to the lowest evaluated bidder.

Dollar Value:

PO value through Rev 4/Rel 0 is [REDACTED]

Contract Status:

Active

Term Begin:

December 2, 2008

Term End:

April 2013

Nature and Scope of Work:

Bechtel's scope includes project management, design engineering, procurement and material handling services, work order planning, construction/implementation, project controls, quality assurance, quality control, radiation protection (alara), safety, security interface, and other services as designated in the Contract documents.

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.
For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 116088

Major Task or Tasks Associated With:

Turbine/Generator Uprate

Vendor Identity:

Siemens Power

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single source

Dollar Value:

Total Max Dollar Value Through Revision 4/Release 0

Contract Status:

Active

Term Begin:

September 29, 2008

Term End:

March 2013

Nature and Scope of Work:

Engineering, Parts and Installation for PSL Turbine/Generator Uprate

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO 117820

Major Task or Tasks Associated With:

Provide Engineering, Procurement and Construction Services for PSL

Vendor Identity:

Bechtel

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

6

Number of Bids Received:

5

Brief Description of Selection Process:

Bidders were evaluated against predetermined technical and commercial criteria, awarding to the lowest evaluated bidder.

Dollar Value:

PO value through Rev 5/Rel 0 is [REDACTED]

Contract Status:

Active

Term Begin:

December 2, 2008

Term End:

December 2012

Nature and Scope of Work:

Bechtel's scope includes project management, design engineering, procurement and material handling services, work order planning, construction/implementation, project controls, quality assurance, quality control, radiation protection (alara), safety, security interface, and other services as designated in the Contract documents.

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 116090

Major Task or Tasks Associated With:

PTN Turbine Generator Uprate

Vendor Identity:

Siemens Power

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Max Contract Value through Rev. 3/Rel 0 is [REDACTED]

Contract Status:

Active

Term Begin:

September 29, 2008

Term End:

March 2013

Nature and Scope of Work:

PTN Engineering, Parts and Installation for Turbine/Generator Uprate

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 118328

Major Task or Tasks Associated With:

PTN Condenser Tube Bundles for Unit 3 & 4

Vendor Identity:

Thermal Engineering International (USA) inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through Revision 5 is [REDACTED]

Contract Status:

Active

Term Begin:

December 19, 2008

Term End:

March 2013

Nature and Scope of Work:

Supply PTN Condenser Tube Bundles

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 118205

Major Task or Tasks Associated With:

PTN MSR's for Units 3 & 4

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

2

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through Revision 2 [REDACTED]

Contract Status:

Active

Term Begin:

December 17, 2008

Term End:

March 2013

Nature and Scope of Work:

Supply PTN Moisture Separator Reheaters

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 118205

Major Task or Tasks Associated With:

PSL MSR's for Units 1 & 2

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

2

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through Revision 5 is [REDACTED]

Contract Status:

Active

Term Begin:

December 17, 2008

Term End:

July 2012

Nature and Scope of Work:

Supply PSL Moisture Separator Reheaters

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 118241

Major Task or Tasks Associated With:

PTN Feedwater Heaters for Units 3 & 4

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

3

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Contract Value through Revision 2

Contract Status:

Active

Term Begin:

December 19, 2008

Term End:

March 2013

Nature and Scope of Work:

Supply PTN Feedwater Heaters

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 112221

Major Task or Tasks Associated With:

Engineering Services

Vendor Identity:

Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Blanket Purchase Order Max Value through Revision 17 to Release 0 is [REDACTED]

Contract Status:

Active

Term Begin:

April 22, 2008

Term End:

December 2012

Nature and Scope of Work:

PSL BOP Engineering

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 112177

Major Task or Tasks Associated With:

Engineering Services

Vendor Identity:

Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Blanket Purchase Order Max Value through Revision 8 to Release 0 is [REDACTED]

Contract Status:

Active

Term Begin:

April 22, 2008

Term End:

open

Nature and Scope of Work:

Engineering for the PSL Uprate Project

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO 117272

Major Task or Tasks Associated With:

Gantry crane repair/modification

Vendor Identity:

American Crane & Equip.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Sole Source/OEM

Dollar Value:

Total Dollar Value through Rev 6 is [REDACTED]

Contract Status:

Active

Term Begin:

November 13, 2008

Term End:

Open

Nature and Scope of Work:

Complete modification of Unit 1 crane and update of electrical components for Unit 2 crane

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 118224

Major Task or Tasks Associated With:

PSL Feedwater Heaters for Units 1 & 2

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Dollar Value thru Revision 6

Contract Status:

Active

Term Begin:

December 17, 2008

Term End:

open

Nature and Scope of Work:

Supply PSL Feedwater Heaters

Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 115485

Major Task or Tasks Associated With:

Eng. Services for NSSS, BOP & Licensing Activities

Vendor Identity:

Proto-Power

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Dollar Value through revision 4 is



Contract Status:

Active

Term Begin:

September 3, 2008

Term End:

Open

Nature and Scope of Work:

PTN Eng. Services for NSSS, BOP and Licensing Activities.

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 118278

Major Task or Tasks Associated With:

PSL Heat Exchangers for Units 1 & 2

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

3

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through revisions 4 is [REDACTED]

Contract Status:

Active

Term Begin:

December 19, 2008

Term End:

Open

Nature and Scope of Work:

Supply PSL Heat Exchangers

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY:

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 105720

Major Task or Tasks Associated With:

PSL Fuels Study

Vendor Identity:

Areva

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Order value through Revision 16 is [REDACTED]

Contract Status:

Active

Term Begin:

September 12, 2007

Term End:

open

Nature and Scope of Work:

Fuels Performance Study and Analysis

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 116796

Major Task or Tasks Associated With:

Ultrasonic Flow Measuring System

Vendor Identity:

Cameron Technologies

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Blanket Purchase Order Value through Revision 1 to Release 0
is [REDACTED]

Contract Status:

Complete

Term Begin:

October 29, 2008

Term End:

December 22, 2011

Nature and Scope of Work:

Ultrasonic Flow Measuring System for PTN

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO 116107

Major Task or Tasks Associated With:

Ultrasonic Flow Measuring System

Vendor Identity:

Cameron Technologies

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Purchase Order Value through Revision 1 is [REDACTED]

Contract Status:

Awarded

Term Begin:

September 29, 2008

Term End:

Open

Nature and Scope of Work:

Ultrasonic Flow Measuring System for PTN

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO 114114

Major Task or Tasks Associated With:

Staff Augmentation

Vendor Identity:

Richard Sipos

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source Justification

Dollar Value:

Total Blanket Purchase Order Value through Revision 6 is



Contract Status:

Active

Term Begin:

July 3, 2008

Term End:

open

Nature and Scope of Work:

Project Management Services

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 4500521317

Major Task or Tasks Associated With:

Inductors

Vendor Identity:

Areva

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive Selection

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

September 8, 2009

Term End:

Open

Nature and Scope of Work:

Supply of Inductors

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-BA

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 126248

Major Task or Tasks Associated With:

Replacement Transformer Coolers

Vendor Identity:

ABB

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

1

Brief Description of Selection Process:

Competitive Selection, Commercial and Technical Evaluation

Dollar Value:

Total Contract Value through Rev 2

Contract Status:

Active

Term Begin:

October 8, 2009

Term End:

Open

Nature and Scope of Work:

Replacement Transformer Coolers

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 126453

Major Task or Tasks Associated With:

Turbine Plant Cooling Water Heat Exchangers

Vendor Identity:

Joseph Oat Corporation

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive Selection, Commercial and Technical Evaluation

Dollar Value:

Total Contract Value through revision 1 is [REDACTED]

Contract Status:

Active

Term Begin:

November 5, 2009

Term End:

Open

Nature and Scope of Work:

Supply Turbine Plant Cooling Water Heat Exchangers

Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO #127777

Major Task or Tasks Associated With:

Estimating Services

Vendor Identity:

High Bridge

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Contract Value through revision 2 is

Contract Status:

Active

Term Begin:

December 8, 2009

Term End:

Open

Nature and Scope of Work:

Estimating Services

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 127881

Major Task or Tasks Associated With:

Procedure Writers

Vendor Identity:

Absolute Consulting

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 22, 2009

Term End:

Open

Nature and Scope of Work:

Procedure Writers

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PQ #118988

Major Task or Tasks Associated With:

Fuel Storage Criticality and Related Analysis (PSL 2)

Vendor Identity:

Holtec

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Purchase Order Value through Revision 4 is [REDACTED]

Contract Status:

Active

Term Begin:

January 22, 2009

Term End:

Open

Nature and Scope of Work:

Fuel Storage Criticality and Related Analysis (PSL 2)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO #118563

Major Task or Tasks Associated With:

Fuel Storage Criticality and Related Analysis (PSL 1)

Vendor Identity:

Holtec

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Purchase Order Value through Revision 5 is



Contract Status:

Active

Term Begin:

January 14, 2009

Term End:

Open

Nature and Scope of Work:

Fuel Storage Criticality and Related Analysis (PSL 1)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO # 4500467077

Major Task or Tasks Associated With:

PSL Generator Step-up Transformers

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

7

Number of Bids Received:

7

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

November 10, 2008

Term End:

Open

Nature and Scope of Work:

PSL Generator Step-up Transformers

Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:
PTN PO # 130612

Major Task or Tasks Associated With:
Condensate Pumps

Vendor Identity:
Flowserv Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
3

Number of Bids Received:
3

Brief Description of Selection Process:
Competitive

Dollar Value:
Total Contract Value through Revision 2 is [REDACTED]

Contract Status:
Active

Term Begin:
April 22, 2010

Term End:
Open

Nature and Scope of Work:
Condensate Pumps

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO #130649

Major Task or Tasks Associated With:

Main Feedwater Pumps

Vendor Identity:

Flowserve Corp

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

1

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

April 22, 2010

Term End:

Open

Nature and Scope of Work:

Main Feedwater Pumps

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 126227

Major Task or Tasks Associated With:

Control System FWH, Moisture Separator

Vendor Identity:

Invensys

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Dollar Value through revision 9 [REDACTED]

Contract Status:

Active

Term Begin:

October 13, 2009

Term End:

Open

Nature and Scope of Work:

Control System FWH, Moisture Separator

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 129689

Major Task or Tasks Associated With:

Turbine Digital Upgrade

Vendor Identity:

Invensys

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Dollar Value through Revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

March 17, 2010

Term End:

Open

Nature and Scope of Work:

Turbine Digital Upgrade

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO # 130272

Major Task or Tasks Associated With:

Electro-Hydraulic Fluid Systems

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Dollar Value through Rev 4 is [REDACTED]

Contract Status:

Active

Term Begin:

April 8, 2010

Term End:

Open

Nature and Scope of Work:

Electro-Hydraulic Fluid Systems

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO # 131928

Major Task or Tasks Associated With:

Pre-planning SL2-19

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Complete

Term Begin:

June 14, 2010

Term End:

February 28, 2011

Nature and Scope of Work:

SL2-19 Pre-planning work to support station milestones for the
Turbine Generator Installation

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO # 131533

Major Task or Tasks Associated With:

Non-Fuels NSSS Interim LAR (PSL 1 & 2)

Vendor Identity:

Areva

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Predetermined Source

Dollar Value:

Total Contract Value through revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

June 10, 2010

Term End:

Open

Nature and Scope of Work:

Non-Fuels NSSS Interim LAR (PSL 1 & 2)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PQ # 131907

Major Task or Tasks Associated With:

Fuels Related Interim LAR/MOD for EPU at PSL

Vendor Identity:

Areva

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Predetermined Source

Dollar Value:

Total Contract Value through Revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

June 11, 2010

Term End:

Open

Nature and Scope of Work:

Fuels Related Interim LAR/MOD for EPU at PSL

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO # 131585

Major Task or Tasks Associated With:

Interim LAR/MOD for EPU at PSL

Vendor Identity:

Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Predetermined Source

Dollar Value:

Total Contract Value through Revision 4 is



Contract Status:

Active

Term Begin:

June 15, 2010

Term End:

Open

Nature and Scope of Work:

Interim LAR/MOD for EPU at PSL

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-E1

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO #131742

Major Task or Tasks Associated With:

LAR/Request for Additional Information

Vendor Identity:

Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Predetermined Source

Dollar Value:

Total Contract value through revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

June 16, 2010

Term End:

Open

Nature and Scope of Work:

LAR/Request for Additional Information for Non-Fuels related scope

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO #131940

Major Task or Tasks Associated With:

Main Steam Turbine Control Replacement

Vendor Identity:

Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

4

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Max Contract value through Rev 2 to Release 0

Contract Status:

Active

Term Begin:

June 30, 2010

Term End:

Open

Nature and Scope of Work:

Main Steam Turbine Control Replacement

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO #2259675

Major Task or Tasks Associated With:

Furnish New Spent Fuel Pool Heat Exchangers

Vendor Identity:

Joseph Oat Corporation

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

2

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

July 23, 2010

Term End:

Open

Nature and Scope of Work:

Furnish New Spent Fuel Pool Heat Exchangers

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 2259669

Major Task or Tasks Associated With:

Rewind/Refurbish Upgrade Condensate Pumps

Vendor Identity:

Tampa Armature Works

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

August 2, 2010

Term End:

Open

Nature and Scope of Work:

Rewind/Refurbish Upgrade Condensate Pumps

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO #2260113

Major Task or Tasks Associated With:

PSL Rod Control System Upgrades

Vendor Identity:

Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Contract Value through Amendment 3

Contract Status:

Active

Term Begin:

September 23, 2010

Term End:

Open

Nature and Scope of Work:

PSL Rod Control System Upgrades

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO #2261747

Major Task or Tasks Associated With:

EPU NSSS Engineering and Modification Support

Vendor Identity:

Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Predetermined Source

Dollar Value:

Total Contract Value through Amendment 2

Contract Status:

Active

Term Begin:

September 23, 2010

Term End:

Open

Nature and Scope of Work:

EPU NSSS Engineering and Modification Support

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO #2264240

Major Task or Tasks Associated With:

PSL 2-19 Turbine Generator Installation Contract

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Contract Status:

Active

Term Begin:

November 17, 2010

Term End:

Open

Nature and Scope of Work:

PSL 2-19 Turbine Generator Installation Contract

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO #2264841

Major Task or Tasks Associated With:

SL 2-19 Technical Support

Vendor Identity:

Batsch Industries

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Contract Value through Amendment 2 [REDACTED]

Contract Status:

Active

Term Begin:

November 30, 2010

Term End:

Open

Nature and Scope of Work:

SL 2-19 Technical Support

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

2264914

Major Task or Tasks Associated With:

CEDMS Power Switch Refurbishment (PSL 2)

Vendor Identity:

Westinhouse Electric

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 7, 2010

Term End:

Open

Nature and Scope of Work:

CEDMS Power Switch Refurbishment (PSL 2)

Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO #2285418

Major Task or Tasks Associated With:

Implementation Spares for Turbine Generator Work

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Contract Value through Amendment 2

Contract Status:

Active

Term Begin:

December 16, 2010

Term End:

Open

Nature and Scope of Work:

Implementation Spares for Turbine Generator Work

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO #2285720

Major Task or Tasks Associated With:

Licensing/Design Basis/Program Modification

Vendor Identity:

Enercon

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

2

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

January 4, 2011

Term End:

Open

Nature and Scope of Work:

Licensing/Design Basis/Program Modification

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO# 2291203

Major Task or Tasks Associated With:

Main Steam Isolation Valve Replacement Actuator

Vendor Identity:

Enertech

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

2

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Contract Value through Amendment 3 [REDACTED]

Contract Status:

Active

Term Begin:

April 21, 2011

Term End:

Open

Nature and Scope of Work:

Main Steam Isolation Valve Replacement Actuator

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO# 2290465

Major Task or Tasks Associated With:

Design, Engineering and Fabrication of Turbine Crossover piping

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

1 [REDACTED]

Contract Status:

Active

Term Begin:

March 31, 2011

Term End:

Open

Nature and Scope of Work:

Design, Engineering and Fabrication of Turbine Crossover piping

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO# 2290614

Major Task or Tasks Associated With:

Main Feedwater Pump Casing Modifications

Vendor Identity:

Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

N/A

Number of Bids Received:

N/A

Brief Description of Selection Process:

Replaces PO 130549

Dollar Value:

Total Contract Value through Amend 1

Contract Status:

Active

Term Begin:

May 2, 2011

Term End:

Open

Nature and Scope of Work:

Main Feedwater Pump Casing Modifications

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO# 2293950

Major Task or Tasks Associated With:

Turbine Generator Pre-Outage Planning PTN 3 & 4

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Contract value through Amendment 1: [REDACTED]

Contract Status:

Active

Term Begin:

June 24, 2011

Term End:

Open

Nature and Scope of Work:

Turbine Generator Pre-Outage Planning PTN 3 & 4
(Turbine Generator Installation)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO# 2295186

Major Task or Tasks Associated With:

Melamic Chevrons for Spent Fuel Pool

Vendor Identity:

Holtec

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

August 2, 2011

Term End:

Open

Nature and Scope of Work:

Melamic Chevrons for Spent Fuel Pool

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO# 2298556

Major Task or Tasks Associated With:

Modification, overhaul and refurbishment of the B and C AFW

Vendor Identity:

Sulzer Pumps

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

September 2, 2011

Term End:

Open

Nature and Scope of Work:

Modification, overhaul and refurbishment of the B and C AFW

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO# 2298406

Major Task or Tasks Associated With:

Fuel Movers for Metamic Inserts

Vendor Identity:

Master Lee Energy Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

1

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

October 12, 2011

Term End:

Open

Nature and Scope of Work:

Fuel Movers for Metamic Inserts

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO# 2297556

Major Task or Tasks Associated With:

Siemens installation of 2A Main Power Transformer

Vendor Identity:

Siemens Energy Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

September 27, 2011

Term End:

Open

Nature and Scope of Work:

Siemens installation of 2A Main Power Transformer

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO# 2295953

Major Task or Tasks Associated With:

Misc Safety Related Wire and Cable

Vendor Identity:

Marmon Wire & Cable

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Contract Value through revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

August 24, 2011

Term End:

Open

Nature and Scope of Work:

Misc Safety Related Wire and Cable

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.
For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO# 2297055

Major Task or Tasks Associated With:

Replacement Unit 2 LP #4 Feedwater Heaters for EPU

Vendor Identity:

Thermal Engineering

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

September 16, 2011

Term End:

Open

Nature and Scope of Work:

Replacement Unit 2 LP #4 Feedwater Heaters for EPU

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO# 2300139

Major Task or Tasks Associated With:

SL 1-24 Turbine Generator Installation

Vendor Identity:

Siemens Energy Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

September 16, 2011

Term End:

Open

Nature and Scope of Work:

SL 1-24 Turbine Generator Installation

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO# 2299624

Major Task or Tasks Associated With:

Upgrade Services for Feedwater Pumps

Vendor Identity:

Ames Group LLC

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Contract Value through revision 1 [REDACTED]

Contract Status:

Active

Term Begin:

November 16, 2011

Term End:

Open

Nature and Scope of Work:

Upgrade Services for Feedwater Pumps

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO# 2300487

Major Task or Tasks Associated With:

Construction Management Oversight Services for SL1-24

Vendor Identity:

Weldtech Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

November 26, 2011

Term End:

Open

Nature and Scope of Work:

Construction Management Oversight Services for SL1-24

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

NF-10-358 and NF-11-178

Major Task or Tasks Associated With:

Spent Fuel Criticality Safety Analysis Support (PTN)

Vendor Identity:

Westinhouse Electric

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

November 2, 2010

Term End:

Open

Nature and Scope of Work:

Spent Fuel Criticality Safety Analysis Support (PTN)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 2301867

Major Task or Tasks Associated With:

Develop Engineering Change Packages for EPU at PTN

Vendor Identity:

Enercon Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This Indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 28, 2011

Term End:

Open

Nature and Scope of Work:

Develop Engineering Change Packages for EPU at PTN

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 2261800

Major Task or Tasks Associated With:

Supply of Simulator SCD Software Translator Upgrade

Vendor Identity:

L 3 Communications Mapps Inc

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Contract Value through Amendment 2 [REDACTED]

Contract Status:

Active

Term Begin:

September 28, 2010

Term End:

Open

Nature and Scope of Work:

Supply of Simulator SCD Software Translator Upgrade

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:
PTN PO # 2301737

Major Task or Tasks Associated With:
Construction Management Oversight Services for PTN

Vendor Identity:
PSI Energy Services

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
[REDACTED]

Contract Status:
Active

Term Begin:
December 21, 2011

Term End:
Open

Nature and Scope of Work:
Construction Management Oversight Services for PTN

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 2301736

Major Task or Tasks Associated With:

Construction Management Oversight Services

Vendor Identity:

Weldtech Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

██████████

Contract Status:

Active

Term Begin:

December 21, 2011

Term End:

Open

Nature and Scope of Work:

Construction Management Oversight Services

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO #2301871

Major Task or Tasks Associated With:

Develop Engineering Changes Packages for EPU at PTN

Vendor Identity:

Zachry Nuclear Engineering

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 28, 2011

Term End:

Open

Nature and Scope of Work:

Develop Engineering Changes Packages for EPU at PTN

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO #2301853

Major Task or Tasks Associated With:

Develop TPCW Changes Packages for EPU at PTN

Vendor Identity:

Sargent & Lundy

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:


December 28, 2011

Term End:

Open

Nature and Scope of Work:

Develop TPCW Changes Packages for EPU at PTN

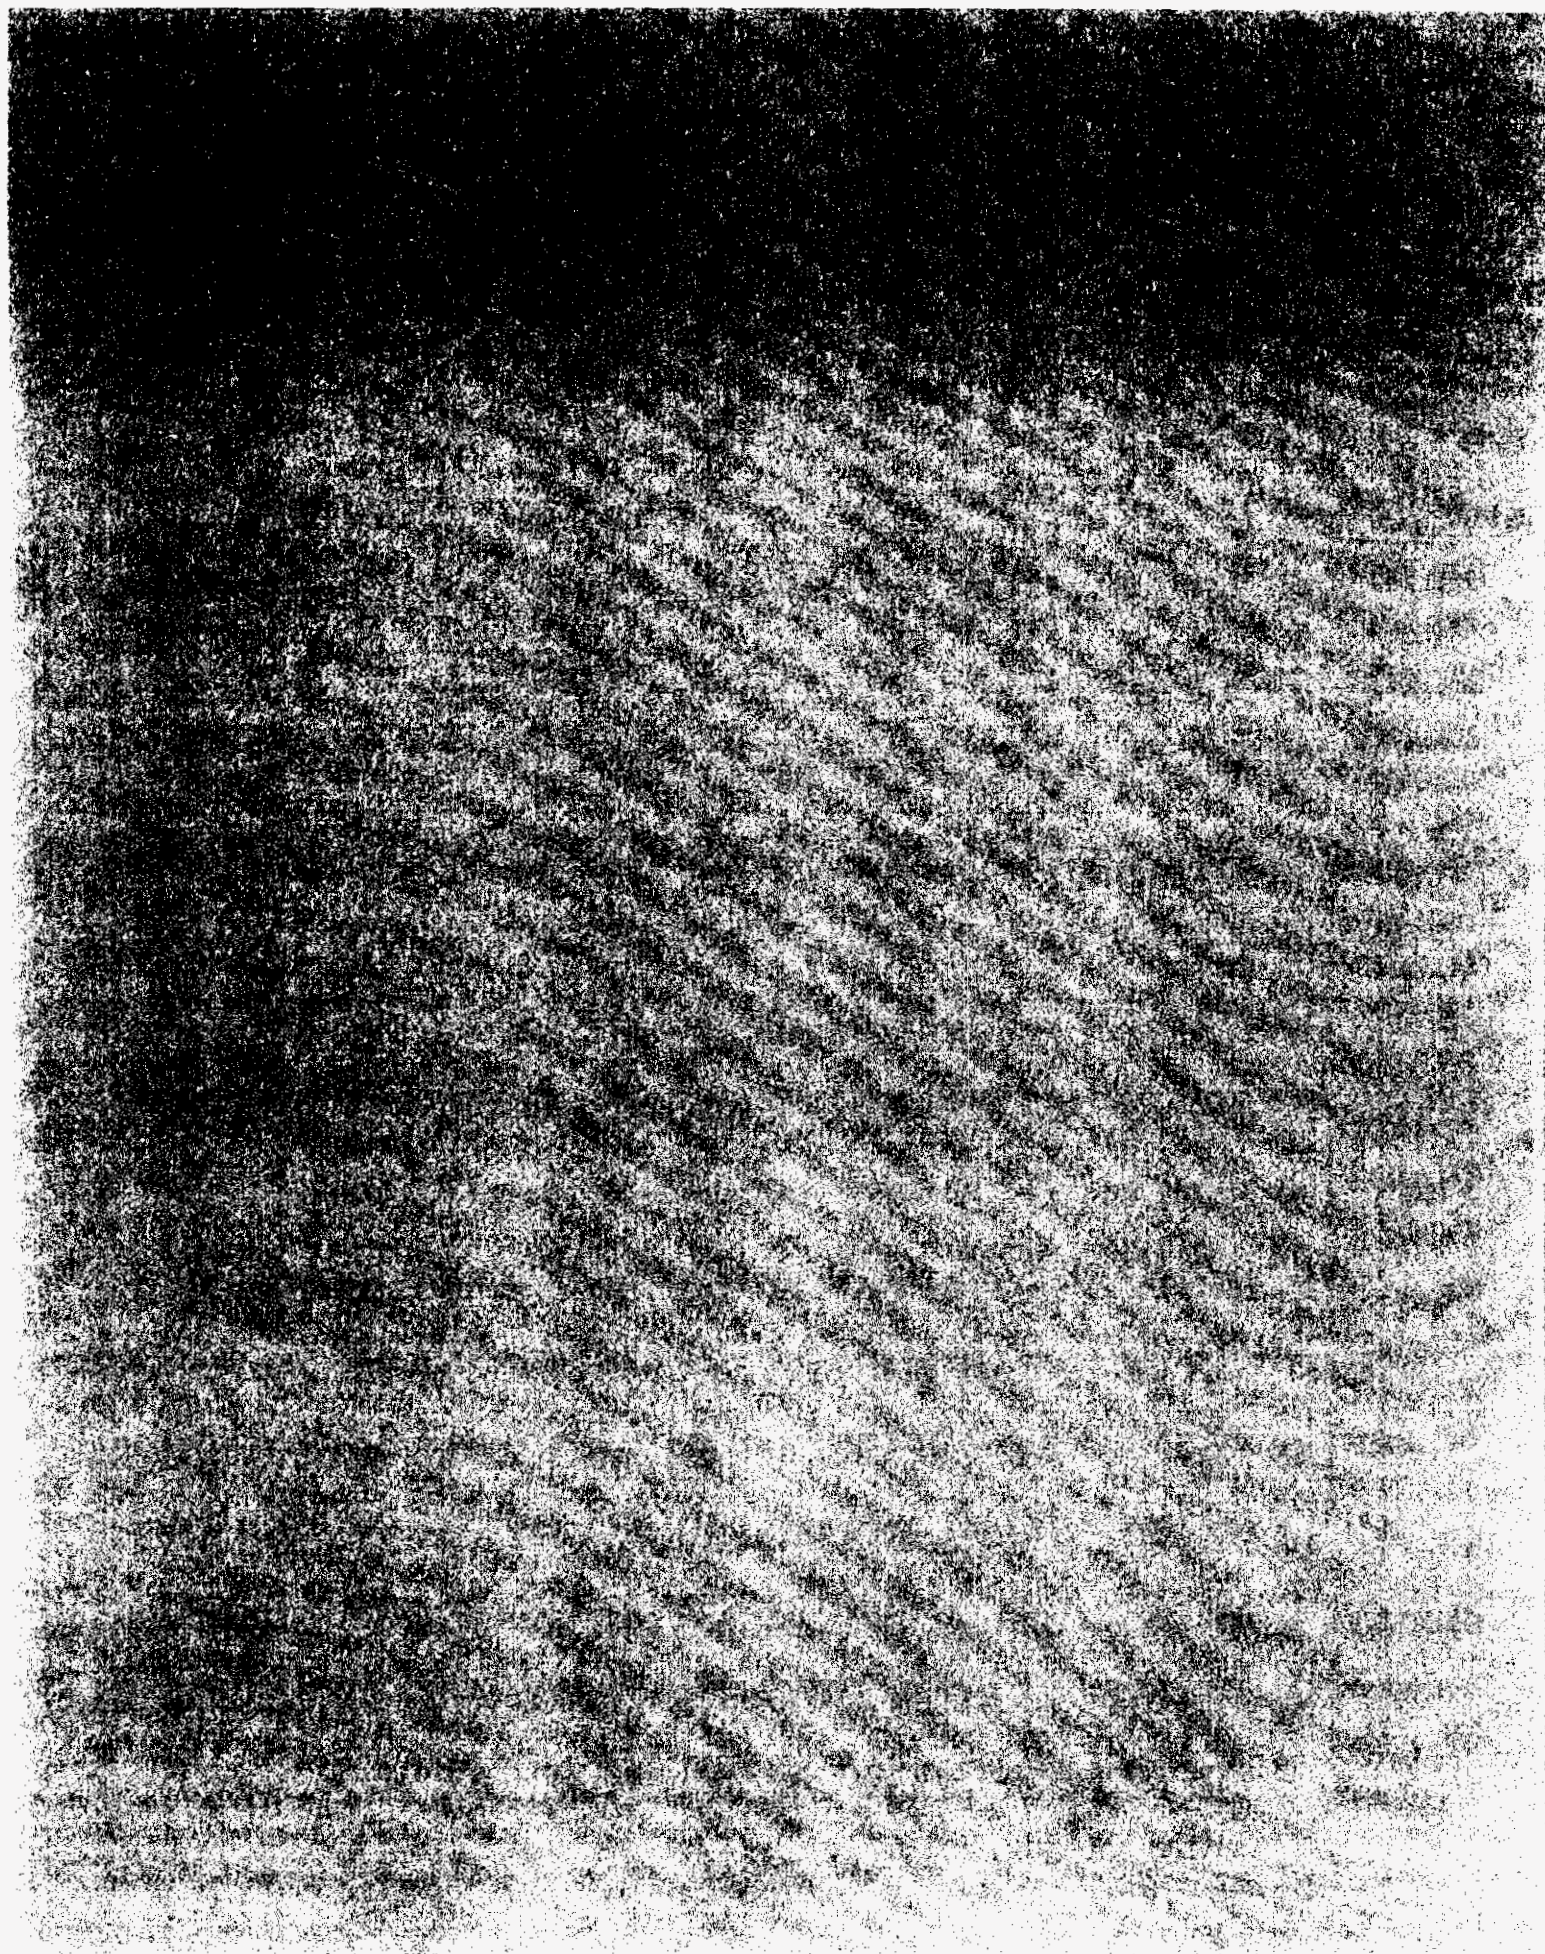

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed

Schedule T-7A

[Section (B)(e)]

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO.: 120009-EI


EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and description of work.

For the Year Ended: 12/31/2011
 Witness: Steven D. Scroggs

CONFIDENTIAL CONFIDENTIAL CONFIDENTIAL CONFIDENTIAL

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Actual amount expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
1	4500395492	Open- CO#38	11/6/2007- open	10/11/2011- open					Bechtel Power Corp	Comp Bid/ Single Source/ Predetermined Source	Engineering Services to Support Preparation of COLA and SCA and Response to post-submittal RAI's.
2	4500404639	Open- CO#6	1/31/2008- open	4/21/2011- open					Westinghouse Electric Co	Sole Source/ Predetermined Source	Engineering Services to Support Preparation of COLA and Response to post-submittal RAI's.
3	4500425707	Open-CO#5	5/23/2008- open	1/3/2011- open					HDR Engineering, Inc.	Comp Bid/ Single Source	Conceptual Engineering of Cooling Water Supply and Discharge
4	4500430034	Open- CO#1	6/16/2008- open	1/28/2011- open					Electric Power Research Institute	Single Source	Advanced Nuclear Technology; Near term deployment of Advanced Light Water Reactors
5	4500443122	Open-CO#3	8/6/2008- open	11/29/2011- open					Eco Metrics, Inc.	Single Source	Environmental Consulting Services
6	4500517152	Open-CO#3	7/10/2009- open	12/17/2010- open					McNabb Hydrogeologic Consulting Inc	Single Source	Turkey Point 6&7 Post SCA Submittal and UIC Licensing Support
7	4500518160	Open-CO#5	7/23/2009- open	6/24/2011- open					Golder Associates Inc	Single Source	Turkey Point 6&7 Post SCA Submittal Support
8	4500518167	Open- CO#6	7/23/2009- open	9/14/2011- open					Environmental Consulting and Technology Inc	Single Source/ Predetermined Source	Turkey Point 6&7 SCA Support
9	4500536449	Open-CO#2	10/12/2009- open	11/29/2011- open					McNabb Hydrogeologic Consulting Inc	Comp Bid/ Single Source	Turkey Point 6&7 UIC Subject Matter Expert Support
10	4500492222	Open-CO#2	3/17/2009- open	12/22/2011- open					Experts US LLC(F/K/A, Jefferson Wells International)	Comp Bid/ Single Source	New Nuclear Audit
11	4500567305	Open-CO#1	6/29/2010- open	9/1/2010- open					Oickerson Florida Inc	Comp Bid	Turkey Point 6&7 Exploratory/UIC Well Site Development
12	4500652043	Open-CO#1	3/3/2011- open	12/29/2011- open					Layne Christensen Company	Comp Bid	Turkey Point 6&7 Exploratory/UIC Well and Dual Zone Monitor Well Installation

A B C D

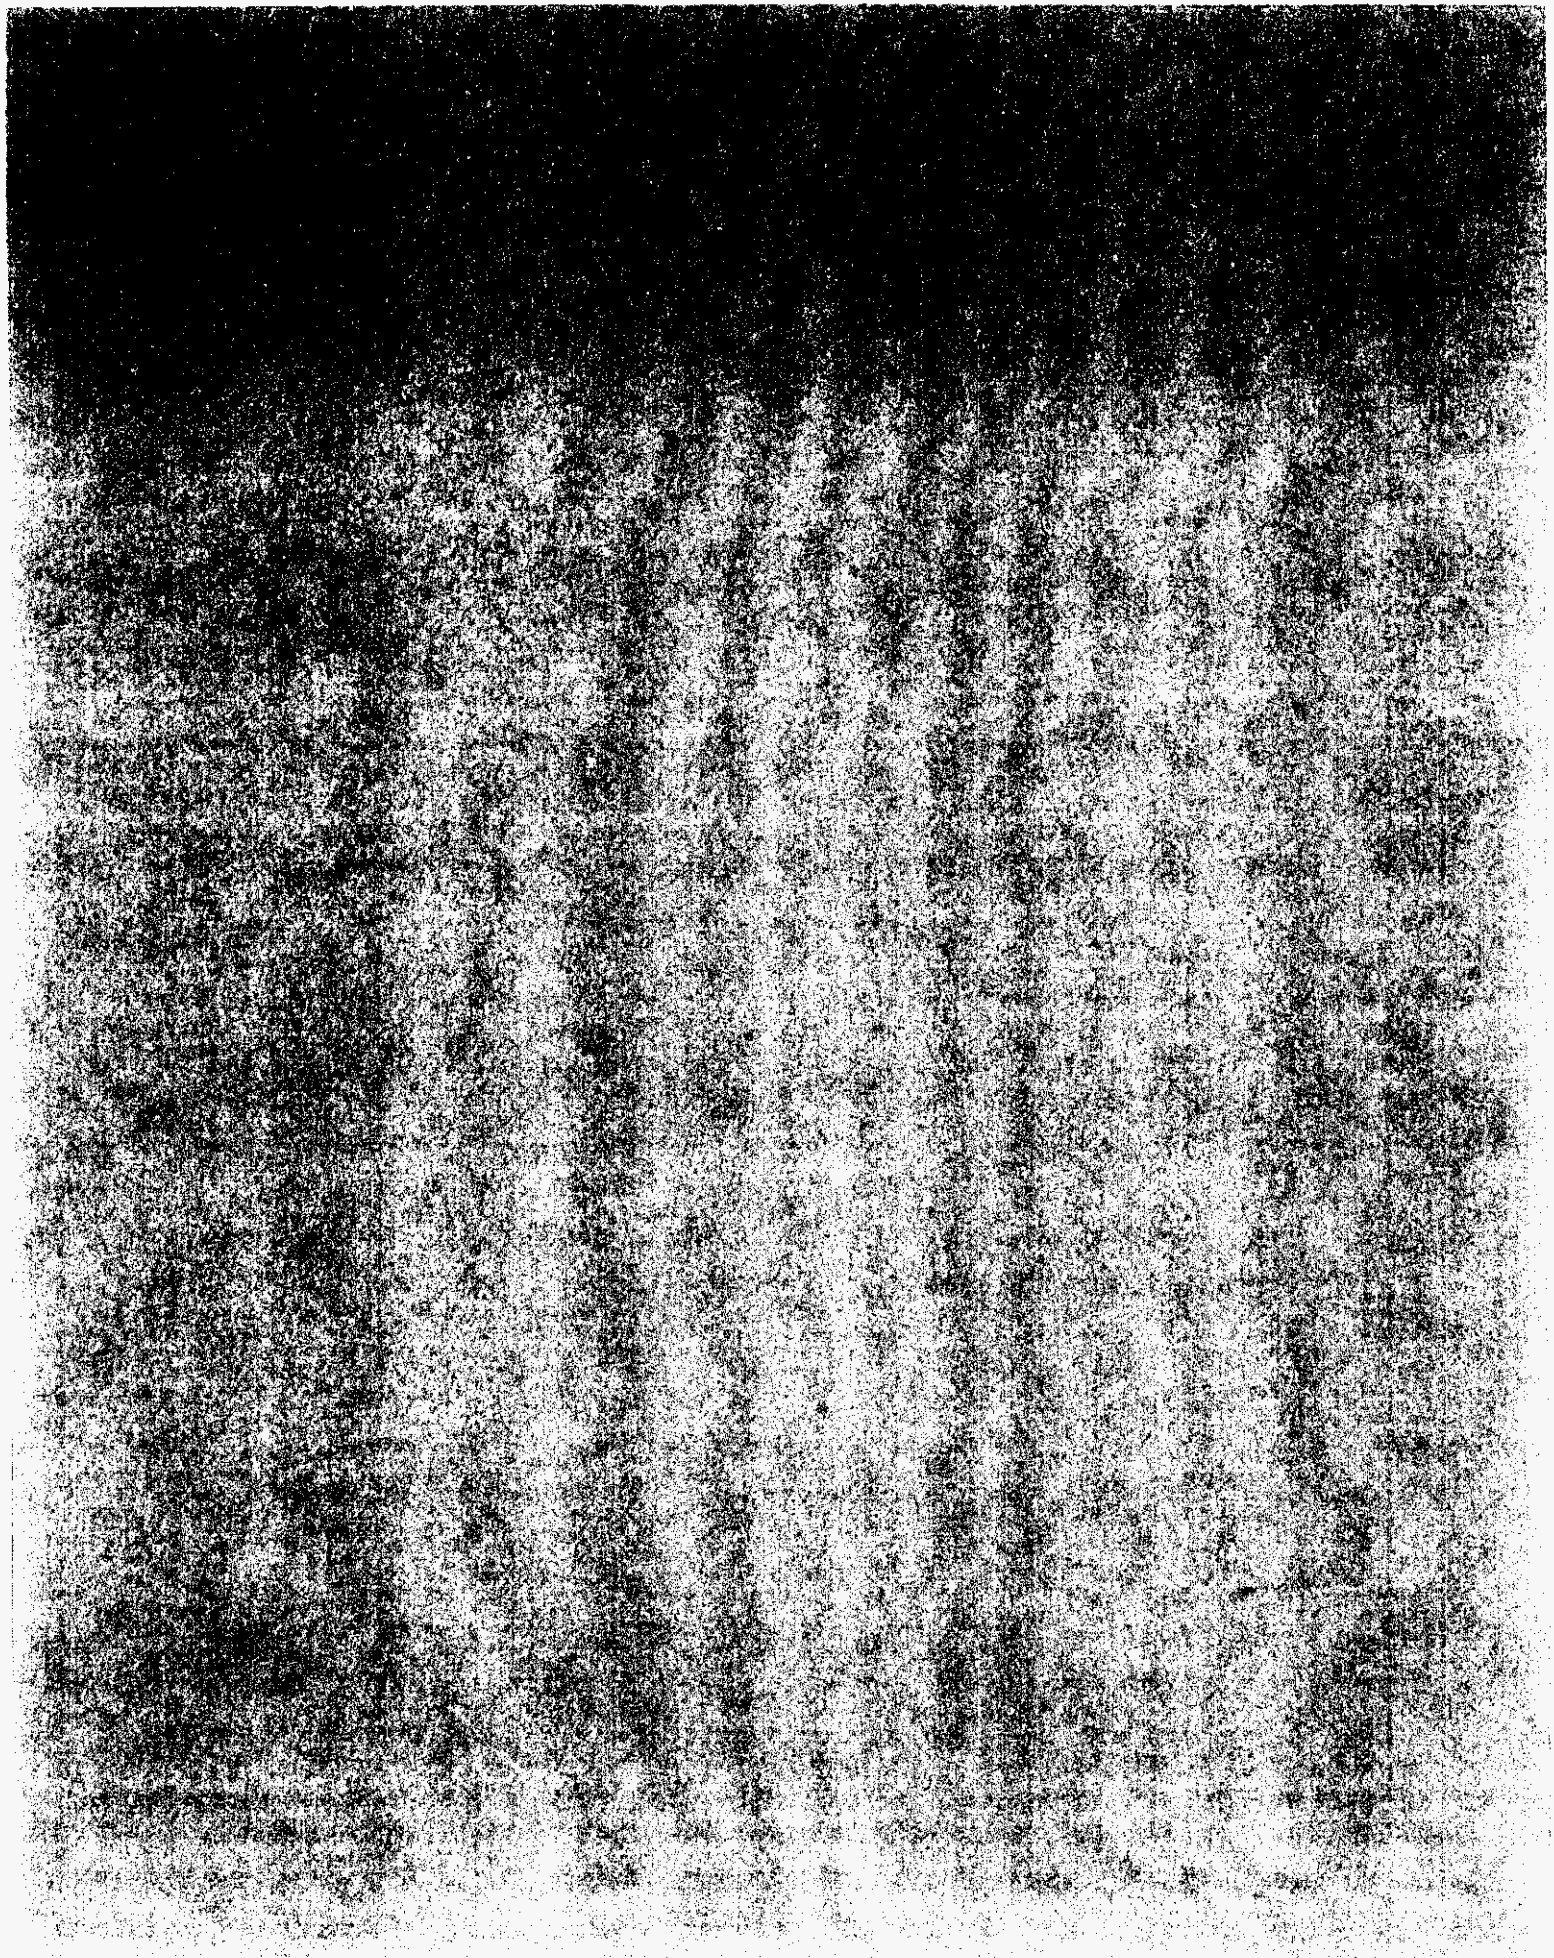

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (b)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:

4500395492

Major Task or Tasks Associated With:

COLA and SCA preparation and support

Vendor Identity:

Bechtel Power Corporation

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct

Number of Vendors Solicited:

Two

Number of Bids Received:

Two

Brief Description of Selection Process:

Initial contract competitively bid; change orders #01-#11
issued single source; all subsequent change orders
issued Predetermined Source

Dollar Value:

1

Contract Status:

Active- CO#38

Term Begin:

11/6/2007

Term End:

2/27/2016

Nature and Scope of Work:

Engineering Services to Support Preparation of COLA
and SCA, including post-submittal support for RAI
responses.

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (B)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: Florida Power & Light Company
DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:
4500404639

Major Task or Tasks Associated With:
COLA support

Vendor Identity:
Westinghouse Electric Company

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
One

Number of Bids Received:
One

Brief Description of Selection Process:
Sole source justification; designated as Predetermined
Source March 2009

Dollar Value:
1 [REDACTED]

Contract Status:
Active- CO#6

Term Begin:
1/31/2008

Term End:
6/29/2014

Nature and Scope of Work:
Engineering Services to Support Preparation of COLA,
including post-submittal support for RAI responses.

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: Florida Power & Light Company
DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:
4500430034

Major Task or Tasks Associated With:
COLA and SCA preparation and support

Vendor Identity:
Electric Power Research Institute

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
Two

Number of Bids Received:
Two

Brief Description of Selection Process:
Single

Dollar Value:

1

Contract Status:
Active- CO#1

Term Begin:
6/16/2008

Term End:
6/29/2014

Nature and Scope of Work:
Engineering Services to Support Preparation of COLA and SCA, including post-submittal support for RAI responses.

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: Florida Power & Light Company
DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:
4500518160

Major Task or Tasks Associated With:
Post SCA Submittal support

Vendor Identity:
Golder Associates, Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct or Indirect relationship with the vendor

Number of Vendors Solicited:
One

Number of Bids Received:
One

Brief Description of Selection Process:
Single source; Designated as Predetermined Source February 2010

Dollar Value:

1

Contract Status:
Active- CO#5

Term Begin:
7/23/2009

Term End:
6/28/2012

Nature and Scope of Work:
Post SCA Submittal support

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (B)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: Florida Power & Light Company
DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:
4500518167

Major Task or Tasks Associated With:
SCA Support

Vendor Identity:
Environmental Consulting and Technology, Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
One

Number of Bids Received:
One

Brief Description of Selection Process:
Single source; Designated as Predetermined Source December 2009

Dollar Value:

1

Contract Status:
Active- CO#6

Term Begin:
7/23/2009

Term End:
6/28/2012

Nature and Scope of Work:
SCA Support

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: Florida Power & Light Company
DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:
4500536449

Major Task or Tasks Associated With:
Turkey Point 6&7 UIC Subject Matter Expert Support

Vendor Identity:
McNabb Hydrogeologic Consulting

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
One

Number of Bids Received:
One

Brief Description of Selection Process:
Competitive Bid for initial Order, Single Source justification for Change Orders

Dollar Value:
1 [REDACTED]

Contract Status:
Active- CO#2

Term Begin:
10/12/2009

Term End:
6/29/2013

Nature and Scope of Work:
Turkey Point 6&7 UIC Subject Matter Expert Support

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: Florida Power & Light Company
DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:
4500587305

Major Task or Tasks Associated With:
Turkey Point Units 6&7 Exploratory/UIC Well Site Development

Vendor Identity:
Dickerson Florida, Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
Eight

Number of Bids Received:
Five

Brief Description of Selection Process:
Competitive Bid

Dollar Value:

1

Contract Status:
Active- CO#1

Term Begin:
6/29/2010

Term End:
6/30/2011

Nature and Scope of Work:
Turkey Point Units 6&7 Exploratory/UIC Well Site Development

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: Florida Power & Light Company
DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:
4500652043

Major Task or Tasks Associated With:
Turkey Point 6&7 Exploratory/UIC Well and Dual Zone Monitor Well Installation

Vendor Identity:
Layne Christensen Company

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
Three

Number of Bids Received:
Three

Brief Description of Selection Process:
Competitive Bid

Dollar Value:

1


Contract Status:
Active- CO#1

Term Begin:
3/3/2011

Term End:
9/27/2012

Nature and Scope of Work:
Turkey Point 6&7 Exploratory/UIC Well and Dual Zone Monitor Well Installation

EXHIBIT B

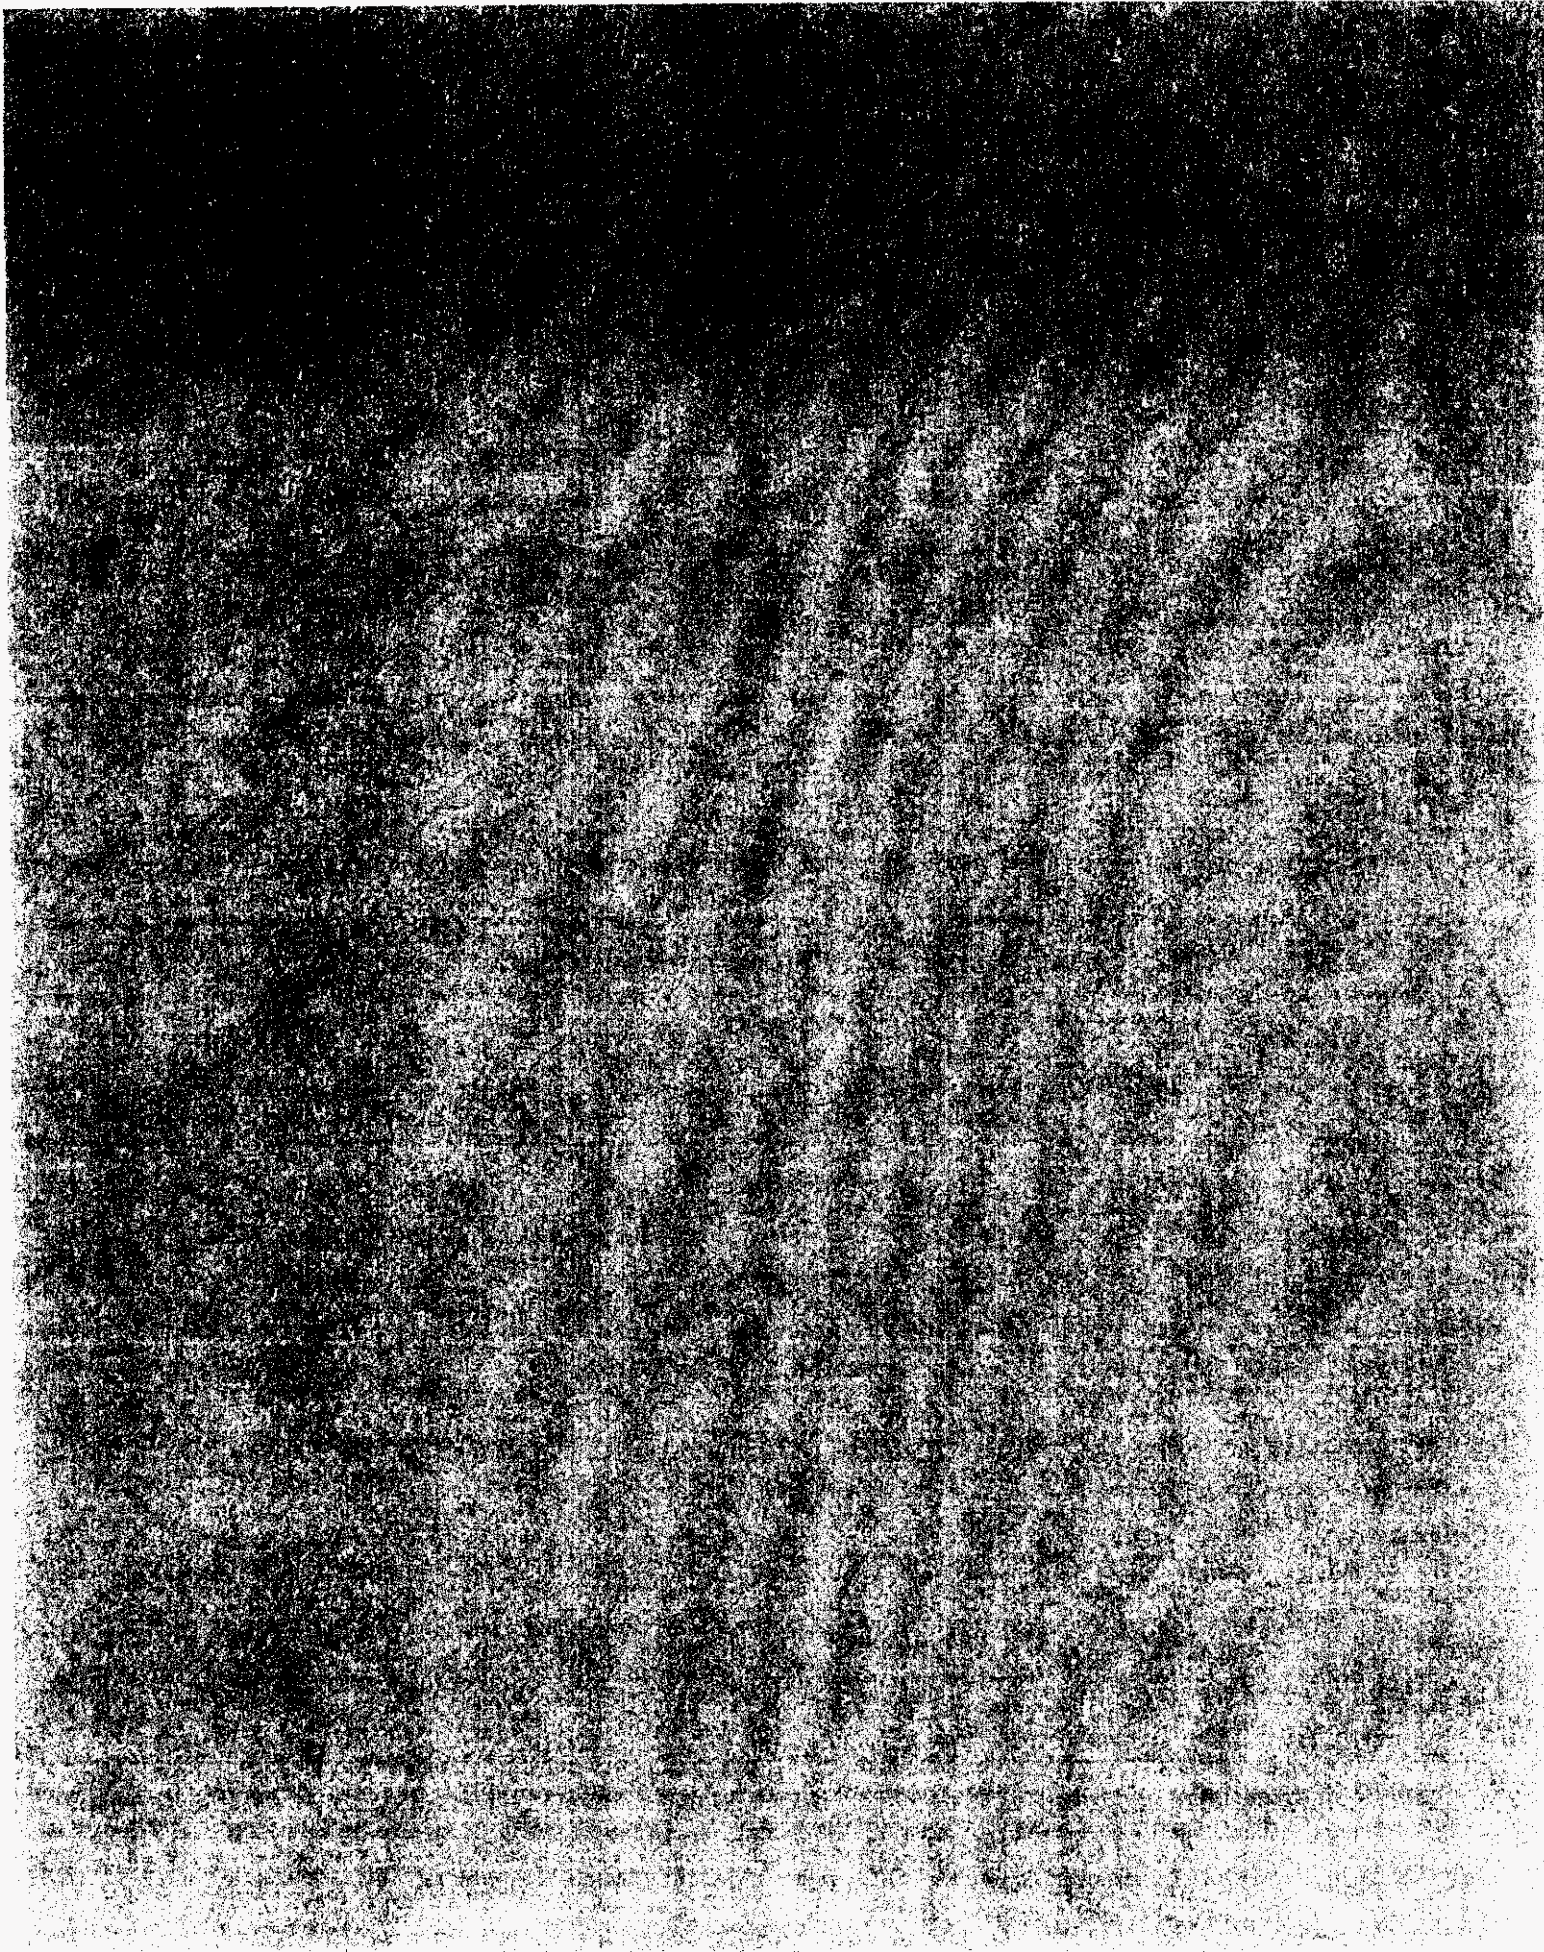

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO. 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. G. Jones

(A)		(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended In Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
1	121869	Open	4/29/09 - open	4/29/09 - open					AAF MCQUAY	Competitive	Supply Normal Containment Coolers and Testing Services (PTN)
2	120769	Open	3/26/09 - open	3/26/09 - open					Calvert Company Inc	Competitive	Iso Phase Bus Duct Coolers and Testing Services (PSL)
3	124436	Open	7/17/09 - open	7/17/09 - open					Calvert Company Inc	Competitive	Iso Phase Bus Duct Coolers, Install, Demo & Testing Services (PTN)
4	121985	Open	4/24/09 - open	4/24/09 - open					Flowserve Corp.	Competitive	Replacement Main Feedwater Pumps & Various Testing (PSL)
5	123137	Open	5/28/09 - open	5/28/09 - open					Flowserve Corp.	Competitive	Main Feedwater Isolation Valves and Testing Services (PTN)
6	125454	Open	8/28/09 - open	8/28/09 - open					Flowserve Corp.	Competitive	Replacement Heater Drain Pumps (PSL)
7	122154	Complete	4/27/09 - 6/15/11	4/27/09 - 6/15/11					Siemens Energy Inc.	Competitive	Step-Up Transformer (PTN)
8	119078	Open	12/9/08 - open	12/9/08 - open					Westinghouse	OEM	NSSS Engineering Analysis and LAR (PTN)
9	119653	Open	11/24/08 - open	11/24/08 - open					Westinghouse	OEM	NSSS Engineering Analysis and LAR (PSL)
10	121847	Open	4/24/09 - open	4/24/09 - open					Westinghouse	OEM	New & Spent Fuel Criticality and Thermal Hydraulic Analysis (PTN)
11	119670	Open	2/18/09 - open	2/18/09 - open					Proto-Power	Single Source	Project Engineering Support (PSL)
12	115297	Open	8/27/08 - open	8/27/08 - open					Areva	Single Source	RSG Design Review and LAR Work (PSL)
13	115338	Open	8/27/08 - open	8/27/08 - open					Areva	Single Source	RCS Design Review (PTN)
14	105353	Complete	10/02/07 - 12/01/11	10/02/07 - 12/01/11					Shaw - Stone & Webster	Sole Source	Engineering Support (PSL & PTN)
15	117809	Open	12/02/08 - open	12/02/08 - open					Bechtel	Competitive Bid	Engineering Procurement Construction (PTN)
16	116088	Open	09/29/08 - open	09/29/08 - open					Siemens	Single Source	Low Pressure Turbine, Exciter, Exciter Inst. (PSL)
17	117820	Open	12/02/08 - open	12/02/08 - open					Bechtel	Competitive Bid	Engineering Procurement Construction (PSL)
18	116090	Open	9/29/08 - open	9/29/08 - open					Siemens	Single Source	Turbine, Generator/Exciter Upgrades & Inst. (PTN)
19	118328	Open	12/19/08 - open	12/19/08 - open					TEI	Competitive Bid	Condenser Tubes (PTN)
20	118206	Open	12/17/08 - open	12/17/08 - open					TEI	Competitive Bid	Moisture Separator Reheaters (PTN)
21	118205	Open	12/17/08 - open	12/17/08 - open					TEI	Competitive Bid	Moisture Separator Reheaters (PSL)
22	118241	Open	12/19/08 - open	12/19/08 - open					TEI	Competitive Bid	Feed Water Heaters (PTN)
23	112221	Open	4/22/08 - open	4/22/08 - open					Shaw - Stone & Webster	Single Source	Licensing Engineering and BOP Spec Development (PSL)
24	112177	Open	4/22/08 - open	4/22/08 - open					Shaw - Stone & Webster	Single Source	Licensing Engineering and BOP Spec Development (PTN)

A B C D

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO: 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

	(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
25	117272	Open	11/13/08 - open	11/13/08 - open					American Crane	Single Source	Gantry Crane Upgrade (PSL)
26	118224	Open	12/17/08 - open	12/17/08 - open					TEI	Competitive Bid	Feed Water Heaters (PSL)
27	115465	Open	9/03/08 - open	9/03/08 - open					Proto-Power	Single Source	Engineering Services (PTN)
28	118278	Open	12/19/08 - open	12/19/08 - open					TEI	Competitive Bid	TCW Heat Exchangers (PSL)
29	105720	Open	9/12/07 - open	9/12/07 - open					AREVA	Single Source	Neutronics Analysis (PSL)
30	116798	Complete	10/29/08 - 12/22/11	10/29/08 - 12/22/11					Cameron	Single Source	Ultrasonic Flow Meter Measuring System (PTN)
31	116107	Open	9/29/08 - open	9/29/08 - open					Cameron	Single Source	Ultrasonic Flow Meter Measuring System (PSL)
32	114114	Open	7/03/08 - open	7/03/08 - open					Richard Sipos	Single Source	Staff Augmentation (PSL)
33	115036	Complete	8/14/08 - 1/06/11	8/14/08 - 01/06/11					Babcock & Wilcox	Single Source	Steam Generator Component Design Review (PSL)
34	112228	Complete	4/23/08 - 06/11/11	4/23/08 - 06/11/11					Westinghouse	Single Source	Steam Generator Services for Moisture Carryover (PTN)
35	113030	Open	5/20/08 - open	5/20/08 - open					FPL Seabrook	Single Source	FPLE personnel supporting FPL Uprates (PSL & PTN)
36	115391	Open	8/29/08 - open	8/29/08 - open					NAI	Single Source	Radiological Consequence Analysis (PSL)
37	112987	Open	5/19/08 - open	5/19/08 - open					NAI	Single Source	Radiological Consequence Analysis (PTN)
38	4500521317	Open	9/08/09 - open	9/08/09 - open					Areva	Competitive	Inductors (PTN)
39	126246	Open	10/08/09 - open	10/08/09 - open					ABB	Competitive	Replacement Transformer Coolers (PSL)
40	126453	Open	11/05/09 - open	11/05/09 - open					Joseph Oat Corporation	Competitive	Cooling Water Heat Exchangers (PTN)
41	127777	Open	12/08/09 - open	12/08/09 - open					High Bridge	Single Source	Estimating Services (PTN)
42	127881	Open	12/22/09 - open	12/22/09 - open					Absolute Consulting	Single Source	Procedure Writers (PTN)
43	123762	Open	6/25/09 - open	6/25/09 - open					Key Controls of Tampa	OEM	Control System Tuning and Dynamic Analysis (PTN)
44	118988	Open	01/22/09 - open	01/22/09 - open					Holtec	Single Source	Fuel Storage Criticality and related analysis (PSL 2)
45	118563	Open	1/14/09 - open	1/14/09 - open					Holtec	Competitive	Fuel Storage Criticality and related analysis (PSL 1)
46	118827	Open	7/28/09 - open	7/28/09 - open					Western Services	Competitive	NSSS Simulator Reactor Core Model Upgrade (PSL)
47	118844	Open	01/15/09 - open	01/15/09 - open					Western Services	Competitive	NSSS Simulator Reactor Core Model Upgrade (PTN)
48	4500467077	Open	11/10/08 - open	11/10/08 - open					Siemens	Competitive	Generator Step-up Transformers (PSL)

A B C D

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET #: 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

	(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
49	130579	Open	5/01/10 - open	5/01/10 - open					Fisher Controls	Competitive	Modified Feedwater Regulating Valves/Actuators (PSL)
50	130160	Open	3/29/10 - open	3/29/10 - open					Flowserve Corp.	Competitive	Replacement Condensate Pumps (PSL)
51	130612	Open	4/22/10 - open	4/22/10 - open					Flowserve Corp.	Competitive	Condensate Pumps (PTN)
52	130649	Open	4/22/10 - open	4/22/10 - open					Flowserve Corp.	Competitive	Main Feedwater Pumps (PTN)
53	126227	Open	10/13/09 - open	10/13/09 - open					Invensys	OEM	Control System FWH, Moisture Separator (PTN)
54	129689	Open	3/17/10 - open	3/17/10 - open					Invensys	Competitive	Turbine Digital Upgrade (PTN)
55	130272	Open	4/08/10 - open	4/08/10 - open					Siemens Energy Inc.	Competitive	Electro-Hydraulic Fluid Systems (PTN)
56	131356	Open	5/21/10 - open	5/21/10 - open					Brand Energy Solutions	Competitive	Supply Scaffolding Material (PTN)
57	131391	Complete	5/25/10 - 4/19/11	5/25/10 - 4/19/11					BRV Construction	Competitive	Design/Construct fabrication area inside the CSF (PTN)
58	131599	Open	5/27/10 - open	5/27/10 - open					All Star Toltels	Competitive	Supply Cleaning Services (PTN)
59	4500586420	Open	6/16/10 - open	6/16/10 - open					Energy Erectors	Competitive	Electrical contract labor work @ 230 kV substation (PTN)
60	131928	Complete	6/14/10 - 02/28/11	6/14/10 - 02/28/11					Siemens Energy Inc.	Single Source	SL2-19 Pre-planning TG Installation Work (PSL2)
61	131533	Open	6/10/10 - open	6/10/10 - open					Areva	OEM	Non-Fuels NSSS Interim LAR (PSL 1 & 2)
62	131907	Open	6/11/10 - open	6/11/10 - open					Areva	OEM	Fuels Related Interim LAR/MOD for EPU (PSL)
63	131585	Open	6/15/10 - open	6/15/10 - open					Shaw - Stone & Webster	PDS	Interim LAR/MOD Support for EPU (PSL)
64	131393	Open	6/10/10 - open	6/10/10 - open					Fisher Controls	Competitive	Heater Drain BOP Replacement Valves (PSL)
65	131742	Open	6/16/10 - open	6/16/10 - open					Westinghouse	PDS	LAR/RAI for Non-Fuels NSSS related scope (PSL)
66	132077	Open	6/17/10 - open	6/17/10 - open					Siemens Energy Inc.	Single Source	Siemens Dedicated Resident Site Manager (PTN)
67	132078	Open	6/17/10 - open	6/17/10 - open					Siemens Energy Inc.	Single Source	Siemens Dedicated Resident Site Manager (PSL)
68	132235	Open	6/24/10 - open	6/24/10 - open					Enercon	Single Source	NFPA 805/Appendix R Support for (PTN)
69	131987	Open	6/25/10 - open	6/25/10 - open					Sargent & Lundy Inc.	Single Source	Engineering for Steam Bypass Control (PSL1)
70	131940	Open	6/30/10 - open	6/30/10 - open					Westinghouse	Competitive	Main Steam Turbine Control Replacement (PSL)
71	132283	Open	6/28/10 - open	6/28/10 - open					Shaw - Stone & Webster	PDS	EPU Feedwater Pump Nozzle Load Reduction (PSL)
72	2259675	Open	7/23/10 - open	7/23/10 - open					Joseph Oat Corporation	Competitive	Furnish New Spent Fuel Pool Heat Exchangers (PTN)

A B C D

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

COMPANY: Florida Power & Light Company

For the Year Ended: 12/31/2011
Witness: T. O. Jones

DOCKET NO: 120009-EI

	(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
73	2259669	Open	8/02/10 - open	8/02/10 - open					TAW	Competitive	Rewind/Refurbish/Upgrade Condensate Pumps (PTN)
74	2259997	Open	8/4/10 - open	8/4/10 - open					SPX Corporation	Replaces 115351	Valve Rework (PTN)
75	2259768	Open	8/06/10 - open	8/06/10 - open					Westinghouse	OEM	Design basis support for Umbrella Mods (PTN)
76	2260155	Open	8/16/10 - open	8/16/10 - open					Siemens Energy Inc.	Single Source	PSL 1-24 Pre-planning TG Installation Work
77	2260113	Open	9/23/10 - open	9/23/10 - open					Westinghouse	OEM	Rod Control System Upgrades (PSL)
78	2261536	Open	9/16/10 - open	9/16/10 - open					Washington Group	Competitive	Feedwater Heater Ultrasonic Testing (PTN)
79	2261750	Open	9/21/10 - open	9/21/10 - open					Modular Space	Competitive	Lease of 15-Wide Trailers for EPU (PTN)
80	2261747	Open	9/23/10 - open	9/23/10 - open					Westinghouse	PDS	EPU NSSS Engineering and Modification Support (PTN)
81	2262094	Open	9/28/10 - open	9/28/10 - open					Structural Integrity	Competitive	Assessment of Min Wall Thickness Effects (PTN)
82	2262201	Open	9/30/10 - open	9/30/10 - open					Fisher Controls	Replaces 131393	Heater Drain BOP Replacement Valves (PSL)
83	2262367	Open	10/04/10 - open	10/04/10 - open					Techcom International	Competitive	Engineering Services for Various Distributing Mods (PTN)
84	2262515	Open	10/06/10 - open	10/06/10 - open					Fisher Controls	Replaces 130576	Modified Feedwater Regulating Valves/Actuators (PSL)
85	2263036	Open	10/19/10 - open	10/19/10 - open					Flowsolve Corp.	Replaces 130180	Replacement Condensate Pumps (PSL)
86	2264195	Complete	11/16/10 - 4/20/11	11/16/10 - 4/20/11					Siemens Energy Inc.	OEM	Replacement Blade Rings (PSL)
87	2264240	Open	11/17/10 - open	11/17/10 - open					Siemens Energy Inc.	Single Source	T/G Installation SL2-19 Outage (PSL)
88	2263052	Open	11/11/10 - open	11/11/10 - open					Invensys	Single Source	Steam Bypass Control System (PSL)
89	2263649	Open	11/10/10 - open	11/10/10 - open					Areva NP Inc.	Competitive	Services of a Project Manager (PTN)
90	2264548	Complete	11/19/10 - 03/28/11	11/19/10 - 03/28/11					Graybar Electric	Competitive	Wire Cable (PTN)
91	2263930	Open	11/11/10 - open	11/11/10 - open					Brand Energy Solutions	Replaces 131356	Supply Scaffolding Material (PTN)
92	2264842	Open	11/30/10 - open	11/30/10 - open					Ronnies Turbine Services Inc.	Single Source	On Site SL2-19 Tech Support (PSL)
93	2264841	Open	11/30/10 - open	11/30/10 - open					Batsch Industries	Single Source	On Site SL2-19 Tech Support (PSL)
94	2264377	Open	11/30/10 - open	11/30/10 - open					Techcom International	Competitive	Turbine Digital Controls Verification and Validation (PTN)
95	2264914	Open	12/07/10 - open	12/07/10 - open					Westinghouse Electric	OEM	CEDMS Power Switch Refurbishment (PSL2)
96	2263951	Open	11/4/10 - open	11/4/10 - open					Graybar Electric	Competitive	Temporary Power Unit Substations for EPU (PTN)

A B C D

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO: 120009-EL

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

	(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
97	2285418	Open	12/16/10 - open	12/16/10 - open					Siemens Energy Inc.	OEM	Impl. Spares for EPU Turbine Gen. Work During SL2-19 (PSL)
98	4500589986	Open	7/6/10 - open	7/6/10 - open					Kennedy Construction	Competitive	Site preparation contract labor work @ 230 kV substation (PTN)
99	2285720	Open	01/4/11 - open	01/4/11 - open					Enercon Services	Competitive	Licensing/Design Basis/Program Modification (PTN)
100	2291203	Open	04/21/11 - open	04/21/11 - open					Enertech	Competitive	Main Steam Isolation Valve Replacement Actuator (PSL)
101	2267242	Open	01/27/11 - open	01/27/11 - open					Engineering Planning & Management	Competitive	Environmental Qualification Document (PTN)
102	2267468	Open	02/10/11 - open	02/10/11 - open					Feedforward Inc.	Competitive	DCS Mods (PSL)
103	2290208	Open	03/25/11 - open	03/25/11 - open					Feedforward Inc.	Competitive	Leading Edge Flow Meter Addition (PTN)
104	2267971	Open	02/15/11 - open	02/15/11 - open					Foster Wheeler North America	Competitive	SJAE Inter/After Condensers (PTN)
105	2290465	Open	03/31/11 - open	03/31/11 - open					Siemens	OEM	Design and Fabrication of Turbine Crossover piping (PTN)
106	2290463	Open	03/31/11 - open	03/31/11 - open					Siemens	OEM	Iron Bolts for Main Steam Generator Stator (PTN)
107	2290842	Open	04/08/11 - open	04/08/11 - open					Siemens	OEM	Blower Stationary Blade Rings (PSL)
108	2286521	Open	01/18/11 - open	01/18/11 - open					Stone & Webster	PDS	MSIV/MSCV Modification to Support EPU (PSL)
109	2264476	Open	05/11/11 - open	05/11/11 - open					Batsch Industries	Single Source	Turbine Generator Technical Support (PTN)
110	2291815	Open	04/28/11 - open	04/28/11 - open					BRV Construction	Competitive	Fossil Warehouse Demolition (PTN)
111	2290614	Open	05/02/11 - open	05/02/11 - open					Flowserve Corp.	Replaces 130649	Main Feedwater Pump Casing Modification (PTN)
112	2292773	Open	05/26/11 - open	05/26/11 - open					AAF MCQUAY	OEM	Design, Engineer, Fabricate and Deliver CRDM Coils (PTN)
113	2293950	Open	06/24/11 - 04/20/11	06/24/11 - 04/20/11					Siemens	Single Source	Turbine Generator Pre-outage planning activities (PTN)
114	2293653	Open	06/29/11 - open	06/29/11 - open					Thermal Engineering	Competitive	Design and Fabrication of Gland Steam Condensers (PTN)
115	2284247	Open	07/06/11 - open	07/06/11 - open					Ecological Associates	Competitive	Biological Plan of Study (PSL)
116	2294341	Open	07/11/11 - open	07/11/11 - open					Allon	Single Source	GL2008-01 Support (PSL)
117	2294494	Open	07/13/11 - open	07/13/11 - open					Enercon Services	Competitive	Emergency Containment Cooler Auto-start (PTN)
118	2294221	Open	07/11/11 - open	07/11/11 - open					Flowserve Corp.	Competitive	Main Steam Isolation Replacement Valves (PSL)
119	2264855	Open	07/21/11 - open	07/21/11 - open					Zachary Nuclear Engineering	Single Source	Project Engineering Support for EPU (PSL)
120	2295186	Open	08/02/11 - open	08/02/11 - open					Holtec International	Single Source	Metamix Chevrans for Spent Fuel Pool (PSL)

A B C D

Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO: 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

	(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
121	2295422	Open	8/10/11 - open	8/10/11 - open					Siemens Energy Inc.	OEM	Support Material for the EPU Turb-Gen Uprate (PTN)
122	2295071	Open	06/01/11 - open	06/01/11 - open					Stone & Webster	Single Source	Unit 1 Vibration and Support Mods for FW & Condensate (PSL)
123	2296049	Open	06/25/11 - open	06/25/11 - open					Cameron Tech.	Replaces 116796	Ultrasonic Flow Meter Measuring System (PTN)
124	2294671	Open	06/19/11 - open	06/19/11 - open					NWT Corporation	Competitive	Moisture Carry Over Testing for EPU (PTN)
125	2296556	Open	09/02/11 - open	09/02/11 - open					Sulzer Pumps	OEM	Modify, overhaul and refurbishment of the B & C AFW (PTN)
126	2296519	Open	09/06/11 - open	09/06/11 - open					Techcom International	Competitive	DCS Integration Plan for 3R26 and 4R27 (PTN)
127	2296623	Open	09/06/11 - open	09/06/11 - open					Tricen Technologies	Competitive	Unit 3 Condenser Tube Eddy Current Testing (PTN)
128	2296797	Open	09/09/11 - open	09/09/11 - open					Coastal Bus & Charter Lines (dba Need A Bus)	Competitive	Shuttle Bus Services for EPU (PSL)
129	2296330	Open	09/09/11 - open	09/09/11 - open					Flowserve Corp.	Competitive	Motor Operated Valves (PTN)
130	2298266	Open	10/12/11 - open	10/12/11 - open					Franmar Corporation	Competitive	Shuttle Bus Services for EPU (PTN)
131	2298406	Open	10/12/11 - open	10/12/11 - open					Master Lee Energy Services	Competitive	Fuel Movers for Metamix Inserts (PSL)
132	2298635	Open	10/14/11 - open	10/14/11 - open					Sargent & Lundy Inc.	Single Source	Engineering Service for the Charging System Modification (PSL 2)
133	2297556	Open	09/27/11 - open	09/27/11 - open					Siemens Energy Inc.	Single Source	Siemens Installation of 2A Main Power Transformer (PSL)
134	2299101	Open	10/27/11 - open	10/27/11 - open					Berkel & Company	Single Source	Mico Pile Construction (PTN)
135	2299894	Open	10/24/11 - open	10/24/11 - open					Day & Zimmermann NPS Inc.	Competitive	Installation of Trailer Support Services (PTN)
136	2299350	Open	11/01/11 - open	11/01/11 - open					Enercon Services Inc.	Competitive	Eng. Evaluation for EPU Mid-Cycle contingency plan (PSL)
137	2299518	Open	11/04/11 - open	11/04/11 - open					Radiation Safety & Control	Competitive	Truck Monitoring/Waste Characterization for EPU (PTN)
138	2297624	Open	10/27/11 - open	10/27/11 - open					Siemens Energy Inc.	OEM	Turbine Valve Conversion to EH (PTN)
139	2299631	Open	11/8/11 - open	11/8/11 - open					Tri-Tool Inc.	Single Source	Unit 1 LP Turbine Extraction Line Services (PSL)
140	2295953	Open	08/24/11 - open	08/24/11 - open					Marmon Wire & Cable	OEM	Misc Safety Related Wire and Cable, line items 1 - 23 (PTN)
141	2297055	Open	09/16/11 - open	09/16/11 - open					Thermal Engineering	Single Source	Replacement LP #4 Feedwater Heaters for EPU (PSL 2)
142	2300139	Open	11/21/11 - open	11/21/11 - open					Siemens Energy Inc.	Single Source	SL1-24 Turb-Gen. Installation (PSL 1)
143	2299624	Open	11/16/11 - open	11/16/11 - open					Ames Group LLC	Single Source	Upgrade Services for Feedwater Pumps (PSL)
144	2300467	Open	11/28/11 - open	11/28/11 - open					Weldtech Services	Single Source	SL1-24 Construction Management Oversight Services (PSL 1)

A B C D

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
True-up Filing: Contracts Executed**

Schedule T-7A

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO: 120009-EI

(1) EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work. Does not include corporate blanket agreements.

For the Year Ended: 12/31/2011
Witness: T. O. Jones

	(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Amount Expended in Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation If any)	Method of Selection and Document ID	Work Description
145	2299618	Open	11/04/11 - open	11/04/11 - open					Radiation Safety & Control	Competitive	Truck Monitoring/Waste Characterization for EPU (PTN)
146	2299350	Open	11/01/11 - open	11/01/11 - open					Enercon Services	Competitive	Engineering evaluation for EPU mid-cycle contingency plan (PSL)
147	2299631	Open	11/08/11 - open	11/08/11 - open					Tri-Tool	Single Source	LP Turbine Extraction Line Services for EPU (PSL 1)
148	NF-10-358 NF-11-178	Open	11/2/10 - open	11/2/10 - open					Westinghouse Electric	OEM	Spent Fuel Pool Critically Safety Analysis Support (PTN)
149	2301813	Open	12/28/11 - open	12/28/11 - open					Enercon Services Inc	Competitive	Motor Operated Valve Transfer Switches for EPU (PSL)
150	2301867	Open	12/28/11 - open	12/28/11 - open					Enercon Services Inc	Single Source	Develop Engineering Change Packages for EPU (PTN)
151	2301038	Open	12/14/11 - open	12/14/11 - open					Graftel Inc.	Competitive	Integrated Leak Rate Testing for EPU (PTN)
152	2261800	Open	09/28/10 - open	09/28/10 - open					L S Communications Mapps Inc	OEM	Supply of Simulator SCD Software Translator Upgrade (PTN)
153	130340	Open	04/02/10 - open	04/02/10 - open					MPR Associates	Competitive	Third Party Review of Siemens Turb-Gen. Analysis (PSL)
154	2301737	Open	12/21/11 - open	12/21/11 - open					PSI Energy Services	Single Source	Construction Management Oversight Services (PTN)
155	2301736	Open	12/21/11 - open	12/21/11 - open					Weldtech Services	Single Source	Construction Management Oversight Services (PTN)
156	2301871	Open	12/28/11 - open	12/28/11 - open					Zachry Nuclear Engineering	Single Source	Develop Engineering Change Packages for EPU (PTN)
157	2301858	Open	12/28/11 - open	12/28/11 - open					Sargent & Lundy Inc	Single Source	Develop TPCW Engineering Change Packages for EPU (PTN)
158	2000053226	Open	11/21/11 - open	11/21/11 - open					Ric-Man Construction	Competitive	Road and parking contract labor work 230kV substation (PTN)

A B C D

Legend:

PDS = Predetermined Source

OEM = Original Equipment Manufacturer

PSL = St. Lucie

PTN = Turkey Point

Notes:

In November 2011, FPL issued a Letter of Agreement (LOA) to Siemens for the PTN 3-26 Turbine Generator installation scope; however, the contract was not issued in 2011.



**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO 121869

Major Task or Tasks Associated With:

Supply Eight (8) Normal Containment Coolers and provide Testing Services

Vendor Identity:

AAF MCQUAY

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to AAF McQuay.

Dollar Value:

Total Contract Value through Revision 3 is



Contract Status:

Active

Term Begin:

April 29, 2009

Term End:

March 2013

Nature and Scope of Work:

Supply Eight (8) Normal Containment Coolers and provide Testing Services

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO 120769

Major Task or Tasks Associated With:

Replacement IsoPhase Bus Duct Coolers

Vendor Identity:

Calvert Company Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

1

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Calvert Company Inc.

Dollar Value:

Total Dollar Value through Revision 2 is



Contract Status:

Active

Term Begin:

March 26, 2009

Term End:

June 2012

Nature and Scope of Work:

Replacement IsoPhase Bus Duct Coolers, Technical Installation Support and Field Testing.

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO 124436

Major Task or Tasks Associated With:

Replacement Isolated Phase BusDuct

Vendor Identity:

Calvert Company inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Calvert Company Inc.

Dollar Value:

Total Dollar Value through Revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

July 17, 2009

Term End:

June 2012

Nature and Scope of Work:

Replacement Isolated Phase BusDuct, Demolition and Installation Services, Evaluation, Testing and Engineering

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO 121985

Major Task or Tasks Associated With:

Replacement Main Feedwater Pumps

Vendor Identity:

Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

5

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Flowsolve Corp.

Dollar Value:

Total Dollar Value through Revision 3 is

Contract Status:

Active

Term Begin:

April 24, 2009

Term End:

June 2012

Nature and Scope of Work:

Replacement Main Feedwater Pumps, spare parts and technical direction of installation.

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO 123137

Major Task or Tasks Associated With:

Main Feedwater Isolation Valves

Vendor Identity:

Flowserve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3


Number of Bids Received:

3

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Flowserve Corp.

Dollar Value:

Total Dollar Value through Revision 1 is 

Contract Status:

Active

Term Begin:

May 28, 2009

Term End:

Open

Nature and Scope of Work:

Main Feedwater Isolation Valves, Technical Field Services, Testing, Engineering and Documentation

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO 125454

Major Task or Tasks Associated With:

Replacement Heater Drain Pumps

Vendor Identity:

Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Flowsolve Corp.

Dollar Value:

Total Dollar Value through Revision 1 is 

Contract Status:

Active

Term Begin:

August 28, 2008

Term End:

June 2012

Nature and Scope of Work:

Replacement Heater Drain Pumps, Spare Heater, Technical Direction

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO 122154

Major Task or Tasks Associated With:

Step-Up Transformers

Vendor Identity:

Siemens Energy Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

2

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Siemens Energy Inc.

Dollar Value:

[REDACTED]

Contract Status:

Complete

Term Begin:

April 27, 2009

Term End:

Complete

Nature and Scope of Work:

Uprate Step-Up Transformers from 850 MVA to 970 MVA

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO 119078

Major Task or Tasks Associated With:

NSSS Engineering Evaluation and LAR Analysis for PTN Units 3 & 4

Vendor Identity:

Westinghouse Electric Co.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Dollar Value through Revision 6 is [REDACTED]

Contract Status:

Active

Term Begin:

Letter of Authorization issued 12/9/08; PO issued 1/26/09

Term End:

Open

Nature and Scope of Work:

NSSS Engineering Evaluation and LAR Analysis for PTN Units 3 & 4

Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the *current nature/scope of work*.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO 119653

Major Task or Tasks Associated With:

NSSS Engineering Evaluation and LAR Analysis for PSL Units 1 & 2

Vendor Identity:

Westinghouse Electric Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Dollar Value through Revision 4 is [REDACTED]

Contract Status:

Active

Term Begin:

Letter of Authorization issued 11/24/08; PO issued 2/17/09

Term End:

open

Nature and Scope of Work:

NSSS Engineering Evaluation and LAR Analysis for PSL Units 1 & 2

Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:
PD 115297 (PSL)

Major Task or Tasks Associated With:
Design Review for LAR (Steam Generator and Reactor Head)

Vendor Identity:
AREVA

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Dollar Value through Revision 8 [REDACTED]

Contract Status:
Active

Term Begin:
August 27, 2008

Term End:
open

Nature and Scope of Work:
Design Review for LAR (Steam Generator and Reactor Head)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:
PTN PO 115338

Major Task or Tasks Associated With:
Engineering Analysis

Vendor Identity:
AREVA

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Dollar Value through Revision 10, [REDACTED]

Contract Status:
Active

Term Begin:
August 27, 2008

Term End:
Open

Nature and Scope of Work:
Design review for the Reactor Coolant system, Control Rod Mechanism, EMA, CFD and BMI

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY:

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 105353

Major Task or Tasks Associated With:

Initial BOP Scoping Support for EPU

Vendor Identity:

Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Sole Source

Dollar Value:

Total Dollar Value through Revision 5 is

Contract Status:

Complete

Term Begin:

October 2, 2007

Term End:

December 1, 2011

Nature and Scope of Work:

BOP Scoping Support (engineering) for the EPU Project

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO 117809

Major Task or Tasks Associated With:

Provide Engineering, Procurement and Construction Services for
PTN

Vendor Identity:

Bechtel

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

6

Number of Bids Received:

5

Brief Description of Selection Process:

Bidders were evaluated against predetermined technical and commercial criteria, awarding to the lowest evaluated bidder.

Dollar Value:

PO value through Rev 4/Rel 0 is [REDACTED]

Contract Status:

Active

Term Begin:

December 2, 2008

Term End:

April 2013

Nature and Scope of Work:

Bechtel's scope includes project management, design engineering, procurement and material handling services, work order planning, construction/implementation, project controls, quality assurance, quality control, radiation protection (alara), safety, security interface, and other services as designated in the Contract documents.

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 116088

Major Task or Tasks Associated With:

Turbine/Generator Uprate

Vendor Identity:

Siemens Power

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single source

Dollar Value:

Total Max Dollar Value through Revision 4/Release 0

Contract Status:

Active

Term Begin:

September 29, 2008

Term End:

March 2013

Nature and Scope of Work:

Engineering, Parts and Installation for PSL Turbine/Generator Uprate

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the *current term of the contract*, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO 117820

Major Task or Tasks Associated With:

Provide Engineering, Procurement and Construction Services for PSL

Vendor Identity:

Bechtel

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

6

Number of Bids Received:

5

Brief Description of Selection Process:

Bidders were evaluated against predetermined technical and commercial criteria, awarding to the lowest evaluated bidder.

Dollar Value:

PO value through Rev 5/Rel 0 is [REDACTED]

Contract Status:

Active

Term Begin:

December 2, 2008

Term End:

December 2012

Nature and Scope of Work:

Bechtel's scope includes project management, design engineering, procurement and material handling services, work order planning, construction/implementation, project controls, quality assurance, quality control, radiation protection (alara), safety, security interface, and other services as designated in the Contract documents.

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 116090

Major Task or Tasks Associated With:

PTN Turbine Generator Uprate

Vendor Identity:

Siemens Power

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Max Contract Value through Rev. 3/Rel 0 is [REDACTED]

Contract Status:

Active

Term Begin:

September 29, 2008

Term End:

March 2013

Nature and Scope of Work:

PTN Engineering, Parts and Installation for Turbine/Generator Uprate

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 118328

Major Task or Tasks Associated With:

PTN Condenser Tube Bundles for Unit 3 & 4

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through Revision 5 is [REDACTED]

Contract Status:

Active

Term Begin:

December 19, 2008

Term End:

March 2013

Nature and Scope of Work:

Supply PTN Condenser Tube Bundles

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 118206

Major Task or Tasks Associated With:

PTN MSR's for Units 3 & 4

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

2

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through Revision 2 [REDACTED]

Contract Status:

Active

Term Begin:

December 17, 2006

Term End:

March 2013

Nature and Scope of Work:

Supply PTN Moisture Separator Reheaters

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 118205

Major Task or Tasks Associated With:

PSL MSR's for Units 1 & 2

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

2

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through Revision 5 is [REDACTED]

Contract Status:

Active

Term Begin:

December 17, 2008

Term End:

July 2012

Nature and Scope of Work:

Supply PSL Moisture Separator Reheaters

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 118241

Major Task or Tasks Associated With:

PTN Feedwater Heaters for Units 3 & 4

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

3

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Contract Value through Revision 2

Contract Status:

Active

Term Begin:

December 19, 2008

Term End:

March 2013

Nature and Scope of Work:

Supply PTN Feedwater Heaters

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 112221

Major Task or Tasks Associated With:

Engineering Services

Vendor Identity:

Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Blanket Purchase Order Max Value through Revision 17 to

Release 0 is [REDACTED]

Contract Status:

Active

Term Begin:

April 22, 2008

Term End:

December 2012

Nature and Scope of Work:

PSL BOP Engineering

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 112177

Major Task or Tasks Associated With:

Engineering Services

Vendor Identity:

Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Blanket Purchase Order Max Value through Revision 8 to Release Q is [REDACTED]

Contract Status:

Active

Term Begin:

April 22, 2008

Term End:

open

Nature and Scope of Work:

Engineering for the PSL Uprate Project

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO 117272

Major Task or Tasks Associated With:

Gantry crane repair/modification

Vendor Identity:

American Crane & Equip.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Sole Source/OEM

Dollar Value:

Total Dollar Value through Rev 6 is [REDACTED]

Contract Status:

Active

Term Begin:

November 13, 2008

Term End:

Open

Nature and Scope of Work:

Complete modification of Unit 1 crane and update of electrical components for Unit 2 crane

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 118224

Major Task or Tasks Associated With:

PSL Feedwater Heaters for Units 1 & 2

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Dollar Value thru Revision 6 [REDACTED]

Contract Status:

Active

Term Begin:

December 17, 2008

Term End:

open

Nature and Scope of Work:

Supply PSL Feedwater Heaters

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 115465

Major Task or Tasks Associated With:

Eng. Services for NSSS, BOP & Licensing Activities

Vendor Identity:

Proto-Power

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Dollar Value through revision 4 is [REDACTED]

Contract Status:

Active

Term Begin:

September 3, 2008

Term End:

Open

Nature and Scope of Work:

PTN Eng. Services for NSSS, BOP and Licensing Activities.

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 118278

Major Task or Tasks Associated With:

PSL Heat Exchangers for Units 1 & 2

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

3

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through revisions 4 is [REDACTED]

Contract Status:

Active

Term Begin:

December 19, 2008

Term End:

Open

Nature and Scope of Work:

Supply PSL Heat Exchangers

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY:

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 105720

Major Task or Tasks Associated With:

PSL Fuels Study

Vendor Identity:

Areva

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Order value through Revision 16 is [REDACTED]

Contract Status:

Active

Term Begin:

September 12, 2007

Term End:

open

Nature and Scope of Work:

Fuels Performance Study and Analysis

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PO # 116796

Major Task or Tasks Associated With:

Ultrasonic Flow Measuring System

Vendor Identity:

Cameron Technologies

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Blanket Purchase Order Value through Revision 1 to Release 0 is [REDACTED]

Contract Status:

Complete

Term Begin:

October 29, 2008

Term End:

December 22, 2011

Nature and Scope of Work:

Ultrasonic Flow Measuring System for PTN

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO 116107

Major Task or Tasks Associated With:

Ultrasonic Flow Measuring System

Vendor Identity:

Cameron Technologies

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Purchase Order Value through Revision 1 is [REDACTED]

Contract Status:

Awarded

Term Begin:

September 29, 2008

Term End:

Open

Nature and Scope of Work:

Ultrasonic Flow Measuring System for PTN

Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO 114114

Major Task or Tasks Associated With:

Staff Augmentation

Vendor Identity:

Richard Sipos

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source Justification

Dollar Value:

Total Blanket Purchase Order Value through Revision 6 is

Contract Status:

Active

Term Begin:

July 3, 2008

Term End:

open

Nature and Scope of Work:

Project Management Services

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 4500521317

Major Task or Tasks Associated With:

Inductors

Vendor Identity:

Areva

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive Selection

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

September 8, 2009

Term End:

Open

Nature and Scope of Work:

Supply of Inductors

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-BA

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 126248

Major Task or Tasks Associated With:

Replacement Transformer Coolers

Vendor Identity:

ABB

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

1

Brief Description of Selection Process:

Competitive Selection, Commercial and Technical Evaluation

Dollar Value:

Total Contract Value through Rev 2

Contract Status:

Active

Term Begin:

October 8, 2009

Term End:

Open

Nature and Scope of Work:

Replacement Transformer Coolers

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PO # 126453

Major Task or Tasks Associated With:

Turbine Plant Cooling Water Heat Exchangers

Vendor Identity:

Joseph Oat Corporation

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive Selection, Commercial and Technical Evaluation

Dollar Value:

Total Contract Value through revision 1 is [REDACTED]

Contract Status:

Active

Term Begin:

November 5, 2009

Term End:

Open

Nature and Scope of Work:

Supply Turbine Plant Cooling Water Heat Exchangers

Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO #127777

Major Task or Tasks Associated With:

Estimating Services

Vendor Identity:

High Bridge

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Contract Value through revision 2 is



Contract Status:

Active

Term Begin:

December 8, 2009

Term End:

Open

Nature and Scope of Work:

Estimating Services

Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 127881

Major Task or Tasks Associated With:

Procedure Writers

Vendor Identity:

Absolute Consulting

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 22, 2009

Term End:

Open

Nature and Scope of Work:

Procedure Writers

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-E1

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO #118988

Major Task or Tasks Associated With:

Fuel Storage Criticality and Related Analysis (PSL 2)

Vendor Identity:

Holtec

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Purchase Order Value through Revision 4 is [REDACTED]

Contract Status:

Active

Term Begin:

January 22, 2009

Term End:

Open

Nature and Scope of Work:

Fuel Storage Criticality and Related Analysis (PSL 2)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO #118563

Major Task or Tasks Associated With:

Fuel Storage Criticality and Related Analysis (PSL 1)

Vendor Identity:

Holtec

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Purchase Order Value through Revision 5 is

Contract Status:

Active

Term Begin:

January 14, 2009

Term End:

Open

Nature and Scope of Work:

Fuel Storage Criticality and Related Analysis (PSL 1)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO # 4500467077

Major Task or Tasks Associated With:

PSL Generator Step-up Transformers

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

7

Number of Bids Received:

7

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

November 10, 2008

Term End:

Open

Nature and Scope of Work:

PSL Generator Step-up Transformers

Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 130612

Major Task or Tasks Associated With:

Condensate Pumps

Vendor Identity:

Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Contract Value through Revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

April 22, 2010

Term End:

Open

Nature and Scope of Work:

Condensate Pumps

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO #130649

Major Task or Tasks Associated With:

Main Feedwater Pumps

Vendor Identity:

Flowserve Corp

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

1

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

April 22, 2010

Term End:

Open

Nature and Scope of Work:

Main Feedwater Pumps

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 126227

Major Task or Tasks Associated With:

Control System FWH, Moisture Separator

Vendor Identity:

Invensys

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Dollar Value through revision 9

Contract Status:

Active

Term Begin:

October 13, 2009

Term End:

Open

Nature and Scope of Work:

Control System FWH, Moisture Separator

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 129689

Major Task or Tasks Associated With:

Turbine Digital Upgrade

Vendor Identity:

Invensys

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Dollar Value through Revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

March 17, 2010

Term End:

Open

Nature and Scope of Work:

Turbine Digital Upgrade

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the *contract number* or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 130272

Major Task or Tasks Associated With:

Electro-Hydraulic Fluid Systems

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Dollar Value through Rev 4 is [REDACTED]

Contract Status:

Active

Term Begin:

April 8, 2010

Term End:

Open

Nature and Scope of Work:

Electro-Hydraulic Fluid Systems

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO # 131928

Major Task or Tasks Associated With:

Pre-planning SL2-19

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Complete

Term Begin:

June 14, 2010

Term End:

February 28, 2011

Nature and Scope of Work:

SL2-19 Pre-planning work to support station milestones for the Turbine Generator Installation

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO # 131533

Major Task or Tasks Associated With:

Non-Fuels NSSS Interim LAR (PSL 1 & 2)

Vendor Identity:

Areva

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Predetermined Source

Dollar Value:

Total Contract Value through revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

June 10, 2010

Term End:

Open

Nature and Scope of Work:

Non-Fuels NSSS Interim LAR (PSL 1 & 2)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO # 131907

Major Task or Tasks Associated With:

Fuels Related Interim LAR/MOD for EPU at PSL

Vendor Identity:

Areva

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Predetermined Source

Dollar Value:

Total Contract Value through Revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

June 11, 2010

Term End:

Open

Nature and Scope of Work:

Fuels Related Interim LAR/MOD for EPU at PSL

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO # 131585

Major Task or Tasks Associated With:

Interim LAR/MOD for EPU at PSL

Vendor Identity:

Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Predetermined Source

Dollar Value:

Total Contract Value through Revision 4 is [REDACTED]

Contract Status:

Active

Term Begin:

June 15, 2010

Term End:

Open

Nature and Scope of Work:

Interim LAR/MOD for EPU at PSL

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:
PSL PO #131742

Major Task or Tasks Associated With:
LAR/Request for Additional Information

Vendor Identity:
Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Predetermined Source

Dollar Value:

Total Contract value through revision 2 is [REDACTED]

Contract Status:
Active

Term Begin:
June 16, 2010

Term End:
Open

Nature and Scope of Work:
LAR/Request for Additional Information for Non-Fuels related scope

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO #131940

Major Task or Tasks Associated With:

Main Steam Turbine Control Replacement

Vendor Identity:

Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

4

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Max Contract value through Rev 2 to Release 0

Contract Status:

Active

Term Begin:

June 30, 2010

Term End:

Open

Nature and Scope of Work:

Main Steam Turbine Control Replacement

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PQ #2259675

Major Task or Tasks Associated With:

Furnish New Spent Fuel Pool Heat Exchangers

Vendor Identity:

Joseph Oat Corporation

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

2

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

July 23, 2010

Term End:

Open

Nature and Scope of Work:

Furnish New Spent Fuel Pool Heat Exchangers

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.
For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 2259669

Major Task or Tasks Associated With:

Rewind/Refurbish Upgrade Condensate Pumps

Vendor Identity:

Tampa Armature Works

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

August 2, 2010

Term End:

Open

Nature and Scope of Work:

Rewind/Refurbish Upgrade Condensate Pumps

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO #2260113

Major Task or Tasks Associated With:

PSL Rod Control System Upgrades

Vendor Identity:

Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Contract Value through Amendment 3 [REDACTED]

Contract Status:

Active

Term Begin:

September 23, 2010

Term End:

Open

Nature and Scope of Work:

PSL Rod Control System Upgrades

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO #2281747

Major Task or Tasks Associated With:

EPU NSSS Engineering and Modification Support

Vendor Identity:

Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Predetermined Source

Dollar Value:

Total Contract Value through Amendment 2 [REDACTED]

Contract Status:

Active

Term Begin:

September 23, 2010

Term End:

Open

Nature and Scope of Work:

EPU NSSS Engineering and Modification Support

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO #2264240

Major Task or Tasks Associated With:

PSL 2-19 Turbine Generator Installation Contract

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

November 17, 2010

Term End:

Open

Nature and Scope of Work:

PSL 2-19 Turbine Generator Installation Contract

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO #2284841

Major Task or Tasks Associated With:

SL 2-19 Technical Support

Vendor Identity:

Batsch Industries

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This Indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Contract Value through Amendment 2 [REDACTED]

Contract Status:

Active

Term Begin:

November 30, 2010

Term End:

Open

Nature and Scope of Work:

SL 2-19 Technical Support

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

2264914

Major Task or Tasks Associated With:

CEDMS Power Switch Refurbishment (PSL 2)

Vendor Identity:

Westinhouse Electric

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 7, 2010

Term End:

Open

Nature and Scope of Work:

CEDMS Power Switch Refurbishment (PSL 2)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO #2285418

Major Task or Tasks Associated With:

Implementation Spares for Turbine Generator Work

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Contract Value through Amendment 2

Contract Status:

Active

Term Begin:

December 16, 2010

Term End:

Open

Nature and Scope of Work:

Implementation Spares for Turbine Generator Work

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO #2285720

Major Task or Tasks Associated With:

Licensing/Design Basis/Program Modification

Vendor Identity:

Enercon

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

2

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

January 4, 2011

Term End:

Open

Nature and Scope of Work:

Licensing/Design Basis/Program Modification

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.
For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO# 2291203

Major Task or Tasks Associated With:

Main Steam Isolation Valve Replacement Actuator

Vendor Identity:

Enertech

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

2

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Contract Value through Amendment 3 [REDACTED]

Contract Status:

Active

Term Begin:

April 21, 2011

Term End:

Open

Nature and Scope of Work:

Main Steam Isolation Valve Replacement Actuator

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO# 2290465

Major Task or Tasks Associated With:

Design, Engineering and Fabrication of Turbine Crossover piping

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

March 31, 2011

Term End:

Open

Nature and Scope of Work:

Design, Engineering and Fabrication of Turbine Crossover piping

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO# 2290614

Major Task or Tasks Associated With:

Main Feedwater Pump Casing Modifications

Vendor Identity:

Flowserve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

N/A

Number of Bids Received:

N/A

Brief Description of Selection Process:

Replaces PO 130549

Dollar Value:

Total Contract Value through Amend 1

Contract Status:

Active

Term Begin:

May 2, 2011

Term End:

Open

Nature and Scope of Work:

Main Feedwater Pump Casing Modifications

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO# 2293950

Major Task or Tasks Associated With:

Turbine Generator Pre-Outage Planning PTN 3 & 4

Vendor Identity:

Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Contract value through Amendment 1 [REDACTED]

Contract Status:

Active

Term Begin:

June 24, 2011

Term End:

Open

Nature and Scope of Work:

Turbine Generator Pre-Outage Planning PTN 3 & 4
(Turbine Generator Installation)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO# 2295188

Major Task or Tasks Associated With:

Metamic Chevrans for Spent Fuel Pool

Vendor Identity:

Holtec

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

August 2, 2011

Term End:

Open

Nature and Scope of Work:

Metamic Chevrans for Spent Fuel Pool

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO# 2296556

Major Task or Tasks Associated With:

Modification, overhaul and refurbishment of the B and C AFW

Vendor Identity:

Sulzer Pumps

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

September 2, 2011

Term End:

Open

Nature and Scope of Work:

Modification, overhaul and refurbishment of the B and C AFW

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO# 2298406

Major Task or Tasks Associated With:

Fuel Movers for Metamic Inserts

Vendor Identity:

Master Lee Energy Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

1

Brief Description of Selection Process:

Competitive

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

October 12, 2011

Term End:

Open

Nature and Scope of Work:

Fuel Movers for Metamic Inserts

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PSL PO# 2287556

Major Task or Tasks Associated With:

Siemens Installation of 2A Main Power Transformer

Vendor Identity:

Siemens Energy Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

September 27, 2011

Term End:

Open

Nature and Scope of Work:

Siemens Installation of 2A Main Power Transformer

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO# 2255953

Major Task or Tasks Associated With:

Misc Safety Related Wire and Cable

Vendor Identity:

Marron Wire & Cable

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Contract Value through revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

August 24, 2011

Term End:

Open

Nature and Scope of Work:

Misc Safety Related Wire and Cable

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO# 2297055

Major Task or Tasks Associated With:

Replacement Unit 2 LP #4 Feedwater Heaters for EPU

Vendor Identity:

Thermal Engineering

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

September 16, 2011

Term End:

Open

Nature and Scope of Work:

Replacement Unit 2 LP #4 Feedwater Heaters for EPU

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO# 2300139

Major Task or Tasks Associated With:

SL 1-24 Turbine Generator Installation

Vendor Identity:

Siemens Energy Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

September 16, 2011

Term End:

Open

Nature and Scope of Work:

SL 1-24 Turbine Generator Installation

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO# 2299924

Major Task or Tasks Associated With:

Upgrade Services for Feedwater Pumps

Vendor Identity:

Ames Group LLC

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Contract Value through revision 1 [REDACTED]

Contract Status:

Active

Term Begin:

November 16, 2011

Term End:

Open

Nature and Scope of Work:

Upgrade Services for Feedwater Pumps

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.
For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PSL PO# 2300487

Major Task or Tasks Associated With:

Construction Management Oversight Services for SL1-24

Vendor Identity:

Weldtech Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

November 28, 2011

Term End:

Open

Nature and Scope of Work:

Construction Management Oversight Services for SL1-24

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

NF-10-358 and NF-11-178

Major Task or Tasks Associated With:

Spent Fuel Criticality Safety Analysis Support (PTN)

Vendor Identity:

Westinhouse Electric

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

1 [REDACTED]

Contract Status:

Active

Term Begin:

November 2, 2010

Term End:

Open

Nature and Scope of Work:

Spent Fuel Criticality Safety Analysis Support (PTN)

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 2301867

Major Task or Tasks Associated With:

Develop Engineering Change Packages for EPU at PTN

Vendor Identity:

Ensercon Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 28, 2011

Term End:

Open

Nature and Scope of Work:

Develop Engineering Change Packages for EPU at PTN

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO # 2251800

Major Task or Tasks Associated With:

Supply of Simulator SCD Software Translator Upgrade

Vendor Identity:

L 3 Communications Mapps Inc

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Contract Value through Amendment 2 [REDACTED]

Contract Status:

Active

Term Begin:

September 28, 2010

Term End:

Open

Nature and Scope of Work:

Supply of Simulator SCD Software Translator Upgrade

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO # 2301737

Major Task or Tasks Associated With:

Construction Management Oversight Services for PTN

Vendor Identity:

PSI Energy Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 21, 2011

Term End:

Open

Nature and Scope of Work:

Construction Management Oversight Services for PTN

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.
For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO # 2301736

Major Task or Tasks Associated With:

Construction Management Oversight Services

Vendor Identity:

Weldtech Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 21, 2011

Term End:

Open

Nature and Scope of Work:

Construction Management Oversight Services

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011
Witness: T. O. Jones

Contract No.:

PTN PO #2301871

Major Task or Tasks Associated With:

Develop Engineering Changes Packages for EPU at PTN

Vendor Identity:

Zachry Nuclear Engineering

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 28, 2011

Term End:

Open

Nature and Scope of Work:

Develop Engineering Changes Packages for EPU at PTN

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed**

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FPL

DOCKET NO: 120009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2011

Witness: T. O. Jones

Contract No.:

PTN PO #2301858

Major Task or Tasks Associated With:

Develop TPCW Changes Packages for EPU at PTN

Vendor Identity:

Sargent & Lundy

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:


December 28, 2011

Term End:

Open

Nature and Scope of Work:

Develop TPCW Changes Packages for EPU at PTN

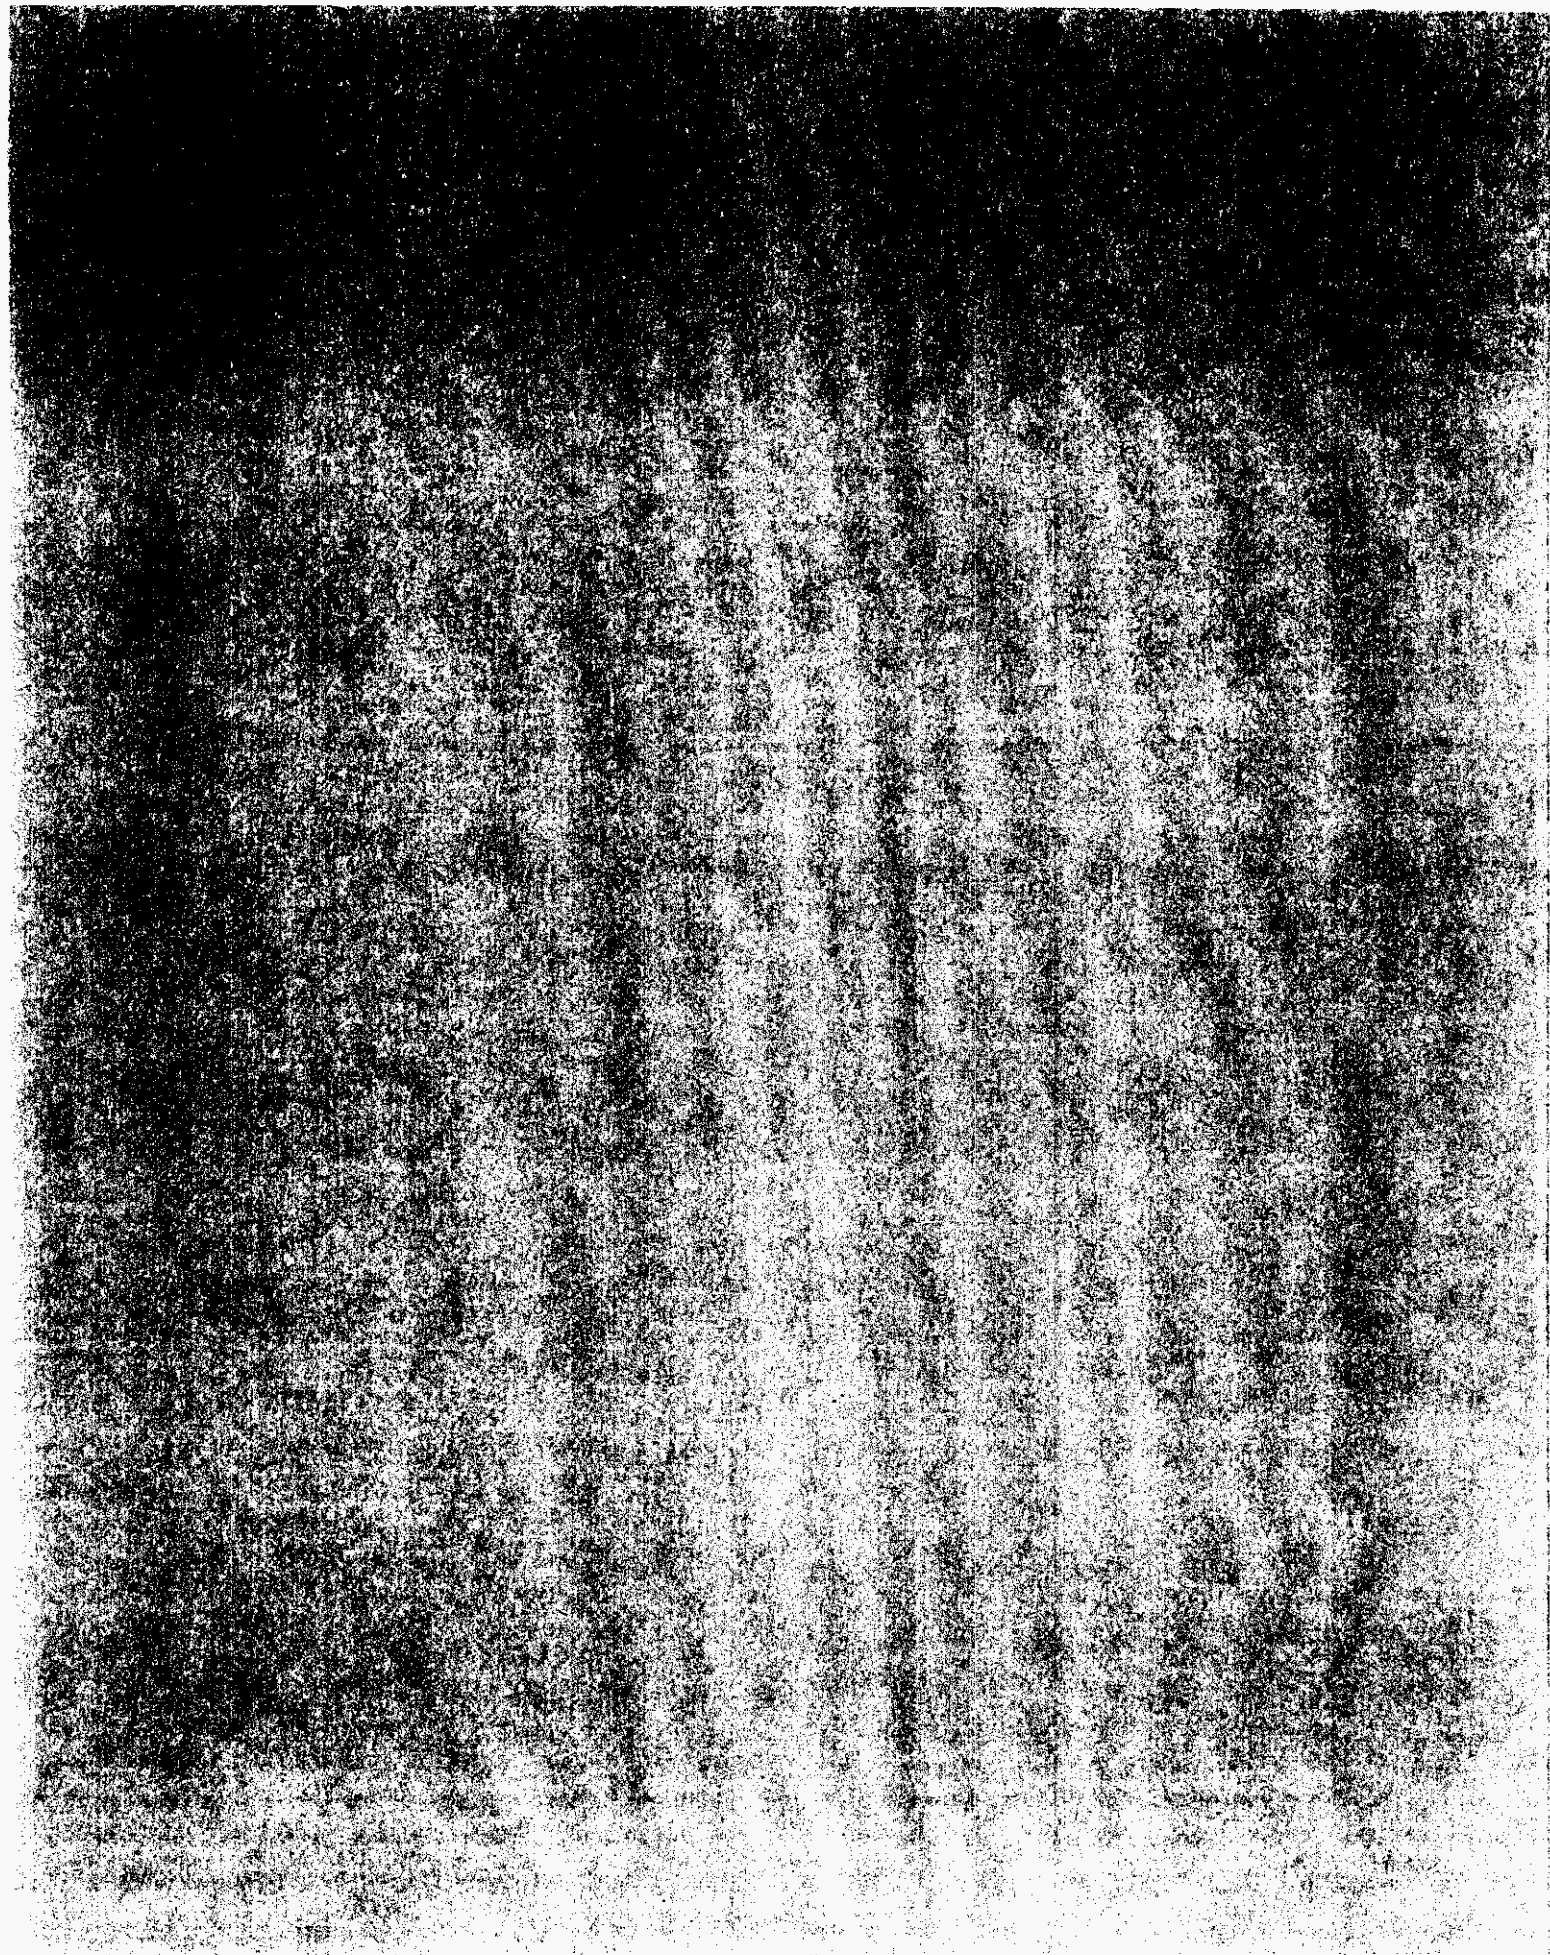

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed

Schedule T-7A

[Section (8)(c)]

FLORIDA PUBLIC SERVICE COMMISSION

EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and description of work.

COMPANY: Florida Power & Light Company


For the Year Ended: 12/31/2011
Witness: Steven D. Scroggs

DOCKET NO.: 120009-EI

CONFIDENTIAL CONFIDENTIAL CONFIDENTIAL CONFIDENTIAL

(A)		(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2010)	Actual amount expended In Current Year (2011)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation If any)	Method of Selection and Document ID	Work Description
1	4500395492	Open- CO#38	11/6/2007- open	10/11/2011- open	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	Bechtel Power Corp	Comp Bid/ Single Source/ Predetermined Source	Engineering Services to Support Preparation of COLA and SCA and Response to post-submittal RA's.
2	4500404639	Open- CO#6	1/31/2008- open	4/21/2011- open					Westinghouse Electric Co	Sole Source/ Predetermined Source	Engineering Services to Support Preparation of COLA and Response to post-submittal RA's.
3	4500425707	Open-CO#5	5/23/2008- open	1/3/2011- open					HDR Engineering, Inc.	Comp Bid/ Single Source	Conceptual Engineering of Cooling Water Supply and Discharge
4	4500430034	Open- CO#1	6/16/2008- open	1/28/2011- open					Electric Power Research Institute	Single Source	Advanced Nuclear Technology; Near term deployment of Advanced Light Water Reactors
5	4500443122	Open-CO#3	8/9/2008- open	11/29/2011- open					Eco Metrics, Inc.	Single Source	Environmental Consulting Services
6	4500517152	Open-CO#3	7/10/2009- open	12/17/2010- open					McNabb Hydrogeologic Consulting Inc	Single Source	Turkey Point 6&7 Post SCA Submittal and UIC Licensing Support
7	4500518160	Open-CO#5	7/23/2009- open	6/24/2011- open					Golder Associates Inc	Single Source	Turkey Point 6&7 Post SCA Submittal Support
8	4500518167	Open- CO#6	7/23/2009- open	9/14/2011- open					Environmental Consulting and Technology Inc	Single Source/ Predetermined Source	Turkey Point 6&7 SCA Support
9	4500538449	Open-CO#2	10/12/2009- open	11/29/2011- open					McNabb Hydrogeologic Consulting Inc	Comp Bid/ Single Source	Turkey Point 6&7 UIC Subject Matter Expert Support
10	4500492222	Open- CO#2	3/17/2009- open	12/22/2011- open					Experts US LLC(FKA, Jefferson Wells International)	Comp Bid/ Single Source	New Nuclear Audit
11	4500587305	Open-CO#1	6/29/2010- open	9/1/2010- open					Dickerson Florida Inc	Comp Bid	Turkey Point 6&7 Exploratory/UIC Well Site Development
12	4500652043	Open-CO#1	3/3/2011- open	12/29/2011- open					Layne Christensen Company	Comp Bid	Turkey Point 6&7 Exploratory/UIC Well and Dual Zone Monitor Well Installation

A B C D

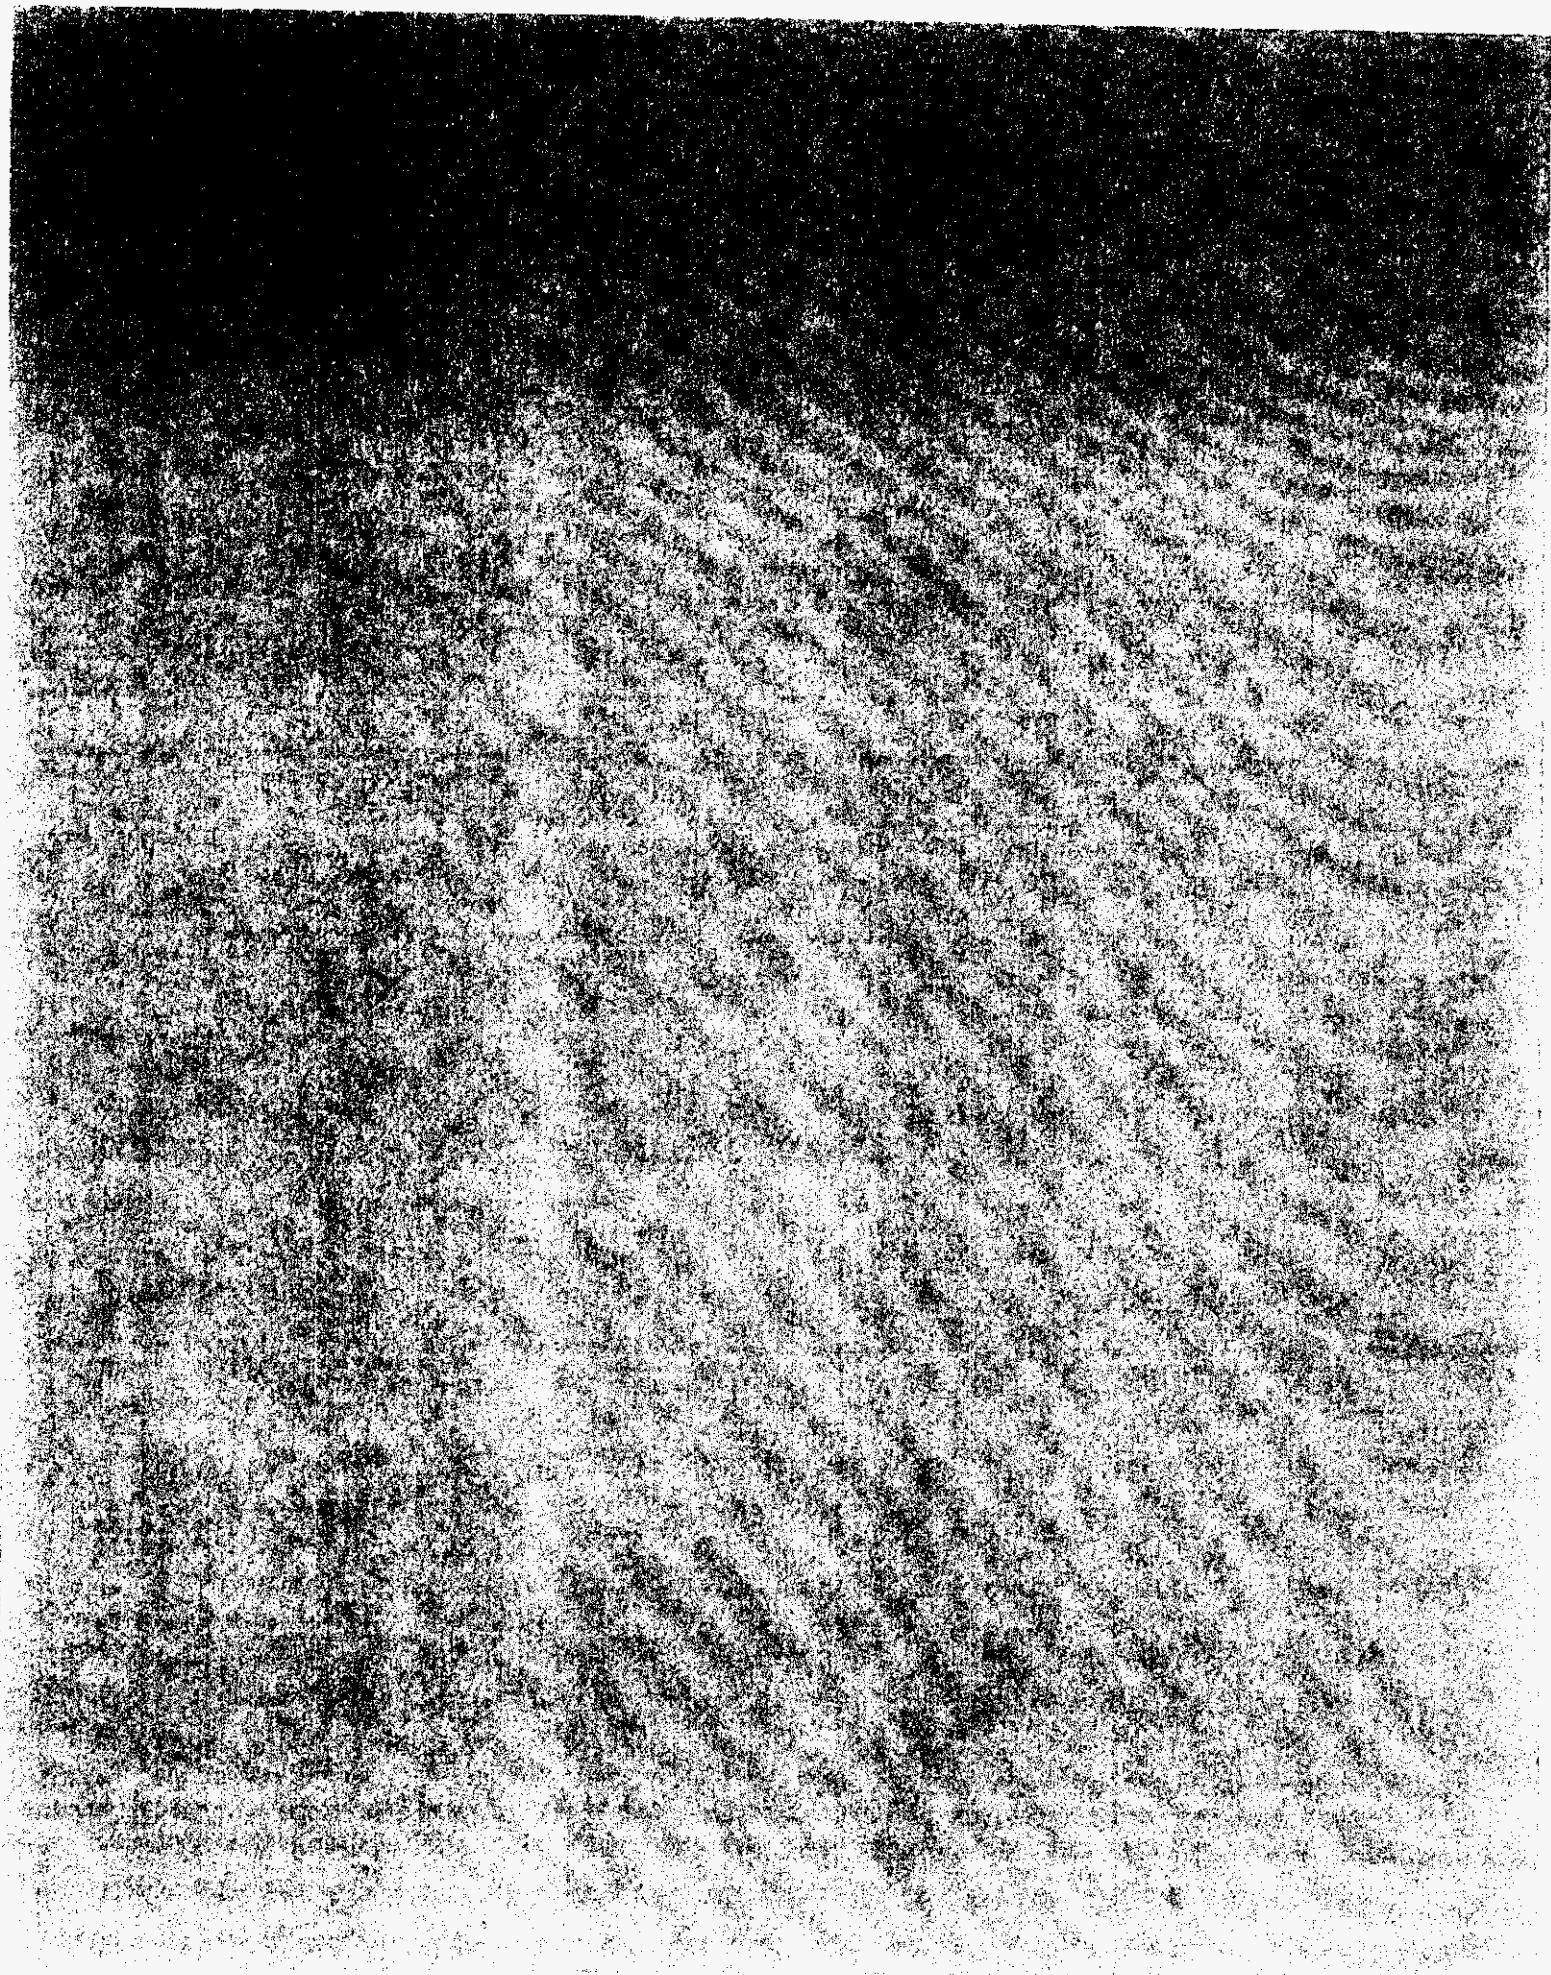

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:

4500395492

Major Task or Tasks Associated With:

COLA and SCA preparation and support

Vendor Identity:

Bechtel Power Corporation

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct

Number of Vendors Solicited:

Two

Number of Bids Received:

Two

Brief Description of Selection Process:

Initial contract competitively bid; change orders #01-#11 issued single source; all subsequent change orders issued Predetermined Source

Dollar Value:

1

Contract Status:

Active- CO#38

Term Begin:

11/6/2007

Term End:

2/27/2016

Nature and Scope of Work:

Engineering Services to Support Preparation of COLA and SCA, including post-submittal support for RAI responses.

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (b)(3)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

COMPANY: Florida Power & Light Company

DOCKET NO.: 120009-EI

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:

4500404639

Major Task or Tasks Associated With:

COLA support

Vendor Identity:

Westinghouse Electric Company

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct

Number of Vendors Solicited:

One

Number of Bids Received:

One

Brief Description of Selection Process:

Sole source justification; designated as Predetermined
Source March 2009

Dollar Value:

1

Contract Status:

Active- CO#6

Term Begin:

1/31/2008

Term End:

6/29/2014

Nature and Scope of Work:

Engineering Services to Support Preparation of COLA,
including post-submittal support for RAI responses.

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: Florida Power & Light Company
DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:

4500430034

Major Task or Tasks Associated With:

COLA and SCA preparation and support

Vendor Identity:

Electric Power Research Institute

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct

Number of Vendors Solicited:

Two

Number of Bids Received:

Two

Brief Description of Selection Process:

Single

Dollar Value:

1

Contract Status:

Active- CO#1

Term Begin:

6/16/2008

Term End:

6/29/2014

Nature and Scope of Work:

Engineering Services to Support Preparation of COLA and SCA, including post-submittal support for RAI responses.

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (B)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:

4500518160

Major Task or Tasks Associated With:

Post SCA Submittal support

Vendor Identity:

Golder Associates, Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct or Indirect relationship with the vendor

Number of Vendors Solicited:

One

Number of Bids Received:

One

Brief Description of Selection Process:

Single source; Designated as Predetermined Source February 2010

Dollar Value:

1

Contract Status:

Active- CO#5

Term Begin:

7/23/2009

Term End:

6/28/2012

Nature and Scope of Work:

Post SCA Submittal support

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: Florida Power & Light Company
DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:

4500518167

Major Task or Tasks Associated With:

SCA Support

Vendor Identity:

Environmental Consulting and Technology, Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct

Number of Vendors Solicited:

One

Number of Bids Received:

One

Brief Description of Selection Process:

Single source; Designated as Predetermined Source December 2009

Dollar Value:

1

Contract Status:

Active- CO#6

Term Begin:

7/23/2009

Term End:

6/28/2012

Nature and Scope of Work:

SCA Support

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (B)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:

4500536449

Major Task or Tasks Associated With:

Turkey Point 6&7 UIC Subject Matter Expert Support

Vendor Identity:

McNabb Hydrogeologic Consulting

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct

Number of Vendors Solicited:

One

Number of Bids Received:

One

Brief Description of Selection Process:

Competitive Bid for initial Order, Single Source justification for Change Orders

Dollar Value:

1

Contract Status:

Active- CO#2

Term Begin:

10/12/2009

Term End:

6/29/2013

Nature and Scope of Work:

Turkey Point 6&7 UIC Subject Matter Expert Support

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO.: 120009-EI

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:

4500587305

Major Task or Tasks Associated With:

Turkey Point Units 6&7 Exploratory/UIC Well Site Development

Vendor Identity:

Dickerson Florida, Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct

Number of Vendors Solicited:

Eight

Number of Bids Received:

Five

Brief Description of Selection Process:

Competitive Bid

Dollar Value:

1

Contract Status:

Active- CO#1

Term Begin:

6/29/2010

Term End:

6/30/2011

Nature and Scope of Work:

Turkey Point Units 6&7 Exploratory/UIC Well Site Development

Project Name: New Nuclear
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Final True-up Filing: Contracts Executed Details

[Section (8)(c)]

Schedule T-7B

FLORIDA PUBLIC SERVICE COMMISSION

EXPLANATION: Provide additional details of contracts executed in excess of \$1 million including, the nature and scope of the work, the nature of any affiliation with selected vendor, the method of vendor selection, brief description of vendor selection process, and current status of the contract.

COMPANY: Florida Power & Light Company

DOCKET NO.: 120009-EI

For the Year Ended 12/31/2011
Witness: Steven D. Scroggs

Contract No.:

4500652043

Major Task or Tasks Associated With:

Turkey Point 6&7 Exploratory/UIC Well and Dual Zone Monitor Well Installation

Vendor Identity:

Layne Christensen Company

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct

Number of Vendors Solicited:

Three

Number of Bids Received:

Three

Brief Description of Selection Process:

Competitive Bid

Dollar Value:

1

Contract Status:

Active- CO#1

Term Begin:

3/3/2011

Term End:

9/27/2012

Nature and Scope of Work:

Turkey Point 6&7 Exploratory/UIC Well and Dual Zone Monitor Well Installation
