

REDACTED

BEFORE THE FLORIDA PUBLIC SERVICE COMMISSION

In re: Nuclear Power Plant Cost
Recovery Clause

Docket No. 110009-EI
Submitted for Filing: July 15, 2011

**PROGRESS ENERGY FLORIDA, INC.'S THIRTEENTH REQUEST FOR
CONFIDENTIAL CLASSIFICATION REGARDING PORTIONS OF THE LATE FILED
EXHIBIT OF JOHN ELNITSKY AND THE LATE FILED EXHIBITS OF JON FRANKE**

Exhibit B

DOCUMENT NUMBER-DATE


04896 JUL 15 =

FPSC-COMMISSION CLERK

CONFIDENTIAL

PEF Planning Scenarios

Docket No. 110009-EI
Progress Energy Florida, Inc.
John Elnitsky 6/13/2011 Deposition
Late Filed Exhibit No. 1



DOCUMENT NUMBER-CAT
04896 JUL 15 =
FPSC-COMMISSION CLERK

**Docket No. 110009-EI, In Re: Nuclear Cost Recovery Clause
Deposition of Jon Franke
June 13, 2011**

Late Filed Exhibit #6: ICCMS contract execution date and amount of contract.

CONFIDENTIAL


The ICCMS contract with Scientech has an effective date of 3/31/11 and was executed by both parties on 4/1/11. The contract is for a [REDACTED]

**Docket No. 110009-EI, In Re: Nuclear Cost Recovery Clause
Deposition of Jon Franke
June 13, 2011**

Late Filed Exhibit #7: The Company's comparable estimate for construction scope of work for the EPU phase prior to when the November 2010 SGT study was conducted.

CONFIDENTIAL

The contractor SGT's construction estimate totaled \$ 112.3M, consisting of the following categories:

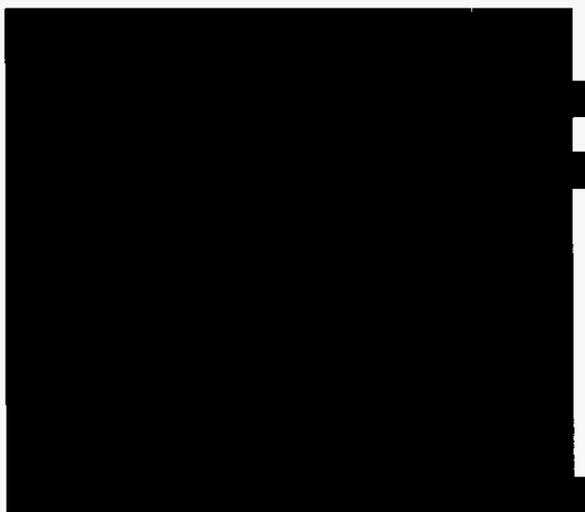

The contractor's construction estimate was reviewed by the EPU project team and resulted in a reduction of \$34.7M to \$77.6M. [REDACTED] in contingency was then added to the contractor's construction estimate based on engineering being approximately 50% complete when the estimate was prepared.

Consequently, in responding to the question presented, the appropriate number for comparison from the SGT study is the total construction estimate added for the Balance of Work portion (which does not include POD or Siemens Turbine Contract) of \$77.6M + [REDACTED]

In Integrated Project Plan ("IPP") Revision 3 dated May 24, 2010, the estimate for construction scope of work for 2010 and 2011/2012 prior to the SGT study being performed in November of 2010 was approximately [REDACTED]. These estimates were not performed like the SGT estimate provided so it is not a direct comparison.
