



Jessica Cano
Principal Attorney
Florida Power & Light Company
700 Universe Boulevard
Juno Beach, FL 33408-0420
(561) 304-5226
(561) 691-7135 (Facsimile)

REDACTED

May 1, 2013

VIA HAND DELIVERY

Ms. Ann Cole
Division of the Commission Clerk and
Administrative Services
Florida Public Service Commission
Betty Easley Conference Center
2540 Shumard Oak Boulevard, Room 110
Tallahassee, FL 32399-0850

claim of confidentiality
 notice of intent
 request for confidentiality
 filed by OPC

For DN 02394-13, which
is in locked storage. You must be
authorized to view this DN.-CLK

RECEIVED-FPSC
13 May -1 PM 2:16
COMMISSION
CLERK

Re: Docket No. 130009-EI; Nuclear Power Plant Cost Recovery Clause

Dear Ms. Cole:

Enclosed for filing on behalf of Florida Power & Light Company ("FPL") is a Request for Confidential Classification of Jones Testimony and Exhibits TOJ-13 and SDS-7. Seven copies of FPL's request, including Exhibits C and D, are included. Also included are one copy of Exhibit A and two copies of Exhibit B.

Exhibit A consists of the confidential documents, and all information that FPL asserts is entitled to confidential treatment has been highlighted. Exhibit B is an edited version of Exhibit A, in which the information FPL asserts is confidential has been redacted. Exhibit C consists of FPL's justification table supporting its Request for Confidential Classification. Exhibit D contains two affidavits in support of FPL's Request for Confidential Classification. Also included in this filing is a compact disc containing FPL's Request for Confidential Classification and Exhibit C only in Microsoft Word format.

Please contact me if you or your Staff has any questions regarding this filing.

Sincerely,

Jessica Cano
Jessica A. Cano

Enclosures
cc: Parties of Record (w/out enc.)

COM
AFD
APA
ECO
ENG
GCL
IDM
TEL
CLK

Florida Power & Light Company

DOCUMENT NUMBER-DATE

02393 MAY-1 2

FPSC-COMMISSION CLERK

BEFORE THE FLORIDA PUBLIC SERVICE COMMISSION

In re: Nuclear Cost)
Recovery Clause)

Docket No. 130009-EI
Filed: May 1, 2013

**FLORIDA POWER & LIGHT COMPANY'S
REQUEST FOR CONFIDENTIAL CLASSIFICATION
OF JONES TESTIMONY AND EXHIBITS TOJ-13 AND SDS-7**

Pursuant to Section 366.093, Florida Statutes, and Rule 25-22.006, Florida Administrative Code, Florida Power & Light Company ("FPL") requests confidential classification of portions of FPL witness Terry Jones's testimony, Exhibit TOJ-13 to the testimony of FPL witness Terry Jones, and Exhibit SDS-7 to the testimony of FPL witness Steven D. Scroggs. In support of its request, FPL states:

1. FPL is filing contemporaneously with this request the petition, testimony and exhibits in support of its Nuclear Power Plant Cost Recovery Amount for the Year 2014. Certain portions of Terry Jones's testimony and Exhibits TOJ-13 and SDS-7 contain confidential information related to competitive interests and confidential contract payment amounts. Pursuant to Rule 25-22.006(3)(a), Florida Administrative Code, FPL is filing this Request for Confidential Classification.

2. The following exhibits are included with and made a part of this request:

a. Exhibit A consists of a copy of the confidential pages on which all information that FPL asserts is entitled to confidential treatment has been highlighted.

b. Exhibit B consists of a copy of the confidential pages on which all information that FPL asserts is entitled to confidential treatment has been redacted.

c. Exhibit C is a table containing an identification of the information highlighted in Exhibit A, together with references to the specific statutory basis or bases

for the claim of confidentiality and to the affidavit in support of the requested classification.

d. Exhibit D includes the affidavits of Bruce Beisler and Steve Scroggs in support of this request.

3. FPL submits that the highlighted information in Exhibit A is proprietary confidential business information within the meaning of Section 366.093(3), Florida Statutes. Section 366.093(3), Florida Statutes, defines confidential information as information that is intended to be and is treated by the company as private in that disclosure of the information would cause harm to the company's business operations or its customers, and has not been disclosed publicly. The confidential information is intended to be and has been treated by FPL as private, its confidentiality has been maintained, and its disclosure would cause harm to FPL and its customers. Pursuant to Section 366.093(3)(2), such information is entitled to confidential treatment and it is exempt from the disclosure provisions of the public records law. Thus, once the Commission determines that the information in question is proprietary confidential business information, the Commission is not required to engage in any further analysis or review such as weighing the harm of disclosure against the public interest in access to the information

4. As the affidavits included in Exhibit D indicate, the information provided by FPL in Exhibits TOJ-13 and SDS-7 contains contractual data, the public disclosure of which would violate nondisclosure provisions of FPL's contracts with certain vendors and impair FPL's ability to contract for goods or services on favorable terms in the future. Such information is protected by Section 366.093(3)(d), Florida Statutes. Additionally, this information and the information identified in the testimony of Terry Jones is competitively sensitive, and disclosure

could impair the competitive business of FPL or its vendors. Such information is protected by Section 366.093(3)(e), Florida Statutes.

5. Upon a finding by the Commission that the information highlighted in Exhibit A, and referenced in Exhibit C, is proprietary confidential business information, the information should not be declassified for a period of at least eighteen (18) months and should be returned to FPL as soon as the information is no longer necessary for the Commission to conduct its business. *See* § 366.093(4), Fla. Stat.

WHEREFORE, FPL respectfully requests confidential classification of the material described herein.

Respectfully submitted,

Jessica A. Cano
Principal Attorney
Florida Power & Light Company
700 Universe Boulevard
Juno Beach, FL 33408
Telephone: (561) 304-5226
Facsimile: (561) 691-7135

By: Jessica Cano
Jessica A. Cano
Fla. Bar No. 0037372

**CERTIFICATE OF SERVICE
DOCKET NO. 130009-EI**

I HEREBY CERTIFY that a true and correct copy of FPL's Request for Confidential Classification of Jones Testimony and Exhibits TOJ-13 and SDS-7 (without exhibits)* was served by hand delivery** or U.S. Mail this 1st day of May, 2013 to the following:

Michael Lawson, Esq.**
Division of Legal Services
Florida Public Service Commission
2540 Shumard Oak Blvd.
Tallahassee, Florida 32399-0850
MLAWSON@PSC.STATE.FL.US

J. R. Kelly, Esq.
Charles Rehwinkel, Esq.
Joseph McGlothlin, Esq.
Erik L. Saylor, Esq.
Office of Public Counsel
c/o The Florida Legislature
111 West Madison Street, Room 812
Tallahassee, Florida 32399
Kelly.jr@leg.state.fl.us
Rehwinkel.Charles@leg.state.fl.us
mcglothlin.joseph@leg.state.fl.us
Saylor.Erik@leg.state.fl.us

J. Michael Walls, Esq.
Blaise N. Gamba, Esq.
Carlton Fields Law Firm
P.O. Box 3239
Tampa, Florida 33601-3239
mwalls@carltonfields.com
bgamba@carltonfields.com
Attorneys for Duke Energy Florida, Inc.

John T. Burnett, Esq.
Dianne M. Triplett, Esq.
Progress Energy Service Company, LLC
P.O. Box 14042
St. Petersburg, Florida 33733-4042
john.burnett@pgnmail.com
dianne.triplett@pgnmail.com
Attorneys for Duke Energy Florida, Inc.

Matthew Bernier, Esq.
Carlton Fields Law Firm
215 S. Monroe Street, Ste. 500
Tallahassee, Florida 32301
mbernier@carltonfields.com

Mr. Paul Lewis, Jr.
106 East College Ave., Suite 800
Tallahassee, Florida 32301-7740
paul.lewisjr@pgnmail.com

Jon C. Moyle, Jr., Esq.
Keefe Anchors Gordon & Moyle, PA
118 North Gadsden Street
Tallahassee, Florida 32301
jmoyle@moylelaw.com
Attorneys for FIPUG

James W. Brew, Esq.
F. Alvin Taylor, Esq.
Brickfield, Burchette, Ritts & Stone, P.C.
1025 Thomas Jefferson Street, NW
Eighth Floor, West Tower
Washington, DC 20007-5201
jbrew@bbrslaw.com
ataylor@bbrslaw.com
Attorneys for PCS Phosphate

By: Jessica Cano
Jessica A. Cano
Fla. Bar No. 0037372

*Exhibits to this Request are not included with the service copies, but copies of Exhibits B, C and D are available upon request.

Exhibit C

Company: Florida Power and Light Company
Title: List of Confidential Documents May 1, 2013 Filing
Docket No.: 130009-EI

Document	Description	No. of Pages	Conf. Y/N	Line No./Col. No.	Florida Statute 366.093 (3) Subsection	Affiant
1	2013 Schedule AE-7A Pre-Construction Costs and Carrying Costs on Construction Cost Balance, New Nuclear (Exhibit SDS – 7)	1	Y	Page 28 Lines 1-19 Columns A-D	(d), (e)	Steven D. Scroggs
2	2013 Schedule AE-7B Pre-Construction Costs and Carrying Costs on Construction Cost Balance, New Nuclear (Exhibit SDS – 7)	9	Y	Pages 29-33 Line 1,2,3,4 Page 34 Lines 1,2,3 Page 35 Lines 1,2,3,4 Pages 36-37 Lines 1,2,3	(d), (e)	Steven D. Scroggs
3	2014 Schedule P-7A Pre-Construction Costs and Carrying Costs on Construction Cost Balance, New Nuclear (Exhibit SDS-7)	1	Y	Page 48 Lines 1-19 Columns A-D	(d), (e)	Steven D. Scroggs
4	2014 Schedule P-7A Pre-Construction Costs and Carrying Costs on Construction Cost Balance, New Nuclear (Exhibit SDS-7)	9	Y	Pages 49-53 Lines 1,2,3,4 Page 54 Lines 1,2,3 Page 55 Lines 1,2,3,4 Page 56-57 Lines 1,2,3	(d), (e)	Steven D. Scroggs

5	2013 Schedule AE-7A Construction Costs and Carrying Costs on Construction Cost Balance, Extended Power Uprate (Exhibit TOJ-13)	7	Y	Page 47 Lines 1-27 Columns A-D Page 48 Lines 28-54 Columns A-D Page 49 Lines 55-81 Columns A-D Page 50 Lines 82-108 Columns A-D Page 51 Lines 109-135 Columns A-D Page 52 Lines 136-160 Columns A-D Page 53 Lines 161-171 Columns A-D	(d), (e)	Bruce Beisler
6	2013 Schedule AE-7B Construction Costs and Carrying Costs on Construction Cost Balance, Extended Power Uprate (Exhibit TOJ-13)	93	Y	Pages 54-146 Line 1	(d), (e)	Bruce Beisler
7	2014 Schedule P-7A Construction Costs and Carrying Costs on Construction Cost Balance, Extended Power Uprate (Exhibit TOJ-13)	7	Y	Page 154 Lines 1-27 Columns A-D Page 155 Lines 28-54 Columns A-D Page 156 Lines 55-81 Columns A-D Page 157 Lines 82-108 Columns A-D Page 158	(d), (e)	Bruce Beisler

				Lines 109-135 Columns A-D Page 159 Lines 136-160 Columns A-D Page 160 Lines 161-171 Columns A-D		
8	2014 Schedule P-7B Construction Costs and Carrying Costs on Construction Cost Balance, Extended Power Uprate (Exhibit TOJ-13)	93	Y	Pages 161-253 Line 1	(d), (e)	Bruce Beisler
9	May 1, 2013 NPPCR Testimony of Terry O. Jones	1	Y	Page 16 Lines 5-13	(e)	Bruce Beisler

EXHIBIT D

BEFORE THE FLORIDA PUBLIC SERVICE COMMISSION

In re: Nuclear Power Plant Cost)
Recovery Clause)

DOCKET NO. 130009-EI

STATE OF FLORIDA)
)
PALM BEACH COUNTY)

AFFIDAVIT OF STEVEN D. SCROGGS

BEFORE ME, the undersigned authority, personally appeared Steven D. Scroggs who, being first duly sworn, deposes and says:

1. My name is Steven D. Scroggs. I am currently employed by Florida Power & Light Company ("FPL") as Senior Director, Project Development. I have personal knowledge of the matters stated in this affidavit.

2. I have reviewed Exhibit C and the documents that are included in FPL's Request for Confidential Classification concerning information provided with its Petition for Approval of Nuclear Power Plant Cost Recovery Amount for the Year 2014, for which I am identified on Exhibit C as the affiant. The documents and materials that I have reviewed contain proprietary confidential business information, including information concerning bids or contractual data. Disclosure of this information would violate FPL's contracts with its vendors, work to the detriment of FPL's competitive interests, impair the competitive interests of its vendors and/or impair FPL's efforts to enter into contracts on commercially favorable terms. To the best of my knowledge, FPL has maintained the confidentiality of these documents and materials.

3. Consistent with the provisions of the Florida Administrative Code, such materials should remain confidential for a period of not less than 18 months. In addition, they should be returned to FPL as soon as the information is no longer necessary for the Commission to conduct its business so that FPL can continue to maintain the confidentiality of these documents.

4. Affiant says nothing further.

Steven D. Scroggs

Steven D. Scroggs

SWORN TO AND SUBSCRIBED before me this 29th day of April 2013, by Steven D. Scroggs, who is personally known to me or who has produced _____ (type of identification) as identification and who did take an oath.

Heather P. Meligonis

Notary Public, State of Florida

My Commission Expires:



BEFORE THE FLORIDA PUBLIC SERVICE COMMISSION

In re: Nuclear Power Plant Cost)
Recovery Clause)

DOCKET NO. 130009-EI

STATE OF FLORIDA)
)
PALM BEACH COUNTY)

AFFIDAVIT OF BRUCE BEISLER


BEFORE ME, the undersigned authority, personally appeared Bruce Beisler who, being first duly sworn, deposes and says:

1. My name is Bruce Beisler. I am currently employed by Florida Power & Light Company ("FPL") as Project Manager - Nuclear. I have personal knowledge of the matters stated in this affidavit.

2. I have reviewed Exhibit C and the documents that are included in FPL's Request for Confidential Classification concerning information provided with its Petition for Approval of Nuclear Power Plant Cost Recovery Amount for the Year 2014, for which I am identified on Exhibit C as the affiant. The documents and materials that I have reviewed contain proprietary confidential business information, including information concerning bids or contractual data and information related to competitive interests. Disclosure of this information would violate FPL's contracts with its vendors, work to the detriment of FPL's competitive interests, impair the competitive interests of its vendors and/or impair FPL's efforts to enter into contracts on commercially favorable terms. To the best of my knowledge, FPL has maintained the confidentiality of these documents and materials.


3. Consistent with the provisions of the Florida Administrative Code, such materials should remain confidential for a period of not less than 18 months. In addition, they should be returned to FPL as soon as the information is no longer necessary for the Commission to conduct its business so that FPL can continue to maintain the confidentiality of these documents.

4. Affiant says nothing further.



Bruce Beisler

SWORN TO AND SUBSCRIBED before me this 30th day of April 2013, by Bruce Beisler, who is personally known to me or who has produced _____ (type of identification) as identification and who did take an oath.



Notary Public, State of Florida

My Commission Expires:





EXHIBIT B

REDACTED

130009-E1

COM	___
AFD	___
APA	___
ECO	___
ENG	___
GCL	___
IDM	1
TEL	___
CLK	___

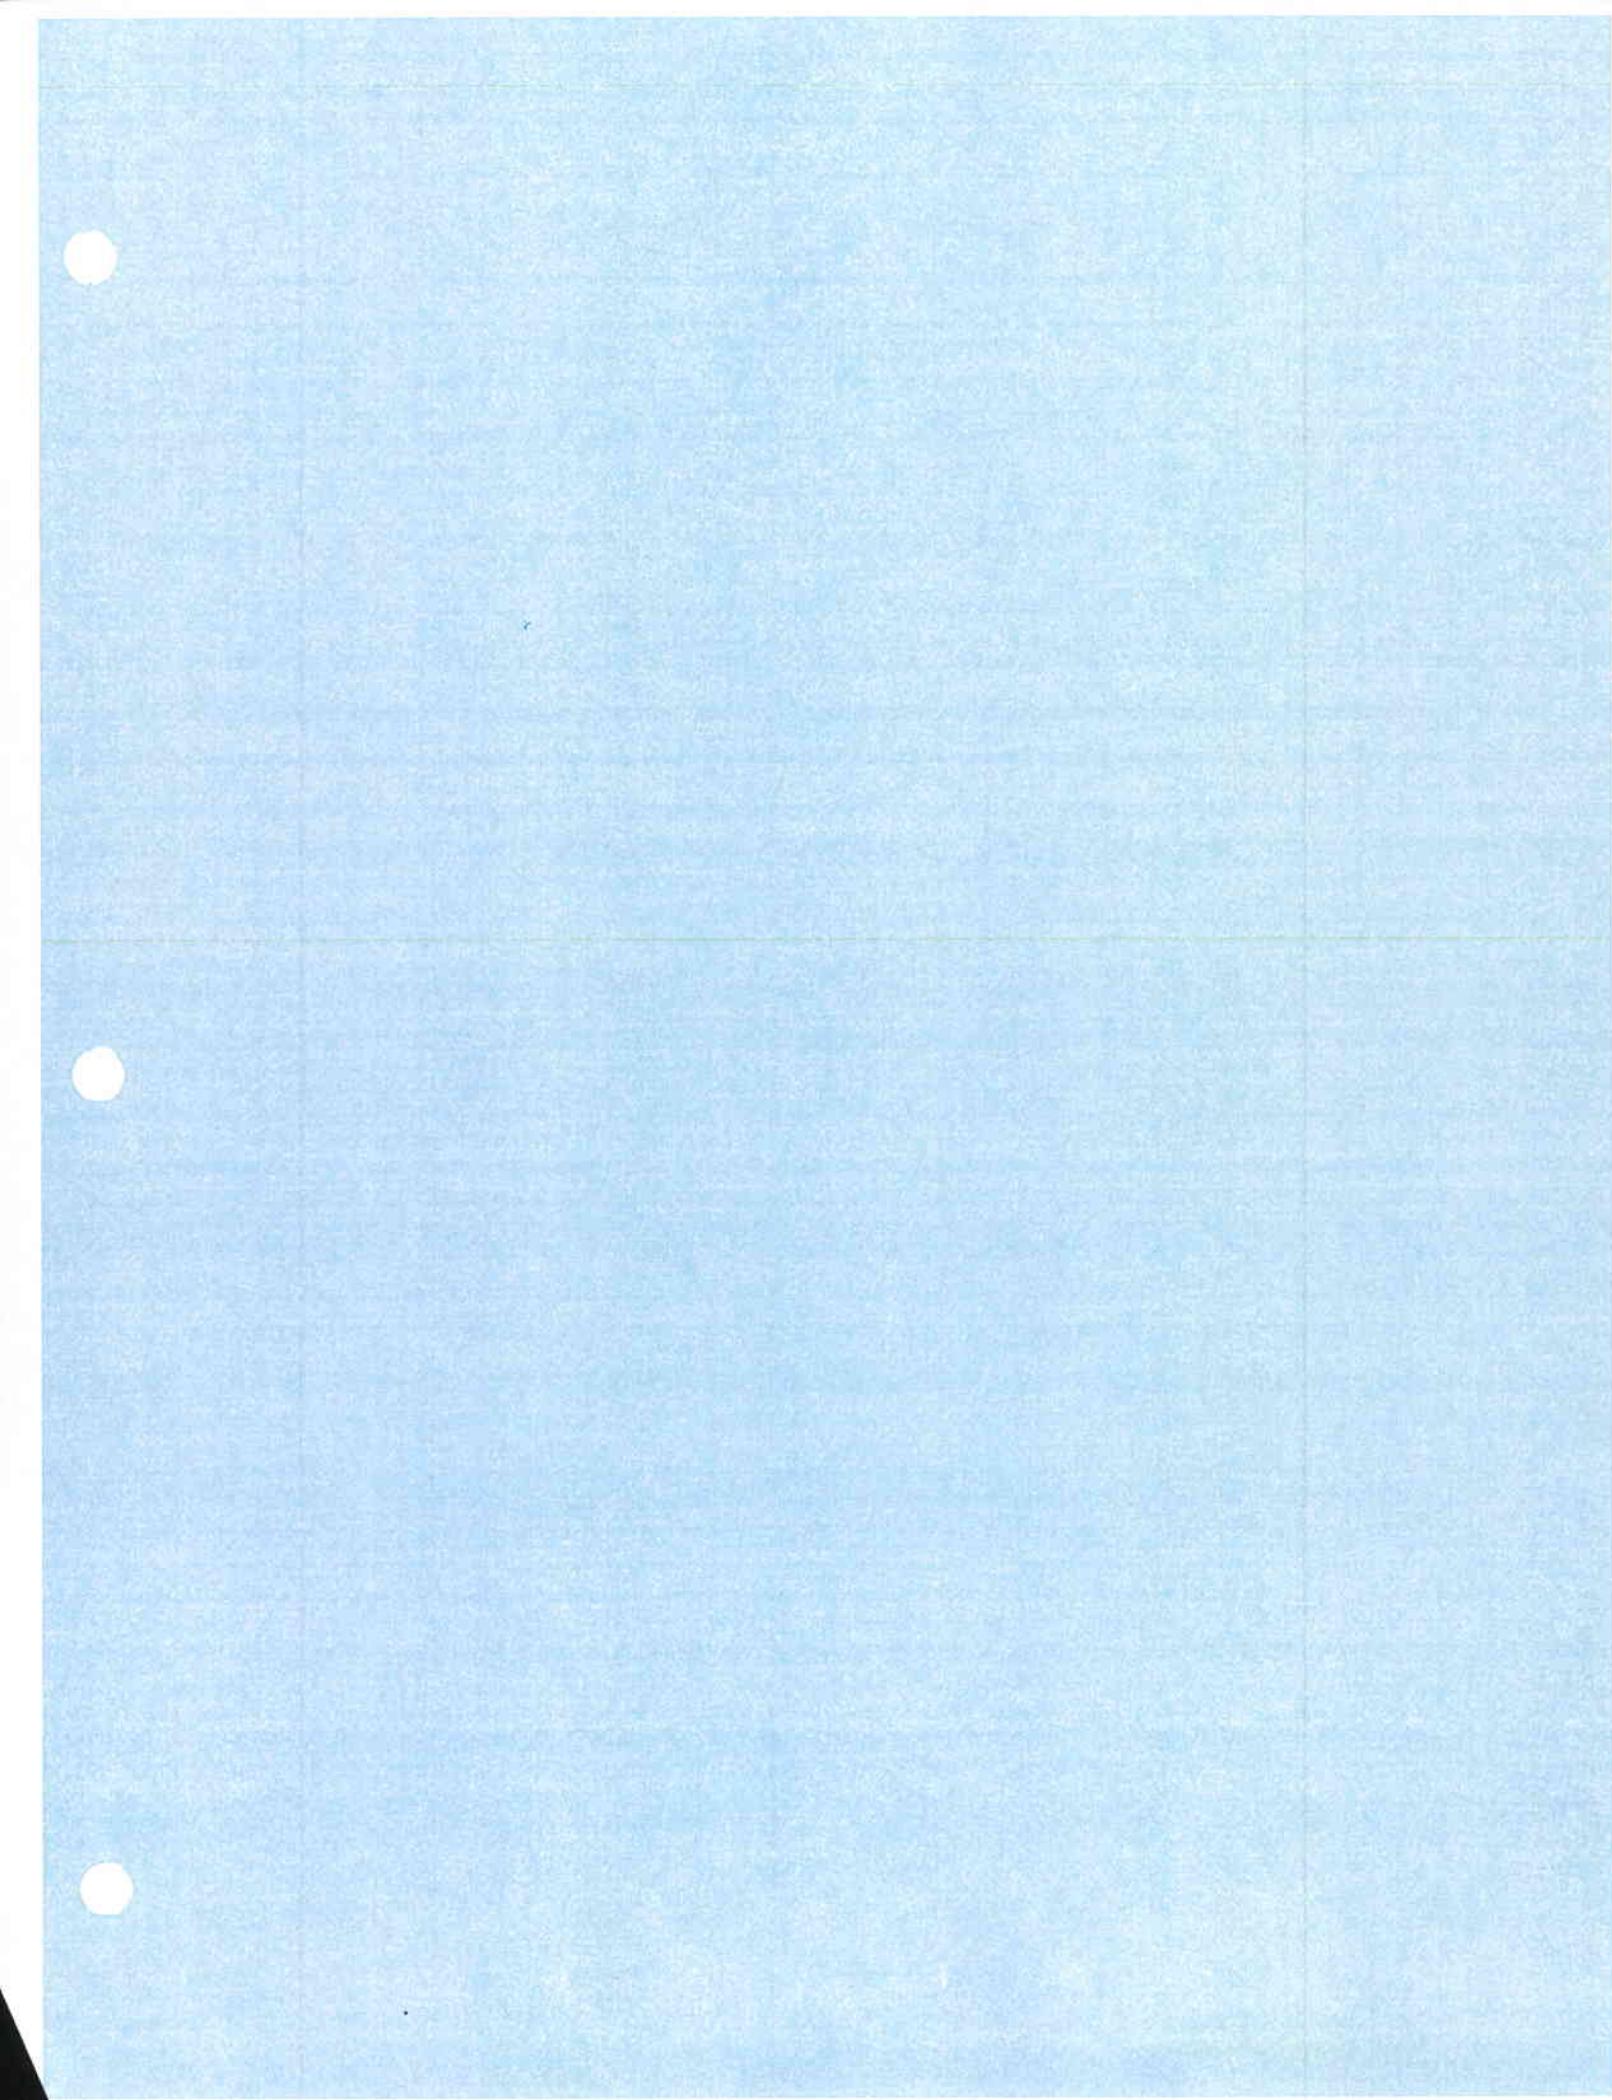

**Turkey Point Units 6&7
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Actual & Estimated Filing: All Contracts Executed in Excess of \$250,000**

Schedule AE-7A

EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the current year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work.

[Section (8)(c)]

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY


For the Year Ended 12/31/2013

Witness: Steven D. Scroggs

DOCKET NO.: 130009-EI

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Confidential Original Amount	Confidential Actual Expended as of Prior Year End (2012)	Confidential Estimate of amount to be Expended in Current Year (2013)	Confidential Estimated Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
1	200062412	Open - CO#5	02/2012 - 06/2012	thru 06/2015					AMEC Environment & Infrastructure	SSJ	Review PTN 6&7 RAI Responses
2	4500681284	Open - CO#4	06/2011 - 12/2012	thru 12/2013					Atkins North American	SSJ	PTN Expert Scientific Analysis
3	4500395492	Open - CO#48	11/2007 - 12/2011	thru 08/2015					Bechtel Power Corp	Comp Bid/ SingleSource/PDS	Engineering Services to Support Preparation of COLA and SCA, and Response to post-submittal RAI's
4	200060695	Open - CO#1	02/2012 - 12/2012	thru 11/2013					Bums & McDonnell	Comp Bid	PTN 6&7 Preliminary Design of the Radial Collector Well System
5	4500667205	Open - CO#7	05/2011 - 12/2012	thru 12/2013					Curtis Group	Single Source	SCA & Land Use - Land use and zoning
6	4500443122	Open - CO#4	08/2008 - 08/2010	thru 01/2014					Eco-Metrics, Inc.	SingleSource	Environmental Consulting Services
7	4500518167	Open - CO#9	07/2009 - 12/2009	thru 06/2013					Environmental Consulting and Technology Inc.	SingleSource/PDS	SCA and post-submittal support
8	4500430034	Open - CO#1	06/2008 - 07/2011	thru 12/2013					EPRI	SingleSource	Advanced Nuclear Technology; Near term deployment of Advanced Light Water Reactors
9	4500492222	Open - CO#2	03/2009 - 12/2011	thru 12/2013					Experis Finance (Formerly Jefferson Wells)	SSJ	New Nuclear Audit
10	4500518160	Open - CO#10	07/2009 - 12/2009	thru 11/2013					Golder & Associates, Inc.	SingleSource/PDS	Post SCA Submittal Support
11	4500425707	Open - CO#8	05/2008 - 08/2008	thru 06/2014					HDR Engineering, Inc.	Comp Bid/SingleSource	Conceptual Engineering of Cooling Water Supply and Discharge
12	4500652043	Open - CO#2	03/2011 - 03/2012	thru 06/2013					Layne Christensen Company	Comp Bid/SingleSource	PTN 6&7 Exploratory/UIC Well Installation
13	4500645896	Open - CO#2	02/2011 - 12/2011	thru 12/2014					McCallum Turner, Inc.	SingleSource	PTN 6&7 COLA Site Selection RAI Support
14	4500517152	Open - CO#5	10/2009 - 12/2010	thru 06/2014					McNabb Hydrogeologic Consulting, Inc.	SingleSource/PDS	Post SCA submittal and UIC Licensing Support
15	4500536449	Open - CO#4	10/2009 - 12/2011	thru 06/2013					McNabb Hydrogeologic Consulting, Inc.	Comp Bid/SingleSource	UIC Subject Matter Expert
16	2000053246	Open	11/2011 - 12/2013	thru 06/2014					Power Engineers Inc.	Single Source	Turkey Point 6&7 Preliminary Analysis of Transmission Facilities (note that this PO replaced 4500474487)
17	4500527549	Open - CO#5	08/2009 - 12/2009	thru 04/2014					TetraTechGeo (formerly GeoTrans, Inc.)	SingleSource	APT Review and Collector Well Modeling Support
18	2000086250	Open	11/2012 - 12/2013	thru 05/2013					University of Miami	SSJ	PTN 6&7 Expert Witness support
19	4500404639	Open - CO#7	01/2008 - 12/2011	thru 08/2015					Westinghouse Electric Co	SoleSource/PDS	Engineering Services to Support Preparation of COLA and Response to post-submittal RAI's

A B C D

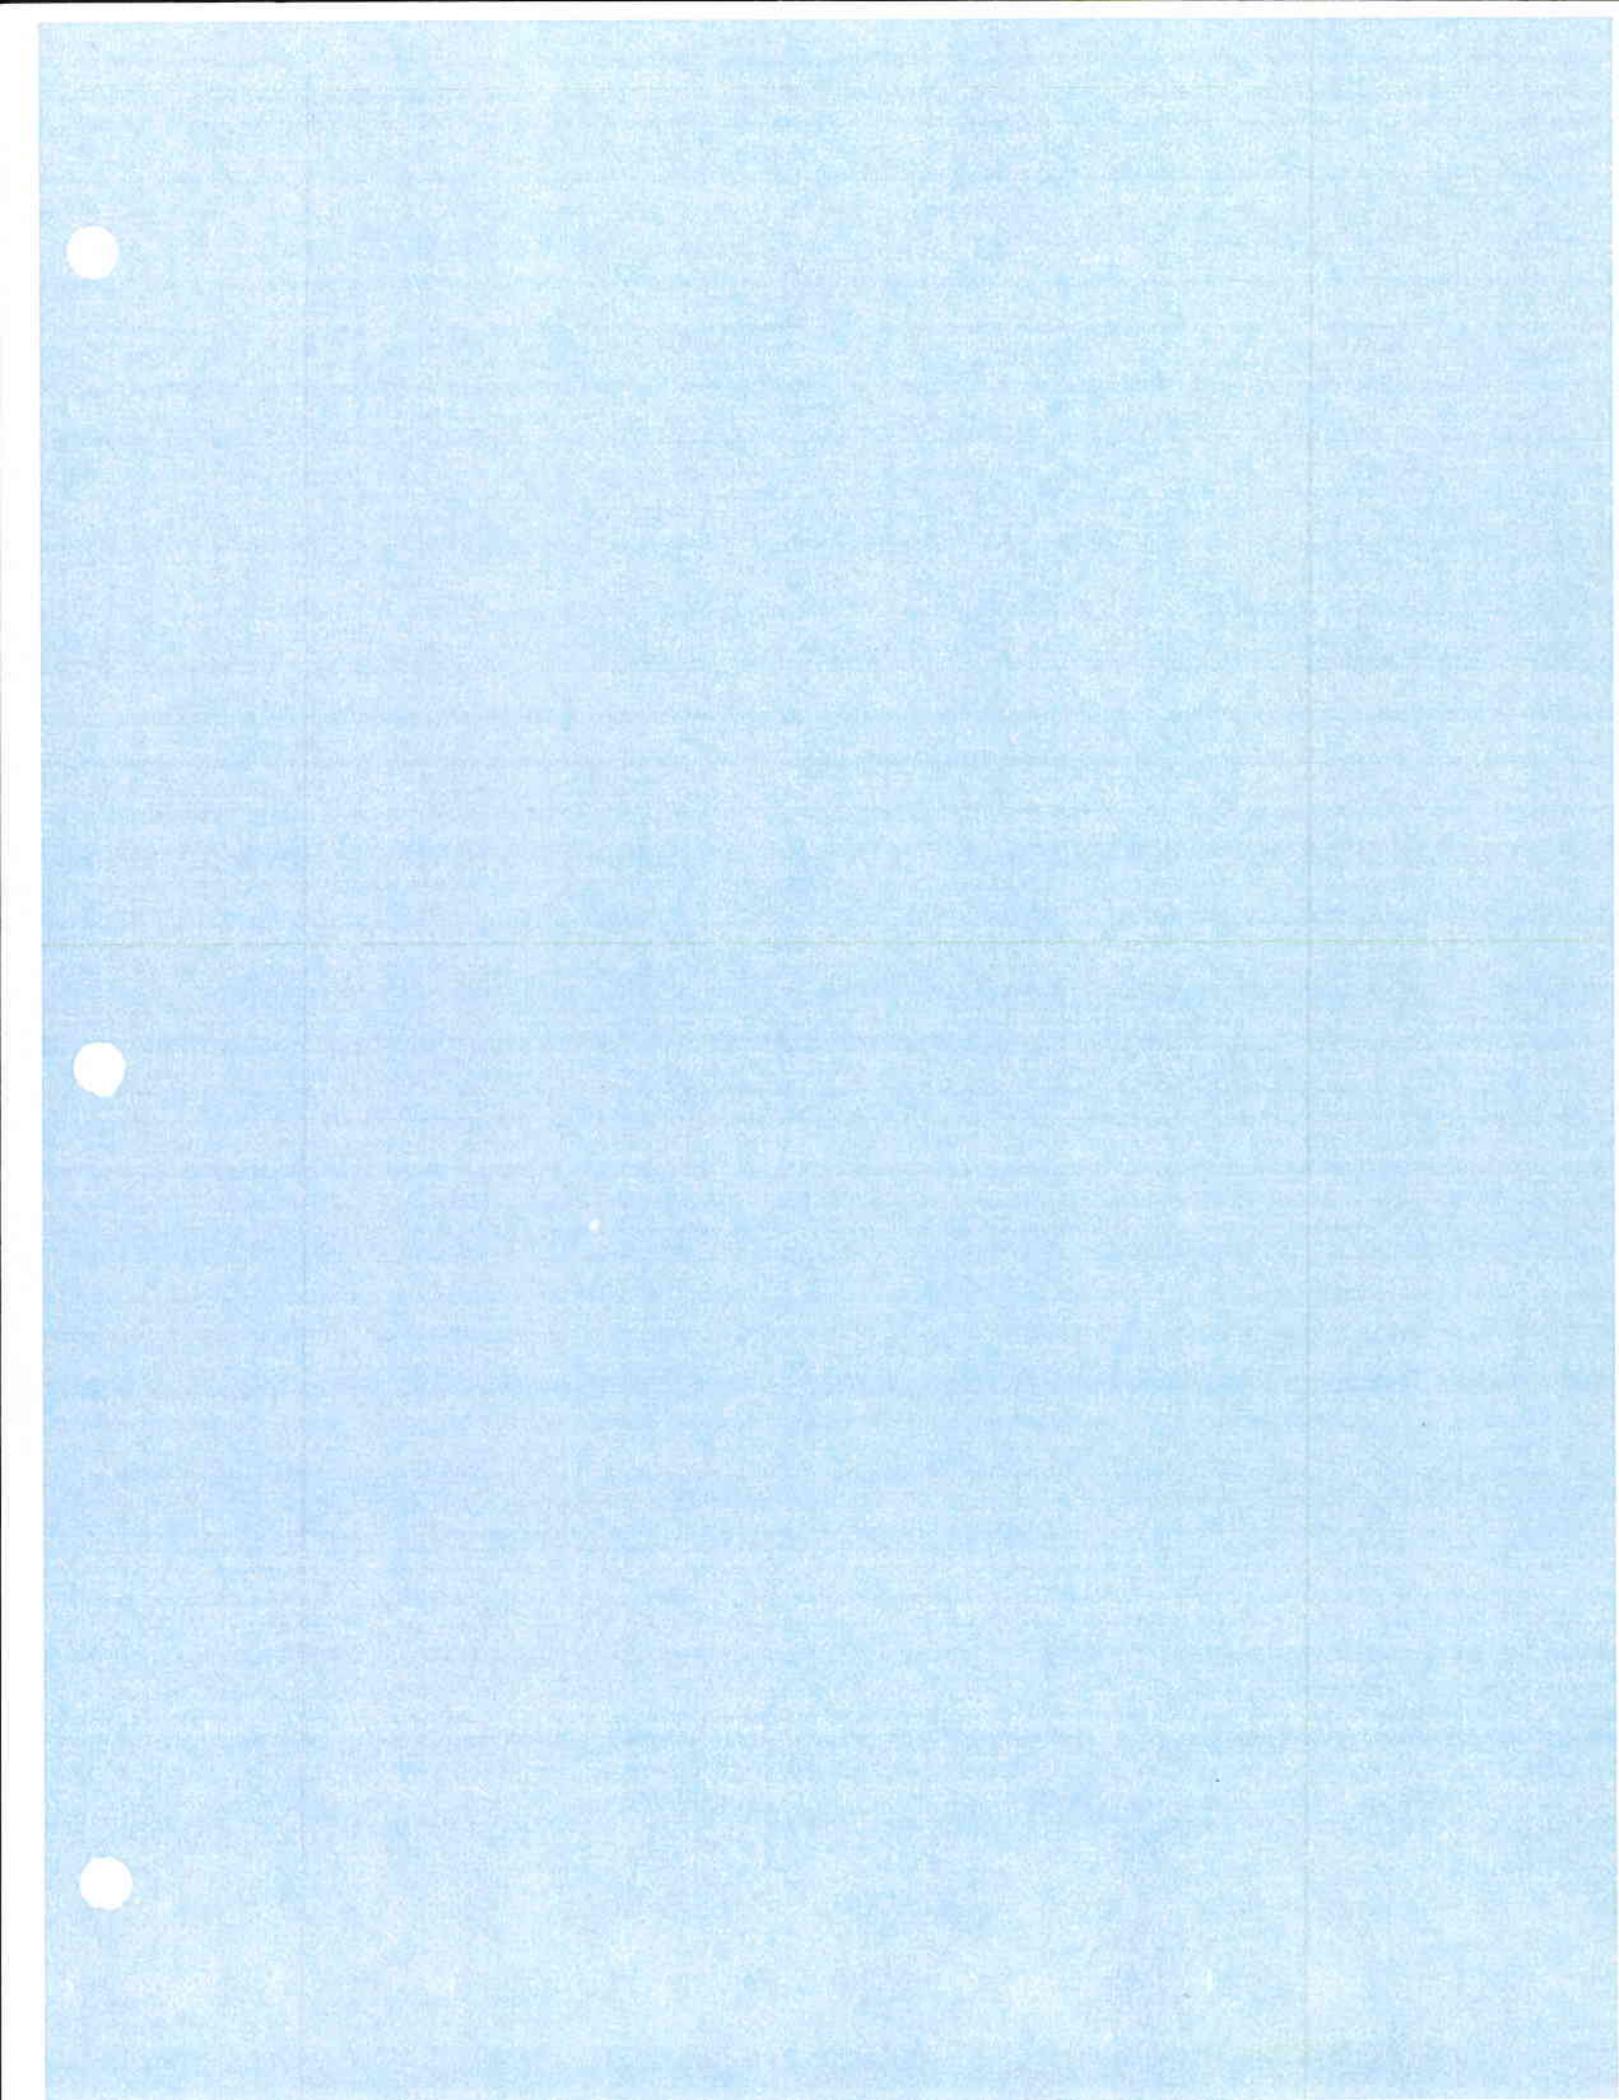

Turkey Point Units 6&7
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Actual & Estimated Filing: All Contracts Executed in Excess of \$1,000,000

Schedule AE-7B

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity vendor affiliation if any, number of vendors solicited, number of bids received, brief description of vendor selection process, current dollar value, current contract status, the current term of the contract, and the current nature/scope of work.

[Section (8)(c)]

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

For the Year Ended 12/31/2013

Witness: Steven D. Scroggs

DOCKET NO.: 130009-EI

Contract No.:
4500395492

Major Task or Tasks Associated With:
COLA and SCA preparation and support

Vendor Identity:
Bechtel Power Corporation

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
Two

Number of Bids Received:
Two

Brief Description of Selection Process:
Initial contract competitively bid, change orders#1-#11 issued single source; subsequent change orders issued as Predetermined Source

Estimated Contract Amount

1 PO Value
2 Expected CO
3 Estimate



4 **Contract Status:**
Active- CO#48, CO#49 Expected in 2013 for [REDACTED]

Term Begin:
11/6/2007
Term End:
8/31/2015

Nature and Scope of Work:
Engineering Services to Support Preparation of COLA and SCA, including post-submittal support for RAI responses

Turkey Point Units 6&7
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Actual & Estimated Filing: All Contracts Executed in Excess of \$1,000,000

Schedule AE-7B

[Section (8)(c)]

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO.: 130009-E1

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity vendor affiliation if any, number of vendors solicited, number of bids received, brief description of vendor selection process, current dollar value, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013

Witness: Steven D. Scroggs

Contract No.:
4500443122

Major Task or Tasks Associated With:
Environmental Consulting Services

Vendor Identity:
Eco-Metrics, Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
One

Number of Bids Received:
One

Brief Description of Selection Process:
Single Source

Estimated Contract Amount
1 PO Value [REDACTED]
2 Expected CO [REDACTED]
3 Estimate [REDACTED]

Contract Status:
4 Active- CO#4, CO expected for [REDACTED] in 2013.

Term Begin:
3/31/2008
Term End:
1/31/2014

Nature and Scope of Work:
Licensing and permitting support for Turkey Point Units 6&7.

Turkey Point Units 6&7
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Actual & Estimated Filing: All Contracts Executed in Excess of \$1,000,000

Schedule AE-7B

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity vendor affiliation if any, number of vendors solicited, number of bids received, brief description of vendor selection process, current dollar value, current contract status, the current term of the contract, and the current nature/scope of work.

[Section (B)(c)]

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

For the Year Ended 12/31/2013

DOCKET NO.: 130009-E1

Witness: Steven D. Scroggs

Contract No.:
4500518167

Major Task or Tasks Associated With:
SCA support

Vendor Identity:
Environmental Consulting and Technology, Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
One

Number of Bids Received:
One

Brief Description of Selection Process:
Single source; Designated as Predetermined Source December 2009

Estimated Contract Amount

1 PO Value [REDACTED]
2 Expected CO [REDACTED]
3 Estimate [REDACTED]

4 Contract Status:
Active- CO#9, CO#10 Expected in 2013 for [REDACTED].

Term Begin:
7/23/2009

Term End:
6/30/2013

Nature and Scope of Work:
SCA support

Turkey Point Units 6&7
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Actual & Estimated Filing: All Contracts Executed in Excess of \$1,000,000

Schedule AE-7B

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity vendor affiliation if any, number of vendors solicited, number of bids received, brief description of vendor selection process, current dollar value, current contract status, the current term of the contract, and the current nature/scope of work.

[Section (8)(c)]

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

For the Year Ended 12/31/2013

Witness: Steven D. Scroggs

DOCKET NO.: 130009-EI

Contract No.:
4500430034

Major Task or Tasks Associated With:
Advanced Nuclear Technology; Near term deployment of Advanced Light Water Reactors

Vendor Identity:
Electric Power Research Institute (EPRI)

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
One

Number of Bids Received:
One

Brief Description of Selection Process:
Single Source

Estimated Contract Amount
1 PO Value [REDACTED]
2 Expected CO [REDACTED]
3 Estimate [REDACTED]

Contract Status:
4 Active- CO#1, CO #2 for [REDACTED] expected in 2013

Term Begin:
6/16/2008
Term End:
12/31/2013

Nature and Scope of Work:
Advanced Nuclear Technology; Near term deployment of Advanced Light Water Reactors

Turkey Point Units 6&7
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Actual & Estimated Filing: All Contracts Executed in Excess of \$1,000,000

Schedule AE-7B

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity vendor affiliation if any, number of vendors solicited, number of bids received, brief description of vendor selection process, current dollar value, current contract status, the current term of the contract, and the current nature/scope of work.

[Section (8)(c)]

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

For the Year Ended 12/31/2013

DOCKET NO.: 130009-EI

Witness: Steven D. Scroggs

Contract No.:
4500518160

Major Task or Tasks Associated With:
Post SCA submittal support

Vendor Identity:
Golder Associates, Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
One

Number of Bids Received:
One

Brief Description of Selection Process:
Single source; designated as Predetermined Source February 2010

Estimated Contract Amount

- 1 PO Value
- 2 Expected CO
- 3 Estimate



Contract Status:

- 4 Active- CO#10, CO #11 Expected in 2013 for

Term Begin:
7/23/2009

Term End:
11/30/2013

Nature and Scope of Work:
Post SCA submittal support

Turkey Point Units 6&7
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Actual & Estimated Filing: All Contracts Executed in Excess of \$1,000,000

Schedule AE-7B

[Section (b)(c)]

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO.: 130009-E1

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity vendor affiliation if any, number of vendors solicited, number of bids received, brief description of vendor selection process, current dollar value, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013

Witness: Steven D. Scroggs

Contract No.:
4500425707

Major Task or Tasks Associated With:
Conceptual Engineering of Cooling Water Supply and Discharge

Vendor Identity:
HDR Engineering, Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
Five

Number of Bids Received:
Four

Brief Description of Selection Process:
Comp Bid/Single Source

Estimated Contract Amount

1 PO Value [REDACTED]
2 Expected CO [REDACTED]
3 Estimate [REDACTED]

Contract Status:
Active- CO#8

Term Begin:
5/19/2008

Term End:
6/29/2014

Nature and Scope of Work:
Conceptual engineering of cooling water supply and discharge.

Turkey Point Units 6&7
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Actual & Estimated Filing: All Contracts Executed in Excess of \$1,000,000

Schedule AE-7B

[Section (b)(c)]

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity vendor affiliation if any, number of vendors solicited, number of bids received, brief description of vendor selection process, current dollar value, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013

Witness: Steven D. Scroggs

DOCKET NO.: 130009-EI

Contract No.:
4500652043

Major Task or Tasks Associated With:
Turkey Point Units 6&7 Exploratory/UIC Well Installation

Vendor Identity:
Layne Christensen Company

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
Three

Number of Bids Received:
Three

Brief Description of Selection Process:
Competitive Bid; Single source

Estimated Contract Amount

- 1 PO Value [REDACTED]
- 2 Expected CO [REDACTED]
- 3 Estimate [REDACTED]

Contract Status:
4 Active- CO#2, CO#3 expected in 2013 for [REDACTED].

Term Begin:
3/3/2011

Term End:
6/30/2013

Nature and Scope of Work:
Turkey Point Units 6&7 Exploratory/UIC Well Installation

Turkey Point Units 6&7
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Actual & Estimated Filing: All Contracts Executed in Excess of \$1,000,000

Schedule AE-7B

[Section (8)(c)]

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO.: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity vendor affiliation if any, number of vendors solicited, number of bids received, brief description of vendor selection process, current dollar value, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013

Witness: Steven D. Scroggs

Contract No.:
4500536449

Major Task or Tasks Associated With:
UIC Subject Matter Expert Support

Vendor Identity:
McNabb Hydrogeologic Consulting, Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
Three

Number of Bids Received:
Three

Brief Description of Selection Process:
Initial contract competitively bid; change orders issued single source

Estimated Contract Amount

- 1 PO Value
- 2 Expected CO
- 3 Estimate



Contract Status:
Active- CO#4

Term Begin:
10/9/2009
Term End:
6/30/2013

Nature and Scope of Work:
UIC Subject Matter Expert Support

Turkey Point Units 6&7
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Actual & Estimated Filing: All Contracts Executed in Excess of \$1,000,000

Schedule AE-7B

[Section (B)(c)]

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO.: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity vendor affiliation if any, number of vendors solicited, number of bids received, brief description of vendor selection process, current dollar value, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013

Witness: Steven D. Scroggs

Contract No.:
4500404639

Major Task or Tasks Associated With:
COLA preparation support

Vendor Identity:
Westinghouse Electric Company

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
One

Number of Bids Received:
One

Brief Description of Selection Process:
Sole source justification; designated as Predetermined Source March 2009

Estimated Contract Amount
1 PO Value [REDACTED]
2 Expected CO [REDACTED]
3 Estimate [REDACTED]

Contract Status:
Active- CO#7

Term Begin:
1/31/2008
Term End:
03/31/2015

Nature and Scope of Work:
Engineering Services to Support Preparation of COLA, including post-submittal support for RAI responses

Turkey Point Units 6&7
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Projection Filing: All Contracts Executed in Excess of \$260,000

Schedule P-7A

EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the current year, amount expended in the subsequent year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work.

[Section (8)(c)]

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

For the Year Ended 12/31/2014

DOCKET NO.: 130009-EI

Witness: Steven D. Scroggs

(A)	(B)	(C)	(D)	Confidential (E)	Confidential (F)	Confidential (G)	Confidential (H)	(I)	(J)	(K)
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Actual/ Estimate Expended as of Current Year End (2013)	Estimate of amount to be Expended in Subsequent Year (2014)	Estimated Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
1	2000062412	Open - CO#5	02/2012 - 06/2012	thru 06/2015				AMEC Environment & Infrastructure	SSJ	Review PTN 6&7 RAI Responses
2	4500681284	Open - CO#4	06/2011 - 12/2012	thru 12/2013				Atkins North American	SSJ	PTN Expert Scientific Analysis
3	4500395492	Open - CO#4B	11/2007 - 12/2011	thru 08/2015				Bechtel Power Corp	Comp Bid/ SingleSource/PDS	Engineering Services to Support Preparation of COLA and SCA, and Response to post-submittal RAI's
4	2000060695	Open - CO#1	02/2012 - 12/2012	thru 11/2013				Burns & McDonnell	Comp Bid	PTN 6&7 Preliminary Design of the Radial Collector Well System
5	4500667205	Open - CO#7	05/2011 - 12/2012	thru 12/2013				Curtis Group	Single Source	SCA & Land Use - Land use and zoning
6	4500443122	Open - CO#4	08/2008 - 08/2010	thru 01/2014				Eco-Metrics, Inc.	SingleSource	Environmental Consulting Services
7	4500518167	Open - CO#9	07/2009 - 12/2009	thru 06/2013				Environmental Consulting and Technology Inc.	SingleSource/PDS	SCA and post-submittal support
8	4500430034	Open - CO#1	06/2008 - 07/2011	thru 12/2013				EPRI	SingleSource	Advanced Nuclear Technology; Near term deployment of Advanced Light Water Reactors
9	4500492222	Open - CO#2	03/2009 - 12/2011	thru 12/2013				Experis Finance (Formerly Jefferson Wells)	SSJ	New Nuclear Audit
10	4500518160	Open - CO#10	07/2009 - 12/2009	thru 11/2013				Golder & Associates, Inc.	SingleSource/PDS	Post SCA Submittal Support
11	4500425707	Open - CO#8	05/2008 - 08/2009	thru 06/2014				HDR Engineering, Inc.	Comp Bid/SingleSource	Conceptual Engineering of Cooling Water Supply and Discharge
12	4500652043	Open - CO#2	03/2011 - 03/2012	thru 06/2013				Layne Christensen Company	Comp Bid/SingleSource	PTN 6&7 Exploratory/UIC Well Installation
13	4500645896	Open - CO#2	02/2011 - 12/2011	thru 12/2014				McCallum Turner, Inc.	SingleSource	PTN 6&7 COLA Site Selection RAI Support
14	4500517152	Open - CO#5	10/2009 - 12/2010	thru 06/2014				McNabb Hydrogeologic Consulting, Inc.	SingleSource/PDS	Post SCA submittal and UIC Licensing Support
15	4500536449	Open - CO#4	10/2009 - 12/2011	thru 06/2013				McNabb Hydrogeologic Consulting, Inc.	Comp Bid/SingleSource	UIC Subject Matter Expert
16	2000053246	Open	11/2011 - 12/2013	thru 06/2014				Power Engineers Inc.	Single Source	Turkey Point 6&7 Preliminary Analysis of Transmission Facilities (note that this PO replaced 4500474487)
17	4500527549	Open - CO#5	08/2009 - 12/2009	thru 04/2014				TetraTechGeo (formerly GeoTrans, Inc.)	SingleSource	APT Review and Collector Well Modeling Support
18	2000086250	Open	11/2012 - 12/2013	thru 05/2013				University of Miami	SSJ	PTN 6&7 Expert Witness support
19	4500404639	Open - CO#7	01/2008 - 12/2011	thru 08/2015				Westinghouse Electric Co	Sole Source/PDS	Engineering Services to Support Preparation of COLA and Response to post-submittal RAI's

A B C D

Turkey Point Units 6&7
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Projection Filing: All Contracts Executed in Excess of \$1,000,000

Schedule P-7B

[Section (B)(c)]

PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity vendor affiliation if any, number of vendors solicited, number of bids received, brief description of vendor selection process, current dollar value, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014

DOCKET NO.: 130009-EI

Witness: Steven D. Scroggs

Contract No.:
4500395492

Major Task or Tasks Associated With:
COLA and SCA preparation and support

Vendor Identity:
Bechtel Power Corporation

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
Two

Number of Bids Received:
Two

Brief Description of Selection Process:
Initial contract competitively bid, change orders#1-#11 issued single source; subsequent change orders issued as Predetermined Source

Estimated Contract Amount

1 PO Value
2 Expected CO
3 Estimate

4 **Contract Status:**
Active- CO#48, CO#49 Expected in 2013 for [REDACTED]

Term Begin:

11/6/2007

Term End:

8/31/2015

Nature and Scope of Work:

Engineering Services to Support Preparation of COLA and SCA, including post-submittal support for RAI respo

Turkey Point Units 6&7
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Projection Filing: All Contracts Executed in Excess of \$1,000,000

Schedule P-7B

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity vendor affiliation if any, number of vendors solicited, number of bids received, brief description of vendor selection process, current dollar value, current contract status, the current term of the contract, and the current nature/scope of work.

[Section (B)(c)]

PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

For the Year Ended 12/31/2014

DOCKET NO.: 130009-EI

Witness: Steven D. Scroggs

Contract No.:
4500443122

Major Task or Tasks Associated With:
Environmental Consulting Services

Vendor Identity:
Eco-Metrics, Inc

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
One

Number of Bids Received:
One

Brief Description of Selection Process:
Single Source

Estimated Contract Amount
1 PO Value [REDACTED]
2 Expected CO [REDACTED]
3 Estimate [REDACTED]

Contract Status:
4 Active- CO#4, CO expected for [REDACTED] in 2013.

Term Begin:
8/31/2008

Term End:
1/31/2014

Nature and Scope of Work:
Licensing and permitting support for Turkey Point Units 6&7.

Turkey Point Units 6&7
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Projection Filing: All Contracts Executed in Excess of \$1,000,000

Schedule P-7B

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity vendor affiliation if any, number of vendors solicited, number of bids received, brief description of vendor selection process, current dollar value, current contract status, the current term of the contract, and the current nature/scope of work.

[Section (8)(c)]

PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

For the Year Ended 12/31/2014

Witness: Steven D. Scroggs

DOCKET NO.: 130009-EI

Contract No.:
4500518167

Major Task or Tasks Associated With:
SCA support

Vendor Identity:
Environmental Consulting and Technology, Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
One

Number of Bids Received:
One

Brief Description of Selection Process:
Single source; Designated as Predetermined Source December 2009

Estimated Contract Amount

- 1 PO Value
- 2 Expected CO
- 3 Estimate

4 Contract Status:
Active- CO#9, CO#10 Expected in 2013 for [REDACTED].

Term Begin:
7/23/2009

Term End:
6/30/2013

Nature and Scope of Work:
SCA support

Turkey Point Units 6&7
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Projection Filing: All Contracts Executed in Excess of \$1,000,000

Schedule P-7B

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity vendor affiliation if any, number of vendors solicited, number of bids received, brief description of vendor selection process, current dollar value, current contract status, the current term of the contract, and the current nature/scope of work.

[Section (8)(c)]

PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

For the Year Ended 12/31/2014

Witness: Steven D. Scroggs

DOCKET NO.: 130009-EI

Contract No.:
4500430034

Major Task or Tasks Associated With:
Advanced Nuclear Technology; Near term deployment of Advanced Light Water Reactors

Vendor Identity:
Electric Power Research Institute (EPRI)

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
One

Number of Bids Received:
One

Brief Description of Selection Process:
Single Source

Estimated Contract Amount

- 1 PO Value
- 2 Expected CO
- 3 Estimate



- 4 Contract Status:
Active- CO #1, CO #2 for [redacted] expected in 2013

Term Begin:

6/16/2008

Term End:

12/31/2013

Nature and Scope of Work:

Advanced Nuclear Technology; Near term deployment of Advanced Light Water Reactors

Turkey Point Units 6&7
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Projection Filing: All Contracts Executed in Excess of \$1,000,000

Schedule P-7B

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity vendor affiliation if any, number of vendors solicited, number of bids received, brief description of vendor selection process, current dollar value, current contract status, the current term of the contract, and the current nature/scope of work.

[Section (B)(c)]

PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

For the Year Ended 12/31/2014

DOCKET NO.: 130009-EI

Witness: Steven D. Scroggs

Contract No.:
4500518160

Major Task or Tasks Associated With:
Post SCA submittal support

Vendor Identity:
Golder Associates, Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
One

Number of Bids Received:
One

Brief Description of Selection Process:
Single source; designated as Predetermined Source February 2010

Estimated Contract Amount

1 PO Value
2 Expected CO
3 Estimate

4 Contract Status:
Active- CO#10, CO #11 Expected in 2013 for [REDACTED].

Term Begin:
7/23/2009

Term End:
11/30/2013

Nature and Scope of Work:
Post SCA submittal support

Turkey Point Units 6&7
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Projection Filing: All Contracts Executed In Excess of \$1,000,000

Schedule P-7B

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity vendor affiliation if any, number of vendors solicited, number of bids received, brief description of vendor selection process, current dollar value, current contract status, the current term of the contract, and the current nature/scope of work.

[Section (B)(c)]

PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

For the Year Ended 12/31/2014

DOCKET NO.: 130009-EI

Witness: Steven D. Scroggs

Contract No.:
4500425707

Major Task or Tasks Associated With:
Conceptual engineering of cooling water supply and discharge

Vendor Identity:
HDR Engineering, Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
Five

Number of Bids Received:
Four

Brief Description of Selection Process:
Comp Bid/Single Source

Estimated Contract Amount

- 1 PO Value
- 2 Expected CO
- 3 Estimate



Contract Status:
Active- CO#0

Term Begin:
5/19/2008
Term End:
6/29/2014

Nature and Scope of Work:
Conceptual engineering of cooling water supply and discharge.

Turkey Point Units G&7
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Projection Filing: All Contracts Executed in Excess of \$1,000,000

Schedule P-7D

[Section (B)(c)]

PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO.: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity vendor affiliation if any, number of vendors solicited, number of bids received, brief description of vendor selection process, current dollar value, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014

Witness: Steven D. Scroggs

Contract No.:
4500652043

Major Task or Tasks Associated With:
Turkey Point Units G&7 Exploratory/UIC Well Installation

Vendor Identity:
Layne Christensen Company

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
Three

Number of Bids Received:
Three

Brief Description of Selection Process:
Competitive Bid; Single source

Estimated Contract Amount

- 1 PO Value
- 2 Expected CO
- 3 Estimate

4 Contract Status:
Active - CO#2, CO#3 expected in 2013 for

Term Begin:

3/3/2011

Term End:

6/30/2013

Nature and Scope of Work:

Turkey Point Units G&7 Exploratory/UIC Well Installation

Turkey Point Units 6&7
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Projection Filing: All Contracts Executed in Excess of \$1,000,000

Schedule P-7B

[Section (B)(c)]

PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO.: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity vendor affiliation if any, number of vendors solicited, number of bids received, brief description of vendor selection process, current dollar value, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014

Witness: Steven D. Scroggs

Contract No.:
4500536-119

Major Task or Tasks Associated With:
UIC Subject Matter Expert Support

Vendor Identity:
McNabb Hydrogeologic Consulting, Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
Three

Number of Bids Received:
Three

Brief Description of Selection Process:
Initial contract competitively bid; change orders issued single source

Estimated Contract Amount

- 1 PO Value
- 2 Expected CO
- 3 Estimate

Contract Status:
Active- CO#4

Term Begin:
10/9/2009
Term End:
6/30/2013

Nature and Scope of Work:
UIC Subject Matter Expert Support

Turkey Point Units 6&7
Pre-Construction Costs and Carrying Costs on Construction Cost Balance
Projection Filing: All Contracts Executed in Excess of \$1,000,000

Schedule P-7D

[Section (b)(c)]

PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO.: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity vendor affiliation if any, number of vendors solicited, number of bids received, brief description of vendor selection process, current dollar value, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014

Witness: Steven D. Scroggs

Contract No.:
4500404639

Major Task or Tasks Associated With:
COLA preparation support

Vendor Identity:
Westinghouse Electric Company

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

Number of Vendors Solicited:
One

Number of Bids Received:
One

Brief Description of Selection Process:
Sole source justification; designated as Predetermined Source March 2009

Estimated Contract Amount

1 PO Value
2 Expected CO
3 Estimate

Contract Status:
Active- CO#7

Term Begin:

1/31/2008

Term End:

8/31/2015

Nature and Scope of Work:
Engineering Services to Support Preparation of COLA, including post-submittal support for RAI responses

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
Actual & Estimate Filing: Contracts Executed**

Schedule AE-7A (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO: 130009-EI

EXPLANATION:

For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2012)	Amount to be Expended in Current Year (2013)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
1	121869	Open	4/29/09 - open	4/29/09 - open					AAF MCQUAY	Competitive	Supply Normal Containment Coolers and Testing Services (PTN)
2	120769	Open	3/26/09 - open	3/26/09 - open					Calvert Company Inc	Competitive	Iso Phase Bus Duct Coolers and Testing Services (PSL)
3	124436	Open	7/17/09 - open	7/17/09 - open					Calvert Company Inc	Competitive	Iso Phase Bus Duct Coolers, Install, Demo & Testing Services (PTN)
4	121985	Closed	4/24/09 - 02/12/13	4/24/09 - 02/12/13					Flowserve Corp.	Competitive	Replacement Main Feedwater Pumps & Various Testing (PSL)
5	123137	Open	5/28/09 - open	5/28/09 - open					Flowserve Corp.	Competitive	Main Feedwater Isolation Valves and Testing Services (PTN)
6	125454	Open	8/28/09 - open	8/28/09 - open					Flowserve Corp.	Competitive	Replacement Heater Drain Pumps (PSL)
7	119078	Open	12/9/08 - open	12/9/08 - open					Westinghouse	OEM	NSSS Engineering Analysis and LAR (PTN)
8	121947	Open	4/24/09 - open	4/24/09 - open					Westinghouse	OEM	New & Spent Fuel Criticality and Thermal Hydraulic Analysis (PTN)
9	115297	Open	8/27/08 - open	8/27/08 - open					Areva	Single Source	RSG Design Review and LAR Work (PSL)
10	115338	Open	8/27/08 - open	8/27/08 - open					Areva	Single Source	Engineering Analysis (PTN)
11	117809	Open	12/02/08 - open	12/02/08 - open					Bechtel	Competitive Bid	Engineering Procurement Construction (PTN)
12	116088	Open	09/29/08 - open	09/29/08 - open					Siemens	Single Source	Low Pressure Turbine, Exciter, Exciter Inst. (PSL)
13	117820	Open	12/02/08 - open	12/02/08 - open					Bechtel	Competitive Bid	Engineering Procurement Construction (PSL)
14	118090	Open	9/29/08 - open	9/29/08 - open					Siemens	Single Source	Turbine, Generator/Exciter Upgrades & Inst. (PTN)
15	118328	Open	12/19/08 - open	12/19/08 - open					TEI	Competitive Bid	Condenser Tubes (PTN)
16	118206	Open	12/17/08 - open	12/17/08 - open					TEI	Competitive Bid	Moisture Separator Reheaters (PTN)
17	118205	Open	12/17/08 - open	12/17/08 - open					TEI	Competitive Bid	Moisture Separator Reheaters (PSL)
18	118241	Open	12/19/08 - open	12/19/08 - open					TEI	Competitive Bid	Feed Water Heaters (PTN)
19	112221	Open	4/22/08 - open	4/22/08 - open					Shaw - Stone & Webster	Single Source	Licensing Engineering and BOP Spec Development (PSL)
20	112177	Open	4/22/08 - open	4/22/08 - open					Shaw - Stone & Webster	Single Source	Licensing Engineering and BOP Spec Development (PTN)
21	117272	Open	11/13/08 - open	11/13/08 - open					American Crane	OEM	Gantry Crane Upgrade (PSL)
22	118224	Open	12/17/08 - open	12/17/08 - open					TEI	Competitive Bid	Feed Water Heaters (PSL)
23	115465	Open	9/03/08 - open	9/03/08 - open					Zachry Nuclear Engineering	Single Source	Engineering Services (PTN)
24	118278	Open	12/19/08 - open	12/19/08 - open					TEI	Competitive Bid	TCW Heat Exchangers (PSL)
25	105720	Open	9/12/07 - open	9/12/07 - open					Areva	Single Source	Fuels Analysis (PSL)
26	116107	Open	9/29/08 - open	9/29/08 - open					Cameron Tech.	Single Source	Ultrasonic Flow Meter Measuring System (PSL)
27	113030	Open	5/20/08 - open	5/20/08 - open					FPL Seabrook	Single Source	FPLE personnel supporting FPL Upgrades (PSL & PTN)

A B C D

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
Actual & Estimate Filing: Contracts Executed**

Schedule AE-7A (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO: 130009-EI

EXPLANATION:

For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2012)	Amount to be Expended in Current Year (2013)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
28	115391	Open	8/29/08 - open	8/29/08 - open					NAI	Single Source	Radiological Consequence Analysis (PSL)
29	112987	Open	5/19/08 - open	5/19/08 - open					Zachry	Single Source	Radiological Consequence Analysis (PTN)
30	126453	Open	11/05/09 - open	11/05/09 - open					Joseph Oat Corporation	Competitive	Cooling Water Heat Exchangers (PTN)
31	127777	Open	12/08/09 - open	12/08/09 - open					High Bridge	Single Source	Estimating Services (PTN)
32	127881	Open	12/22/09 - open	12/22/09 - open					Absolute Consulting	Single Source	Procedure Writers (PTN)
33	123762	Open	6/25/09 -open	6/25/09 -open					Key Controls of Tampa	OEM	Control System Tuning and Dynamic Analysis (PTN)
34	118563	Closed	1/14/09 - 01/29/13	1/14/09 - 01/29/13					Holtec	Competitive	Fuel Storage Criticality and related analysis (PSL 1)
35	130160	Open	3/29/10 -open	3/29/10 -open					Flowserve Corp.	Competitive	Replacement Condensate Pumps (PSL)
36	130812	Open	4/22/10 - open	4/22/10 - open					Flowserve Corp.	Competitive	Condensate Pumps (PTN)
37	130649	Open	4/22/10 - open	4/22/10 - open					Flowserve Corp.	Competitive	Main Feedwater Pumps (PTN)
38	126227	Open	10/13/09 - open	10/13/09 - open					Invensys	OEM	Control System FWH, Moisture Separator (PTN)
39	129689	Open	3/17/10 - open	3/17/10 - open					Invensys	Competitive	Turbine Digital Upgrade (PTN)
40	130272	Open	4/08/10 - open	4/08/10 - open					Siemens Energy Inc.	Competitive	Electro-Hydraulic Fluid Systems (PTN)
41	131599	Open	5/27/10 - open	5/27/10 - open					All Star Toilets	Competitive	Supply Cleaning Services (PTN)
42	131533	Closed	6/10/10 -01/29/13	6/10/10 -01/29/13					Areva	PDS	Non-Fuels NSSS Interim LAR (PSL 1 & 2)
43	131907	Closed	6/11/10 - 01/29/13	6/11/10 - 01/29/13					Areva	PDS	Fuels Related Interim LAR/MOD for EPU (PSL)
44	131585	Closed	6/15/10 - 02/20/13	6/15/10 - 02/20/13					Shaw - Stone & Webster	PDS	Interim LAR/MOD Support for EPU (PSL)
45	131742	Open	6/16/10 - open	6/16/10 - open					Westinghouse	PDS	LAR/RAI for Non-Fuels NSSS related scope (PSL)
46	132077	Open	6/17/10 - open	6/17/10 - open					Siemens Energy Inc.	Single Source	Siemens Dedicated Resident Site Manager (PTN)
47	132235	Open	6/24/10 - open	6/24/10 - open					Enercon	Single Source	NFPA 805/Appendix R Support for (PTN)
48	131940	Open	6/30/10 - open	6/30/10 - open					Westinghouse	Competitive	Main Steam Turbine Control Replacement (PSL)
49	132283	Closed	6/28/10 - 01/29/13	6/28/10 - 01/29/13					Shaw - Stone & Webster	PDS	EPU Feedwater Pump Nozzle Load Reduction (PSL)
50	2259675	Open	7/23/10 - open	7/23/10 - open					Joseph Oat Corporation	Competitive	Furnish New Spent Fuel Pool Heat Exchangers (PTN)
51	2259669	Open	8/02/10 - open	8/02/10 - open					TAW	Competitive	Rewind/Refurbish/Upgrade Condensate Pumps (PTN)
52	2259768	Open	8/06/10 - open	8/06/10 - open					Westinghouse	OEM	Design basis support for Umbrella Mods (PTN)
53	2260113	Open	9/23/10 - open	9/23/10 - open					Westinghouse	OEM	Rod Control System Upgrades (PSL)
54	2261536	Open	9/16/10 - open	9/16/10 - open					Washington Group	Competitive	Feedwater Heater Ultrasonic Testing (PTN)

A B C D

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Actual & Estimate Filing: Contracts Executed**

Schedule AE-7A (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO: 130009-EI

EXPLANATION:

For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2012)	Amount to be Expended in Current Year (2013)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
55	2261750	Open	9/21/10 - open	9/21/10 - open					Modular Space	Competitive	Lease of 15-Wide Trailers for EPU (PTN)
56	2261747	Open	9/23/10 - open	9/23/10 - open					Westinghouse	PDS	EPU NSSS Engineering and Modification Support (PTN)
57	2262094	Open	9/28/10 - open	9/28/10 - open					Structural Integrity	Competitive	Assessment of Min Wall Thickness Effects (PTN)
58	2262367	Open	10/04/10 - open	10/04/10 - open					Techcom International	Competitive	Engineering Services for Various Distributing Mods (PTN)
59	2262515	Open	10/06/10 - open	10/06/10 - open					Fisher Controls	Replaces 130579	Modified Feedwater Regulating Valves/Actuators (PSL)
60	2263038	Open	10/19/10 - open	10/19/10 - open					Flowsolve Corp.	Replaces 130180	Replacement Condensate Pumps (PSL)
61	2263052	Closed	11/11/10 - 01/31/13	11/11/10 - 01/31/13					Invensys	Single Source	Steam Bypass Control System (PSL)
62	2263549	Open	11/10/10 - open	11/10/10 - open					Areva NP Inc	Competitive	Services of a Project Manager (PTN)
63	2263930	Open	11/11/10 - open	11/11/10 - open					Brand Energy Solutions	Replaces 131356	Supply Scaffolding Material (PTN)
64	2264842	Closed	11/30/10 - 01/17/2013	11/30/10 - 01/17/2013					Ronnies Turbine Services Inc	Single Source	On Site SL2-19 Tech Support (PSL)
65	2264377	Open	11/30/10 - open	11/30/10 - open					Techcom International	Competitive	Turbine Digital Controls Verification and Validation (PTN)
66	2264914	Open	12/07/10 - open	12/07/10 - open					Westinghouse Electric	OEM	CEDMS Power Switch Refurbishment (PSL2)
67	2265418	Open	12/16/10 - open	12/16/10 - open					Siemens Energy Inc.	OEM	Impl. Spares for EPU Turbine Gen. Work During SL2-19 (PSL)
68	2285720	Open	01/4/11 - open	01/4/11 - open					Enercon Services	Competitive	Licensing/Design Basis/Program Modification (PTN)
69	2287468	Open	02/10/11 - open	02/10/11 - open					Feedforward Inc.	Competitive	DCS Mods (PSL)
70	2290208	Open	03/25/11 - open	03/25/11 - open					Feedforward Inc.	Competitive	Leading Edge Flow Meter Addition (PTN)
71	2290465	Closed	03/31/11 - 01/15/13	03/31/11 - 01/15/13					Siemens	OEM	Design and Fabrication of Turbine Crossover piping (PTN)
72	2286521	Closed	01/18/11 - 01/23/13	01/18/11 - 01/23/13					Shaw - Stone & Webster	PDS	MSIV/MSCV Modification to Support EPU (PSL)
73	2264476	Open	05/11/11 - open	05/11/11 - open					Batsch Industries	Single Source	Turbine Generator Technical Support (PTN)
74	2291815	Open	04/28/11 - open	04/28/11 - open					BRV Construction	Competitive	Fossil Warehouse Demolition (PTN)
75	2290614	Open	05/02/11 - open	05/02/11 - open					Flowsolve Corp.	Replaces 130649	Main Feedwater Pump Casing Modification (PTN)
76	2292773	Open	05/26/11 - open	05/26/11 - open					American Air Filter Co.	OEM	Design, Engineer, Fabricate and Deliver CROM Coils (PTN)
77	2293950	Open	06/24/11 - open	06/24/11 - open					Siemens	Single Source	Turbine Generator Pre-outage planning activities (PTN)
78	2293653	Open	06/29/11 - open	06/29/11 - open					Thermal Engineering	Competitive	Design and Fabrication of Gland Steam Condensers (PTN)
79	2294341	Open	07/11/11 - open	07/11/11 - open					Allon	Single Source	GL2008-01 Support (PSL)
80	2294494	Open	07/13/11 - open	07/13/11 - open					Enercon Services	Competitive	Emergency Containment Cooler Auto-start (PTN)
81	2294855	Open	07/21/11 - open	07/21/11 - open					Zachry Nuclear Engineering	Single Source	Project Engineering Support for EPU (PSL)

A B C D

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Actual & Estimate Filing: Contracts Executed**

Schedule AE-7A (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION

EXPLANATION:

For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work.

COMPANY: Florida Power & Light Company

For the Year Ended 12/31/2013

Witness: T. O. Jones

DOCKET NO: 130009-EI

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2012)	Amount to be Expended in Current Year (2013)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
82	2295422	Closed	8/10/11 - 01/05/13	8/10/11 - 01/05/13					Siemens Energy Inc.	OEM	Support Material for the EPU Turb-Gen Uprate (PTN)
83	2295071	Open	08/01/11 - open	08/01/11 - open					Shaw - Stone & Webster	Single Source	Unit 1 Vibration and Support Mods for FW & Condensate (PSL)
84	2296049	Open	08/25/11 - open	08/25/11 - open					Cameron Tech.	Replaces 116796	Ultrasonic Flow Meter Measuring System (PTN)
85	2294671	Open	08/19/11 - open	08/19/11 - open					NWT Corporation	Competitive	Moisture Carry Over Testing for EPU (PTN)
86	2296556	Open	09/02/11 - open	09/02/11 - open					Sutzer Pumps	OEM	Modify, overhaul and refurbishment of the B & C AFW (PTN)
87	2296519	Open	09/06/11 - open	09/06/11 - open					Techcom International	Competitive	DCS Integration Plan for 3R26 and 4R27 (PTN)
88	2296797	Closed	09/09/11 - 01/17/13	09/09/11 - 01/17/13					Coastal Bus & Charter Lines (dba Need A Bus)	Competitive	Shuttle Bus Services for EPU (PSL)
89	2296266	Open	10/12/11 - open	10/12/11 - open					Franmar Corporation	Competitive	Shuttle Bus Services for EPU (PTN)
90	2296406	Open	10/12/11 - open	10/12/11 - open					Master Lee Energy Services	Competitive	Fuel Movers for Metamic Inserts (PSL)
91	2296635	Open	10/14/11 - open	10/14/11 - open					Sargent & Lundy Inc	Single Source	Engineering Service for the Charging System Modification (PSL 2)
92	2299101	Open	10/27/11 - open	10/27/11 - open					Berkel & Company	Single Source	Mico Pile Construction (PTN)
93	2296894	Open	10/24/11 - open	10/24/11 - open					Day & Zimmermann NPS Inc.	Competitive	Installation of Trailer Support Services (PTN)
94	2299350	Closed	11/01/11 - 01/17/13	11/01/11 - 01/17/13					Enercon Services Inc	Competitive	Eng. Evaluation for EPU Mid-Cycle contingency plan (PSL)
95	2296618	Open	11/04/11 - open	11/04/11 - open					Radiation Safety & Control	Competitive	Truck Monitoring/Waste Characterization for EPU (PTN)
96	2297624	Open	10/27/11 - open	10/27/11 - open					Siemens Energy Inc.	OEM	Turbine Valve Conversion to EH (PTN)
97	2296631	Closed	11/8/11 - 1/17/13	11/8/11 - 1/17/13					Tri-Tool Inc	Single Source	Unit 1 LP Turbine Extraction Line Services (PSL)
98	2297055	Open	09/16/11 - open	09/16/11 - open					Thermal Engineering	Single Source	Replacement LP #4 Feedwater Heaters for EPU (PSL 2)
99	2300139	Open	11/21/11 - open	11/21/11 - open					Siemens Energy Inc	Single Source	SL1-24 Turb-Gen. Installation (PSL 1)
100	2296624	Closed	11/16/11 - 01/17/13	11/16/11 - 01/17/13					Ames Group LLC	Single Source	Upgrade Services for Feedwater Pumps (PSL)
101	2301867	Open	12/28/11 - open	12/28/11 - open					Enercon Services Inc	Single Source	Develop Engineering Change Packages for EPU (PTN)
102	2301038	Open	12/14/11 - open	12/14/11 - open					Grafel Inc.	Competitive	Integrated Leak Rate Testing for EPU (PTN)
103	2261800	Open	09/28/10 - open	09/28/10 - open					L 3 Communications Mapps Inc	OEM	Supply of Simulator SCD Software Translator Upgrade (PTN)
104	130340	Closed	04/02/10 - 02/21/13	04/02/10 - 02/21/13					MPR Associates	Competitive	Third Party Review of Siemens Turb-Gen. Analysis (PSL)
105	2301737	Open	12/21/11 - open	12/21/11 - open					PCI Energy Services	Single Source	Construction Management Oversight Services (PTN)
106	2301736	Open	12/21/11 - open	12/21/11 - open					Weldtech Services	Single Source	Construction Management Oversight Services (PTN)
107	2301871	Open	12/28/11 - open	12/28/11 - open					Zachry Nuclear Engineering	Single Source	Develop Engineering Change Packages for EPU (PTN)
108	2301856	Open	12/28/11 - open	12/28/11 - open					Sargent & Lundy Inc	Single Source	Develop TPCW Engineering Change Packages for EPU (PTN)

A B C D

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
Actual & Estimate Filing: Contracts Executed**

Schedule AE-7A (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO: 130009-EI

EXPLANATION:

For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2012)	Amount to be Expended in Current Year (2013)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
109	2302164	Open	01/25/12 - open	01/25/12 - open					Arnes Group LLC	Single Source	Valve Upgrade Services for EPU/PTN 3 & 4
110	2298833	Open	10/19/2011 - open	10/19/2011 - open					Chiefland Development	Competitive	SL1-24 Environmental Support and Lube Oil Tank Cleaning
111	2302548	Closed	01/17/12 - 02/19/13	01/17/12 - 02/19/13					Enercon Services Inc	Competitive	EQ Documentation Package Updates (PSL)
112	2303882	Open	02/23/12 - open	02/23/12 - open					Feedforward Inc.	Competitive	PSL Unit 2 EPU Mods for SBCS, Calorimetric and Feedwater Control
113	2295577	Open	08/15/11 - open	08/15/11 - open					Numerical Applications Inc	Replaces 115391	Radiological Consequence Analyses (PSL)
114	2303610	Open	02/15/12 - open	02/15/12 - open					Shaw - Stone & Webster	Single Source	Engineering Support for Extended Power Upgrade (PTN)
115	2303735	Open	02/14/12 - open	02/14/12 - open					Siemens Energy Inc	Single Source	3R26 Outage Implementation Services for EPU at PTN
116	2302300	Open	01/11/12 - open	01/11/12 - open					Shaw - Stone & Webster	PDS	Unit 2 DEH Turbine Control System Replacement for EPU at PSL
117	2303097	Open	01/30/12 - open	01/30/12 - open					Structural Preservation Systems, Inc.	Competitive	Assessment and repair of foundation for condensate motor PIT Area (PTN)
118	2304432	Open	02/28/12 - open	02/28/12 - open					Weldtech Services	Single Source	EPU Welding Implementation and Installation Services (PTN)
119	2304197	Open	03/08/12 - open	03/08/12 - open					Homestead Miami	Real Estate Transaction	Offsite Parking Facility (PTN)
120	2304908	Open	03/08/12 - open	03/08/12 - open					Zachry Nuclear Engineering	Single Source	Engineering and EC Support for PTN
121	2301063	Open	12/13/11 - open	12/13/2011 - open					B&K Installations	Competitive	Fabricate Spargers for EPU at PTN
122	2288913	Open	03/02/11 - open	03/02/11 - open					United Rentals	PDS	Light Tower Rental for EPU at PTN
123	2302888	Open	01/23/12 - open	01/23/12 - open					All Star Toilets	Replaces 131599	Portable Toilet Services (PTN)
124	2307710	Closed	05/15/12 - 01/31/13	05/15/12 - 01/31/13					Areva NP Inc	Replaces 105720	Unit 1 mid-Cycle Analysis (PSL)
125	2308808	Open	06/12/12 - open	06/12/12 - open					Calvert Company Inc	Replaces 124438	Replacement of Isolated Phase Bus Duct (PTN)
126	2307375	Closed	05/03/12 - 01/30/13	05/03/12 - 01/30/13					Nucorp	Single Source	Nuclear Grade Air Traps (PSL)
127	2308917	Open	06/13/12 - open	06/13/12 - open					Sargent & Lundy Inc	Single Source	EPU Procedure Recovery Plan Support (PSL)
128	2263063	Open	10/19/10 - open	10/19/10 - open					United Rentals	Competitive*	Light Tower Rentals for EPU Surplus Parking (PTN)
129	2307342	Open	05/02/12 - open	05/02/12 - open					American Air Filter	OEM	Onsite Technical Support for the Normal Containment Cooler (PTN)
130	2309312	Open	06/25/12 - open	06/25/12 - open					Arnes Group LLC	Single Source	Valve Actuator Support Specialty Services (PSL)
131	2311019	Open	08/16/12 - open	08/16/12 - open					Andersen Chavet & Andersen Inc.	Competitive	Develop a Preventative Maintenance Plan for EPU at PSL
132	2306547	Closed	04/11/12 - 01/31/13	04/11/12 - 01/31/13					Conger & Elsa	Single Source	PCV-8802 Contract Root Cause Evaluation (PSL)
133	2308236	Open	05/22/12 - open	05/22/12 - open					Enercon Services, Inc	Single Source	Task 1: IST and ILRT/LLRT Program Support (PSL)
134	2309442	Open	07/09/12 - open	07/09/12 - open					J. Givoo Consultants	Competitive	Start-Up and Testing Support (PSL)
135	2310597	Open	07/26/12 - open	07/26/12 - open					K Machine	Single Source	3R26 and 4R27 Outage Machining Support for EPU

A B C D

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Actual & Estimate Filing: Contracts Executed**

Schedule AE-7A (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION

EXPLANATION:

For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work.

COMPANY: Florida Power & Light Company

For the Year Ended 12/31/2013

Witness: T. O. Jones

DOCKET NO: 130009-EI

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2012)	Amount to be Expended in Current Year (2013)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
136	2264321	Open	11/15/2010 - open	11/15/2010 - open					Modular Space	PDS	On Site Modular Office Space Rental (PSL)
137	2309693	Open	07/06/12 - open	07/06/12 - open					PCI Energy Services	Competitive	Implementation and Installation of Unit 4 Spent Fuel Pool Heat Exchangers
138	2311510	Open	08/16/12 - open	08/16/12 - open					Shaw - Stone & Webster	Single Source	Engineering Support for EPU (PTN unit 4)
139	2310927	Open	08/07/12 - open	08/07/12 - open					Siemens Energy Inc	Single Source	PSL 2-20 Turbine Generator Services
140	2311900	Open	09/05/12 - open	09/05/12 - open					Siemens Energy Inc	Single Source	PTN 4-27 Turbine Generator Services
141	2312716	Closed	09/18/12 - 02/14/13	09/18/12 - 02/14/13					Trican Technologies	Single Source	Unit 4 Eddy Current Testing on Condenser Tube Bundle
142	2303837	Open	04/24/12 - open	04/24/12 - open					Thermal Engineering	OEM	Installation and Mod Engineering Support for EPU at PTN
143	2310214	Open	07/17/12 - open	07/17/12 - open					Whiting Services Inc	OEM	3R26 and 4R27 Outage Crane Support
144	2310390	Open	07/25/12 - open	07/25/12 - open					Williams Plant Services LLC	Single Source	Unit 2 Alpha Main Transformer Upgrade Support
145	2311037	Open	08/10/12 - open	08/10/12 - open					Williams Specialty Services	Replaces Blanket 4500412063	Coating Services in Support of PTN EPU Project
146	2293283	Open	06/02/11 - open	06/02/11 - open					Nucon	Competitive	CREVS Testing at PSL
147	2313411	Open	10/08/12 - open	10/08/12 - open					Sims Crane & Equipment Co.	Competitive	Rental of Misc Equipments (PTN)
148	2314332	Open	10/30/12 - open	10/30/12 - open					Team Industrial Services Inc	Single Source	Radiography Testing Services for EPU at PTN
149	2314744	Open	11/09/12 - open	11/09/12 - open					Aggreko	Competitive	Support Performance of ILRT (PTN)
150	2315146	Open	11/21/12 - open	11/21/12 - open					Brand Energy Solutions, LLC	Replaces 2263930	Scaffold Rental to Support EPU (PTN)
151	2315635	Open	12/14/12 - open	12/14/12 - open					Control Components	Single Source	Turbine Bypass and Steam Dump Control Systems Valves (PTN)
152	2314797	Open	11/12/12 - open	11/12/12 - open					Curtiss Wright Flow Control	Single Source	NDE Oversight and Preservice Examinations (PTN)
153	2315305	Open	12/03/12 - open	12/03/12 - open					Land & Sea	Competitive	Delivery Fuel and Refuel Misc Equip at Site (PTN)
154	2315379	Closed	11/30/12 - 01/30/13	11/30/12 - 01/30/13					Magnetrol International	Competitive	Transmitters (PTN)
155	2315153	Open	11/21/12 - open	11/21/12 - open					Westinghouse Electric Co	OEM	Unit 3 Secondary System Stability (PTN)
156	2310959	Open	10/10/12 - open	10/10/12 - open					Shaw - Stone & Webster	Single Source	Onsite Engineering Manager (PSL)
157	2316596	Open	01/29/13 - open	01/29/13 - open					GE Mobile Water Inc.	Competitive	Condensate Polishers (PTN)
158	2315472	Open	12/04/12 - open	12/04/12 - open					Sargent & Lundy Inc	Single Source**	On Site Support for Dampening Flow Oscillations (PTN)
159	2317235	Open	02/19/13 - open	02/19/13 - open					The Merrick Group inc.	Competitive	Unit 3 Condenser Tube Bundles Hydrolasing (PTN)
160	2301976	Open	02/01/12 - open	02/01/12 - open					Westinghouse Electric Co	OEM	Spent Fuel handling Modification for EPU (PSL)

A B C D

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
Actual & Estimate Filing: Contracts Executed**

Schedule AE-7A (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Actual Expended as of Prior Year End (2012)	Amount to be Expended in Current Year (2013)	Estimate of Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
161	2262359 RIs 7	Open	05/10/12 - open	05/10/12 - open					Atlas Copco USA Holdings	Competitive	Rental of Air Compressors (PTN)
162	2260135 RIs 14	Open	10/26/10 - open	10/26/10 - open					Bartlett Nuclear Inc	Competitive	Radiation Protection Services PSL
163	2262301 RIs 13	Open	01/30/12 - open	01/30/12 - open					Bartlett Nuclear Inc	BPO 2262301 Replaces BPO 113293 (Competitive)	Radiation Protection Services PTN
164	2262301 RIs 17	Open	06/21/12 - open	06/21/12 - open					Bartlett Nuclear Inc	BPO 2262301 Replaces BPO 113293 (Competitive)	Radiation Protection Services PTN
165	2287944 RIs 4	Open	03/07/12 - open	03/07/12 - open					Energy Solutions, LLC	BPO 2287944 Replaces BPO 99395 (Single Source)	EPU Radioactive Waste Disposal Services (PTN)
166	2260140 RIs 53	Open	11/26/11 - open	11/26/11 - open					G4S Regulated Security Solutions Inc.	BPO 2260140 Replaces BPO 118419 (Single Source)	Security Services PSL 1-24 and PSL 2-20 (PSL)
167	2260140 RIs 86	Open	12/17/12 - open	12/17/12 - open					G4S Regulated Security Solutions Inc.	BPO 2260140 Replaces BPO 118419 (Single Source)	Security Services for Unit 4 EPU (PTN)
168	2286053 RIs 8	Open	05/10/12 - open	05/10/12 - open					GE Mobile Water Inc.	Competitive	Condenser Clean Up and Water Filtration Services (PTN)
169	2293072 RIs 21	Open	11/01/12 - open	11/01/12 - open					Industrial Testing Laboratory	Competitive	EPU Quality Control Support Services for 4R27 (PTN)
170	2293489 RIs 7	Open	09/07/11 - open	09/07/11 - open					Stone & Webster Construction Inc	Competitive	Supplementary Maintenance and Related Services (PTN)
171	2293489 RIs 9	Open	10/13/11 - open	10/13/11 - open					Stone & Webster Construction Inc	Competitive	Supplementary Maintenance and Related Services (PSL)

A B C D

Legend:
PDS = Predetermined Source
OEM = Original Equipment Manufacturer
PSL = St. Lucie
PTN = Turkey Point

* The original amount of the contract was less than \$25,000; however, a subsequent revision required competitive bidding.
** The original amount of the contract was less than \$25,000; however, a subsequent revision required a single source justification (SSJ).

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO 121869

Major Task or Tasks Associated With:
Supply Eight (8) Normal Containment Coolers and provide Testing Services

Vendor Identity:
AAF MCQUAY

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
4

Number of Bids Received:
2

Brief Description of Selection Process:
Competitive selection with a technical and commercial evaluation process resulting in an award to AAF McQuay.

Dollar Value:
Total Contract Value through Revision 4 is [REDACTED]

Contract Status:
Active

Term Begin:
April 29, 2009

Term End:
Open

Nature and Scope of Work:
Supply Eight (8) Normal Containment Coolers and provide Testing Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PSL PO 120769

Major Task or Tasks Associated With:

Replacement IsoPhase Bus Duct Coolers

Vendor Identity:

Calvert Company Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

1

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Calvert Company Inc.

Dollar Value:

Total Dollar Value through Revision 6 is [REDACTED]

Contract Status:

Active

Term Begin:

March 26, 2009

Term End:

Open

Nature and Scope of Work:

Replacement IsoPhase Bus Duct Coolers, Technical Installation Support and Field Testing.

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PTN PO 124436

Major Task or Tasks Associated With:

Replacement Isolated Phase BusDuct

Vendor Identity:

Calvert Company Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Calvert Company Inc.

Dollar Value:

Total Dollar Value through Revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

July 17, 2009

Term End:

Open

Nature and Scope of Work:

Replacement Isolated Phase BusDuct, Demolition and Installation Services, Evaluation, Testing and Engineering

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PSL PO 121985

Major Task or Tasks Associated With:
Replacement Main Feedwater Pumps

Vendor Identity:
Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
5

Number of Bids Received:
2

Brief Description of Selection Process:
Competitive selection with a technical and commercial evaluation process resulting in an award to Flowsolve Corp.

Dollar Value:

Total Dollar Value through Revision 6 is [REDACTED]

Contract Status:
Closed

Term Begin:
April 24, 2009

Term End:
February 12, 2013

Nature and Scope of Work:
Replacement Main Feedwater Pumps, spare parts and technical direction of installation.

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO 123137

Major Task or Tasks Associated With:
Main Feedwater Isolation Valves

Vendor Identity:
Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
3

Number of Bids Received:
3

Brief Description of Selection Process:
Competitive selection with a technical and commercial evaluation process resulting in an award to Flowsolve Corp.

Dollar Value:
[REDACTED]

Contract Status:
Active

Term Begin:
May 28, 2009

Term End:
Open

Nature and Scope of Work:
Main Feedwater Isolation Valves, Technical Field Services, Testing, Engineering and Documentation

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PSL PO 125454

Major Task or Tasks Associated With:

Replacement Heater Drain Pumps

Vendor Identity:

Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to Flowsolve Corp.

Dollar Value:

Total Dollar Value through Revision 3 is [REDACTED]

Contract Status:

Active

Term Begin:

August 28, 2009

Term End:

Open

Nature and Scope of Work:

Replacement Heater Drain Pumps, Spare Heater, Technical Direction

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PTN PO 119078

Major Task or Tasks Associated With:

NSSS Engineering Evaluation and LAR Analysis for PTN Units 3 & 4

Vendor Identity:

Westinghouse Electric Co.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Dollar Value through Revision 6 is [REDACTED]

Contract Status:

Active

Term Begin:

Letter of Authorization issued 12/9/08; PO issued 1/26/09

Term End:

Open

Nature and Scope of Work:

NSSS Engineering Evaluation and LAR Analysis for PTN Units 3 & 4

St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed

1

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PSL PO 115297

Major Task or Tasks Associated With:
Design Review for LAR (Steam Generator and Reactor Head)

Vendor Identity:
AREVA

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Dollar Value through Revision 8 [REDACTED]

Contract Status:
Active

Term Begin:
August 27, 2008

Term End:
Open

Nature and Scope of Work:
Design Review for LAR (Steam Generator and Reactor Head)

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PTN PO 115338

Major Task or Tasks Associated With:

Engineering Analysis

Vendor Identity:

AREVA

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Dollar Value through Revision 11 [REDACTED]

Contract Status:

Active

Term Begin:

August 27, 2008

Term End:

Open

Nature and Scope of Work:

Design review for the Reactor Coolant system, Control Rod Mechanism, EMA, CFD and BMI

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO 117809

Major Task or Tasks Associated With:
Provide Engineering, Procurement and Construction Services for PTN

Vendor Identity:
Bechtel

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
6

Number of Bids Received:
5

Brief Description of Selection Process:
Bidders were evaluated against predetermined technical and commercial criteria, awarding to the lowest evaluated bidder.

Dollar Value:
PO value through Rev 10/Rel 0 [REDACTED]

Contract Status:
Active

Term Begin:
December 2, 2008

Term End:
Open

Nature and Scope of Work:
Bechtel's scope includes project management, design engineering, procurement and material handling services, work order planning, construction/implementation, project controls, quality assurance, quality control, radiation protection (alara), safety, security interface, and other services as designated in the Contract documents.

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PO # 116088

Major Task or Tasks Associated With:
Turbine/Generator Uprate

Vendor Identity:
Siemens Power

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single source

Dollar Value:
Total Blanket Purchase Order Max Value through Revision 7/Release
C [REDACTED]

Contract Status:
Active

Term Begin:
September 29, 2008

Term End:
Open

Nature and Scope of Work:
Engineering, Parts and Installation for PSL Turbine/Generator Uprate

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PSL PO 117820

Major Task or Tasks Associated With:

Provide Engineering, Procurement and Construction Services for PSL

Vendor Identity:

Bechtel

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

6

Number of Bids Received:

5

Brief Description of Selection Process:

Bidders were evaluated against predetermined technical and commercial criteria, awarding to the lowest evaluated bidder.

Dollar Value:

PO value through Rev 11/Rel 0 is [REDACTED]

Contract Status:

Active

Term Begin:

December 2, 2008

Term End:

Open

Nature and Scope of Work:

Bechtel's scope includes project management, design engineering, procurement and material handling services, work order planning, construction/implementation, project controls, quality assurance, quality control, radiation protection (alara), safety, security interface, and other services as designated in the Contract documents.

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PO # 116090

Major Task or Tasks Associated With:

PTN Turbine Generator Uprate

Vendor Identity:

Siemens Power

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Blanket Purchase Order Max Value through Rev. 4/Rel 0 is [REDACTED]

Contract Status:

Active

Term Begin:

September 29, 2008

Term End:

Open

Nature and Scope of Work:

PTN Engineering, Parts and Installation for Turbine/Generator Uprate

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PO # 118328

Major Task or Tasks Associated With:

PTN Condenser Tube Bundles for Unit 3 & 4

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through Revision 7 is [REDACTED]

Contract Status:

Active

Term Begin:

December 19, 2008

Term End:

Open

Nature and Scope of Work:

Supply PTN Condenser Tube Bundles

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PO # 118206

Major Task or Tasks Associated With:
PTN MSR's for Units 3 & 4

Vendor Identity:
Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
3

Number of Bids Received:
2

Brief Description of Selection Process:
The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:
Total Dollar Value through Revision 2 [REDACTED]

Contract Status:
Active

Term Begin:
December 17, 2008

Term End:
Open

Nature and Scope of Work:
Supply PTN Moisture Separator Reheaters

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PO # 118205

Major Task or Tasks Associated With:

PSL MSR's for Units 1 & 2

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

2

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through Revision 6 is [REDACTED]

Contract Status:

Active

Term Begin:

December 17, 2008

Term End:

Open

Nature and Scope of Work:

Supply PSL Moisture Separator Reheaters

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PO # 118241

Major Task or Tasks Associated With:

PTN Feedwater Heaters for Units 3 & 4

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

3

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Contract Value through Revision 3 [REDACTED]

Contract Status:

Active

Term Begin:

December 13, 2008

Term End:

Open

Nature and Scope of Work:

Supply PTN Feedwater Heaters

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PO # 112221

Major Task or Tasks Associated With:

PSL Licensing Engineering and BOP Spec Development

Vendor Identity:

Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Blanket Purchase Order Max Value through Revision 20 to

Release 0 is [REDACTED]

Contract Status:

Active

Term Begin:

April 22, 2008

Term End:

Open

Nature and Scope of Work:

PSL Licensing Engineering and BOP Spec Development

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PO # 112177

Major Task or Tasks Associated With:
PTN Licensing Engineering and BOP Spec Development

Vendor Identity:
Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Blanket Purchase Order Max Value through Revision 8 to Release 0 is [REDACTED]

Contract Status:
Active

Term Begin:
April 22, 2008

Term End:
Open

Nature and Scope of Work:
PTN Licensing Engineering and BOP Spec Development

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PO 117272

Major Task or Tasks Associated With:
Gantry crane repair/modification

Vendor Identity:
American Crane

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
OEM

Dollar Value:
Total Dollar Value through Rev 6 is [REDACTED]

Contract Status:
Active

Term Begin:
November 13, 2008

Term End:
Open

Nature and Scope of Work:
Complete modification of Unit 1 crane and update of electrical components for Unit 2 crane

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PO # 118224

Major Task or Tasks Associated With:

PSL Feedwater Heaters for Units 1 & 2

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Dollar Value thru Revision 8 [REDACTED]

Contract Status:

Active

Term Begin:

December 17, 2008

Term End:

Open

Nature and Scope of Work:

Supply PSL Feedwater Heaters

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PO # 115465

Major Task or Tasks Associated With:

Eng. Services for NSSS, BOP & Licensing Activities

Vendor Identity:

Zachry Nuclear Engineering

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Dollar Value through revision 4 is [REDACTED]

Contract Status:

Active

Term Begin:

September 3, 2009

Term End:

Open

Nature and Scope of Work:

PTN Eng. Services for NSSS, BOP and Licensing Activities.

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PO # 118278

Major Task or Tasks Associated With:

PSL Heat Exchangers for Units 1 & 2

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

3

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through Revision 5 is [REDACTED]

Contract Status:

Active

Term Begin:

December 19, 2008

Term End:

Open

Nature and Scope of Work:

Supply PSL Heat Exchangers

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PO # 105720

Major Task or Tasks Associated With:

PSL Fuels Analysis

Vendor Identity:

Areva

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Order value through Revision 17 is [REDACTED]

Contract Status:

Active

Term Begin:

September 12, 2007

Term End:

Open

Nature and Scope of Work:

Fuels Performance Study and Analysis

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PO 116107

Major Task or Tasks Associated With:
Ultrasonic Flow Measuring System

Vendor Identity:
Cameron Technologies

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Purchase Order Value through Revision 1 is [REDACTED]

Contract Status:
Active

Term Begin:
September 29, 2008

Term End:
Open

Nature and Scope of Work:
Ultrasonic Flow Measuring System for PTN

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PO # 126453

Major Task or Tasks Associated With:
Turbine Plant Cooling Water Heat Exchangers

Vendor Identity:
Joseph Oat Corporation

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
3

Number of Bids Received:
3

Brief Description of Selection Process:
Competitive Selection, Commercial and Technical Evaluation

Dollar Value:
Total Contract Value through revision 1 is [REDACTED]

Contract Status:
Active

Term Begin:
November 5, 2009

Term End:
Open

Nature and Scope of Work:
Supply Turbine Plant Cooling Water Heat Exchangers

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO #127777

Major Task or Tasks Associated With:
Estimating Services

Vendor Identity:
High Bridge

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Contract Value through revision 2 is [REDACTED]

Contract Status:
Active

Term Begin:
December 8, 2009

Term End:
Open

Nature and Scope of Work:
Estimating Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO # 127881

Major Task or Tasks Associated With:
Procedure Writers

Vendor Identity:
Absolute Consulting

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
[REDACTED]

Contract Status:
Active

Term Begin:
December 22, 2009

Term End:
Open

Nature and Scope of Work:
Procedure Writers

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PSL PO #118563

Major Task or Tasks Associated With:

Fuel Storage Criticality and Related Analysis (PSL 1)

Vendor Identity:

Holtec

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Purchase Order Value through Revision 7 is [REDACTED]

Contract Status:

Closed

Term Begin:

January 14, 2009

Term End:

January 29, 2013

Nature and Scope of Work:

Fuel Storage Criticality and Related Analysis (PSL 1)

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO # 130612

Major Task or Tasks Associated With:
Condensate Pumps

Vendor Identity:
Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
3

Number of Bids Received:
3

Brief Description of Selection Process:
Competitive

Dollar Value:
Total Contract Value through Revision 2 is [REDACTED]

Contract Status:
Active

Term Begin:
April 22, 2010

Term End:
Open

Nature and Scope of Work:
Condensate Pumps

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO #130649

Major Task or Tasks Associated With:
Main Feedwater Pumps

Vendor Identity:
Flowsolve Corp

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
3

Number of Bids Received:
1

Brief Description of Selection Process:
Competitive

Dollar Value:
[REDACTED]

Contract Status:
Active

Term Begin:
April 22, 2010

Term End:
Open

Nature and Scope of Work:
Main Feedwater Pumps

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO # 126227

Major Task or Tasks Associated With:
Control System FWH, Moisture Separator

Vendor Identity:
Invensys

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
OEM

Dollar Value:
Total Dollar Value through revision 12 is [REDACTED]

Contract Status:
Active

Term Begin:
October 13, 2009

Term End:
Open

Nature and Scope of Work:
Control System FWH, Moisture Separator

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO # 129689

Major Task or Tasks Associated With:
Turbine Digital Upgrade

Vendor Identity:
Invensys

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
3

Number of Bids Received:
3

Brief Description of Selection Process:
Competitive

Dollar Value:
Total Dollar Value through Revision 4 is [REDACTED]

Contract Status:
Active

Term Begin:
March 17, 2010

Term End:
Open

Nature and Scope of Work:
Turbine Digital Upgrade

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO # 130272

Major Task or Tasks Associated With:
Electro-Hydraulic Fluid Systems

Vendor Identity:
Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
3

Number of Bids Received:
3

Brief Description of Selection Process:
Competitive

Dollar Value:
Total Dollar Value through Rev 5 is [REDACTED]

Contract Status:
Active

Term Begin:
April 8, 2010

Term End:
Open

Nature and Scope of Work:
Electro-Hydraulic Fluid Systems

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PSL PO # 131533

Major Task or Tasks Associated With:
Non-Fuels NSSS Interim LAR (PSL 1 & 2)

Vendor Identity:
Areva

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Predetermined Source

Dollar Value:
Total Contract Value through Revision 4 is [REDACTED]

Contract Status:
Closed

Term Begin:
June 10, 2010

Term End:
January 29, 2013

Nature and Scope of Work:
Non-Fuels NSSS Interim LAR (PSL 1 & 2)

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PSL PO # 131907

Major Task or Tasks Associated With:
Fuels Related Interim LAR/MOD for EPU at PSL

Vendor Identity:
Areva

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Predetermined Source

Dollar Value:
Total Contract Value through Revision 5 is [REDACTED]

Contract Status:
Closed

Term Begin:
June 11, 2010

Term End:
January 29, 2013

Nature and Scope of Work:
Fuels Related Interim LAR/MOD for EPU at PSL

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-E1

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PSL PO # 131585

Major Task or Tasks Associated With:
Interim LAR/MOD for EPU at PSL

Vendor Identity:
Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Predetermined Source

Dollar Value:
Total Contract Value through Revision 8 is [REDACTED]

Contract Status:
Closed

Term Begin:
June 15, 2010

Term End:
February 20, 2013

Nature and Scope of Work:
Interim LAR/MOD for EPU at PSL

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PSL PO #131742

Major Task or Tasks Associated With:
LAR/Request for Additional Information

Vendor Identity:
Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Predetermined Source

Dollar Value:
Total Contract value through Revision 4 is [REDACTED]

Contract Status:
Active

Term Begin:
June 16, 2010

Term End:
Open

Nature and Scope of Work:
LAR/Request for Additional Information for Non-Fuels related scope

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PSL PO #131940

Major Task or Tasks Associated With:
Main Steam Turbine Control Replacement

Vendor Identity:
Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
4

Number of Bids Received:
4

Brief Description of Selection Process:
Competitive

Dollar Value:
Total Blanket PO Max Value through Rev 2 to Release 0 [REDACTED]

Contract Status:
Active

Term Begin:
June 30, 2010

Term End:
Open

Nature and Scope of Work:
Main Steam Turbine Control Replacement

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO #2259675

Major Task or Tasks Associated With:
Furnish New Spent Fuel Pool Heat Exchangers

Vendor Identity:
Joseph Oat Corporation

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
2

Number of Bids Received:
2

Brief Description of Selection Process:
Competitive

Dollar Value:
[REDACTED]

Contract Status:
Active

Term Begin:
July 23, 2010

Term End:
Open

Nature and Scope of Work:
Furnish New Spent Fuel Pool Heat Exchangers

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO # 2259669

Major Task or Tasks Associated With:
Rewind/Refurbish Upgrade Condensate Pumps

Vendor Identity:
Tampa Armature Works

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
4

Number of Bids Received:
2

Brief Description of Selection Process:
Competitive

Dollar Value:
██████████

Contract Status:
Active

Term Begin:
August 2, 2010

Term End:
Open

Nature and Scope of Work:
Rewind/Refurbish Upgrade Condensate Pumps

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PSL PO #2260113

Major Task or Tasks Associated With:
PSL Rod Control System Upgrades

Vendor Identity:
Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
OEM

Dollar Value:
Total Contract Value through Amendment \$ [REDACTED]

Contract Status:
Active

Term Begin:
September 23, 2010

Term End:
Open

Nature and Scope of Work:
PSL Rod Control System Upgrades

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO #2261747

Major Task or Tasks Associated With:
EPU NSSS Engineering and Modification Support

Vendor Identity:
Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Predetermined Source

Dollar Value:
Total Contract Value through Amendment 4 [REDACTED]

Contract Status:
Active

Term Begin:
September 23, 2010

Term End:
Open

Nature and Scope of Work:
EPU NSSS Engineering and Modification Support

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PSL PO #2263036

Major Task or Tasks Associated With:
Condensate Pumps (PSL)

Vendor Identity:
Flowserve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
N/A

Number of Bids Received:
N/A

Brief Description of Selection Process:
Replaces PO 130160, which was competitively bid.

Dollar Value:
Total Contract Value through Amendment 2 [REDACTED]

Contract Status:
Active

Term Begin:
October 19, 2010

Term End:
Open

Nature and Scope of Work:
Replacement Condensate Pumps (PSL)

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO #2263549

Major Task or Tasks Associated With:
Project Management

Vendor Identity:
Areva NP Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
2

Number of Bids Received:
2

Brief Description of Selection Process:
Competitive

Dollar Value:
Total Dollar Value through Amendment #1 [REDACTED]

Contract Status:
Active

Term Begin:
November 10, 2010

Term End:
Open

Nature and Scope of Work:
Services of a Project Manager

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO #2263930

Major Task or Tasks Associated With:
Scaffolding Material

Vendor Identity:
Brand Energy Solutions

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
N/A

Number of Bids Received:
N/A

Brief Description of Selection Process:
Replaces 131356, which was competitively bid.

Dollar Value:
Total Dollar Value through Amendment #2 [REDACTED]

Contract Status:
Active

Term Begin:
November 11, 2010

Term End:
Open

Nature and Scope of Work:
Supply of Scaffolding

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PSL PO #2264914

Major Task or Tasks Associated With:
CEDMS Power Switch Refurbishment (PSL 2)

Vendor Identity:
Westinhouse Electric

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
OEM

Dollar Value:
Total Dollar Value through Amendment #1 is [REDACTED]

Contract Status:
Active

Term Begin:
December 7, 2010

Term End:
Open

Nature and Scope of Work:
CEDMS Power Switch Refurbishment (PSL 2)

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PSL PO #2285418

Major Task or Tasks Associated With:
Implementation Spares for Turbine Generator Work

Vendor Identity:
Siemens Energy Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
OEM

Dollar Value:
Total Contract Value through Amendment 3 [REDACTED]

Contract Status:
Active

Term Begin:
December 10, 2010

Term End:
Open

Nature and Scope of Work:
Implementation Spares for Turbine Generator Work

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO #2285720

Major Task or Tasks Associated With:
Licensing/Design Basis/Program Modification

Vendor Identity:
Enercon Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
2

Number of Bids Received:
2

Brief Description of Selection Process:
Competitive

Dollar Value:
[REDACTED]

Contract Status:
Active

Term Begin:
January 4, 2011

Term End:
Open

Nature and Scope of Work:
Licensing/Design Basis/Program Modification

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO# 2290465

Major Task or Tasks Associated With:
Design, Engineering and Fabrication of Turbine Crossover piping

Vendor Identity:
Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
OEM

Dollar Value:
██████████

Contract Status:
Closed

Term Begin:
March 31, 2011

Term End:
January 15, 2013

Nature and Scope of Work:
Design, Engineering and Fabrication of Turbine Crossover piping

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
FSL PO# 2286521

Major Task or Tasks Associated With:
MSIV/MSCV Modifications

Vendor Identity:
Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
PDS

Dollar Value:
Total Dollar Value through Amendment #4 ██████████

Contract Status:
Closed

Term Begin:
January 18, 2011

Term End:
January 23, 2013

Nature and Scope of Work:
MSIV/MSCV Modifications

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PTN PO# 2290614

Major Task or Tasks Associated With:

Main Feedwater Pump Casing Modifications

Vendor Identity:

Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

N/A

Number of Bids Received:

N/A

Brief Description of Selection Process:

Replaces PO 130649, which was competitively bid.

Dollar Value:

Total Contract Value through Amend 2 [REDACTED]

Contract Status:

Active

Term Begin:

May 2, 2011

Term End:

Open

Nature and Scope of Work:

Main Feedwater Pump Casing Modifications

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO# 2293950

Major Task or Tasks Associated With:
Turbine Generator Pre-Outage Planning PTN 3 & 4

Vendor Identity:
Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Contract value through Amendment 1 [REDACTED]

Contract Status:
Active

Term Begin:
June 24, 2011

Term End:
Open

Nature and Scope of Work:
Turbine Generator Pre-Outage Planning PTN 3 & 4
(Turbine Generator Installation)

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PSL PO# 2294855

Major Task or Tasks Associated With:
Project Engineering

Vendor Identity:
Zachry Nuclear Engineering

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Dollar Value through Amendment #4 [REDACTED]

Contract Status:
Active

Term Begin:
July 21, 2011

Term End:
Open

Nature and Scope of Work:
Project Engineering Support

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PSL PO# 2295071

Major Task or Tasks Associated With:

Unit 1 Vibration and Support Mods for FW & Condensate

Vendor Identity:

Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Dollar Value through Amendment #3 [REDACTED]

Contract Status:

Active

Term Begin:

August 1, 2011

Term End:

Open

Nature and Scope of Work:

Unit 1 Vibration and Support Mods for FW & Condensate

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO# 2296556

Major Task or Tasks Associated With:
Modification, overhaul and refurbishment of the B and C AFW

Vendor Identity:
Sulzer Pumps

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
OEM

Dollar Value:
Contract Value through Amendment 2 is [REDACTED]

Contract Status:
Active

Term Begin:
September 2, 2011

Term End:
Open

Nature and Scope of Work:
Modification, overhaul and refurbishment of the B and C AFW

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO# 2298266

Major Task or Tasks Associated With:
Shuttle Bus Service

Vendor Identity:
Frammar Corporation

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
3

Number of Bids Received:
2

Brief Description of Selection Process:
Competitive

Dollar Value:
Total Dollar Value through Amendment #1 [REDACTED]

Contract Status:
Active

Term Begin:
October 12, 2011

Term End:
Open

Nature and Scope of Work:
Shuttle Bus Service

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PSL PO# 2298406

Major Task or Tasks Associated With:

Fuel Movers for Metamic Inserts

Vendor Identity:

Master Lee Energy Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

1

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Dollar Value through Amendment 2 is [REDACTED]

Contract Status:

Active

Term Begin:

October 12, 2011

Term End:

Open

Nature and Scope of Work:

Fuel Movers for Metamic Inserts

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO# 2299618

Major Task or Tasks Associated With:
Truck Monitoring/Waste Characterization

Vendor Identity:
Radiation Safety & Control

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
2

Number of Bids Received:
2

Brief Description of Selection Process:
Competitive

Dollar Value:
Total Dollar Value through Amendment #1 [REDACTED]

Contract Status:
Active

Term Begin:
November 4, 2011

Term End:
Open

Nature and Scope of Work:
Truck Monitoring/Waste Characterization

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PSL PO# 2297055

Major Task or Tasks Associated With:
Replacement Unit 2 LP #4 Feedwater Heaters for EPU

Vendor Identity:
Thermal Engineering

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Dollar Value through Amendment # [REDACTED]

Contract Status:
Active

Term Begin:
September 16, 2011

Term End:
Open

Nature and Scope of Work:
Replacement Unit 2 LP #4 Feedwater Heaters for EPU

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PSL PO# 2300139

Major Task or Tasks Associated With:
SL 1-24 Turbine Generator Installation

Vendor Identity:
Siemens Energy Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Dollar Value through Amendment #1 [REDACTED]

Contract Status:
Active

Term Begin:
November 21, 2011

Term End:
Open

Nature and Scope of Work:
SL 1-24 Turbine Generator Installation

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PSL PO# 2299624

Major Task or Tasks Associated With:
Upgrade Services for Feedwater Pumps

Vendor Identity:
Ames Group LLC

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Contract Value through Revision 4 [REDACTED]

Contract Status:
Closed

Term Begin:
November 16, 2011

Term End:
January 17, 2013

Nature and Scope of Work:
Upgrade Services for Feedwater Pumps

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PTN PO # 2301867

Major Task or Tasks Associated With:

Develop Engineering Change Packages for EPU at PTN

Vendor Identity:

Enercon Services Inc

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Dollar Value through Amendment #3 [REDACTED]

Contract Status:

Active

Term Begin:

December 20, 2011

Term End:

Open

Nature and Scope of Work:

Develop Engineering Change Packages for EPU at PTN

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO # 2261800

Major Task or Tasks Associated With:
Supply of Simulator SCD Software Translator Upgrade

Vendor Identity:
L3 Communications Mapps Inc

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
O&A

Dollar Value:
Total Contract Value through Amendment 4 [REDACTED]

Contract Status:
Active

Term Begin:
September 28, 2010

Term End:
Open

Nature and Scope of Work:
Supply of Simulator SCD Software Translator Upgrade

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO # 2301737

Major Task or Tasks Associated With:
Construction Management Oversight Services for PTN

Vendor Identity:
PCI Energy Services

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
[REDACTED]

Contract Status:
Active

Term Begin:
December 21, 2011

Term End:
Open

Nature and Scope of Work:
Construction Management Oversight Services for PTN

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO # 2301736

Major Task or Tasks Associated With:
Construction Management Oversight Services

Vendor Identity:
Weldtech Services

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
[REDACTED]

Contract Status:
Active

Term Begin:
December 21, 2011

Term End:
Open

Nature and Scope of Work:
Construction Management Oversight Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO #2301871

Major Task or Tasks Associated With:
Develop Engineering Changes Packages for EPU at PTN

Vendor Identity:
Zachry Nuclear Engineering

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Contract Value through Amendment 1 [REDACTED]

Contract Status:
Active

Term Begin:
December 28, 2011

Term End:
Open

Nature and Scope of Work:
Develop Engineering Changes Packages for EPU at PTN

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO #2301858

Major Task or Tasks Associated With:
Develop TPCW Changes Packages for EPU at PTN

Vendor Identity:
Sargent & Lundy Inc

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Contract Value through Amendment #1 [REDACTED]

Contract Status:
Active

Term Begin:
December 28, 2011

Term End:
Open

Nature and Scope of Work:
Develop TPCW Changes Packages for EPU at PTN

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PTN PO #2302164

Major Task or Tasks Associated With:

Valve Upgrade Services for EPU/PTN 3 & 4

Vendor Identity:

Ames Group LLC

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Dollar Value through Amendment 2 is [REDACTED]

Contract Status:

Active

Term Begin:

January 25, 2012

Term End:

Open

Nature and Scope of Work:

Valve Upgrade Services for EPU/PTN 3 & 4

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO #2303610

Major Task or Tasks Associated With:
Engineering Support

Vendor Identity:
Chaw - Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Dollar Value through Amendment #2 [REDACTED]

Contract Status:
Active

Term Begin:
February 15, 2012

Term End:
Open

Nature and Scope of Work:
Engineering Support

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO #2303735

Major Task or Tasks Associated With:
3R26 Outage Implementation Services for EPU at PTN

Vendor Identity:
Siemens Energy Inc

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Dollar Value through Amendment #1 [REDACTED]

Contract Status:
Active

Term Begin:
February 14, 2012

Term End:
Open

Nature and Scope of Work:
3R26 Outage Implementation Services for EPU at PTN

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PSL PO #2302300

Major Task or Tasks Associated With:

Unit 2 DEH Turbine Control System Replacement for EPU at PSL

Vendor Identity:

Shaw - Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Predetermined Source

Dollar Value:

Total Dollar Value through Amendment 002 is [REDACTED]

Contract Status:

Active

Term Begin:

January 11, 2012

Term End:

Open

Nature and Scope of Work:

Unit 2 DEH Turbine Control System Replacement for EPU at PSL

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO #2304432

Major Task or Tasks Associated With:
EPU Welding Implementation and Installation Services

Vendor Identity:
Weldtech Services

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Dollar Value through Amendment #5 is [REDACTED]

Contract Status:
Active

Term Begin:
February 28, 2012

Term End:
Open

Nature and Scope of Work:
EPU Welding Implementation and Installation Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO #2304908

Major Task or Tasks Associated With:
Engineering and EC Support for PTN

Vendor Identity:
Zachry Nuclear Engineering

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Dollar Value through Amendment 2 [REDACTED]

Contract Status:
Active

Term Begin:
March 8, 2012

Term End:
Open

Nature and Scope of Work:
Engineering and EC Support for PTN

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PSL PO #2307710

Major Task or Tasks Associated With:
Unit 1 Mid-cycle Analysis

Vendor Identity:
Areva NP Inc

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
N/A

Number of Bids Received:
N/A

Brief Description of Selection Process:
Replaces 105720

Dollar Value:
[REDACTED]

Contract Status:
Closed

Term Begin:
May 15, 2012

Term End:
January 31, 2013

Nature and Scope of Work:
Unit 1 Mid-cycle Analysis

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO #2308803

Major Task or Tasks Associated With:
Replacement of Isolated Phase Bus Duct

Vendor Identity:
Calvert Company Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
N/A

Number of Bids Received:
N/A

Brief Description of Selection Process:
Replaces 124436, which was competitively bid.

Dollar Value:
Total Dollar Value through Amendment #1 [REDACTED]

Contract Status:
Active

Term Begin:
June 12, 2012

Term End:
Open

Nature and Scope of Work:
Replacement of Isolated Phase Bus Duct

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PSL PO #2309312

Major Task or Tasks Associated With:
Valve Actuator Support Specialty Services

Vendor Identity:
Ames Group LLC

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Dollar Value through Amendment #1 [REDACTED]

Contract Status:
Active

Term Begin:
June 25, 2012

Term End:
Open

Nature and Scope of Work:
Valve Actuator Support Specialty Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
FPL PO #2300442

Major Task or Tasks Associated With:
Start-Up and Testing Support

Vendor Identity:
J. Givoo Consultants

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
5

Number of Bids Received:
4

Brief Description of Selection Process:
Competitive

Dollar Value:
Total Dollar Value through Amendment #2 is [REDACTED]

Contract Status:
Active

Term Begin:
July 9, 2012

Term End:
Open

Nature and Scope of Work:
Start-Up and Testing Support

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PTN PO #2309693

Major Task or Tasks Associated With:

Implementation and Installation of Unit 4 Spent Fuel Pool Heat Exchangers

Vendor Identity:

PCE Energy Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

7

Number of Bids Received:

4

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Dollar Value through Amendment 1 [REDACTED]

Contract Status:

Active

Term Begin:

July 6, 2012

Term End:

Open

Nature and Scope of Work:

Implementation and Installation of Unit 4 Spent Fuel Pool Heat Exchangers

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PTN PO #2311510

Major Task or Tasks Associated With:

Engineering Support for EPU (PTN 4)

Vendor Identity:

Shaw - Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

██████████

Contract Status:

Active

Term Begin:

August 16, 2012

Term End:

Open

Nature and Scope of Work:

Engineering Support for EPU (PTN 4)

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PSL PO #2310927

Major Task or Tasks Associated With:

PSL 2-20 Turbine Generator Services

Vendor Identity:

Siemens Energy Inc

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Dollar Value through Amendment #1 [REDACTED]

Contract Status:

Active

Term Begin:

August 7, 2012

Term End:

Open

Nature and Scope of Work:

PSL 2-20 Turbine Generator Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO #2311900

Major Task or Tasks Associated With:
PTN 4-27 Turbine Generator Services

Vendor Identity:
Siemens Energy Inc

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
[REDACTED]

Contract Status:
Active

Term Begin:
September 5, 2012

Term End:
Open

Nature and Scope of Work:
PTN 4-27 Turbine Generator Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PTN PO 2311037

Major Task or Tasks Associated With:

Coating Services

Vendor Identity:

Williams Specialty Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

N/A

Number of Bids Received:

N/A

Brief Description of Selection Process:

Replaces Corporate Blanket 4500412063, which was competitively bid.

Dollar Value:

██████████

Contract Status:

Active

Term Begin:

August 10, 2012

Term End:

Open

Nature and Scope of Work:

Coating Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PTN PO 2314332

Major Task or Tasks Associated With:

Radiography Testing Services

Vendor Identity:

Team Industrial Services Inc

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

* This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total dollar value through Revision 1 is [REDACTED]

Contract Status:

Active

Term Begin:

October 30, 2012

Term End:

Open

Nature and Scope of Work:

Radiography Testing Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN PO 2315635

Major Task or Tasks Associated With:
Turbine Bypass and Steam Dump Control Systems Valves

Vendor Identity:
Control Components

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
██████████

Contract Status:
Active

Term Begin:
December 14, 2012

Term End:
Open

Nature and Scope of Work:
Turbine Bypass and Steam Dump Control Systems Valves

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PSL PO #2301976

Major Task or Tasks Associated With:
Spent Fuel Handling

Vendor Identity:
Westinghouse Electric Co.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
OEM

Dollar Value:
Total Dollar Value through Amendment #3 is [REDACTED]

Contract Status:
Active

Term Begin:
February 1, 2012

Term End:
Open

Nature and Scope of Work:
Spent fuel handling modification for EPU

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PSL Release 014 Blanket Contract 2260135

Major Task or Tasks Associated With:

Radiation Protection Services

Vendor Identity:

Bartlett Nuclear Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Blanket Contract 2260135 Replaces Blanket Contract 113086 which was issued on a competitive basis.

Dollar Value:

Total Dollar Value through Amendment #5 is [REDACTED]

Contract Status:

Active

Term Begin:

October 26, 2010

Term End:

Open

Nature and Scope of Work:

Radiation Protection Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PTN Release 013 Blanket Contract 2262301

Major Task or Tasks Associated With:

Radiation Protection Services

Vendor Identity:

Bartlett Nuclear Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Blanket Contract 2262301 Replaces Blanket Contract 113293 which was issued on a competitive basis.

Dollar Value:

Total Dollar Value through Amendment #1: [REDACTED]

Contract Status:

Active

Term Begin:

January 30, 2012

Term End:

Open

Nature and Scope of Work:

Radiation Protection Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

COMPANY: FLORIDA POWER & LIGHT COMPANY

For the Year Ended 12/31/2013
Witness: T. O. Jones

DOCKET NO: 130009-EI

Contract No.:

PTN Release 017 Blanket Contract 2262301

Major Task or Tasks Associated With:

Radiation Protection Services

Vendor Identity:

Bartlett Nuclear Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Blanket Contract 2262301 Replaces Blanket Contract 113293 which was issued on a competitive basis.

Dollar Value:

██████████

Contract Status:

Active

Term Begin:

June 21, 2012

Term End:

Open

Nature and Scope of Work:

Radiation Protection Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN Release 004 to Blanket Contract 2287944

Major Task or Tasks Associated With:
EPU Radioactive Waste Disposal

Vendor Identity:
Energy Solutions, LLC

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Blanket Contract 2287944 replaced Blanket Contract 99395 which was issued as a Single Source.

Dollar Value:
[REDACTED]

Contract Status:
Active

Term Begin:
March 7, 2012

Term End:
Open

Nature and Scope of Work:
EPU Radioactive Waste Disposal

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

PTN Release 086 to Blanket Contract 2260140

Major Task or Tasks Associated With:

Security Services for EPU Unit 4

Vendor Identity:

G4S Regulated Security Solutions Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Blanket Contract 2260140 Replaces Blanket Contract 118419 which was issued as a Single Source.

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 17, 2012

Term End:

Open

Nature and Scope of Work:

Security Services for EPU Unit 4

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:
PTN Release 007 to Blanket Contract 2293489

Major Task or Tasks Associated With:
Supplementary Maintenance and Related Services

Vendor Identity:
Stone & Webster Construction Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
3

Number of Bids Received:
3

Brief Description of Selection Process:
Blanket Contract 2293489 was competitively bid

Dollar Value:
Total Dollar Value through Amendment # 5 is ██████████

Contract Status:
Active

Term Begin:
September 7, 2011

Term End:
Open

Nature and Scope of Work:
Supplementary Maintenance and Related Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Actual and Estimated Filing: Contracts Executed**

Schedule AE-7B (Actual/Estimated)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2013
Witness: T. O. Jones

Contract No.:

P&L Release 009 to Blanket Contract 2293489

Major Task or Tasks Associated With:

Supplementary Maintenance and Related Services

Vendor Identity:

Stone & Webster Construction Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Blanket Contract 2293489 was competitively bid

Dollar Value:

Total Dollar Value through Amendment # 1 is [REDACTED]

Contract Status:

Active

Term Begin:

October 13, 2011

Term End:

Open

Nature and Scope of Work:

Supplementary Maintenance and Related Services

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
Projection Filing: Contracts Executed**

Schedule P-7A (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO: 130009-EI

EXPLANATION:

For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Projection Expended as of Prior Year End (2013)	Amount to be Expended in Current Year (2014)	Projection Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
1	121869	Open	4/29/09 - open	4/29/09 - open					AAF MCQUAY	Competitive	Supply Normal Containment Coolers and Testing Services (PTN)
2	120769	Open	3/26/09 - open	3/26/09 - open					Calvert Company Inc	Competitive	Iso Phase Bus Duct Coolers and Testing Services (PSL)
3	124436	Open	7/17/09 - open	7/17/09 - open					Calvert Company Inc	Competitive	Iso Phase Bus Duct Coolers, Install, Demo & Testing Services (PTN)
4	121985	Closed	4/24/09 - 02/12/13	4/24/09 - 02/12/13					Flowsolve Corp.	Competitive	Replacement Main Feedwater Pumps & Various Testing (PSL)
5	123137	Open	5/28/09 - open	5/28/09 - open					Flowsolve Corp.	Competitive	Main Feedwater Isolation Valves and Testing Services (PTN)
6	125454	Open	8/28/09 - open	8/28/09 - open					Flowsolve Corp.	Competitive	Replacement Heater Drain Pumps (PSL)
7	119078	Open	12/9/08 - open	12/9/08 - open					Westinghouse	OEM	NSSS Engineering Analysis and LAR (PTN)
8	121947	Open	4/24/09 - open	4/24/09 - open					Westinghouse	OEM	New & Spent Fuel Criticality and Thermal Hydraulic Analysis (PTN)
9	115297	Open	8/27/08 - open	8/27/08 - open					Areva	Single Source	RSG Design Review and LAR Work (PSL)
10	115338	Open	8/27/08 - open	8/27/08 - open					Areva	Single Source	Engineering Analysis (PTN)
11	117809	Open	12/02/08 - open	12/02/08 - open					Bechtel	Competitive Bid	Engineering Procurement Construction (PTN)
12	116088	Open	09/29/08 - open	09/29/08 - open					Siemens	Single Source	Low Pressure Turbine, Exciter, Exciter Inst. (PSL)
13	117820	Open	12/02/08 - open	12/02/08 - open					Bechtel	Competitive Bid	Engineering Procurement Construction (PSL)
14	116090	Open	9/29/08 - open	9/29/08 - open					Siemens	Single Source	Turbine, Generator/Exciter Upgrades & Inst. (PTN)
15	118328	Open	12/19/08 - open	12/19/08 - open					TEI	Competitive Bid	Condenser Tubes (PTN)
16	118206	Open	12/17/08 - open	12/17/08 - open					TEI	Competitive Bid	Moisture Separator Reheaters (PTN)
17	118205	Open	12/17/08 - open	12/17/08 - open					TEI	Competitive Bid	Moisture Separator Reheaters (PSL)
18	118241	Open	12/19/08 - open	12/19/08 - open					TEI	Competitive Bid	Feed Water Heaters (PTN)
19	112221	Open	4/22/08 - open	4/22/08 - open					Shaw - Stone & Webster	Single Source	Licensing Engineering and BOP Spec Development (PSL)
20	112177	Open	4/22/08 - open	4/22/08 - open					Shaw - Stone & Webster	Single Source	Licensing Engineering and BOP Spec Development (PTN)
21	117272	Open	11/13/08 - open	11/13/08 - open					American Crane	OEM	Gantry Crane Upgrade (PSL)
22	118224	Open	12/17/08 - open	12/17/08 - open					TEI	Competitive Bid	Feed Water Heaters (PSL)
23	115465	Open	9/03/08 - open	9/03/08 - open					Zachry Nuclear Engineering	Single Source	Engineering Services (PTN)
24	118278	Open	12/19/08 - open	12/19/08 - open					TEI	Competitive Bid	TCW Heat Exchangers (PSL)
25	105720	Open	9/12/07 - open	9/12/07 - open					Areva	Single Source	Fuels Analysis (PSL)
26	116107	Open	9/29/08 - open	9/29/08 - open					Cameron Tech.	Single Source	Ultrasonic Flow Meter Measuring System (PSL)
27	113030	Open	5/20/08 - open	5/20/08 - open					FPL Seabrook	Single Source	FPLE personnel supporting FPL Upgrades (PSL & PTN)

A B C D
1 of 100

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Projection Filing: Contracts Executed**

Schedule P-7A (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO: 130009-EI

EXPLANATION:

For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work.

For the Year Ended 12/31/2014

Witness: T. O. Jones

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Projection Expended as of Prior Year End (2013)	Amount to be Expended in Current Year (2014)	Projection Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
28	115391	Open	8/29/08 - open	8/29/08 - open					NAI	Single Source	Radiological Consequence Analysis (PSL)
29	112987	Open	5/19/08 - open	5/19/08 - open					Zachry	Single Source	Radiological Consequence Analysis (PTN)
30	126453	Open	11/05/09 - open	11/05/09 - open					Joseph Oat Corporation	Competitive	Cooling Water Heat Exchangers (PTN)
31	127777	Open	12/08/09 - open	12/08/09 - open					High Bridge	Single Source	Estimating Services (PTN)
32	127881	Open	12/22/09 - open	12/22/09 - open					Absolute Consulting	Single Source	Procedure Writers (PTN)
33	123762	Open	6/25/09 -open	6/25/09 -open					Key Controls of Tampa	OEM	Control System Tuning and Dynamic Analysis (PTN)
34	118563	Closed	1/14/09 - 01/29/13	1/14/09 - 01/29/13					Holtec	Competitive	Fuel Storage Criticality and related analysis (PSL 1)
35	130160	Open	3/29/10 -open	3/29/10 -open					Flowsolve Corp.	Competitive	Replacement Condensate Pumps (PSL)
36	130612	Open	4/22/10 - open	4/22/10 - open					Flowsolve Corp.	Competitive	Condensate Pumps (PTN)
37	130649	Open	4/22/10 - open	4/22/10 - open					Flowsolve Corp.	Competitive	Main Feedwater Pumps (PTN)
38	126227	Open	10/13/09 - open	10/13/09 - open					Invensys	OEM	Control System FWH, Moisture Separator (PTN)
39	129689	Open	3/17/10 - open	3/17/10 - open					Invensys	Competitive	Turbine Digital Upgrade (PTN)
40	130272	Open	4/08/10 - open	4/08/10 - open					Siemens Energy Inc.	Competitive	Electro-Hydraulic Fluid Systems (PTN)
41	131599	Open	5/27/10 - open	5/27/10 - open					All Star Toilets	Competitive	Supply Cleaning Services (PTN)
42	131533	Closed	6/10/10 -01/29/13	6/10/10 -01/29/13					Areva	PDS	Non-Fuels NSSS Interim LAR (PSL 1 & 2)
43	131907	Closed	6/11/10 - 01/29/13	6/11/10 - 01/29/13					Areva	PDS	Fuels Related Interim LAR/MOD for EPU (PSL)
44	131585	Closed	6/15/10 - 02/20/13	6/15/10 - 02/20/13					Shaw - Stone & Webster	PDS	Interim LAR/MOD Support for EPU (PSL)
45	131742	Open	6/16/10 - open	6/16/10 - open					Westinghouse	PDS	LAR/RAI for Non-Fuels NSSS related scope (PSL)
46	132077	Open	6/17/10 - open	6/17/10 - open					Siemens Energy Inc.	Single Source	Siemens Dedicated Resident Site Manager (PTN)
47	132235	Open	6/24/10 - open	6/24/10 - open					Enercon	Single Source	NFPA 805/Appendix R Support for (PTN)
48	131940	Open	6/30/10 - open	6/30/10 - open					Westinghouse	Competitive	Main Steam Turbine Control Replacement (PSL)
49	132283	Closed	6/28/10 - 01/29/13	6/28/10 - 01/29/13					Shaw - Stone & Webster	PDS	EPU Feedwater Pump Nozzle Load Reduction (PSL)
50	2259675	Open	7/23/10 - open	7/23/10 - open					Joseph Oat Corporation	Competitive	Furnish New Spent Fuel Pool Heat Exchangers (PTN)
51	2259669	Open	8/02/10 - open	8/02/10 - open					TAW	Competitive	Rewind/Refurbish/Upgrade Condensate Pumps (PTN)
52	2259768	Open	8/06/10 - open	8/06/10 - open					Westinghouse	OEM	Design basis support for Umbrella Mods (PTN)
53	2260113	Open	9/23/10 - open	9/23/10 - open					Westinghouse	OEM	Rod Control System Upgrades (PSL)
54	2261536	Open	9/16/10 - open	9/16/10 - open					Washington Group	Competitive	Feedwater Heater Ultrasonic Testing (PTN)

A B C D 2 of 100

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Projection Filing: Contracts Executed**

Schedule P-7A (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO: 130009-EI

EXPLANATION:

For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Projection Expended as of Prior Year End (2013)	Amount to be Expended in Current Year (2014)	Projection Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
55	2261750	Open	9/21/10 - open	9/21/10 - open					Modular Space	Competitive	Lease of 15-Wide Trailers for EPU (PTN)
56	2261747	Open	9/23/10 - open	9/23/10 - open					Westinghouse	PDS	EPU NSSS Engineering and Modification Support (PTN)
57	2262094	Open	9/28/10 - open	9/28/10 - open					Structural Integrity	Competitive	Assessment of Min Wall Thickness Effects (PTN)
58	2262367	Open	10/04/10 - open	10/04/10 - open					Techcom International	Competitive	Engineering Services for Various Distributing Mods (PTN)
59	2262515	Open	10/06/10 - open	10/06/10 - open					Fisher Controls	Replaces 130579	Modified Feedwater Regulating Valves/Actuators (PSL)
60	2263036	Open	10/19/10 - open	10/19/10 - open					Flowsolve Corp.	Replaces 130160	Replacement Condensate Pumps (PSL)
61	2263052	Closed	11/11/10 - 01/31/13	11/11/10 - 01/31/13					Invensys	Single Source	Steam Bypass Control System (PSL)
62	2263549	Open	11/10/10 - open	11/10/10 - open					Areva NP Inc	Competitive	Services of a Project Manager (PTN)
63	2263930	Open	11/11/10 - open	11/11/10 - open					Brand Energy Solutions	Replaces 131356	Supply Scaffolding Material (PTN)
64	2264842	Closed	11/30/10 - 01/17/2013	11/30/10 - 01/17/2013					Ronnies Turbine Services Inc	Single Source	On Site SL2-19 Tech Support (PSL)
65	2264377	Open	11/30/10 - open	11/30/10 - open					Techcom International	Competitive	Turbine Digital Controls Verification and Validation (PTN)
66	2264914	Open	12/07/10 - open	12/07/10 - open					Westinghouse Electric	OEM	CEDMS Power Switch Refurbishment (PSL2)
67	2285418	Open	12/16/10 - open	12/16/10 - open					Siemens Energy Inc.	OEM	Impl. Spares for EPU Turbine Gen. Work During SL2-19 (PSL)
68	2285720	Open	01/4/11 - open	01/4/11 - open					Enercon Services	Competitive	Licensing/Design Basis/Program Modification (PTN)
69	2287468	Open	02/10/11 - open	02/10/11 - open					Feedforward Inc.	Competitive	DCS Mods (PSL)
70	2290208	Open	03/25/11 - open	03/25/11 - open					Feedforward Inc.	Competitive	Leading Edge Flow Meter Addition (PTN)
71	2290465	Closed	03/31/11 - 01/15/13	03/31/11 - 01/15/13					Siemens	OEM	Design and Fabrication of Turbine Crossover piping (PTN)
72	2286521	Closed	01/18/11 - 01/23/13	01/18/11 - 01/23/13					Shaw - Stone & Webster	PDS	MSIV/MSCV Modification to Support EPU (PSL)
73	2264476	Open	05/11/11 - open	05/11/11 - open					Batsch Industries	Single Source	Turbine Generator Technical Support (PTN)
74	2291815	Open	04/28/11 - open	04/28/11 - open					BRV Construction	Competitive	Fossil Warehouse Demolition (PTN)
75	2290614	Open	05/02/11 - open	05/02/11 - open					Flowsolve Corp.	Replaces 130649	Main Feedwater Pump Casing Modification (PTN)
76	2292773	Open	05/26/11 - open	05/26/11 - open					American Air Filter Co.	OEM	Design, Engineer, Fabricate and Deliver CRDM Coils (PTN)
77	2293950	Open	06/24/11 - open	06/24/11 - open					Siemens	Single Source	Turbine Generator Pre-outage planning activities (PTN)
78	2293653	Open	06/29/11 - open	06/29/11 - open					Thermal Engineering	Competitive	Design and Fabrication of Gland Steam Condensers (PTN)
79	2294341	Open	07/11/11 - open	07/11/11 - open					Ailon	Single Source	GL2008-01 Support (PSL)
80	2294494	Open	07/13/11 - open	07/13/11 - open					Enercon Services	Competitive	Emergency Containment Cooler Auto-start (PTN)
81	2294855	Open	07/21/11 - open	07/21/11 - open					Zachry Nuclear Engineering	Single Source	Project Engineering Support for EPU (PSL)

A B C D
3 of 100

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Projection Filing: Contracts Executed**

Schedule P-7A (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO: 130009-EI

EXPLANATION:

For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work.

For the Year Ended 12/31/2014

Witness: T. O. Jones

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Projection Expended as of Prior Year End (2013)	Amount to be Expended in Current Year (2014)	Projection Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
82	2295422	Closed	8/10/11 - 01/05/13	8/10/11 - 01/05/13					Siemens Energy Inc.	OEM	Support Material for the EPU Turb-Gen Uprate (PTN)
83	2295071	Open	08/01/11 - open	08/01/11 - open					Shaw - Stone & Webster	Single Source	Unit 1 Vibration and Support Mods for FW & Condensate (PSL)
84	2296049	Open	08/25/11 - open	08/25/11 - open					Cameron Tech.	Replaces 116798	Ultrasonic Flow Meter Measuring System (PTN)
85	2294671	Open	08/19/11 - open	08/19/11 - open					NWT Corporation	Competitive	Moisture Carry Over Testing for EPU (PTN)
86	2296556	Open	09/02/11 - open	09/02/11 - open					Sulzer Pumps	OEM	Modify, overhaul and refurbishment of the B & C AFW (PTN)
87	2296519	Open	09/06/11 - open	09/06/11 - open					Techcom International	Competitive	DCS Integration Plan for 3R26 and 4R27 (PTN)
88	2296797	Closed	09/09/11 - 01/17/13	09/09/11 - 01/17/13					Coastal Bus & Charter Lines (dba Need A Bus)	Competitive	Shuttle Bus Services for EPU (PSL)
89	2298266	Open	10/12/11 - open	10/12/11 - open					Franmar Corporation	Competitive	Shuttle Bus Services for EPU (PTN)
90	2298406	Open	10/12/11 - open	10/12/11 - open					Master Lee Energy Services	Competitive	Fuel Movers for Metamic Inserts (PSL)
91	2298635	Open	10/14/11 - open	10/14/11 - open					Sargent & Lundy Inc	Single Source	Engineering Service for the Charging System Modification (PSL 2)
92	2299101	Open	10/27/11 - open	10/27/11 - open					Berkel & Company	Single Source	Mico Pile Construction (PTN)
93	2298894	Open	10/24/11 - open	10/24/11 - open					Day & Zimmermann NPS Inc	Competitive	Installation of Trailer Support Services (PTN)
94	2299350	Closed	11/01/11 - 01/17/13	11/01/11 - 01/17/13					Enercon Services Inc	Competitive	Eng. Evaluation for EPU Mid-Cycle contingency plan (PSL)
95	2299618	Open	11/04/11 - open	11/04/11 - open					Radiation Safety & Control	Competitive	Truck Monitoring/Waste Characterization for EPU (PTN)
96	2297624	Open	10/27/11 - open	10/27/11 - open					Siemens Energy Inc.	OEM	Turbine Valve Conversion to EH (PTN)
97	2299631	Closed	11/8/11 - 1/17/13	11/8/11 - 1/17/13					Tri-Tool Inc	Single Source	Unit 1 LP Turbine Extraction Line Services (PSL)
98	2297055	Open	09/16/11 - open	09/16/11 - open					Thermal Engineering	Single Source	Replacement LP #4 Feedwater Heaters for EPU (PSL 2)
99	2300139	Open	11/21/11 - open	11/21/11 - open					Siemens Energy Inc	Single Source	SL1-24 Turb-Gen. Installation (PSL 1)
100	2299624	Closed	11/16/11 - 01/17/13	11/16/11 - 01/17/13					Arnes Group LLC	Single Source	Upgrade Services for Feedwater Pumps (PSL)
101	2301867	Open	12/28/11 - open	12/28/11 - open					Enercon Services Inc	Single Source	Develop Engineering Change Packages for EPU (PTN)
102	2301038	Open	12/14/11 - open	12/14/11 - open					Grafel Inc.	Competitive	Integrated Leak Rate Testing for EPU (PTN)
103	2261800	Open	09/28/10 - open	09/28/10 - open					L 3 Communications Mapps Inc	OEM	Supply of Simulator SCD Software Translator Upgrade (PTN)
104	130340	Closed	04/02/10 - 02/21/13	04/02/10 - 02/21/13					MPR Associates	Competitive	Third Party Review of Siemens Turb-Gen. Analysis (PSL)
105	2301737	Open	12/21/11 - open	12/21/11 - open					PCI Energy Services	Single Source	Construction Management Oversight Services (PTN)
106	2301736	Open	12/21/11 - open	12/21/11 - open					Weldtech Services	Single Source	Construction Management Oversight Services (PTN)
107	2301871	Open	12/28/11 - open	12/28/11 - open					Zachry Nuclear Engineering	Single Source	Develop Engineering Change Packages for EPU (PTN)
108	2301858	Open	12/28/11 - open	12/28/11 - open					Sargent & Lundy Inc	Single Source	Develop TPCW Engineering Change Packages for EPU (PTN)

A B C of 100 D

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Projection Filing: Contracts Executed**

Schedule P-7A (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Projection Expended as of Prior Year End (2013)	Amount to be Expended in Current Year (2014)	Projection Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
109	2302164	Open	01/25/12 - open	01/25/12 - open					Ames Group LLC	Single Source	Valve Upgrade Services for EPU/PTN 3 & 4
110	2298833	Open	10/19/2011 - open	10/19/2011 - open					Chiefland Development	Competitive	SL1-24 Environmental Support and Lube Oil Tank Cleaning
111	2302548	Closed	01/17/12 - 02/19/13	01/17/12 - 02/19/13					Enercon Services Inc	Competitive	EQ Documentation Package Updates (PSL)
112	2303882	Open	02/23/12 - open	02/23/12 - open					Feedforward Inc.	Competitive	PSL Unit 2 EPU Mods for SBCS, Calorimetric and Feedwater Control
113	2295577	Open	08/15/11 - open	08/15/11 - open					Numerical Applications Inc	Replaces 115391	Radiological Consequence Analyses (PSL)
114	2303610	Open	02/15/12 - open	02/15/12 - open					Shaw - Stone & Webster	Single Source	Engineering Support for Extended Power Uprate (PTN)
115	2303735	Open	02/14/12 - open	02/14/12 - open					Siemens Energy Inc	Single Source	3R26 Outage Implementation Services for EPU at PTN
116	2302300	Open	01/11/12 - open	01/11/12 - open					Shaw - Stone & Webster	PDS	Unit 2 DEH Turbine Control System Replacement for EPU at PSL
117	2303097	Open	01/30/12 - open	01/30/12 - open					Structural Preservation Systems, Inc.	Competitive	Assessment and repair of foundation for condensate motor PIT Area (PTN)
118	2304432	Open	02/28/12 - open	02/28/12 - open					Weldtech Services	Single Source	EPU Welding Implementation and Installation Services (PTN)
119	2304197	Open	03/08/12 - open	03/08/12 - open					Homestead Miami	Real Estate Transaction	Offsite Parking Facility (PTN)
120	2304908	Open	03/08/12 - open	03/08/12 - open					Zachry Nuclear Engineering	Single Source	Engineering and EC Support for PTN
121	2301063	Open	12/13/11 - open	12/13/2011 - open					B&K Installations	Competitive	Fabricate Spargers for EPU at PTN
122	2288913	Open	03/02/11 - open	03/02/11 - open					United Rentals	PDS	Light Tower Rental for EPU at PTN
123	2302888	Open	01/23/12 - open	01/23/12 - open					All Star Toilets	Replaces 131599	Portable Toilet Services (PTN)
124	2307710	Closed	05/15/12 - 01/31/13	05/15/12 - 01/31/13					Areva NP Inc	Replaces 105720	Unit 1 mid-Cycle Analysis (PSL)
125	2308808	Open	06/12/12 - open	06/12/12 - open					Calvert Company Inc	Replaces 124436	Replacement of Isolated Phase Bus Duct (PTN)
126	2307375	Closed	05/03/12 - 01/30/13	05/03/12 - 01/30/13					Nucorp	Single Source	Nuclear Grade Air Traps (PSL)
127	2308917	Open	06/13/12 - open	06/13/12 - open					Sargent & Lundy Inc	Single Source	EPU Procedure Recovery Plan Support (PSL)
128	2263063	Open	10/19/10 - open	10/19/10 - open					United Rentals	Competitive*	Light Tower Rentals for EPU Surplus Parking (PTN)
129	2307342	Open	05/02/12 - open	05/02/12 - open					American Air Filter	OEM	Onsite Technical Support for the Normal Containment Cooler (PTN)
130	2309312	Open	06/25/12 - open	06/25/12 - open					Ames Group LLC	Single Source	Valve Actuator Support Specialty Services (PSL)
131	2311019	Open	08/16/12 - open	08/16/12 - open					Andersen Chavet & Andersen Inc.	Competitive	Develop a Preventative Maintenance Plan for EPU at PSL
132	2306547	Closed	04/11/12 - 01/31/13	04/11/12 - 01/31/13					Conger & Elsa	Single Source	PCV-8802 Contract Root Cause Evaluation (PSL)
133	2308236	Open	05/22/12 - open	05/22/12 - open					Enercon Services, Inc	Single Source	Task 1: IST and ILRT/LLRT Program Support (PSL)
134	2308442	Open	07/09/12 - open	07/09/12 - open					J. Givoo Consultants	Competitive	Start-Up and Testing Support (PSL)
135	2310597	Open	07/26/12 - open	07/26/12 - open					K Machine	Single Source	3R26 and 4R27 Outage Machining Support for EPU

A B C D
5 of 100

**Project Name: Extended Power Upgrade
Construction Costs and Carrying Costs on Construction Cost Balance
Projection Filing: Contracts Executed**

Schedule P-7A (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: Florida Power & Light Company

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Projection Expended as of Prior Year End (2013)	Amount to be Expended in Current Year (2014)	Projection Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
136	2264321	Open	11/15/2010 - open	11/15/2010 - open					Modular Space	PDS	On Site Modular Office Space Rental (PSL)
137	2309693	Open	07/06/12 - open	07/06/12 - open					PCI Energy Services	Competitive	Implementation and Installation of Unit 4 Spent Fuel Pool Heat Exchangers
138	2311510	Open	08/16/12 - open	08/16/12 - open					Shaw - Stone & Webster	Single Source	Engineering Support for EPU (PTN unit 4)
139	2310927	Open	08/07/12 - open	08/07/12 - open					Siemens Energy Inc	Single Source	PSL 2-20 Turbine Generator Services
140	2311900	Open	09/05/12 - open	09/05/12 - open					Siemens Energy Inc	Single Source	PTN 4-27 Turbine Generator Services
141	2312716	Closed	09/18/12 - 02/14/13	09/18/12 - 02/14/13					Tricen Technologies	Single Source	Unit 4 Eddy Current Testing on Condenser Tube Bundle
142	2303837	Open	04/24/12 - open	04/24/12 - open					Thermal Engineering	OEM	Installation and Mod Engineering Support for EPU at PTN
143	2310214	Open	07/17/12 - open	07/17/12 - open					Whiting Services Inc	OEM	3R26 and 4R27 Outage Crane Support
144	2310390	Open	07/25/12 - open	07/25/12 - open					Williams Plant Services LLC	Single Source	Unit 2 Alpha Main Transformer Upgrade Support
145	2311037	Open	08/10/12 - open	08/10/12 - open					Williams Specialty Services	Replaces Blanket 4500412063	Coating Services in Support of PTN EPU Project
146	2293283	Open	06/02/11 - open	06/02/11 - open					Nucon	Competitive	CREVS Testing at PSL
147	2313411	Open	10/08/12 - open	10/08/12 - open					Sims Crane & Equipment Co.	Competitive	Rental of Misc Equipments (PTN)
148	2314332	Open	10/30/12 - open	10/30/12 - open					Team Industrial Services Inc	Single Source	Radiography Testing Services for EPU at PTN
149	2314744	Open	11/09/12 - open	11/09/12 - open					Aggreko	Competitive	Support Performance of ILRT (PTN)
150	2315146	Open	11/21/12 - open	11/21/12 - open					Brand Energy Solutions, LLC	Replaces 2283930	Scaffold Rental to Support EPU (PTN)
151	2315635	Open	12/14/12 - open	12/14/12 - open					Control Components	Single Source	Turbine Bypass and Steam Dump Control Systems Valves (PTN)
152	2314797	Open	11/12/12 - open	11/12/12 - open					Curtiss Wright Flow Control	Single Source	NDE Oversight and Preservice Examinations (PTN)
153	2315305	Open	12/03/12 - open	12/03/12 - open					Land & Sea	Competitive	Delivery Fuel and Refuel Misc Equip at Site (PTN)
154	2315379	Closed	11/30/12 - 01/30/13	11/30/12 - 01/30/13					Magnetrol International	Competitive	Transmitters (PTN)
155	2315153	Open	11/21/12 - open	11/21/12 - open					Westinghouse Electric Co	OEM	Unit 3 Secondary System Stability (PTN)
156	2310959	Open	10/10/12 - open	10/10/12 - open					Shaw - Stone & Webster	Single Source	Onsite Engineering Manager (PSL)
157	2316596	Open	01/29/13 - open	01/29/13 - open					GE Mobile Water Inc.	Competitive	Condensate Polishers (PTN)
158	2315472	Open	12/04/12 - open	12/04/12 - open					Sargent & Lundy Inc	Single Source**	On Site Support for Dampening Flow Oscillations (PTN)
159	2317235	Open	02/19/13 - open	02/19/13 - open					The Merrick Group Inc.	Competitive	Unit 3 Condenser Tube Bundles Hydrolasing (PTN)
160	2301976	Open	02/01/12 - open	02/01/12 - open					Westinghouse Electric Co	OEM	Spent Fuel handling Modification for EPU (PSL)

A B C D

**Project Name: Extended Power Uprate
Construction Costs and Carrying Costs on Construction Cost Balance
Projection Filing: Contracts Executed**

Schedule P-7A (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

EXPLANATION:

For all executed contracts exceeding \$250,000, (including change orders), provide the contract number or identifier, status, original and current contract terms, original amount, amount expended as of the end of the prior year, amount expended in the year, estimated final contract amount, name of contractor and affiliations if any, method of selection including identification of justification documents, and a description of work.

COMPANY: Florida Power & Light Company

For the Year Ended 12/31/2014

Witness: T. O. Jones


DOCKET NO: 130009-EI

(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	
Line No.	Contract No.	Status of Contract	Original Term of Contract	Current Term of Contract	Original Amount	Projection Expended as of Prior Year End (2013)	Amount to be Expended in Current Year (2014)	Projection Final Contract Amount	Name of Contractor (and Affiliation if any)	Method of Selection and Document ID	Work Description
161	2262359 Rls 7	Open	05/10/12 - open	05/10/12 - open					Atlas Copco USA Holdings	Competitive	Rental of Air Compressors (PTN)
162	2260135 Rls 14	Open	10/26/10 - open	10/26/10 - open					Bartlett Nuclear Inc	Competitive	Radiation Protection Services PSL
163	2262301 Rls 13	Open	01/30/12 - open	01/30/12 - open					Bartlett Nuclear Inc	BPO 2262301 Replaces BPO 113293 (Competitive)	Radiation Protection Services PTN
164	2262301 Rls 17	Open	06/21/12 - open	06/21/12 - open					Bartlett Nuclear Inc	BPO 2262301 Replaces BPO 113293 (Competitive)	Radiation Protection Services PTN
165	2287944 Rls 4	Open	03/07/12 - open	03/07/12 - open					Energy Solutions, LLC	BPO 2287944 Replaces BPO 99395 (Single Source)	EPU Radioactive Waste Disposal Services (PTN)
166	2260140 Rls 53	Open	11/26/11 - open	11/26/11 - open					G4S Regulated Security Solutions Inc.	BPO 2260140 Replaces BPO 118419 (Single Source)	Security Services PSL 1-24 and PSL 2-20 (PSL)
167	2260140 Rls 86	Open	12/17/12 - open	12/17/12 - open					G4S Regulated Security Solutions Inc.	BPO 2260140 Replaces BPO 118419 (Single Source)	Security Services for Unit 4 EPU (PTN)
168	2286053 Rls 8	Open	05/10/12 - open	05/10/12 - open					GE Mobile Water Inc.	Competitive	Condenser Clean Up and Water Filtration Services (PTN)
169	2293072 Rls 21	Open	11/01/12 - open	11/01/12 - open					Industrial Testing Laboratory	Competitive	EPU Quality Control Support Services for 4R27 (PTN)
170	2293489 Rls 7	Open	09/07/11 - open	09/07/11 - open					Stone & Webster Construction Inc	Competitive	Supplementary Maintenance and Related Services (PTN)
171	2293489 Rls 9	Open	10/13/11 - open	10/13/11 - open					Stone & Webster Construction Inc	Competitive	Supplementary Maintenance and Related Services (PSL)

A B C D

Legend:
PDS = Predetermined Source
OEM = Original Equipment Manufacturer
PSL = St. Lucie
PTN = Turkey Point

* The original amount of the contract was less than \$25,000; however, a subsequent revision required competitive bidding.
** The original amount of the contract was less than \$25,000; however, a subsequent revision required a single source justification (SSJ).

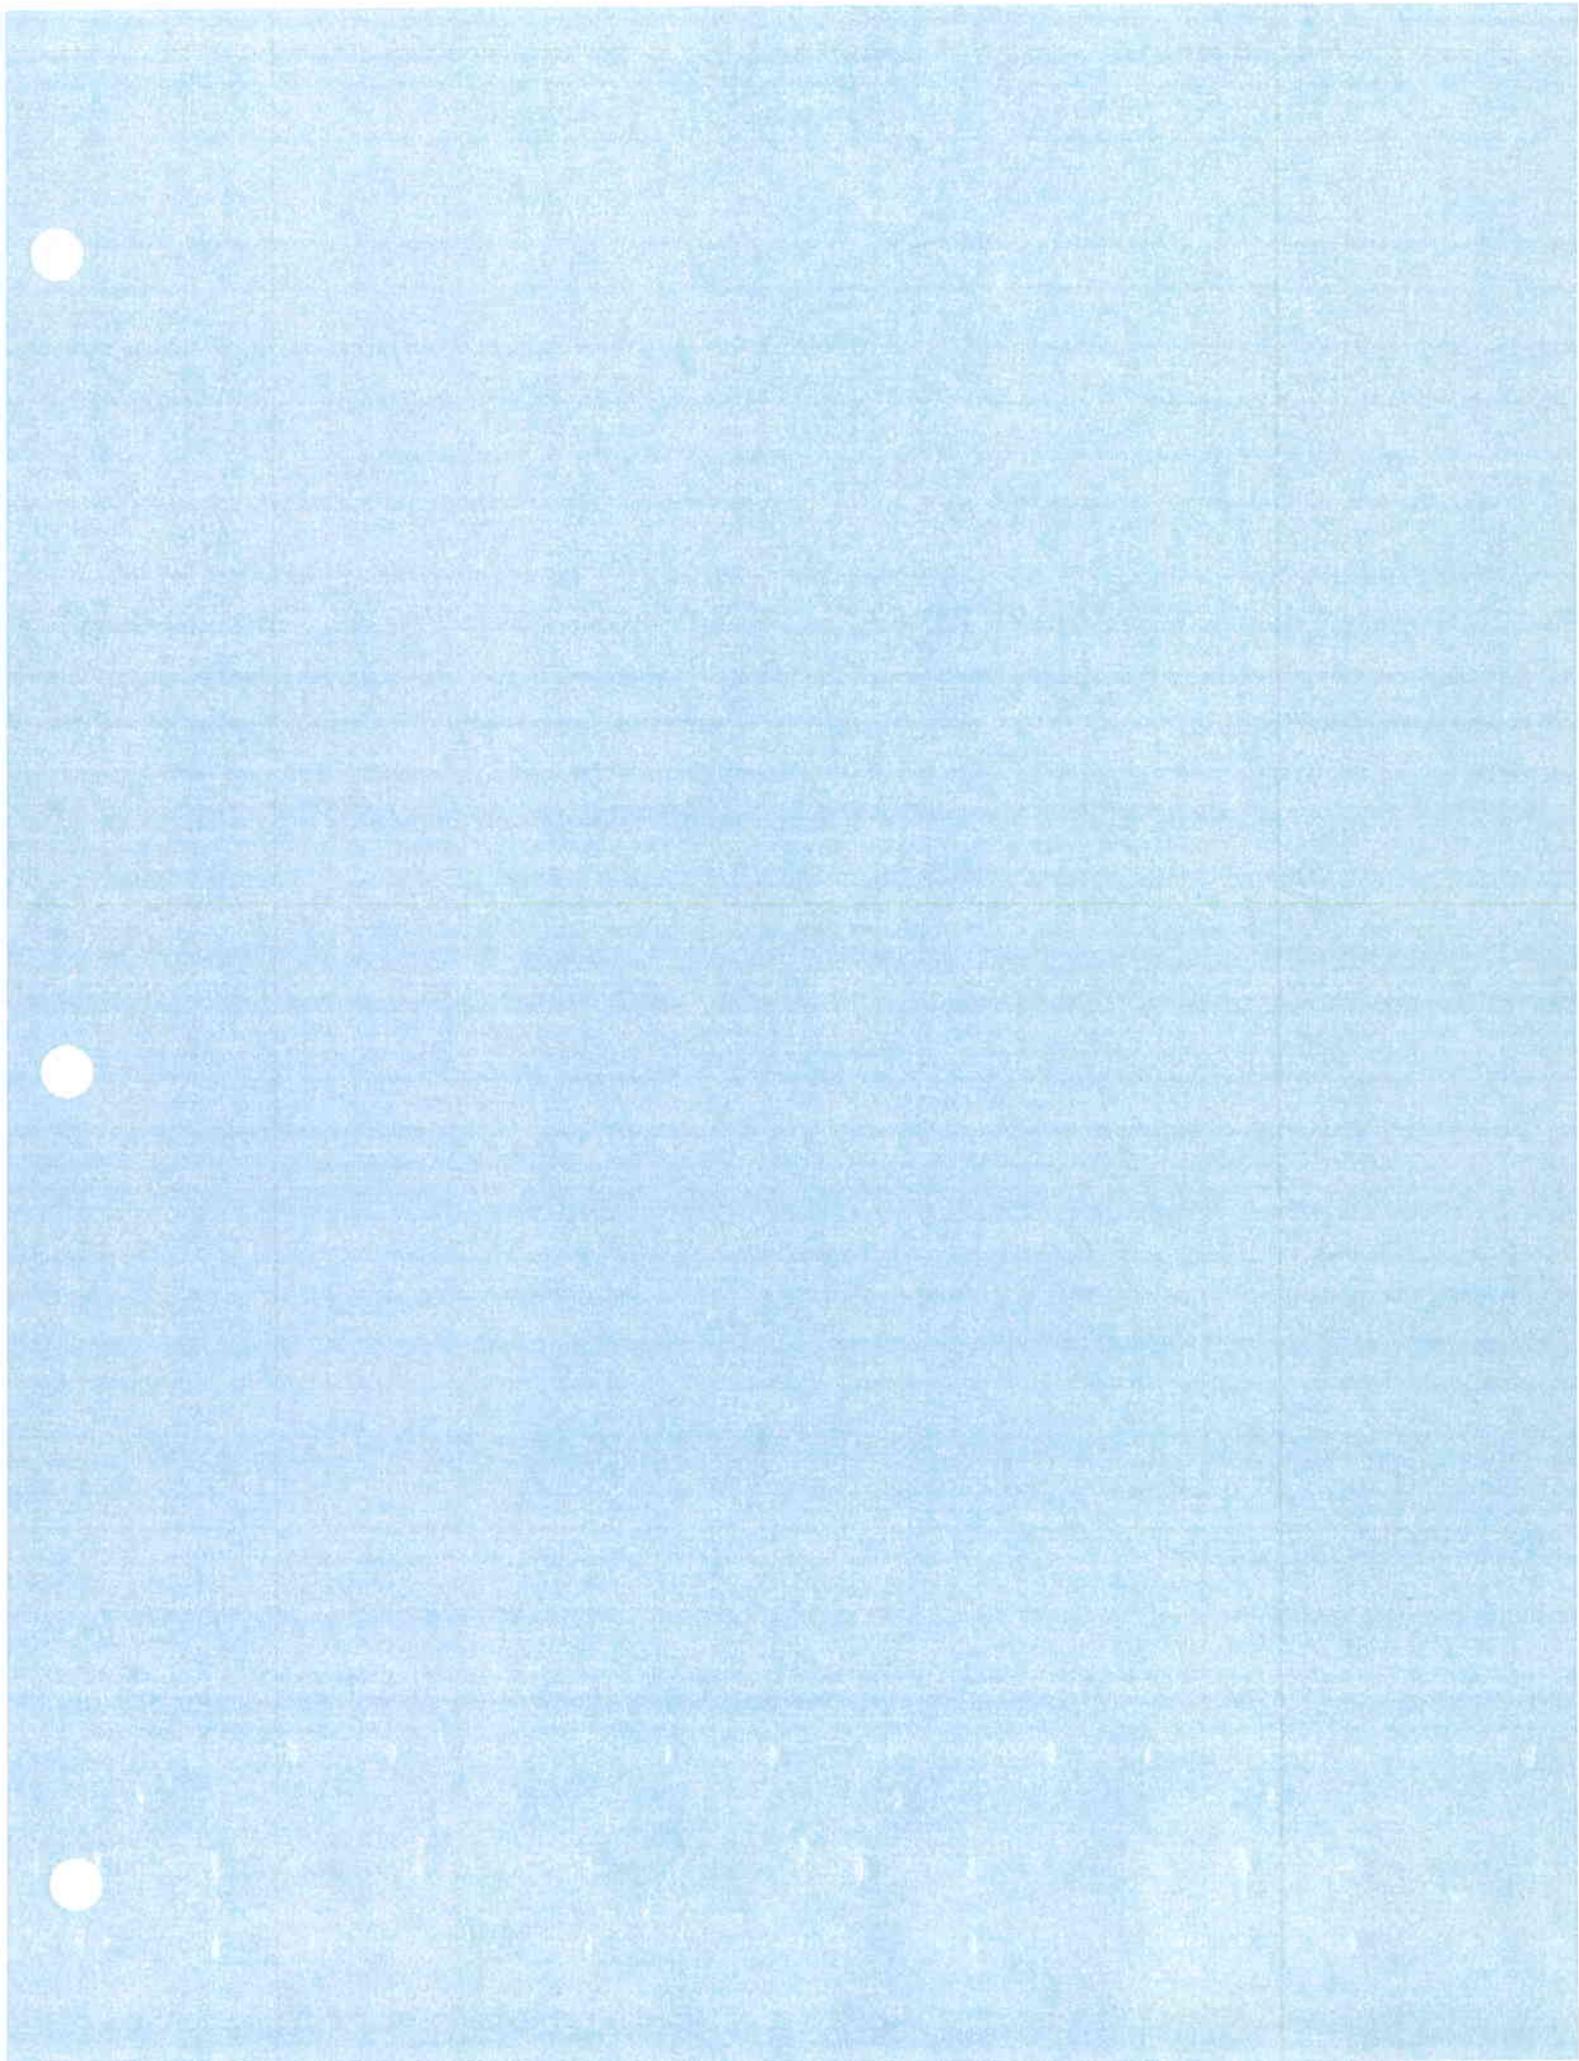

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PTN PO 121869

Major Task or Tasks Associated With:

Supply Eight (8) Normal Containment Coolers and provide Testing Services

Vendor Identity:

AAF MCQUAY

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive selection with a technical and commercial evaluation process resulting in an award to AAF McQuay.

Dollar Value:

Total Contract Value through Revision 4 is [REDACTED]

Contract Status:

Active

Term Begin:

April 29, 2009

Term End:

Open

Nature and Scope of Work:

Supply Eight (8) Normal Containment Coolers and provide Testing Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PSL PO 120769

Major Task or Tasks Associated With:
Replacement IsoPhase Bus Duct Coolers

Vendor Identity:
Calvert Company Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
4

Number of Bids Received:
1

Brief Description of Selection Process:
Competitive selection with a technical and commercial evaluation process resulting in an award to Calvert Company Inc.

Dollar Value:
Total Dollar Value through Revision 6 is ██████████

Contract Status:
Active

Term Begin:
March 26, 2009

Term End:
Open

Nature and Scope of Work:
Replacement IsoPhase Bus Duct Coolers, Technical Installation Support and Field Testing.

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO 124436

Major Task or Tasks Associated With:
Replacement Isolated Phase BusDuct

Vendor Identity:
Calvert Company Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
3

Number of Bids Received:
3

Brief Description of Selection Process:
Competitive selection with a technical and commercial evaluation process resulting in an award to Calvert Company Inc.

Dollar Value:
Total Dollar Value through Revision 2 is [REDACTED]

Contract Status:
Active

Term Begin:
July 17, 2009

Term End:
Open

Nature and Scope of Work:
Replacement Isolated Phase BusDuct, Demolition and Installation Services, Evaluation, Testing and Engineering

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PSL PO 121985

Major Task or Tasks Associated With:
Replacement Main Feedwater Pumps

Vendor Identity:
Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
5

Number of Bids Received:
2

Brief Description of Selection Process:
Competitive selection with a technical and commercial evaluation process resulting in an award to Flowsolve Corp.

Dollar Value:
Total Dollar Value through Revision 6 is [REDACTED]

Contract Status:
Closed

Term Begin:
April 24, 2009

Term End:
February 12, 2013

Nature and Scope of Work:
Replacement Main Feedwater Pumps, spare parts and technical direction of installation.

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO 123137

Major Task or Tasks Associated With:
Main Feedwater Isolation Valves

Vendor Identity:
Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
3

Number of Bids Received:
3

Brief Description of Selection Process:
Competitive selection with a technical and commercial evaluation process resulting in an award to Flowsolve Corp.

Dollar Value:
[REDACTED]

Contract Status:
Active

Term Begin:
May 28, 2009

Term End:
Open

Nature and Scope of Work:
Main Feedwater Isolation Valves, Technical Field Services, Testing, Engineering and Documentation

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PSL PO 125454

Major Task or Tasks Associated With:
Replacement Heater Drain Pumps

Vendor Identity:
Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
3

Number of Bids Received:
3

Brief Description of Selection Process:
Competitive selection with a technical and commercial evaluation process resulting in an award to Flowsolve Corp.

Dollar Value:
Total Dollar Value through Revision 3 is [REDACTED]

Contract Status:
Active

Term Begin:
August 28, 2009

Term End:
Open

Nature and Scope of Work:
Replacement Heater Drain Pumps, Spare Heater, Technical Direction

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PTN PO 119078

Major Task or Tasks Associated With:

NSSS Engineering Evaluation and LAR Analysis for PTN Units 3 & 4

Vendor Identity:

Westinghouse Electric Co.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Dollar Value through Revision 6 is [REDACTED]

Contract Status:

Active

Term Begin:

Letter of Authorization issued 12/9/08; PO issued 1/26/09

Term End:

Open

Nature and Scope of Work:

NSSS Engineering Evaluation and LAR Analysis for PTN Units 3 & 4

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jorles

Contract No.:

PSL PO 115297

Major Task or Tasks Associated With:

Design Review for LAR (Steam Generator and Reactor Head)

Vendor Identity:

AREVA

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Dollar Value through Revision 8 [REDACTED]

Contract Status:

Active

Term Begin:

August 27, 2008

Term End:

Open

Nature and Scope of Work:

Design Review for LAR (Steam Generator and Reactor Head)

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO 115338

Major Task or Tasks Associated With:
Engineering Analysis

Vendor Identity:
AREVA

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Dollar Value through Revision 11 [REDACTED]

Contract Status:
Active

Term Begin:
August 27, 2008

Term End:
Open

Nature and Scope of Work:
Design review for the Reactor Coolant system, Control Rod Mechanism, EMA, CFD and BMI

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO 117809

Major Task or Tasks Associated With:
Provide Engineering, Procurement and Construction Services for PTN

Vendor Identity:
Bechtel

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
6

Number of Bids Received:
5

Brief Description of Selection Process:
Bidders were evaluated against predetermined technical and commercial criteria, awarding to the lowest evaluated bidder.

Dollar Value:
PO value through Rev 10/Rel 0 [REDACTED]

Contract Status:
Active

Term Begin:
December 2, 2008

Term End:
Open

Nature and Scope of Work:
Bechtel's scope includes project management, design engineering, procurement and material handling services, work order planning, construction/implementation, project controls, quality assurance, quality control, radiation protection (alara), safety, security interface, and other services as designated in the Contract documents.

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PO # 116088

Major Task or Tasks Associated With:

Turbine/Generator Uprate

Vendor Identity:

Siemens Power

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single source

Dollar Value:

Total Blanket Purchase Order Max Value through Revision
7/Release 0 [REDACTED]

Contract Status:

Active

Term Begin:

September 29, 2008

Term End:

Open

Nature and Scope of Work:

Engineering, Parts and Installation for PSL Turbine/Generator Uprate

**St. Lucie and Turkey Point Upgrade Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PSL PO 117820

Major Task or Tasks Associated With:

Provide Engineering, Procurement and Construction Services for PSL

Vendor Identity:

Bechtel

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

6

Number of Bids Received:

5

Brief Description of Selection Process:

Bidders were evaluated against predetermined technical and commercial criteria, awarding to the lowest evaluated bidder.

Dollar Value:

PO value through Rev 11/Rel 0 is [REDACTED]

Contract Status:

Active

Term Begin:

December 2, 2008

Term End:

Open

Nature and Scope of Work:

Bechtel's scope includes project management, design engineering, procurement and material handling services, work order planning, construction/implementation, project controls, quality assurance, quality control, radiation protection (alara), safety, security interface, and other services as designated in the Contract documents.

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PO # 116090

Major Task or Tasks Associated With:

PTN Turbine Generator Uprate

Vendor Identity:

Siemens Power

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Blanket Purchase Order Max Value through Rev. 4/Rel 0 is [REDACTED]

Contract Status:

Active

Term Begin:

September 29, 2008

Term End:

Open

Nature and Scope of Work:

PTN Engineering, Parts and Installation for Turbine/Generator Uprate

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PO # 118328

Major Task or Tasks Associated With:

PTN Condenser Tube Bundles for Unit 3 & 4

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through Revision 7 is [REDACTED]

Contract Status:

Active

Term Begin:

December 19, 2008

Term End:

Open

Nature and Scope of Work:

Supply PTN Condenser Tube Bundles

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PO # 118206

Major Task or Tasks Associated With:

PTN MSR's for Units 3 & 4

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

2

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through Revision 2 [REDACTED]

Contract Status:

Active

Term Begin:

December 17, 2008

Term End:

Open

Nature and Scope of Work:

Supply PTN Moisture Separator Reheaters

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PO # 118205

Major Task or Tasks Associated With:
PSL MSR's for Units 1 & 2

Vendor Identity:
Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
3

Number of Bids Received:
2

Brief Description of Selection Process:
The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:
Total Dollar Value through Revision 6 is [REDACTED]

Contract Status:
Active

Term Begin:
December 17, 2008

Term End:
Open

Nature and Scope of Work:
Supply PSL Moisture Separator Reheaters

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PO # 118241

Major Task or Tasks Associated With:

PTN Feedwater Heaters for Units 3 & 4

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

3

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Contract Value through Revision 3 [REDACTED]

Contract Status:

Active

Term Begin:

December 19, 2008

Term End:

Open

Nature and Scope of Work:

Supply PTN Feedwater Heaters

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PO # 112221

Major Task or Tasks Associated With:

PSL Licensing Engineering and BOP Spec Development

Vendor Identity:

Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Blanket Purchase Order Max Value through Revision 20 to Release 0 is [REDACTED]

Contract Status:

Active

Term Begin:

April 22, 2008

Term End:

Open

Nature and Scope of Work:

PSL Licensing Engineering and BOP Spec Development

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PO # 112177

Major Task or Tasks Associated With:

PTN Licensing Engineering and BOP Spec Development

Vendor Identity:

Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Blanket Purchase Order Max Value through Revision 8 to Release 0 is [REDACTED]

Contract Status:

Active

Term Begin:

April 22, 2008

Term End:

Open

Nature and Scope of Work:

PTN Licensing Engineering and BOP Spec Development

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PO 117272

Major Task or Tasks Associated With:

Gantry crane repair/modification

Vendor Identity:

American Crane

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

OEM

Dollar Value:

Total Dollar Value through Rev 6 is [REDACTED]

Contract Status:

Active

Term Begin:

November 13, 2008

Term End:

Open

Nature and Scope of Work:

Complete modification of Unit 1 crane and update of electrical components for Unit 2 crane

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PO # 118224

Major Task or Tasks Associated With:
PSL Feedwater Heaters for Units 1 & 2

Vendor Identity:
Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
4

Number of Bids Received:
3

Brief Description of Selection Process:
Competitive

Dollar Value:
Total Dollar Value thru Revision 8 [REDACTED]

Contract Status:
Active

Term Begin:
December 17, 2008

Term End:
Open

Nature and Scope of Work:
Supply PSL Feedwater Heaters

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PO # 115465

Major Task or Tasks Associated With:

Eng. Services for NSSS, BOP & Licensing Activities

Vendor Identity:

Zachry Nuclear Engineering

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Dollar Value through revision 4 is [REDACTED]

Contract Status:

Active

Term Begin:

September 3, 2008

Term End:

Open

Nature and Scope of Work:

PTN Eng. Services for NSSS, BOP and Licensing Activities.

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PO # 118278

Major Task or Tasks Associated With:

PSL Heat Exchangers for Units 1 & 2

Vendor Identity:

Thermal Engineering International (USA) Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

3

Brief Description of Selection Process:

The evaluation process included technical and commercial clarifications with award made to TEI as the total evaluated low bidder.

Dollar Value:

Total Dollar Value through Revision 5 is [REDACTED]

Contract Status:

Active

Term Begin:

December 19, 2008

Term End:

Open

Nature and Scope of Work:

Supply PSL Heat Exchangers

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PO # 105720

Major Task or Tasks Associated With:

PSL Fuels Analysis

Vendor Identity:

Areva

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Order value through Revision 17 is [REDACTED]

Contract Status:

Active

Term Begin:

September 12, 2007

Term End:

Open

Nature and Scope of Work:

Fuels Performance Study and Analysis

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-E1

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PO 116107

Major Task or Tasks Associated With:

Ultrasonic Flow Measuring System

Vendor Identity:

Cameron Technologies

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Purchase Order Value through Revision 1 is [REDACTED]

Contract Status:

Active

Term Begin:

September 29, 2008

Term End:

Open

Nature and Scope of Work:

Ultrasonic Flow Measuring System for PTN

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PO # 126453

Major Task or Tasks Associated With:
Turbine Plant Cooling Water Heat Exchangers

Vendor Identity:
Joseph Oat Corporation

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
3

Number of Bids Received:
3

Brief Description of Selection Process:
Competitive Selection, Commercial and Technical Evaluation

Dollar Value:
Total Contract Value through revision 1 is [REDACTED]

Contract Status:
Active

Term Begin:
November 5, 2009

Term End:
Open

Nature and Scope of Work:
Supply Turbine Plant Cooling Water Heat Exchangers

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PTN PO #127777

Major Task or Tasks Associated With:

Estimating Services

Vendor Identity:

High Bridge

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Contract Value through revision 2 is [REDACTED]

Contract Status:

Active

Term Begin:

December 8, 2009

Term End:

Open

Nature and Scope of Work:

Estimating Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PTN PO # 127881

Major Task or Tasks Associated With:

Procedure Writers

Vendor Identity:

Absolute Consulting

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

██████████

Contract Status:

Active

Term Begin:

December 22, 2009

Term End:

Open

Nature and Scope of Work:

Procedure Writers

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PSL PO #118563

Major Task or Tasks Associated With:
Fuel Storage Criticality and Related Analysis (PSL 1)

Vendor Identity:
Holtec

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
3

Number of Bids Received:
2

Brief Description of Selection Process:
Competitive

Dollar Value:
Total Purchase Order Value through Revision 7 is [REDACTED]

Contract Status:
Closed

Term Begin:
January 14, 2009

Term End:
January 29, 2013

Nature and Scope of Work:
Fuel Storage Criticality and Related Analysis (PSL 1)

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO # 130612

Major Task or Tasks Associated With:
Condensate Pumps

Vendor Identity:
Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
3

Number of Bids Received:
3

Brief Description of Selection Process:
Competitive

Dollar Value:
Total Contract Value through Revision 2 is [REDACTED]

Contract Status:
Active

Term Begin:
April 22, 2010

Term End:
Open

Nature and Scope of Work:
Condensate Pumps

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PTN PO #130649

Major Task or Tasks Associated With:

Main Feedwater Pumps

Vendor Identity:

Flowsolve Corp

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

1

Brief Description of Selection Process:

Competitive

Dollar Value:

██████████

Contract Status:

Active

Term Begin:

April 22, 2010

Term End:

Open

Nature and Scope of Work:

Main Feedwater Pumps

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO # 126227

Major Task or Tasks Associated With:
Control System FWH, Moisture Separator

Vendor Identity:
Invensys

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
OEM

Dollar Value:
Total Dollar Value through revision 12 is [REDACTED]

Contract Status:
Active

Term Begin:
October 13, 2009

Term End:
Open

Nature and Scope of Work:
Control System FWH, Moisture Separator

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PTN PO # 129689

Major Task or Tasks Associated With:

Turbine Digital Upgrade

Vendor Identity:

Invensys

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Dollar Value through Revision 4 is [REDACTED]

Contract Status:

Active

Term Begin:

March 17, 2010

Term End:

Open

Nature and Scope of Work:

Turbine Digital Upgrade

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO # 130272

Major Task or Tasks Associated With:
Electro-Hydraulic Fluid Systems

Vendor Identity:
Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
3

Number of Bids Received:
3

Brief Description of Selection Process:
Competitive

Dollar Value:
Total Dollar Value through Rev 5 is [REDACTED]

Contract Status:
Active

Term Begin:
April 8, 2010

Term End:
Open

Nature and Scope of Work:
Electro-Hydraulic Fluid Systems

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PSL PO # 131533

Major Task or Tasks Associated With:
Non-Fuels NSSS Interim LAR (PSL 1 & 2)

Vendor Identity:
Areva

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Predetermined Source

Dollar Value:
Total Contract Value through Revision 4 is [REDACTED]

Contract Status:
Closed

Term Begin:
June 10, 2010

Term End:
January 29, 2013

Nature and Scope of Work:
Non-Fuels NSSS Interim LAR (PSL 1 & 2)

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PSL PO # 131907

Major Task or Tasks Associated With:
Fuels Related Interim LAR/MOD for EPU at PSL

Vendor Identity:
Areva

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Predetermined Source

Dollar Value:
Total Contract Value through Revision 5 is [REDACTED]

Contract Status:
Closed

Term Begin:
June 11, 2010

Term End:
January 29, 2013

Nature and Scope of Work:
Fuels Related Interim LAR/MOD for EPU at PSL

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PSL PO # 131585

Major Task or Tasks Associated With:
Interim LAR/MOD for EPU at PSL

Vendor Identity:
Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Predetermined Source

Dollar Value:
Total Contract Value through Revision 8 is [REDACTED]

Contract Status:
Closed

Term Begin:
June 15, 2010

Term End:
February 20, 2013

Nature and Scope of Work:
Interim LAR/MOD for EPU at PSL

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PSL PO #131742

Major Task or Tasks Associated With:
LAR/Request for Additional Information

Vendor Identity:
Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Predetermined Source

Dollar Value:
Total Contract value through Revision 4 is [REDACTED]

Contract Status:
Active

Term Begin:
June 16, 2010

Term End:
Open

Nature and Scope of Work:
LAR/Request for Additional Information for Non-Fuels related scope

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PSL PO #131940

Major Task or Tasks Associated With:
Main Steam Turbine Control Replacement

Vendor Identity:
Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
4

Number of Bids Received:
4

Brief Description of Selection Process:
Competitive

Dollar Value:
Total Blanket PO Max Value through Rev 2 to Release 0 [REDACTED]

Contract Status:
Active

Term Begin:
June 30, 2010

Term End:
Open

Nature and Scope of Work:
Main Steam Turbine Control Replacement

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO #2259675

Major Task or Tasks Associated With:
Furnish New Spent Fuel Pool Heat Exchangers

Vendor Identity:
Joseph Out Corporation

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
2

Number of Bids Received:
2

Brief Description of Selection Process:
Competitive

Dollar Value:
[REDACTED]

Contract Status:
Active

Term Begin:
July 23, 2010

Term End:
Open

Nature and Scope of Work:
Furnish New Spent Fuel Pool Heat Exchangers

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

COMPANY: FLORIDA POWER & LIGHT COMPANY

For the Year Ended 12/31/2014

DOCKET NO: 130009-EI

Witness: T. O. Jones

Contract No.:

PTN PO # 2259669

Major Task or Tasks Associated With:

Rewind/Refurbish Upgrade Condensate Pumps

Vendor Identity:

Tampa Armature Works

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

4

Number of Bids Received:

2

Brief Description of Selection Process:

Competitive

Dollar Value:

██████████

Contract Status:

Active

Term Begin:

August 2, 2010

Term End:

Open

Nature and Scope of Work:

Rewind/Refurbish Upgrade Condensate Pumps

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PSL PO #2260113

Major Task or Tasks Associated With:
PSL Rod Control System Upgrades

Vendor Identity:
Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
OEM

Dollar Value:
Total Contract Value through Amendment 3 [REDACTED]

Contract Status:
Active

Term Begin:
September 23, 2010

Term End:
Open

Nature and Scope of Work:
PSL Rod Control System Upgrades

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO #2261747

Major Task or Tasks Associated With:
EPU NSSS Engineering and Modification Support

Vendor Identity:
Westinghouse

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Predetermined Source

Dollar Value:
Total Contract Value through Amendment 4 [REDACTED]

Contract Status:
Active

Term Begin:
September 23, 2010

Term End:
Open

Nature and Scope of Work:
EPU NSSS Engineering and Modification Support

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PSL PO #22G3036

Major Task or Tasks Associated With:
Condensate Pumps (PSL)

Vendor Identity:
Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
N/A

Number of Bids Received:
N/A

Brief Description of Selection Process:
Replaces PO 130100, which was competitively bid.

Dollar Value:
Total Contract Value through Amendment 2 [REDACTED]

Contract Status:
Active

Term Begin:
October 19, 2010

Term End:
Open

Nature and Scope of Work:
Replacement Condensate Pumps (PSL)

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO #2263549

Major Task or Tasks Associated With:
Project Management

Vendor Identity:
Areva NP Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
2

Number of Bids Received:
2

Brief Description of Selection Process:
Competitive

Dollar Value:
Total Dollar Value through Amendment #1 [REDACTED]

Contract Status:
Active

Term Begin:
November 10, 2010

Term End:
Open

Nature and Scope of Work:
Services of a Project Manager

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO #2263930

Major Task or Tasks Associated With:
Scaffolding Material

Vendor Identity:
Brand Energy Solutions

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
N/A

Number of Bids Received:
N/A

Brief Description of Selection Process:
Replaces 131356, which was competitively bid.

Dollar Value:
Total Dollar Value through Amendment #2 [REDACTED]

Contract Status:
Active

Term Begin:
November 11, 2010

Term End:
Open

Nature and Scope of Work:
Supply of Scaffolding

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PSL PO #2264914

Major Task or Tasks Associated With:
CEDMS Power Switch Refurbishment (PSL 2)

Vendor Identity:
Westinhouse Electric

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
OEM

Dollar Value:
Total Dollar Value through Amendment #1 is [REDACTED]

Contract Status:
Active

Term Begin:
December 7, 2010

Term End:
Open

Nature and Scope of Work:
CEDMS Power Switch Refurbishment (PSL 2)

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PSL PO #2285418

Major Task or Tasks Associated With:
Implementation Spares for Turbine Generator Work

Vendor Identity:
Siemens Energy Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
OEM

Dollar Value:
Total Contract Value through Amendment 3 [REDACTED]

Contract Status:
Active

Term Begin:
December 16, 2010

Term End:
Open

Nature and Scope of Work:
Implementation Spares for Turbine Generator Work

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
FPL PO #2285720

Major Task or Tasks Associated With:
Licensing/Design Basis/Program Modification

Vendor Identity:
Enercon Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
2

Number of Bids Received:
2

Brief Description of Selection Process:
Competitive

Dollar Value:
[REDACTED]

Contract Status:
Active

Term Begin:
January 4, 2011

Term End:
Open

Nature and Scope of Work:
Licensing/Design Basis/Program Modification

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO# 2290465

Major Task or Tasks Associated With:
Design, Engineering and Fabrication of Turbine Crossover piping

Vendor Identify:
Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
OEM

Dollar Value:
██████████

Contract Status:
Closed

Term Begin:
March 31, 2011

Term End:
January 15, 2013

Nature and Scope of Work:
Design, Engineering and Fabrication of Turbine Crossover piping

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PSL PO# 2286521

Major Task or Tasks Associated With:
MSIV/MSCV Modifications

Vendor Identity:
Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
PDS

Dollar Value:
Total Dollar Value through Amendment #4 [REDACTED]

Contract Status:
Closed

Term Begin:
January 18, 2011

Term End:
January 23, 2013

Nature and Scope of Work:
MSIV/MSCV Modifications

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO# 2290614

Major Task or Tasks Associated With:
Main Feedwater Pump Casing Modifications

Vendor Identity:
Flowsolve Corp.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
N/A

Number of Bids Received:
N/A

Brief Description of Selection Process:
Replaces PO 130649, which was competitively bid.

Dollar Value:
Total Contract Value through Amend 2 [REDACTED]

Contract Status:
Active

Term Begin:
May 2, 2011

Term End:
Open

Nature and Scope of Work:
Main Feedwater Pump Casing Modifications

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO# 2293950

Major Task or Tasks Associated With:
Turbine Generator Pre-Outage Planning PTN 3 & 4

Vendor Identity:
Siemens

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Contract value through Amendment 1 [REDACTED]

Contract Status:
Active

Term Begin:
June 24, 2011

Term End:
Open

Nature and Scope of Work:
Turbine Generator Pre-Outage Planning PTN 3 & 4
(Turbine Generator Installation)

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PSL PO# 2294855

Major Task or Tasks Associated With:
Project Engineering

Vendor Identity:
Zachry Nuclear Engineering

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Dollar Value through Amendment #4 [REDACTED]

Contract Status:
Active

Term Begin:
July 21, 2011

Term End:
Open

Nature and Scope of Work:
Project Engineering Support

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PSL PO# 2295071

Major Task or Tasks Associated With:
Unit 1 Vibration and Support Mods for FW & Condensate

Vendor Identity:
Shaw Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Dollar Value through Amendment #3 [REDACTED]

Contract Status:
Active

Term Begin:
August 1, 2011

Term End:
Open

Nature and Scope of Work:
Unit 1 Vibration and Support Mods for FW & Condensate

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO# 2296556

Major Task or Tasks Associated With:
Modification, overhaul and refurbishment of the B and C AFW

Vendor Identity:
Sulzer Pumps

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
OEM

Dollar Value:
Contract Value through Amendment 2 is [REDACTED]

Contract Status:
Active

Term Begin:
September 2, 2011

Term End:
Open

Nature and Scope of Work:
Modification, overhaul and refurbishment of the B and C AFW

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO# 2298266

Major Task or Tasks Associated With:
Shuttle Bus Service

Vendor Identity:
Franmar Corporation

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
3

Number of Bids Received:
2

Brief Description of Selection Process:
Competitive

Dollar Value:
Total Dollar Value through Amendment #1 [REDACTED]

Contract Status:
Active

Term Begin:
October 12, 2011

Term End:
Open

Nature and Scope of Work:
Shuttle Bus Service

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PSL PO# 2298406

Major Task or Tasks Associated With:
Fuel Movers for Metamic Inserts

Vendor Identity:
Master Leo Energy Services

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
3

Number of Bids Received:
1

Brief Description of Selection Process:
Competitive

Dollar Value:
Total Dollar Value through Amendment 2 is [REDACTED]

Contract Status:
Active

Term Begin:
October 12, 2011

Term End:
Open

Nature and Scope of Work:
Fuel Movers for Metamic Inserts

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO# 2290610

Major Task or Tasks Associated With:
Truck Monitoring/Waste Characterization

Vendor Identity:
Radiation Safety & Control

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
2

Number of Bids Received:
2

Brief Description of Selection Process:
Competitive

Dollar Value:
Total Dollar Value through Amendment #1 [REDACTED]

Contract Status:
Active

Term Begin:
November 4, 2011

Term End:
Open

Nature and Scope of Work:
Truck Monitoring/Waste Characterization

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PSL PO# 2297055

Major Task or Tasks Associated With:
Replacement Unit 2 LP #4 Feedwater Heaters for EPU

Vendor Identity:
Thermal Engineering

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Dollar Value through Amendment #1 [REDACTED]

Contract Status:
Active

Term Begin:
September 16, 2011

Term End:
Open

Nature and Scope of Work:
Replacement Unit 2 LP #4 Feedwater Heaters for EPU

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PSL PO# 2300139

Major Task or Tasks Associated With:
SL 1-24 Turbine Generator Installation

Vendor Identity:
Siemens Energy Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Dollar Value through Amendment #1 [REDACTED]

Contract Status:
Active

Term Begin:
November 21, 2011

Term End:
Open

Nature and Scope of Work:
SL 1-24 Turbine Generator Installation

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PSL PO# 2299624

Major Task or Tasks Associated With:
Upgrade Services for Feedwater Pumps

Vendor Identity:
Ames Group LLC

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Contract Value through Revision 4 [REDACTED]

Contract Status:
Closed

Term Begin:
November 16, 2011

Term End:
January 17, 2013

Nature and Scope of Work:
Upgrade Services for Feedwater Pumps

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO # 2301867

Major Task or Tasks Associated With:
Develop Engineering Change Packages for EPU at PTN

Vendor Identity:
Enercon Services Inc

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Dollar Value through Amendment #3 [REDACTED]

Contract Status:
Active

Term Begin:
December 28, 2011

Term End:
Open

Nature and Scope of Work:
Develop Engineering Change Packages for EPU at PTN

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO # 2261800

Major Task or Tasks Associated With:
Supply of Simulator SCD Software Translator Upgrade

Vendor Identity:
L 3 Communications Mapps Inc

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
OEM

Dollar Value:
Total Contract Value through Amendment 4 [REDACTED]

Contract Status:
Active

Term Begin:
September 28, 2010

Term End:
Open

Nature and Scope of Work:
Supply of Simulator SCD Software Translator Upgrade

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO # 2301737

Major Task or Tasks Associated With:
Construction Management Oversight Services for PTN

Vendor Identity:
PCI Energy Services

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
██████████

Contract Status:
Active

Term Begin:
December 21, 2011

Term End:
Open

Nature and Scope of Work:
Construction Management Oversight Services for PTN

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130000-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO # 2301736

Major Task or Tasks Associated With:
Construction Management Oversight Services

Vendor Identity:
Weldtech Services

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
[REDACTED]

Contract Status:
Active

Term Begin:
December 21, 2011

Term End:
Open

Nature and Scope of Work:
Construction Management Oversight Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO #2301871

Major Task or Tasks Associated With:
Develop Engineering Changes Packages for EPU at PTN

Vendor Identity:
Zachry Nuclear Engineering

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Contract Value through Amendment 1: ██████████

Contract Status:
Active

Term Begin:
December 28, 2011

Term End:
Open

Nature and Scope of Work:
Develop Engineering Changes Packages for EPU at PTN

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO #2301858

Major Task or Tasks Associated With:
Develop TPCW Changes Packages for EPU at PTN

Vendor Identity:
Sargent & Lundy Inc

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Contract Value through Amendment #1 [REDACTED]

Contract Status:
Active

Term Begin:
December 28, 2011

Term End:
Open

Nature and Scope of Work:
Develop TPCW Changes Packages for EPU at PTN

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO #2302164

Major Task or Tasks Associated With:
Valve Upgrade Services for EPU/PTN 3 & 4

Vendor Identity:
Ames Group LLC

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Dollar Value through Amendment 2 is [REDACTED]

Contract Status:
Active

Term Begin:
January 25, 2012

Term End:
Open

Nature and Scope of Work:
Valve Upgrade Services for EPU/PTN 3 & 4

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO #2303610

Major Task or Tasks Associated With:
Engineering Support

Vendor Identity:
Shaw - Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Dollar Value through Amendment #2 [REDACTED]

Contract Status:
Active

Term Begin:
February 15, 2012

Term End:
Open

Nature and Scope of Work:
Engineering Support

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PTN PO #2303735

Major Task or Tasks Associated With:

3R26 Outage Implementation Services for EPU at PTN

Vendor Identity:

Siemens Energy Inc

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Dollar Value through Amendment #1 [REDACTED]

Contract Status:

Active

Term Begin:

February 14, 2012

Term End:

Open

Nature and Scope of Work:

3R26 Outage Implementation Services for EPU at PTN

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PSL PO #2302300

Major Task or Tasks Associated With:
Unit 2 DEH Turbine Control System Replacement for EPU at PSL

Vendor Identity:
Shaw - Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Predetermined Source

Dollar Value:
Total Dollar Value through Amendment 002 is [REDACTED]

Contract Status:
Active

Term Begin:
January 11, 2012

Term End:
Open

Nature and Scope of Work:
Unit 2 DEH Turbine Control System Replacement for EPU at PSL

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO #2304432

Major Task or Tasks Associated With:
EPU Welding Implementation and Installation Services

Vendor Identity:
Weldtech Services

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Dollar Value through Amendment #5 is [REDACTED]

Contract Status:
Active

Term Begin:
February 28, 2012

Term End:
Open

Nature and Scope of Work:
EPU Welding Implementation and Installation Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO #2304903

Major Task or Tasks Associated With:
Engineering and EC Support for PTN

Vendor Identity:
Zachry Nuclear Engineering

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Dollar Value through Amendment 2 [REDACTED]

Contract Status:
Active

Term Begin:
March 8, 2012

Term End:
Open

Nature and Scope of Work:
Engineering and EC Support for PTN

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PSL PO #2307710

Major Task or Tasks Associated With:
Unit 1 Mid-cycle Analysis

Vendor Identity:
Areva NP Inc

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.
Number of Vendors Solicited:
N/A

Number of Bids Received:
N/A

Brief Description of Selection Process:
Replaces 105720

Dollar Value:
██████████

Contract Status:
Closed

Term Begin:
May 15, 2012

Term End:
January 31, 2013

Nature and Scope of Work:
Unit 1 Mid-cycle Analysis

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO #2308808

Major Task or Tasks Associated With:
Replacement of Isolated Phase Bus Duct

Vendor Identity:
Calvert Company Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
N/A

Number of Bids Received:
N/A

Brief Description of Selection Process:
Replaces 124436, which was competitively bid.

Dollar Value:
Total Dollar Value through Amendment #1 [REDACTED]

Contract Status:
Active

Term Begin:
June 12, 2012

Term End:
Open

Nature and Scope of Work:
Replacement of Isolated Phase Bus Duct

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PSL PO #2309312

Major Task or Tasks Associated With:
Valve Actuator Support Specialty Services

Vendor Identity:
Ames Group LLC

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
Total Dollar Value through Amendment #1: [REDACTED]

Contract Status:
Active

Term Begin:
June 25, 2012

Term End:
Open

Nature and Scope of Work:
Valve Actuator Support Specialty Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PSL PO #2309442

Major Task or Tasks Associated With:
Start-Up and Testing Support

Vendor Identity:
J. Givoo Consultants

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
5

Number of Bids Received:
4

Brief Description of Selection Process:
Competitive

Dollar Value:
Total Dollar Value through Amendment #2 is [REDACTED]

Contract Status:
Active

Term Begin:
July 9, 2012

Term End:
Open

Nature and Scope of Work:
Start-Up and Testing Support

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130000-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PTN PO #2309693

Major Task or Tasks Associated With:

Implementation and Installation of Unit 4 Spent Fuel Pool Heat Exchangers

Vendor Identity:

PCI Energy Services

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

7

Number of Bids Received:

4

Brief Description of Selection Process:

Competitive

Dollar Value:

Total Dollar Value through Amendment 1 [REDACTED]

Contract Status:

Active

Term Begin:

July 6, 2012

Term End:

Open

Nature and Scope of Work:

Implementation and Installation of Unit 4 Spent Fuel Pool Heat Exchangers

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

COMPANY: FLORIDA POWER & LIGHT COMPANY

For the Year Ended 12/31/2014

DOCKET NO: 130009-EI

Witness: T. O. Jones

Contract No.:
PTN PO #2311510

Major Task or Tasks Associated With:
Engineering Support for EPU (PTN 4)

Vendor Identity:
Shaw - Stone & Webster

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
██████████

Contract Status:
Active

Term Begin:
August 16, 2012

Term End:
Open

Nature and Scope of Work:
Engineering Support for EPU (PTN 4)

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PSL PO #2310927

Major Task or Tasks Associated With:

PSL 2-20 Turbine Generator Services

Vendor Identity:

Siemens Energy Inc

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total Dollar Value through Amendment #1 [REDACTED]

Contract Status:

Active

Term Begin:

August 7, 2012

Term End:

Open

Nature and Scope of Work:

PSL 2-20 Turbine Generator Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO #2311900

Major Task or Tasks Associated With:
PTN 4-27 Turbine Generator Services

Vendor Identity:
Siemens Energy Inc

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
Single Source

Dollar Value:
[REDACTED]

Contract Status:
Active

Term Begin:
September 5, 2012

Term End:
Open

Nature and Scope of Work:
PTN 4-27 Turbine Generator Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN PO 2311037

Major Task or Tasks Associated With:
Coating Services

Vendor Identity:
Williams Specialty Services

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
N/A

Number of Bids Received:
N/A

Brief Description of Selection Process:
Replaces Corporate Blanket 4500412063, which was competitively bid.

Dollar Value:
[REDACTED]

Contract Status:
Active

Term Begin:
August 10, 2012

Term End:
Open

Nature and Scope of Work:
Coating Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PTN PO 2314332

Major Task or Tasks Associated With:

Radiography Testing Services

Vendor Identity:

Team Industrial Services Inc

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

Total dollar value through Revision 1 is [REDACTED]

Contract Status:

Active

Term Begin:

October 30, 2012

Term End:

Open

Nature and Scope of Work:

Radiography Testing Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PTN PO 2315635

Major Task or Tasks Associated With:

Turbine Bypass and Steam Dump Control Systems Valves

Vendor Identity:

Control Components

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Single Source

Dollar Value:

██████████

Contract Status:

Active

Term Begin:

December 14, 2012

Term End:

Open

Nature and Scope of Work:

Turbine Bypass and Steam Dump Control Systems Valves

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PSL PO #2301976

Major Task or Tasks Associated With:
Spent Fuel Handling

Vendor Identity:
Westinghouse Electric Co.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
1

Number of Bids Received:
1

Brief Description of Selection Process:
OEM

Dollar Value:
Total Dollar Value through Amendment #3 is [REDACTED]

Contract Status:
Active

Term Begin:
February 1, 2012

Term End:
Open

Nature and Scope of Work:
Spent fuel handling modification for EPU

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PSL Release 014 Blanket Contract 2260135

Major Task or Tasks Associated With:

Radiation Protection Services

Vendor Identity:

Bartlett Nuclear Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Blanket Contract 2260135 Replaces Blanket Contract 113086 which was issued on a competitive basis.

Dollar Value:

Total Dollar Value through Amendment #5 is [REDACTED]

Contract Status:

Active

Term Begin:

October 26, 2010

Term End:

Open

Nature and Scope of Work:

Radiation Protection Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:
PTN Release 013 Blanket Contract 2262301

Major Task or Tasks Associated With:
Radiation Protection Services

Vendor Identity:
Bartlett Nuclear Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):
Direct*
*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:
3

Number of Bids Received:
3

Brief Description of Selection Process:
Blanket Contract 2262301 Replaces Blanket Contract 113293 which was issued on a competitive basis.

Dollar Value:
Total Dollar Value through Amendment #1 [REDACTED]

Contract Status:
Active

Term Begin:
January 30, 2012

Term End:
Open

Nature and Scope of Work:
Radiation Protection Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PTN Release 017 Blanket Contract 2262301

Major Task or Tasks Associated With:

Radiation Protection Services

Vendor Identity:

Bartlett Nuclear Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Blanket Contract 2262301 Replaces Blanket Contract 113293 which was issued on a competitive basis.

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

June 21, 2012

Term End:

Open

Nature and Scope of Work:

Radiation Protection Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PTN Release 004 to Blanket Contract 2287944

Major Task or Tasks Associated With:

EPU Radioactive Waste Disposal

Vendor Identity:

Energy Solutions, LLC

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Blanket Contract 2287944 replaced Blanket Contract 99395 which was issued as a Single Source.

Dollar Value:

██████████

Contract Status:

Active

Term Begin:

March 7, 2012

Term End:

Open

Nature and Scope of Work:

EPU Radioactive Waste Disposal

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION

COMPANY: FLORIDA POWER & LIGHT COMPANY

DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PTN Release 086 to Blanket Contract 2260140

Major Task or Tasks Associated With:

Security Services for EPU Unit 4

Vendor Identity:

G4S Regulated Security Solutions Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

1

Number of Bids Received:

1

Brief Description of Selection Process:

Blanket Contract 2260140 Replaces Blanket Contract 118419 which was issued as a Single Source.

Dollar Value:

[REDACTED]

Contract Status:

Active

Term Begin:

December 17, 2012

Term End:

Open

Nature and Scope of Work:

Security Services for EPU Unit 4

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PTN Release 007 to Blanket Contract 2293489

Major Task or Tasks Associated With:

Supplementary Maintenance and Related Services

Vendor Identity:

Stone & Webster Construction Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Blanket Contract 2293489 was competitively bid

Dollar Value:

Total Dollar Value through Amendment # 5 is [REDACTED]

Contract Status:

Active

Term Begin:

September 7, 2011

Term End:

Open

Nature and Scope of Work:

Supplementary Maintenance and Related Services

**St. Lucie and Turkey Point Uprate Project
Construction Costs and Carrying Costs on Construction Cost Balance
Projected Filing: Contracts Executed**

Schedule P-7B (Projection)

FLORIDA PUBLIC SERVICE COMMISSION
COMPANY: FLORIDA POWER & LIGHT COMPANY
DOCKET NO: 130009-EI

EXPLANATION: For all executed contracts exceeding \$1,000,000, including change orders, provide the contract number or identifier, major tasks, vendor identity, vendor affiliation if any, number of vendors solicited, number of bids received, current contract status, the current term of the contract, and the current nature/scope of work.

For the Year Ended 12/31/2014
Witness: T. O. Jones

Contract No.:

PSL Release 009 to Blanket Contract 2293489

Major Task or Tasks Associated With:

Supplementary Maintenance and Related Services

Vendor Identity:

Stone & Webster Construction Inc.

Vendor Affiliation (specify 'direct' or 'indirect'):

Direct*

*This indicates the contractual arrangement. FPL has no direct or indirect corporate affiliation with the vendor.

Number of Vendors Solicited:

3

Number of Bids Received:

3

Brief Description of Selection Process:

Blanket Contract 2293489 was competitively bid

Dollar Value:

Total Dollar Value through Amendment # 1 is [REDACTED]

Contract Status:

Active

Term Begin:


October 13, 2011

Term End:


Open

Nature and Scope of Work:

Supplementary Maintenance and Related Services

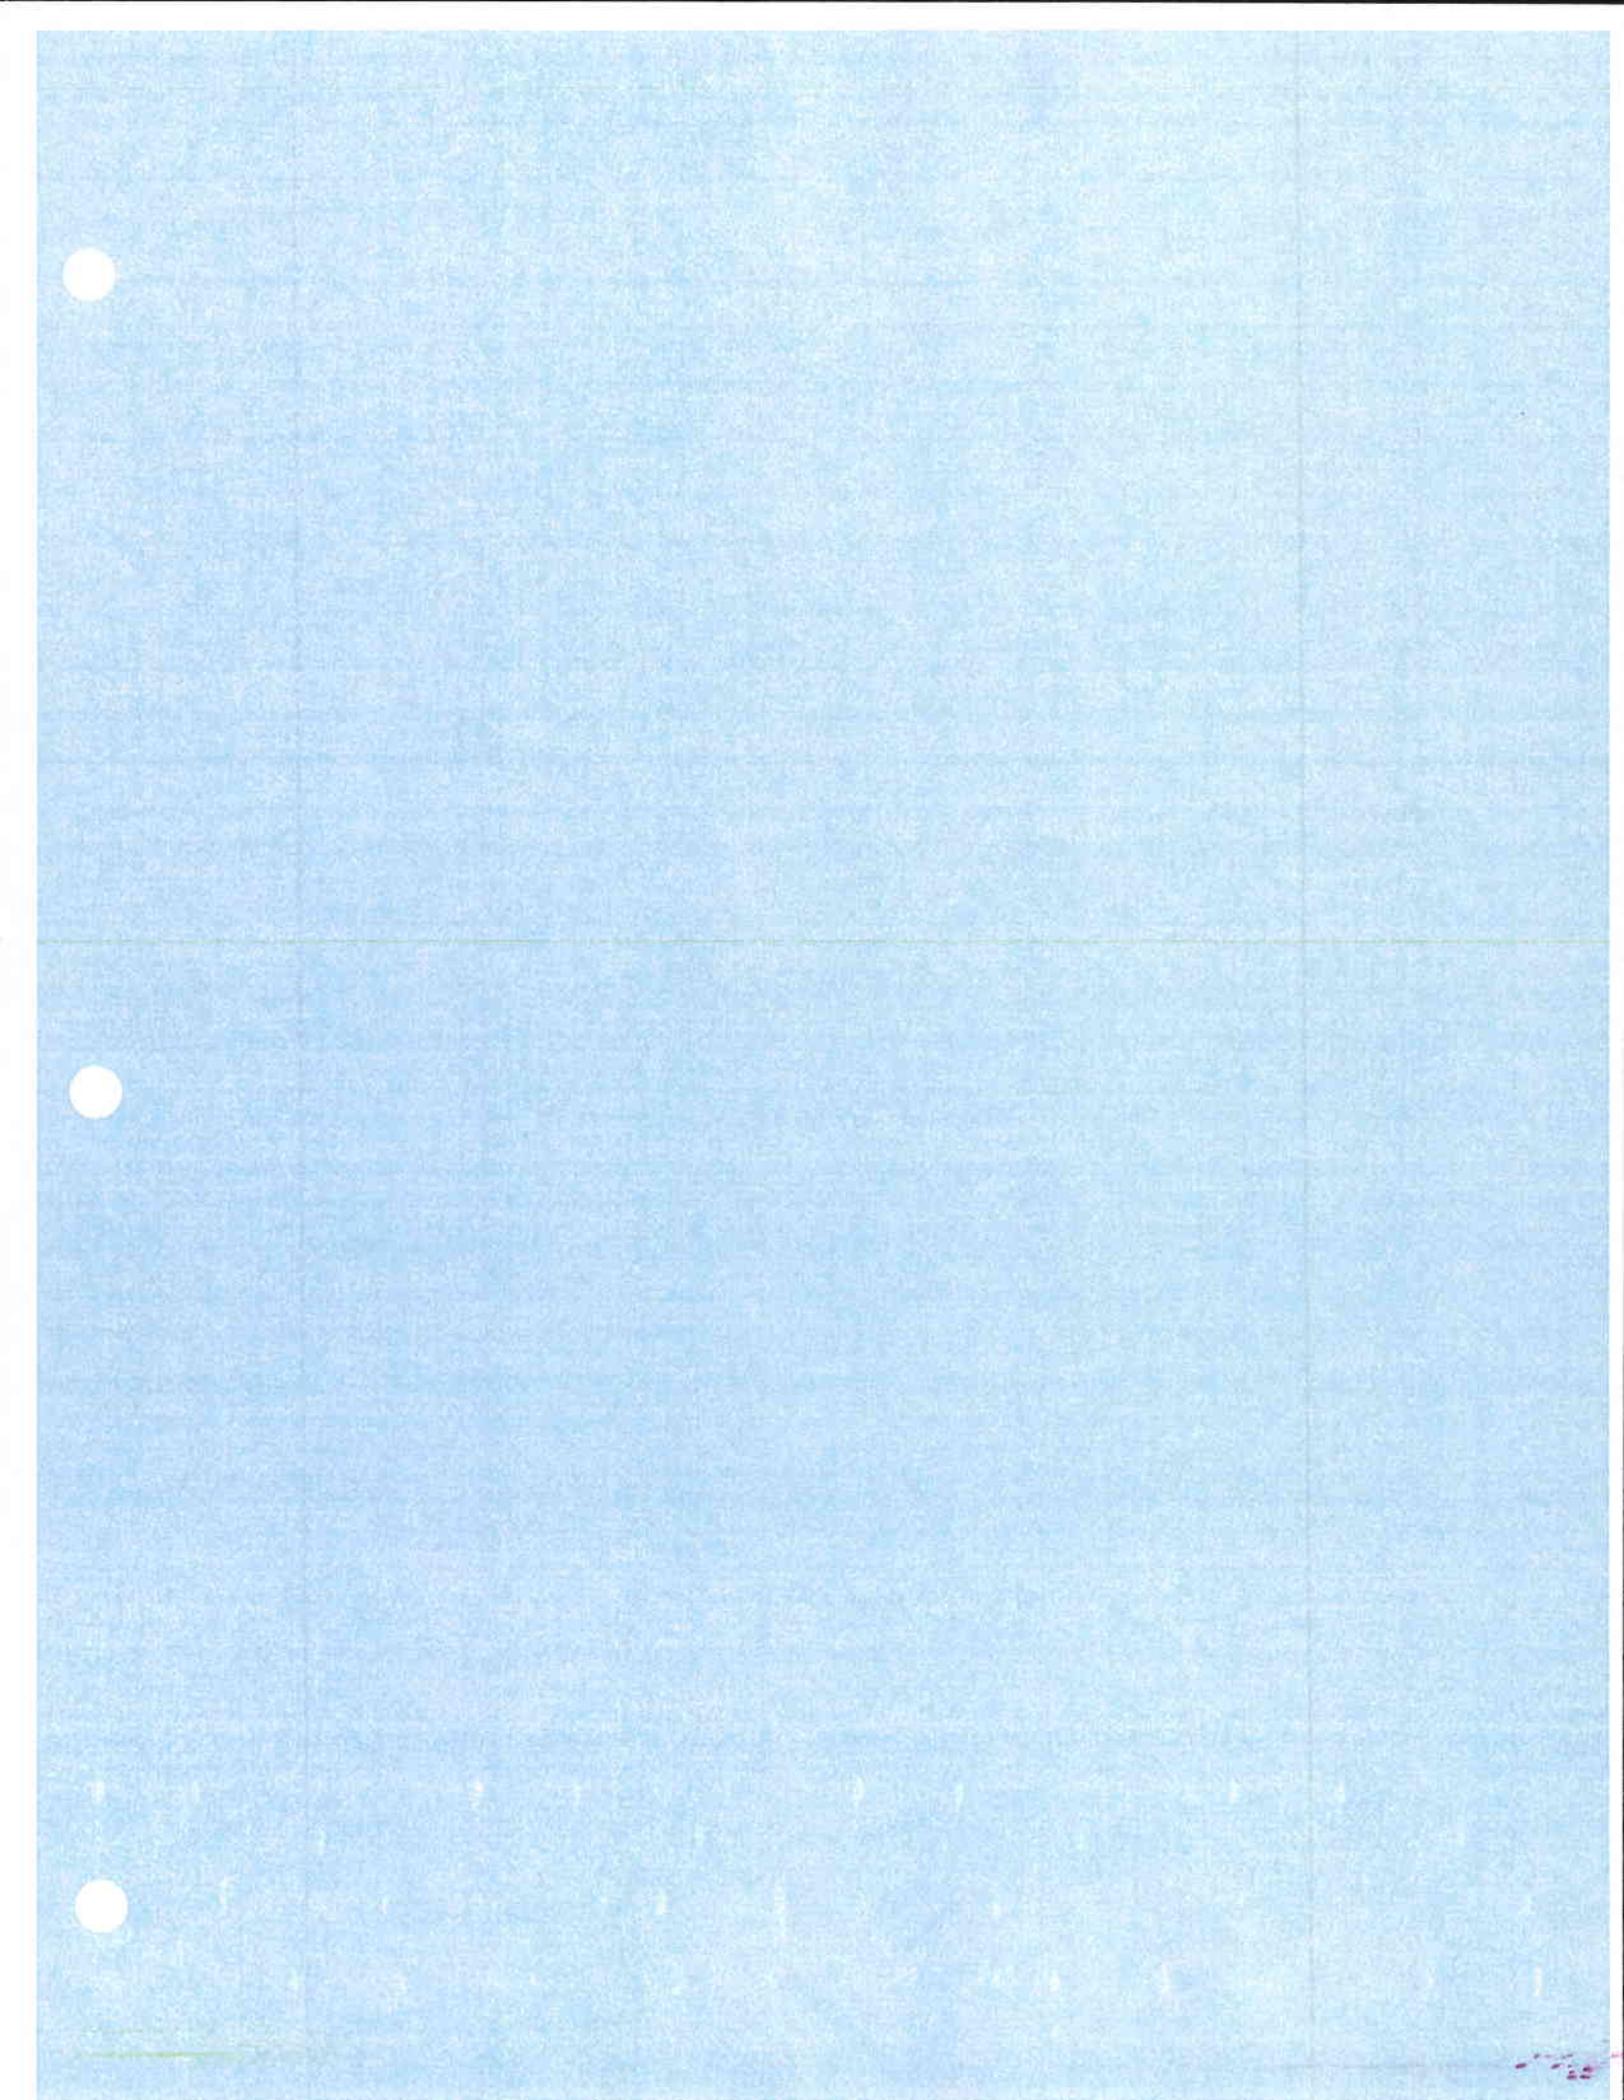

1 were based upon previous experience, known scope(s) of work, productivity
2 factors, and prevailing pertinent wage rates. Cash flow projections for items
3 identified in the Risk Register were based upon anticipated engineering,
4 material procurement, and outage implementation time horizons.

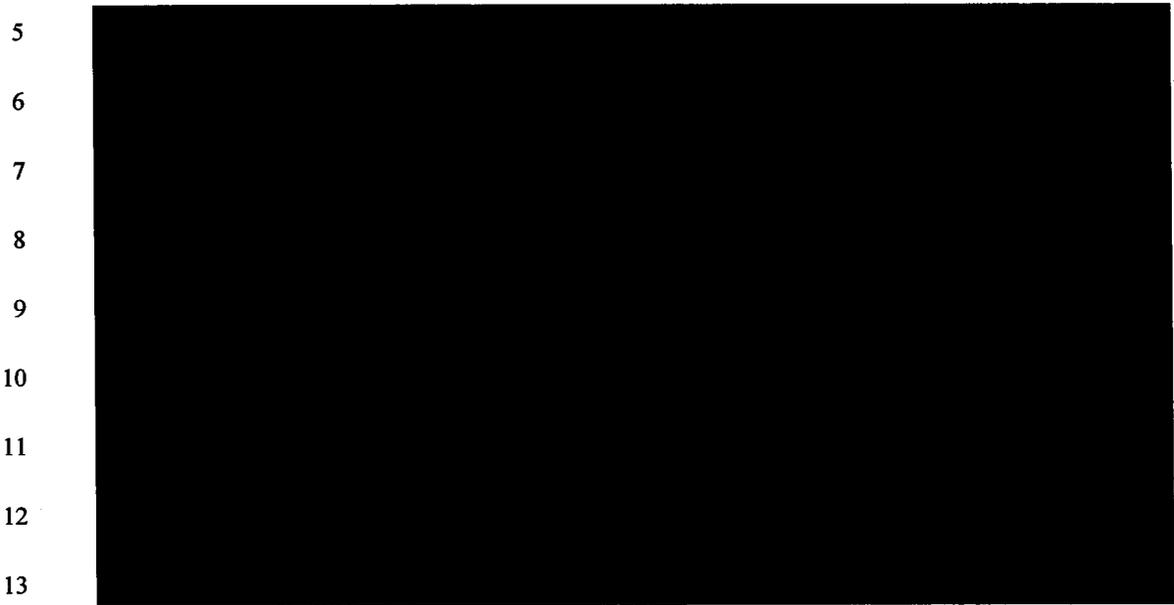

14 **Q. What types of costs does FPL plan to incur for the Uprate project in**
15 **2013?**

16 A. As indicated in Exhibit TOJ-13, Schedules AE-4 and AE-6, and summarized
17 in Exhibit TOJ-26, costs are being incurred in the following categories:
18 Licensing; Engineering & Design; Project Management; Power Block
19 Engineering, Procurement, Etc.; Non-Power Block Engineering, Procurement,
20 Etc.; EPU Recoverable O&M; and Transmission Capital. There are no
21 Permitting costs in 2013. Please note that the dollar values in my testimony
22 are the estimated EPU resource requirements, and do not include certain

